



**Downey Unified**  
SCHOOL DISTRICT

# Facilities Update

February 24, 2026

# Agenda

---

- First Four Update
- Update on Funding
- Recommendation Criteria
- Site Selection Phase II TK-K



**Downey Unified**  
SCHOOL DISTRICT

# First Four



# Update



**Downey Unified**  
SCHOOL DISTRICT



# Time, Cost, Scope: The Reality of Public Construction

---

Project success hinges on balancing three competing priorities: cost, scope, and time

- **Budget**
- **Scope**
- **Schedule**





# From Unbuildable to Unstoppable: How We Secured and Strengthened Measure K

---

## Where We Started (2019-2023)

- Early designed exceeded Measure K funding capacity and were not buildable.
- Cost estimates lacked value engineering, sequencing logic, and modernization best practices.
- Workstreams were fragmented across four architects and four contactors operating independently.
- Pre-construction guidance focused on cutting scope rather than optimizing solutions for students.

## Why This Matters

The original program trajectory would have exhausted funds before delivering promised projects. We chose to pause, diagnose, and rebuild the foundation; **ensuring long-term success.**



# Timeline Breakdown

---

## Phase 1: Original Design Jan 2023 – Jan 2024 (12 months)

- Result: Overbudget + no DSA submission
- No vertical progress.

## Phase 2: Pre Construction Lease-Leaseback Contractor Attempt Feb 2024 – April 2024 (3 months)

- Result: Still overbudget

## Phase 3: District-Led Reset April 2024 – Feb 2025 (10 months)

- Result: Within 5 months, DSA packages start getting submitted



# Timeline Breakdown – Original Design

---

## Original Design Jan 2023 – Jan 2024 (12 months)

- Result: Overbudget + no DSA submission
- No vertical progress.

## DSA Submission & Approval June 2024 – June 2025 (12 months)

- Design Development to Construction Documents
- DSA submission and approval

## Construction Start – June 2025-May 2026 - **\$100 million over budget**



# The Reset: What We Did to Protect Measure K

---

## Our Leadership Act

- Re-engineered all four sites to ensure *every project is fully* buildable within bond funding.
- Standardized design packages, site logic, and DSA submission structures across architects.
- Applied rigorous cost validation and benchmarking across four firms to eliminate unnecessary inflation.
- Introduced CUUBE and other modernization strategies that produced up to \$66M in systemwide savings without reducing quality.
- Shifted to an active-owner model, driving accountability, accuracy, and alignment districtwide.

## The Result

Measure K now has a **unified, disciplined, financially sound program** that protects community dollars and strengthens long-term outcomes.



# Building It Right: DSA as a Strategic Advantage

---

## Where We Are Today

- Rio Hondo: Modernization complete; new construction in process.
- Garcia: Modernization  $\frac{3}{4}$  complete, new construction awaiting approval
- Rio San Gabriel: TK/K and modernization fully approved; remaining packages in final review cycle. TK-K footings and steel complete.
- Carpenter: Round 2 DSA responses submitted, DSA 3<sup>rd</sup> round scheduled for mid-March for construction and modernization.


## What This Shows

Your facilities team has created a steady, reliable, well-managed pipeline



# DSA Timeline Breakdown

Site	Package	Duration in DSA
Carpenter	PARKING LOT	7 months
	MOD	Est. 9 months
	NEW CONST.	Est. 9 months
Garcia	MOD	10 months
	NEW CONST.	Est. 9 months
Rio Hondo	MOD	5 months
	NEW CONST.	8 months
Rio San Gabriel	TK/K	9 months
	MOD	9 months
	ADMIN	6.5 months
	KITCHEN	7 months
	NEW CLASSRMS	Est. 7 months



# June 2025 Timeline

## Rio Hondo Elementary School Phasing Plan

### Modernization

DSA Submission – Fall 2024 thru Winter 2024  
Construction – Winter 2025 thru Summer 2026

### TK/K Buildings

DSA Submission – Winter 2024 thru Spring 2025  
Construction – Summer 2025 thru Winter 2025

### New Building


DSA Submission – Spring 2025 thru Fall 2025  
Construction – Winter 2025 thru Summer 2026

### Site Work/Parking Lots

DSA Submission – Fall 2024 thru Winter 2024  
Construction – Winter 2025 thru Summer 2026

**Completion Date August 2026**





# Adjusted Timeline


## Rio Hondo Elementary School Phasing Plan



\* **Still on track for Summer 2026**



# Rio Hondo Elementary School Phasing Plan

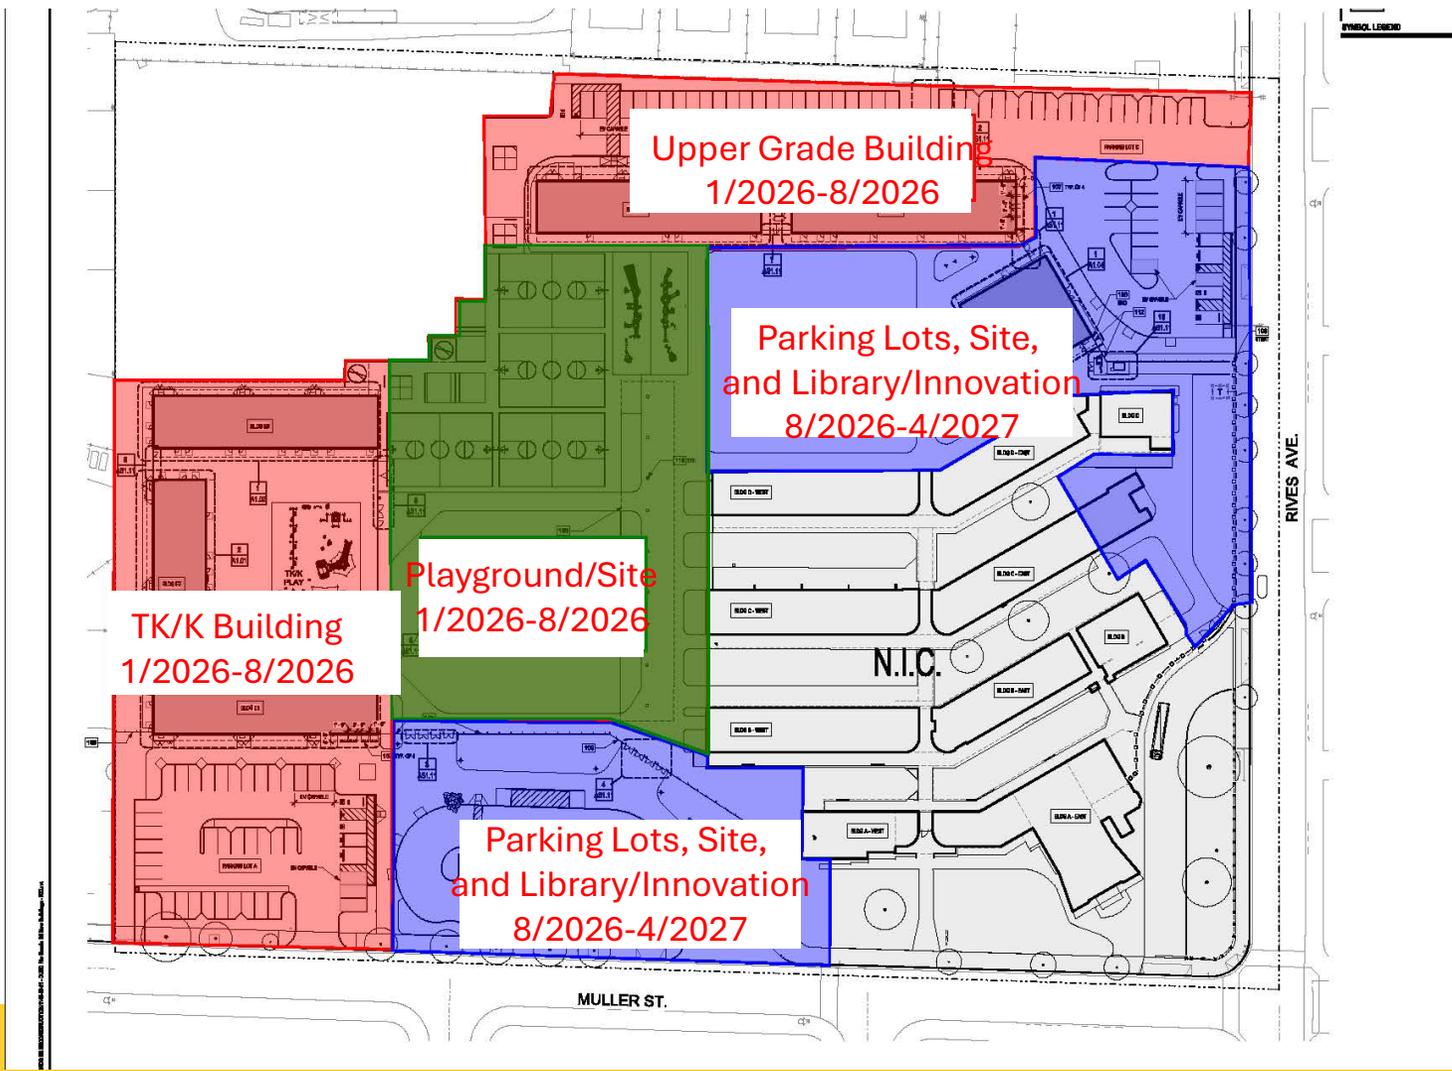


**PENDING:**

- **Kitchen & Lunch Shelters**



# Rio Hondo Elementary School Phasing Plan

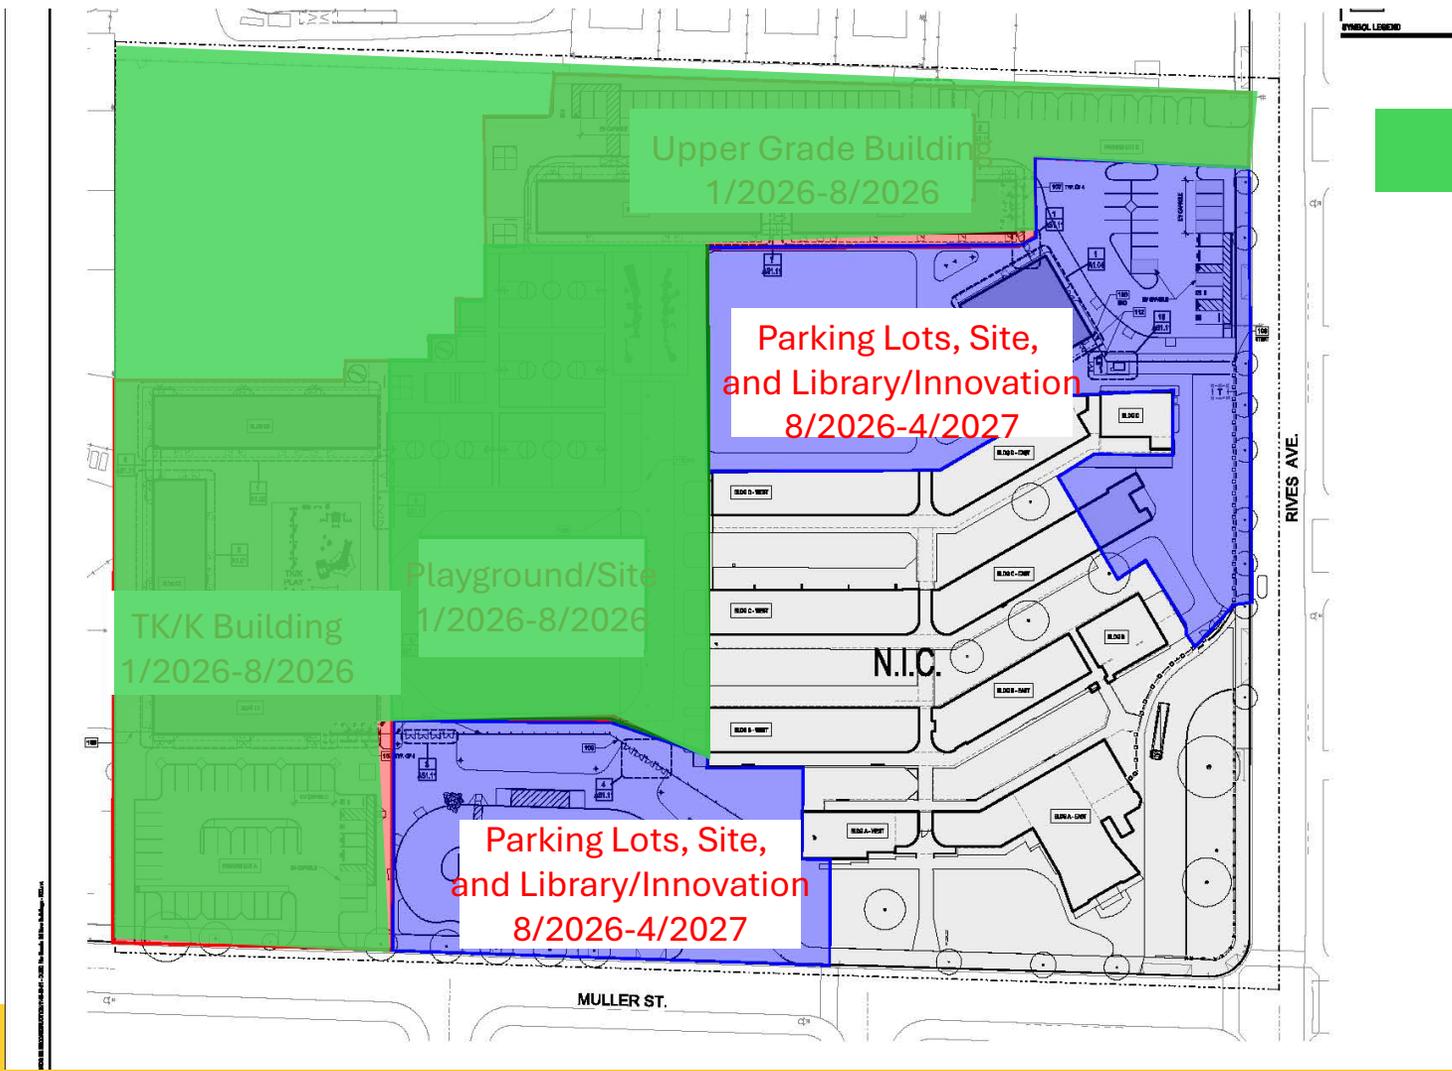

**Areas Complete by Summer 2026**

**PENDING:**

- **Kitchen & Lunch Shelters**



Downey Unified  
SCHOOL DISTRICT

# June 2025 Timeline

## Rio San Gabriel Elementary School Phasing Plan



**Completion Date August 2026**





Downey Unified  
SCHOOL DISTRICT

# Adjusted Timeline

## Rio San Gabriel Elementary School Phasing Plan

\*

TK/K Buildings

DSA Submission – Fall 2024 thru Fall 2025  
Construction – Fall 2025 thru Summer 2026

\*

Modernization

DSA Submission – Winter 2024 thru Spring 2025  
Construction – Spring 2026 thru Summer 2026

New Buildings

Admin & 5 Classroom Building

DSA Submission – Spring 2025 thru Fall 2025  
Construction – Fall 2026 thru Summer 2027

Site Work/Parking Lots

DSA Submission – Spring 2025 thru Fall 2025  
Construction – Winter 2025 thru Summer 2027

**\* Still on track for Summer 2026**





# Rio San Gabriel Elementary School Phasing Plan



**SITE PLAN**

NOTE: REFER TO INCLUDE OR WHERE SHOWN EXCEPT THE DRAWINGS CALL OUT.

LEGEND:

- AD
- MG
- MS
- CS
- DS
- DS


**SITE PLAN**

1. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
2. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
3. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
4. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
5. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
6. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
7. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
8. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
9. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
10. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
11. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
12. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.
13. REFER TO CIVIL PLANS FOR ALL PLANNING AND ADJUSTMENTS.

**Pending Approvals in DSA:**  
**New Classroom Building - Anticipated approval end of February**  
**Kitchen Modernization - Anticipated approval mid March**



# Rio San Gabriel Elementary School Phasing Plan

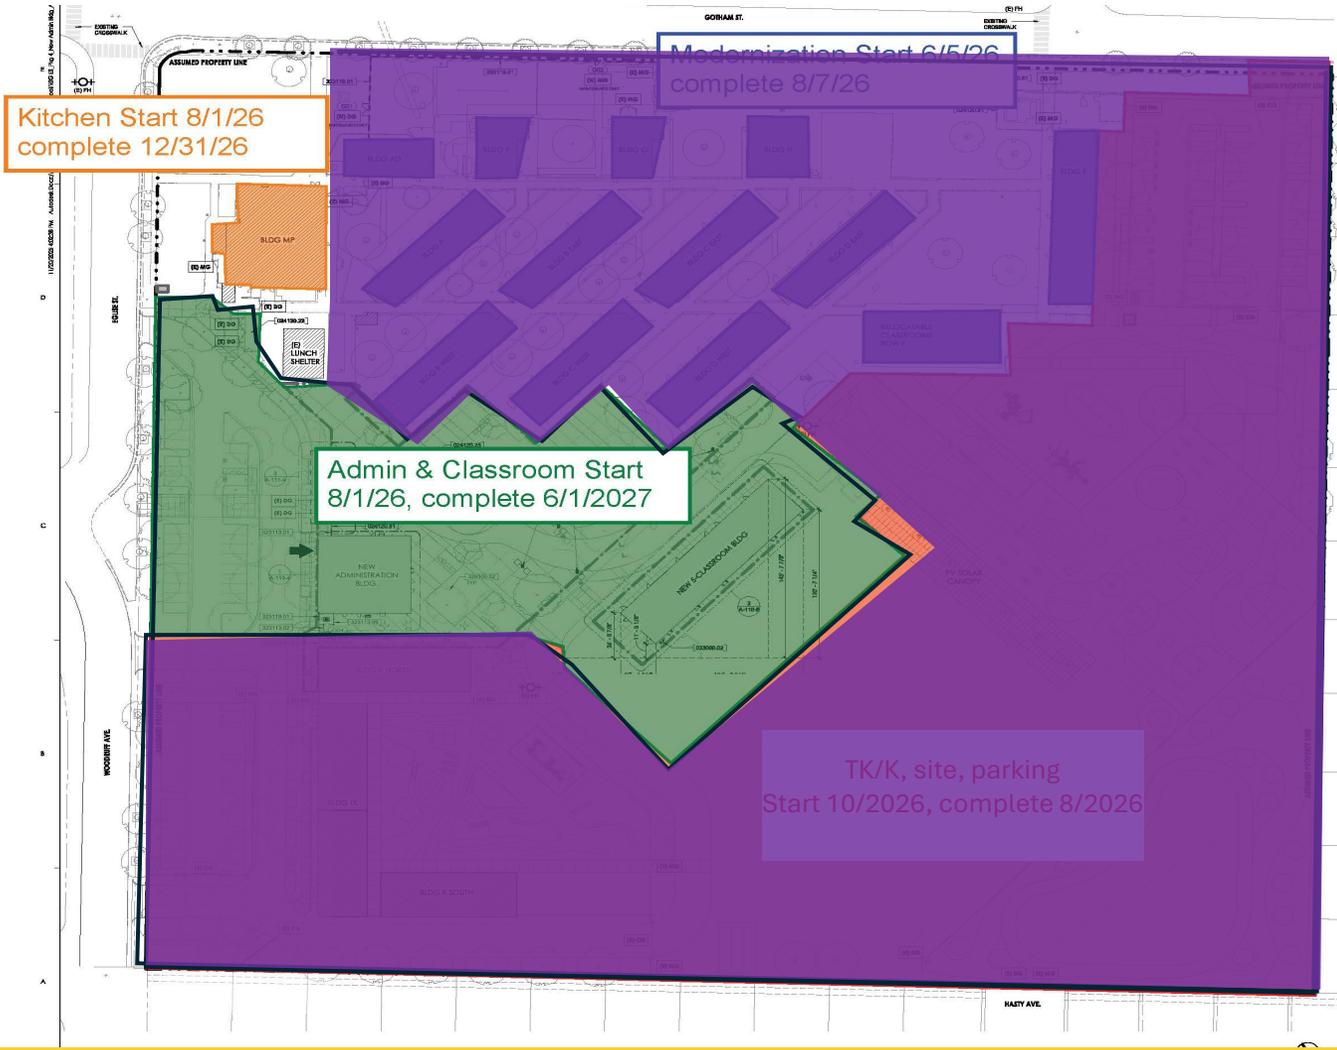

 **Areas Complete by Summer 2026**

NOTE: KEYNOTES INCLUDE OR WHILE SOME EXTEND TO THE DRAWINGS ONLY.

**SITE PLAN 1**

+O+  
05 PH

— — — — —  
— — — — —  
— — — — —  
— — — — —  
— — — — —  
— — — — —

**SITE PLAN 2**

1. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
2. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
3. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
4. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
5. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
6. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
7. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
8. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
9. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
10. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
11. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
12. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.
13. REFER TO CIVIL PERMITS FOR PLANNING AND PERMITS.



Downey Unified  
SCHOOL DISTRICT

# June 2025 Timeline

## Garcia Elementary School Phasing Plan



**Completion Date August 2026**





Downey Unified  
SCHOOL DISTRICT

# Adjusted Timeline

## Garcia Elementary School Phasing Plan




\* Still on track for Summer 2026






# Garcia Elementary School Phasing Plan

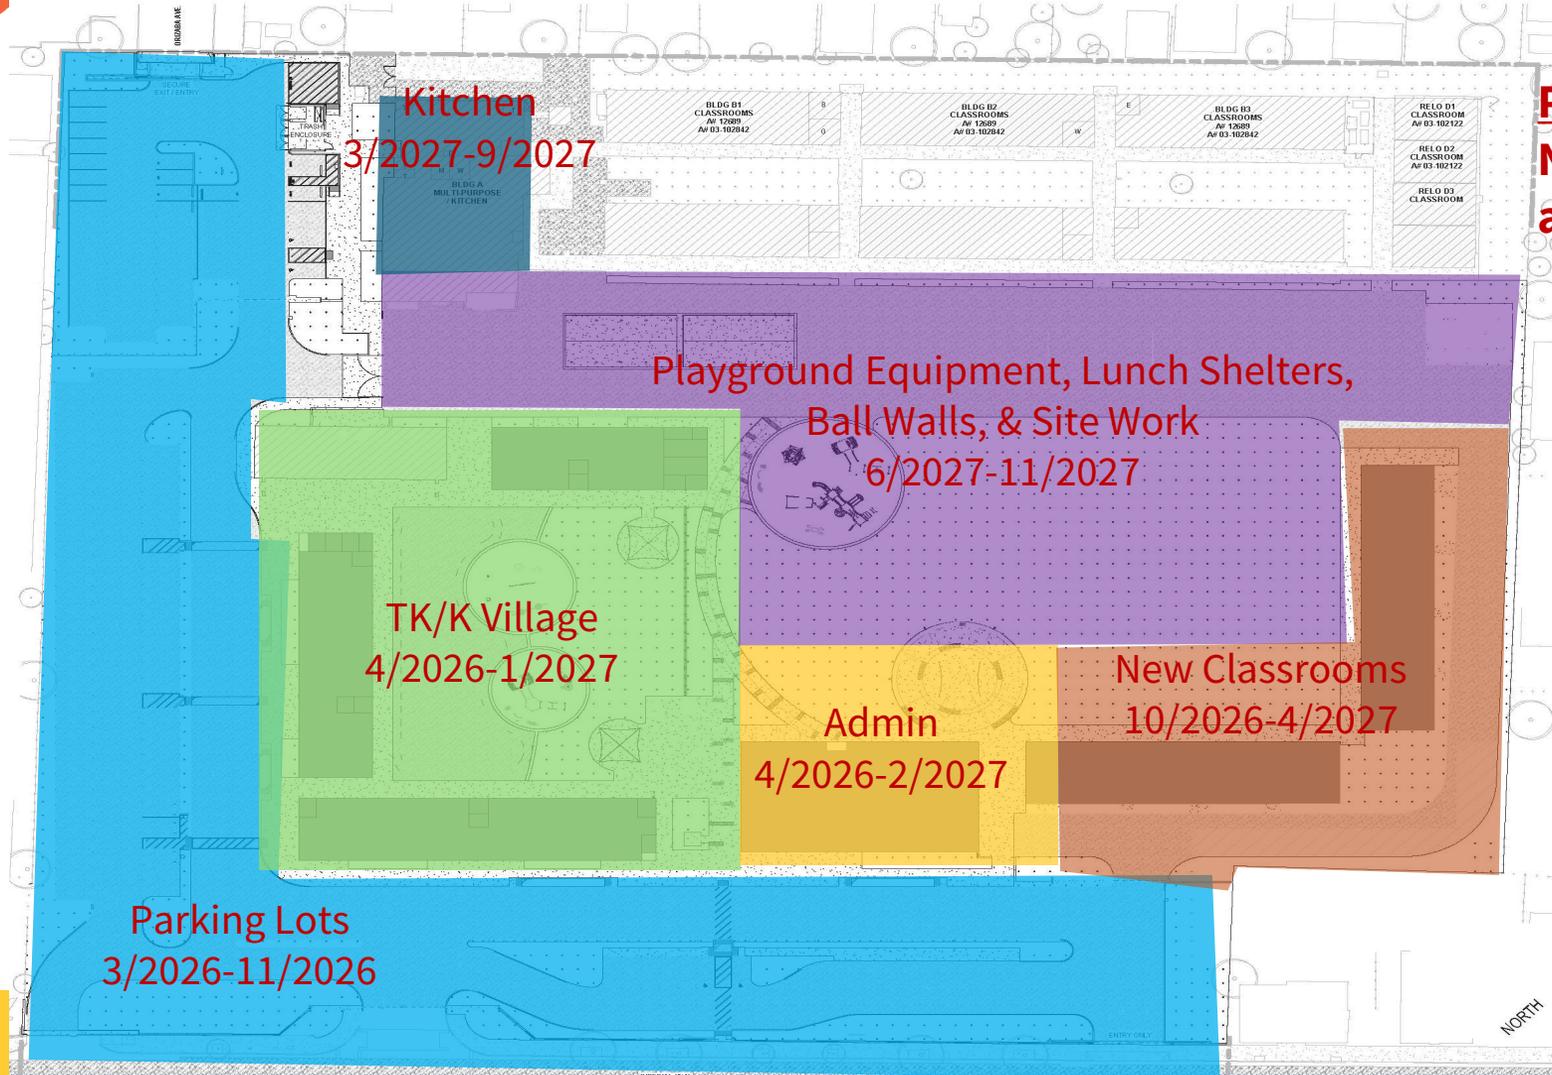

**Pending Approvals in DSA:**  
**New Construction – Anticipated approval beginning of March**



# Garcia Elementary School Phasing Plan

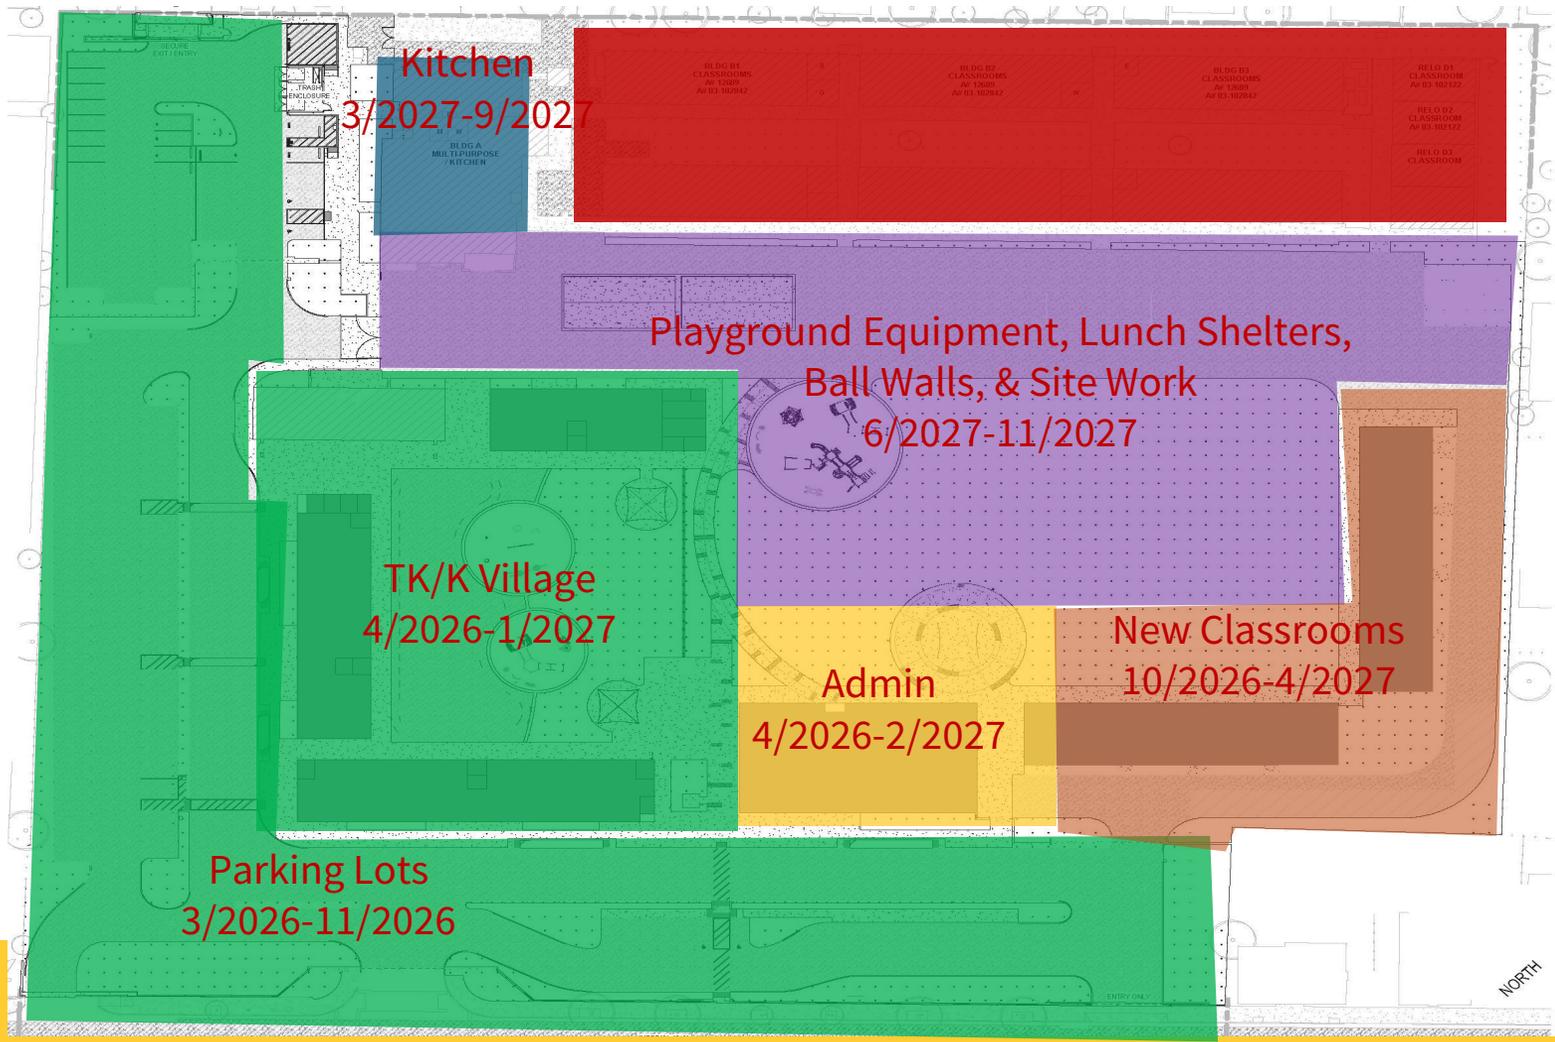



Downey Unified  
SCHOOL DISTRICT

# June 2025 Timeline

## Carpenter Elementary School Phasing Plan

**TK/K & New Building**

DSA Submission – Fall 2024 thru Spring 2025  
Construction – Summer 2025 thru Spring 2026



**Modernization**

DSA Submission – Spring 2025 thru Winter 2025  
Construction – Spring 2026 thru Summer 2026



**Site Work/  
Parking Lots**

DSA Submission – Fall 2024 thru Spring 2025  
Construction – Spring 2026 through Summer 2026

**Completion Date August 2026**





Downey Unified  
SCHOOL DISTRICT

# Adjusted Timeline

## Carpenter Elementary School Phasing Plan

TK/K & New Building

DSA Submission – Spring 2025 thru Spring 2026  
Construction – Spring 2026 thru Spring 2027

\* Modernization

DSA Submission – Spring 2025 thru Spring 2026  
Construction – Spring 2026 thru Summer 2026

\* Site Work/  
Parking Lots


DSA Submission – Winter 2024 thru Winter 2025  
Construction – Spring 2026 through Summer 2026

\* Still on track for Summer 2026





# Carpenter Elementary School Phasing Plan

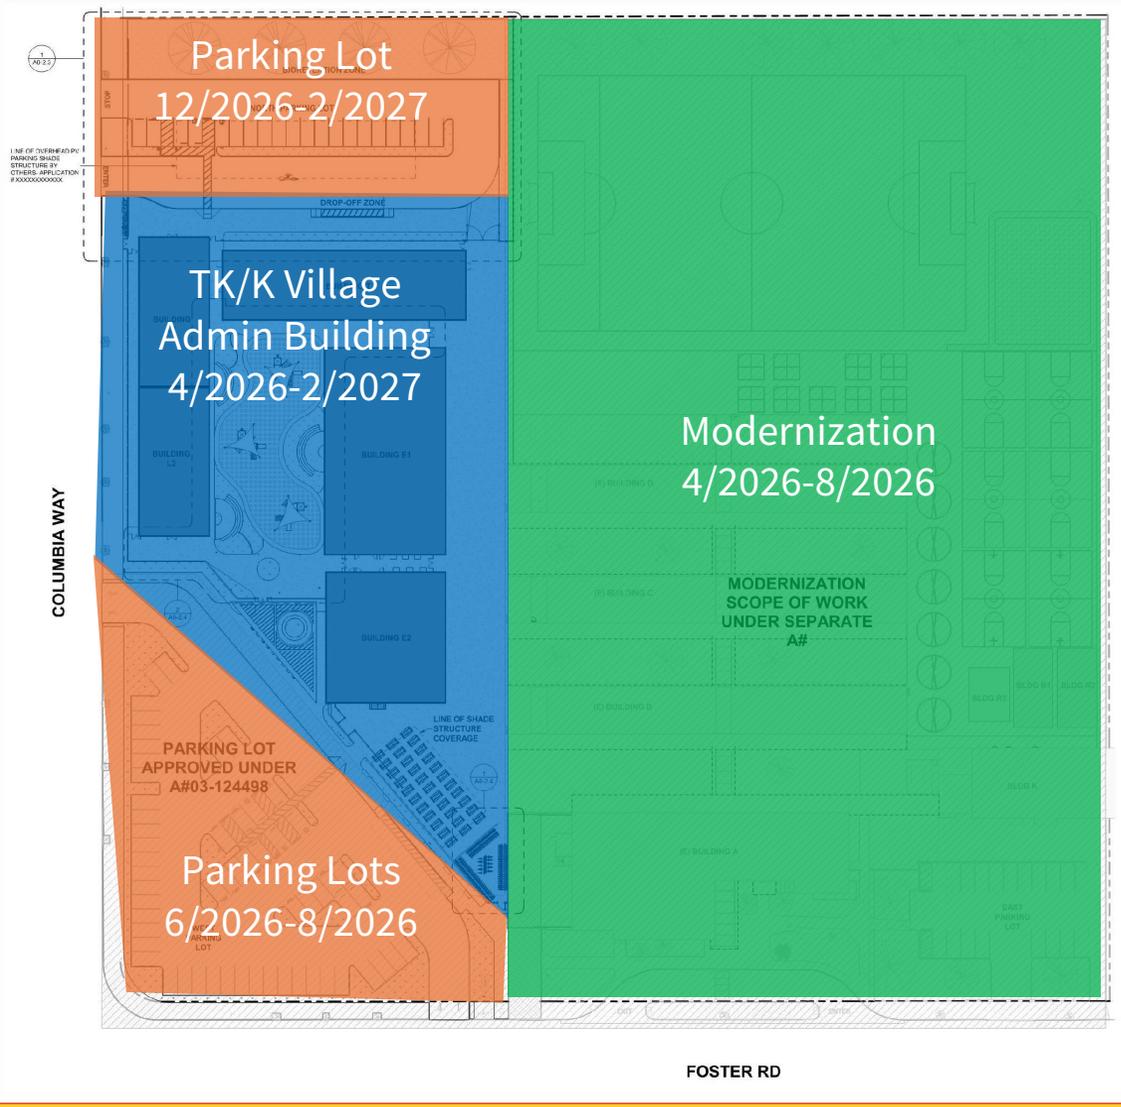

**DSA Dates:**  
**Modernization – Anticipated approval end of February**  
**New Construction – Anticipated approval beginning March**





# Summary of Work at All Sites

---

## On Target by August 2026

- **Carpenter:** Modernization, Main Parking Lot, ½ New Buildings
- **Garcia:** Modernization, ½ TK/K Buildings
- **Rio Hondo:** Modernization, TK/K Village, and New Classroom Buildings
- **Rio San Gabriel:** Modernization, TK/K Village, and Parking Lots

## Adjusted Schedule Items

- **Carpenter:** ½ New Buildings
- **Garcia:** ½ TK/K Village, Admin, New Classroom Buildings
- **Rio Hondo:** Library/Innovation, Parking Lots
- **Rio San Gabriel:** Admin and New Classroom Building

# State Bond vs. No State Bond Site Layouts

## If Proposition 2 passes in November...

- Remove most portables on site
- Modernize/build administration buildings
- Address non-student experience areas

## If Proposition 2 **DOES NOT** pass in November...

- Some portables remain on sites
- Focus on student-experience areas



# How Do We Know We Are On Track?

- “You seem to be only looking out for your budget,” Blach Construction (January 2026).
- Dedicated, active, district-focused management results in outcomes that beat plan estimates.

Site	Original FPM Budget**	Lease-Leaseback Estimate	Updated No Proposition 2	Updated No Proposition 2 (w/CES Office)	Proposition 2 Passes	Current Project Est	Current Est Savings
Carpenter*	\$38,476,106	\$86,250,000	\$66,000,000	\$71,871,519	\$71,871,519	\$71,871,519	TBD
Garcia (Imperial)	\$49,352,179	\$80,000,000	\$60,000,000	\$60,000,000	\$73,585,451	\$66,876,112	\$6,709,339
Rio Hondo	\$37,734,608	\$74,554,064	\$45,000,000	\$45,000,000	\$57,093,651	\$47,030,567	\$10,063,084
Rio San Gabriel	39257418	\$83,750,000	\$45,000,000	\$45,000,000	\$56,869,726	\$49,050,139	\$7,819,587
Total	\$164,820,311	\$324,554,064	\$216,000,000	\$221,871,519	\$259,420,347	\$234,828,337	\$24,592,010

\* DSA Expected ~3/5/26

\*\* Includes soft costs



# Reflections & Takeaways

---

**Better Communication – Good News & Bad News**

**Future Phases – Single Architect**

**Plan Approval For Next Sites**



# Rio Hondo Elementary School – Modernization

**COMPLETED**





# Rio Hondo Elementary School – New Construction



**2 of 3 TK/K Classroom Building Steel**



**3 of 3 TK/K Classroom Building Steel**





## Rio San Gabriel Elementary School – TK/K Buildings & Parking Lot



**K North and TK North & South Buildings**



**Standing Under K North Building**





## **Rio San Gabriel Elementary School – TK/K Buildings & Parking Lot**



**Temporary Entrance to Northeast Teacher Lot**



**Northeast Teacher Lot**





# Garcia Elementary School - Modernization





**Downey Unified**  
SCHOOL DISTRICT

**BREAK**

# Funding



# Update



**Downey Unified**  
SCHOOL DISTRICT



# Downey Unified School District Measure K

## Original Base Case Bond Phasing Plan Placed on November Ballot

- ✓ **Assumed Annual Assessed Valuation Growth Rate for Planning Purposes: 4.50%**
- ✓ **Targeted Tax Rate of \$50 Per \$100,000 of Assessed Valuation**
- ✓ **Nominal Use of Capital Appreciation Bonds**

### Bond Issuance Phasing Plan Five Equal Draws Over 12 Years

Series A (Year 1):	\$100,800,000
Series B (Year 4):	\$100,800,000
Series C (Year 7):	\$100,800,000
Series D (Year 10):	\$100,800,000
Series E (Year 12):	\$100,800,000



# Downey Unified School District Measure K Modified Bond Phasing Plan With Highest First Draw

- ✓ **Assumed Annual Assessed Valuation Growth Rate for Planning Purposes: 4.50%**
- ✓ **Targeted Tax Rate of \$50 Per \$100,000 of Assessed Valuation**
- ✓ **Nominal Use of Capital Appreciation Bonds**

## Bond Phasing Plan With Highest First Draw / All Remaining Draws At Least \$80 Million

<b>Series A (Year 1):</b>	<b>\$125,000,000</b>
Series B (Year 4):	\$80,000,000
Series C (Year 7):	\$110,000,000
Series D (Year 10):	\$80,000,000
Series E (Year 12):	\$109,000,000




# Changes to the Plan

---

- Market Forces
  - Assessed Value (AV) Growth Rates
  - Interest Rates
- Proposition 2 Passed: Project Scope Increased

# District Assessed Value <sup>(1)</sup>

The District's 2025-26 AV increased **3.75%** over 2024-25 AV to \$17.75 billion

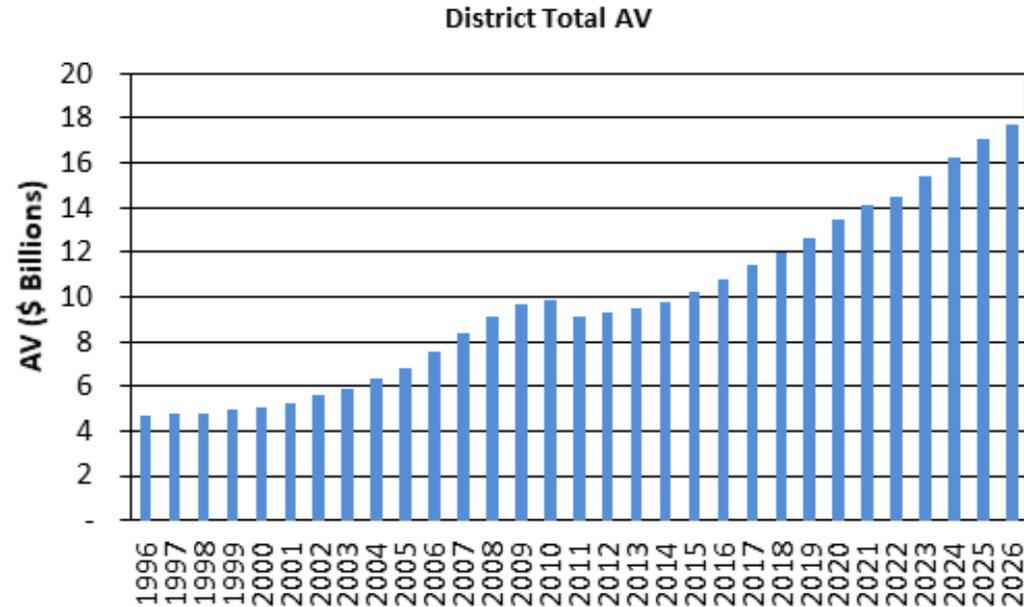

<b>Growth Statistics</b>			
<b>Annualized Growth Rates:</b>		<b>Lowest Rolling Averages:</b>	
1-year:	3.75 %	3-year:	-1.25 %
5-year:	4.63	5-year:	0.33
10-year:	5.12	10-year:	2.74
15-year:	4.51	15-year:	3.54
20-year:	4.37	20-year:	4.24
25-year:	4.98	25-year:	4.51
30-year:	4.53	30-year:	4.53

(1) Source: California Municipal Statistics, Inc.

# Municipal Bond Interest Rates

Municipal bond interest rates have increased significantly from the historic lows during the pandemic

- ◆ The District's Measure K bond program was built on the assumption that the interest rates achieved for Measure O, Series C (sold in May 2021) would remain unchanged for the life of Measure K <sup>(1)</sup>



(1) Source: presentation made to Board of Trustees, dated January 11, 2022.

(2) Index reflects average yield to worst of investment grade, tax-exempt general obligation bonds with at least one-year to maturity. Source: Bloomberg.

# Measure K

Measure K was approved in November 2022 for \$504 million with an estimated tax rate of \$50 per \$100,000 of AV

- ◆ Series A bonds issued for \$125 million in June 2023
- ◆ Series B bonds planned for \$100 million during 2025-26
  - The District’s aggregate Measure K 2025-26 tax rate was set at \$54.83 per \$100,000 of AV
    - The tax rate exceeds the rate estimated to voters on the ballot (\$50 per \$100,000 of AV)
- ◆ The original issuance plan called for the remaining bonds to be sold through 2035
  - Based on ~2.3% interest rates and 4.5% annual assessed valuation (“AV”) growth

The District may need

**Estimated Current Bonding Capacity**<sup>(1)</sup>

2025-26 Total AV with Unitary	\$18,053,002,866
Statutory Debt Limit Factor	x 2.50%
Bonding Capacity	451,325,072
Outstanding General Obligation Bonds	(342,664,450)
Available Bonding Capacity	\$ 108,660,621

(1) Subject to confirmation by the Los Angeles County Auditor-Controller’s office.



## Downey Unified School District Measure K Modified Bond Phasing Plan With Highest First Draw

- ✓ **Annual AV Growth Rate: 3.0% for 2026-2027 and 4.25% thereafter (not 4.5%)**
- ✓ **Targeted Tax Rate of \$60 Per \$100,000 of Assessed Valuation**
- ✓ **Interest Rate 4.8% for Series B; 5.25% for remainder (not historical lows)**


### Bond Phasing Plan With Highest First Draw / All Remaining Draws At Least \$80 Million

Series A (Year 1/2023):	\$125,000,000 / \$125,000,000
Series B (Year 4/2026):	\$80,000,000 / \$100,000,000
Series C (Year 7/2028):	\$110,000,000 / \$25,000,000
Series D (Year 10):	\$80,000,000
Series E (Year 12):	\$109,000,000



# Downey Unified School District

## Steps in the Issuance of Measure K Series B Bonds

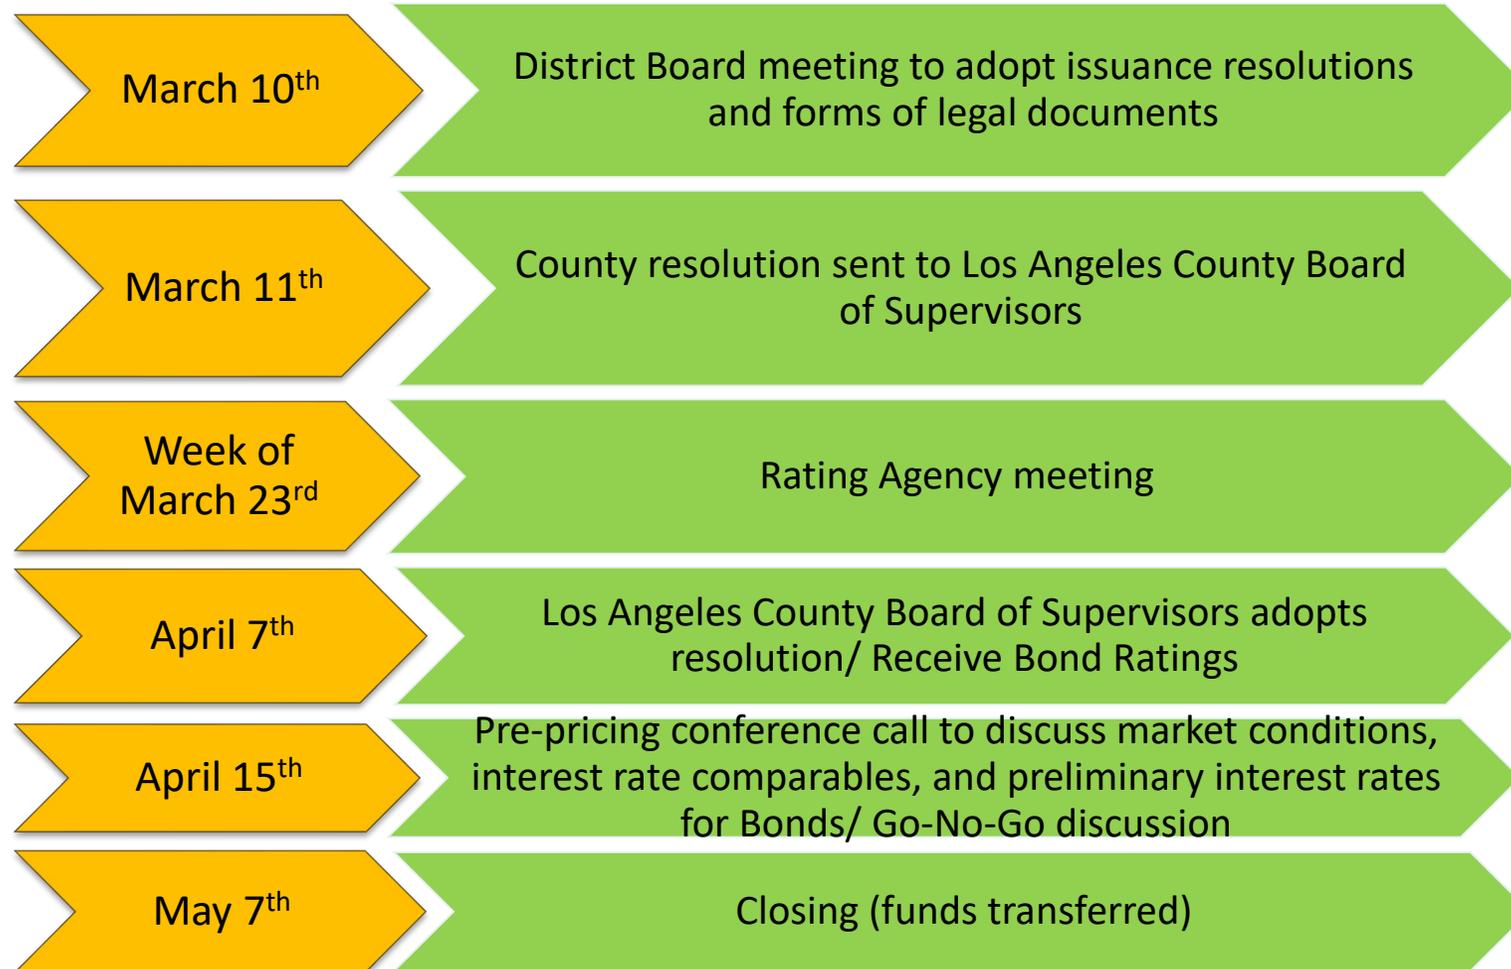



# Financing Path Forward

---

**Series B:** Stick to the original plan + Proposition 2 scope

**March 10:** Discuss alternative financing options with Municipal Advisor

# Phase II Recommendation



## Criteria



**Downey Unified**  
SCHOOL DISTRICT



## School Site Priority Rationale

---

1. Program
2. Condition of Portables
3. Student Drop-Off/Pick-Up
4. Geographic Location
5. State Funding
6. Interim Housing



# Recommended Sites Phase II

---

1. Price Elementary School
2. Williams Elementary School
3. Alameda Elementary School



# Price Elementary School

---

## 1) Instructional Program:

- Large campus (697 students)
- Comprehensive general and special education population
- Grow larger through inter-district transfer process (high demand school)
- New buildings and parking lots for buffer

## 2) Condition of Portables:

- Nineteen portables that are in decent but dated condition
- Replacement due to age of structures

## 3) Drop Off:

- Drop off and pick up off Suva St. and Tweedy Ln. – only two lanes
- Double park and block lanes during drop off and pick up



# Price Elementary School

---

## 4) Geographic Location:

- Northwest quadrant

## 5) State Matching Funding Opportunities:

- Based upon current eligibility, to maximize funds.

## 6) Minimize Interim Housing Needs:

- Reduce costs of bond program by using existing portables

## PRICE ELEMENTARY

TK/K:

Current – 3TK/4K

29/30 – 4TK/4K



## Price

Elementary School

Existing Site Plan

- (2) Kinder Classrooms
- (18) Classrooms
- (19) Portables


PRICE ELEMENTARY

**TK/K:**

Current – 3TK/4K

29/30 – 4TK/4K

**19 portables**

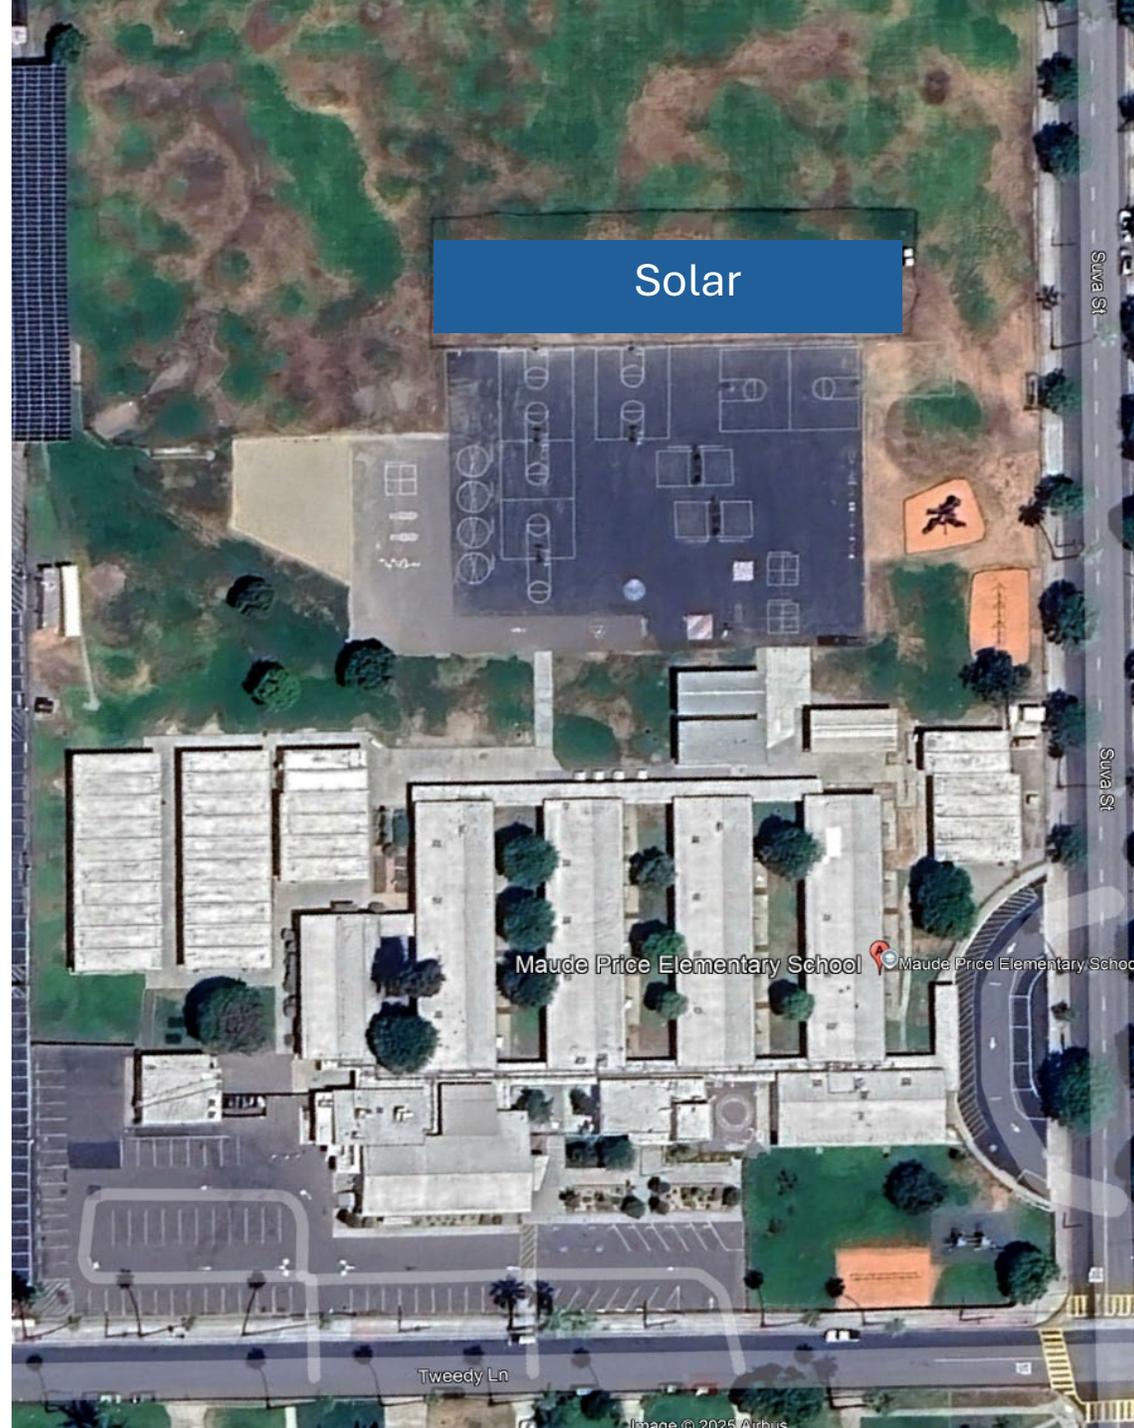

## PRICE ELEMENTARY

**TK/K:**

Current – 3TK/4K

29/30 – 4TK/4K

**19 portables**

Remove 6 portables

2 – Basic Skills → A5 & A6

1 – RSP → A7

1 – Speech → A8


1 – Kinder → New TK/K village

1 – YMCA → E21

Pricing: TOTAL - \$18 million

**TK/K Village ONLY**

- 8 Classrooms - \$15 million
- Site work/playground - \$3 million

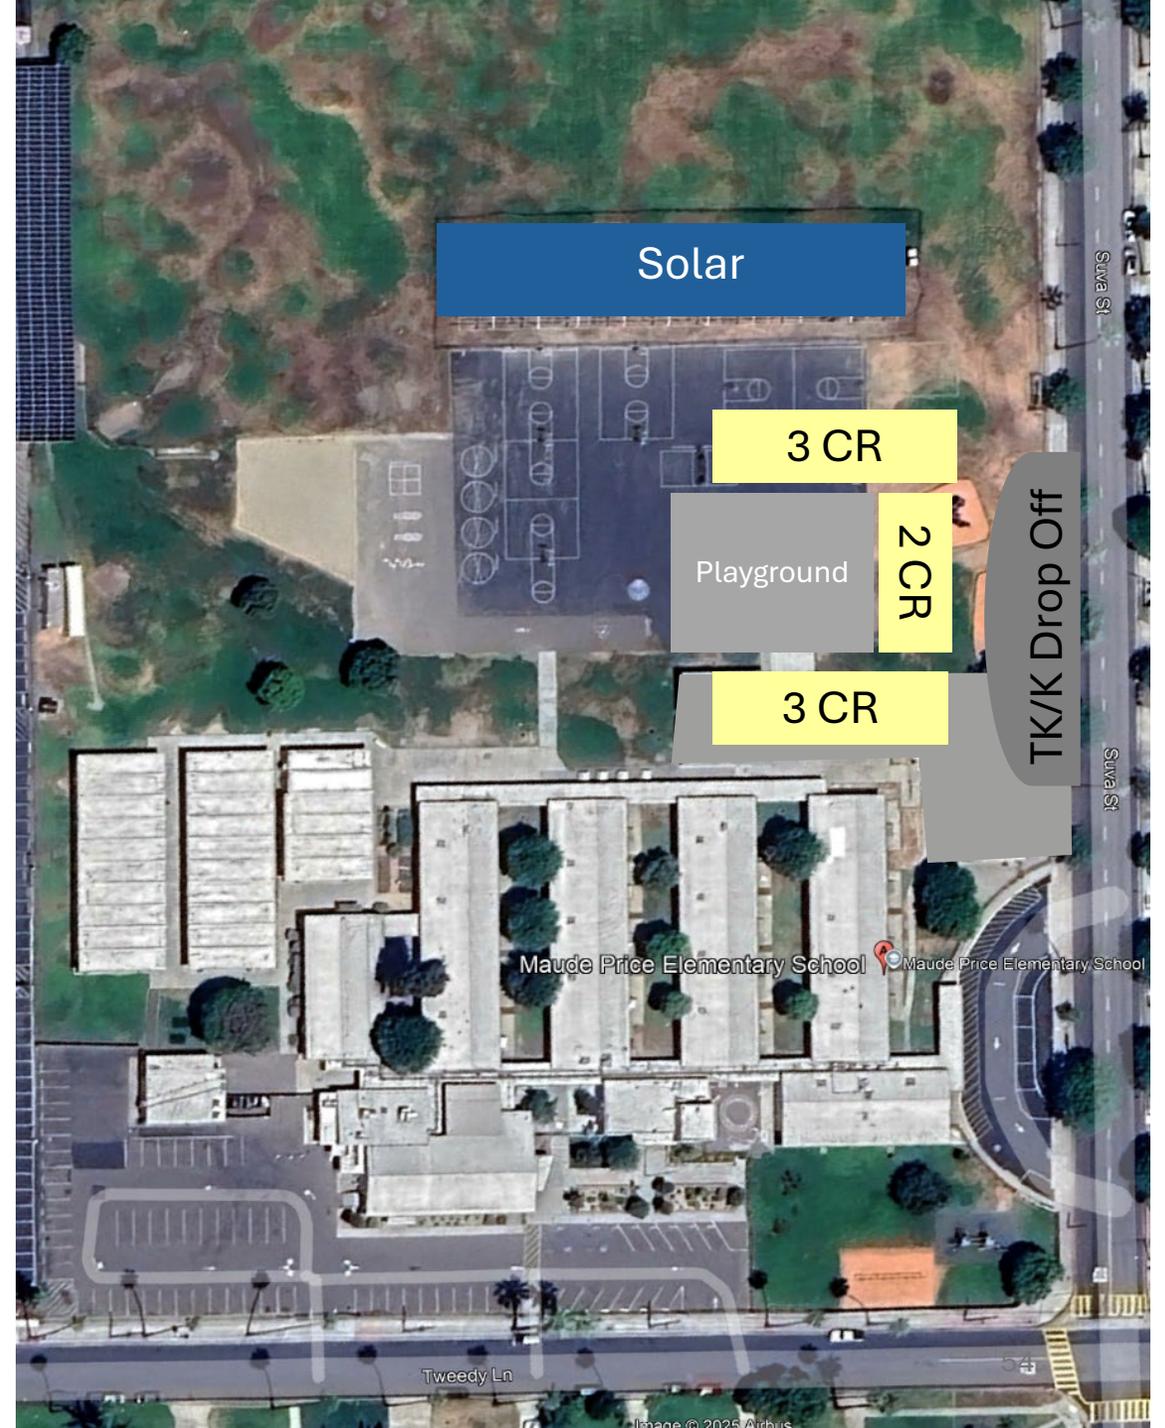



# Williams Elementary School

---

- 1) Instructional Program:
  - Comprehensive general and special education population
  - Kinder class and playground open toward Julius Ave. & Arnett St.
  - New TK and Kinder classrooms provide barrier from public
- 2) Condition of Portables:
  - Sixteen portables that are in decent but dated condition
  - Replacement due to age of structures
- 3) Drop Off:
  - Expands drop off and pick up off on Arnett St.
  - Illegal parking in driveways of neighboring properties



# Williams Elementary School

---

## 4) Geographic Location:

- West quadrant

## 5) State Matching Funding Opportunities:

- Based upon current eligibility, to maximize funds.

## 6) Minimize Interim Housing Needs:

- Reduce costs of bond program by using existing portables

# WILLIAMS ELEMENTARY – TK-3rd

## TK/K:

Current – 4TK/7K

29/30 – 6TK/6K

**1 TK SDC**

**16 Portables**



## Williams

Elementary School

Existing Site Plan

(2) Kinder Classrooms

(21) Classrooms

(16) Portables

**WILLIAMS ELEMENTARY**


**TK/K:**

Current – 4TK/7K

29/30 – 6TK/6K

**1 TK SDC**

**16 Portables**

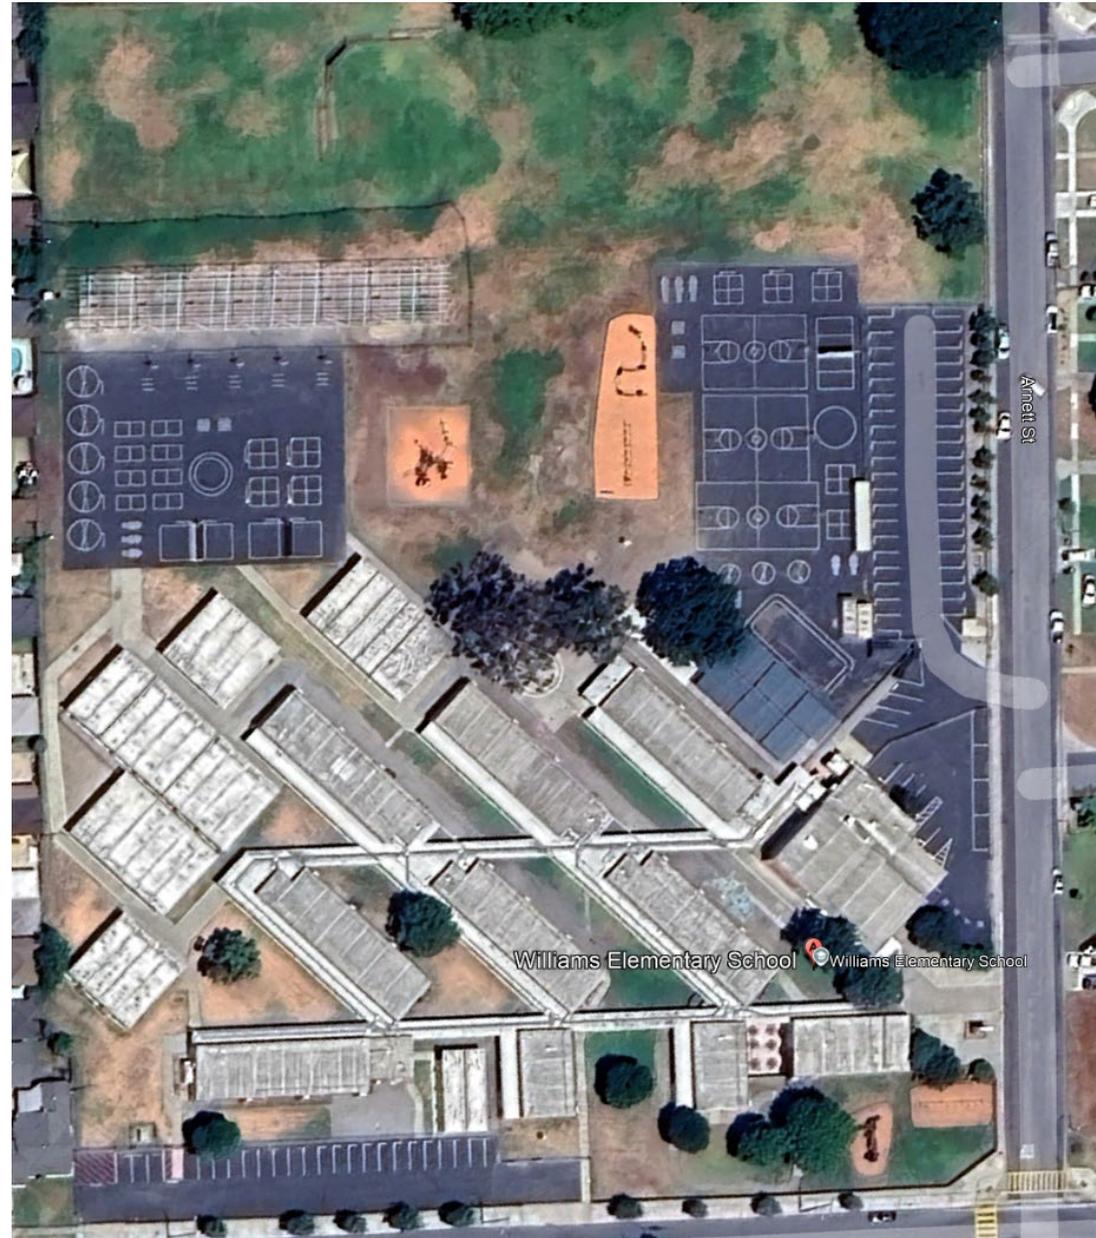

## WILLIAMS ELEMENTARY

**TK/K:**

Current – 4TK/7K

29/30 – 6TK/6K


**1 TK SDC**

**16 Portables**

Pricing: TOTAL - \$28 million

### **TK/K Village ONLY**

- 13 Classrooms - \$24 million
- Site work/playground/parking lot - \$4 million

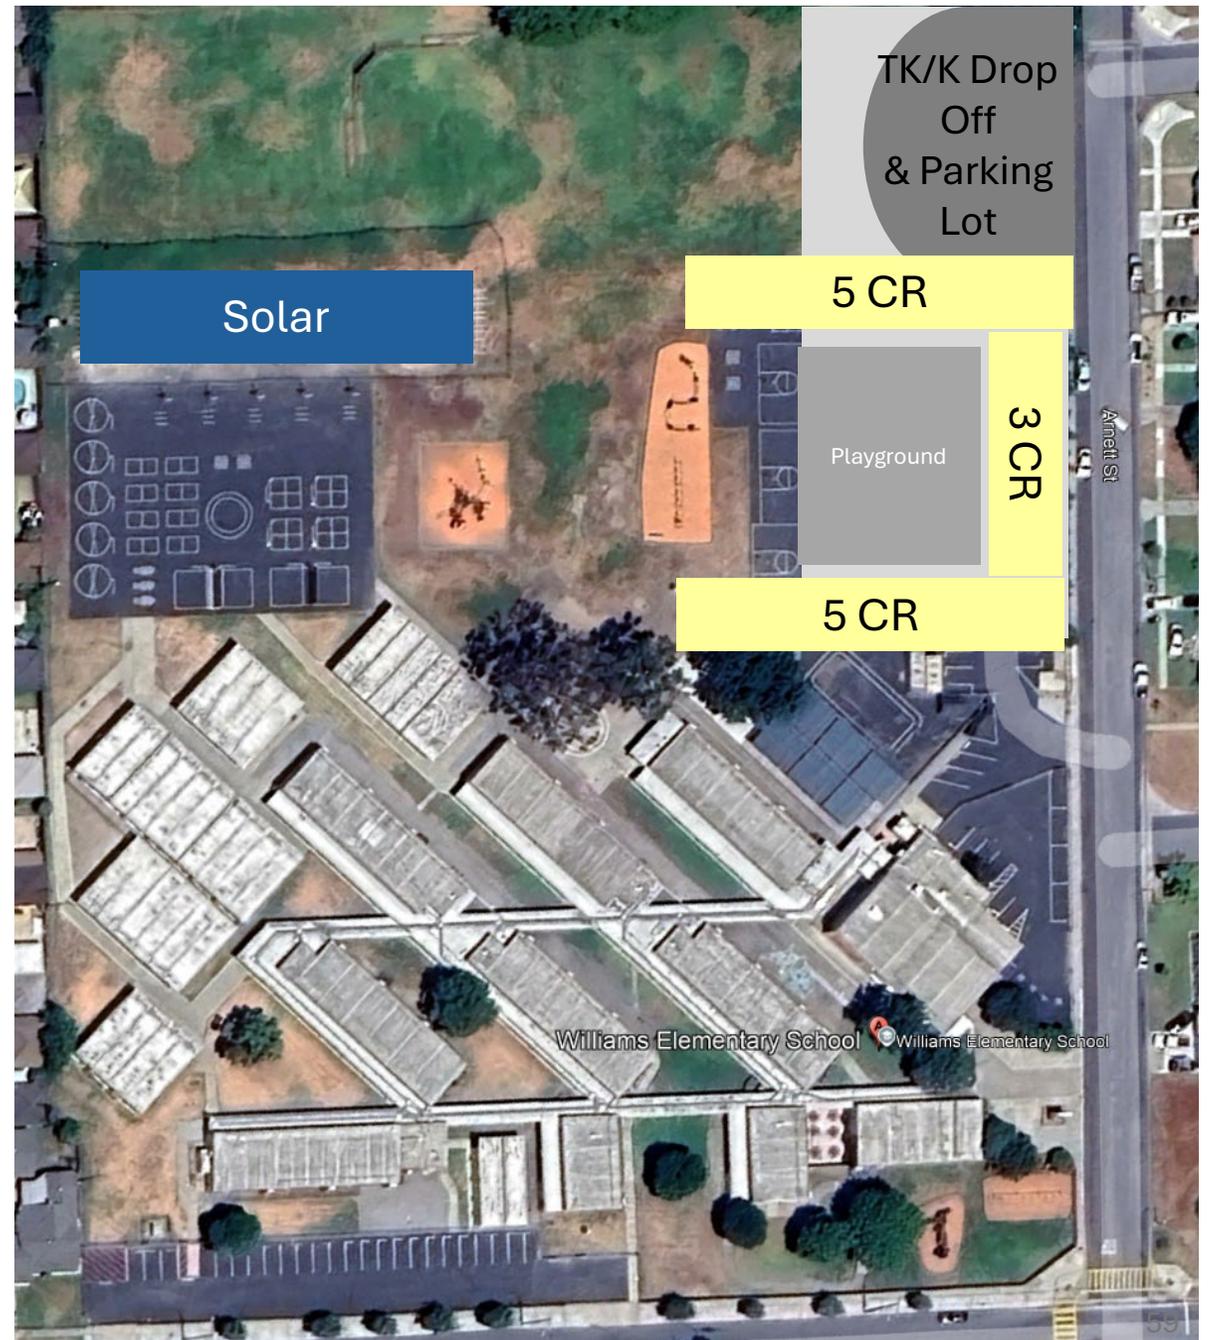



# Alameda Elementary School

---

## 1) Instructional Program:

- Comprehensive general and special education population
- Providing least restrictive environment for TK-K special education students

## 2) Condition of Portables:

- 5 portables that are in sub-standard condition
- Replacement due to age of structures

## 3) Drop Off:

- Arrival and departure paths embedded in the parking lot
- Traffic pattern congested
- Need for separate foot and car traffic off Alameda St. (on Patton Rd.)
- New TK-K classes and playground open away from street and parking



# Alameda Elementary School

---

## 4) Geographic Location:

- Central quadrant

## 5) State Matching Funding Opportunities:

- Based upon current eligibility, to maximize funds

## 6) Minimize Interim Housing Needs:

- No interim housing necessary

# ALAMEDA ELEMENTARY

TK/K:

Current – 2TK/4K

29/30 – 3TK/4K

2 TK SDC

5 Portables

## Alameda

Elementary School

### Existing Site Plan

- (2) Kinder Classrooms
- (38) Classrooms
- (5) Portables
- 45 total



ALAMEDA ELEMENTARY


**TK/K:**

Current – 2TK/4K

29/30 – 3TK/4K

**2 TK SDC**

**5 Portables**

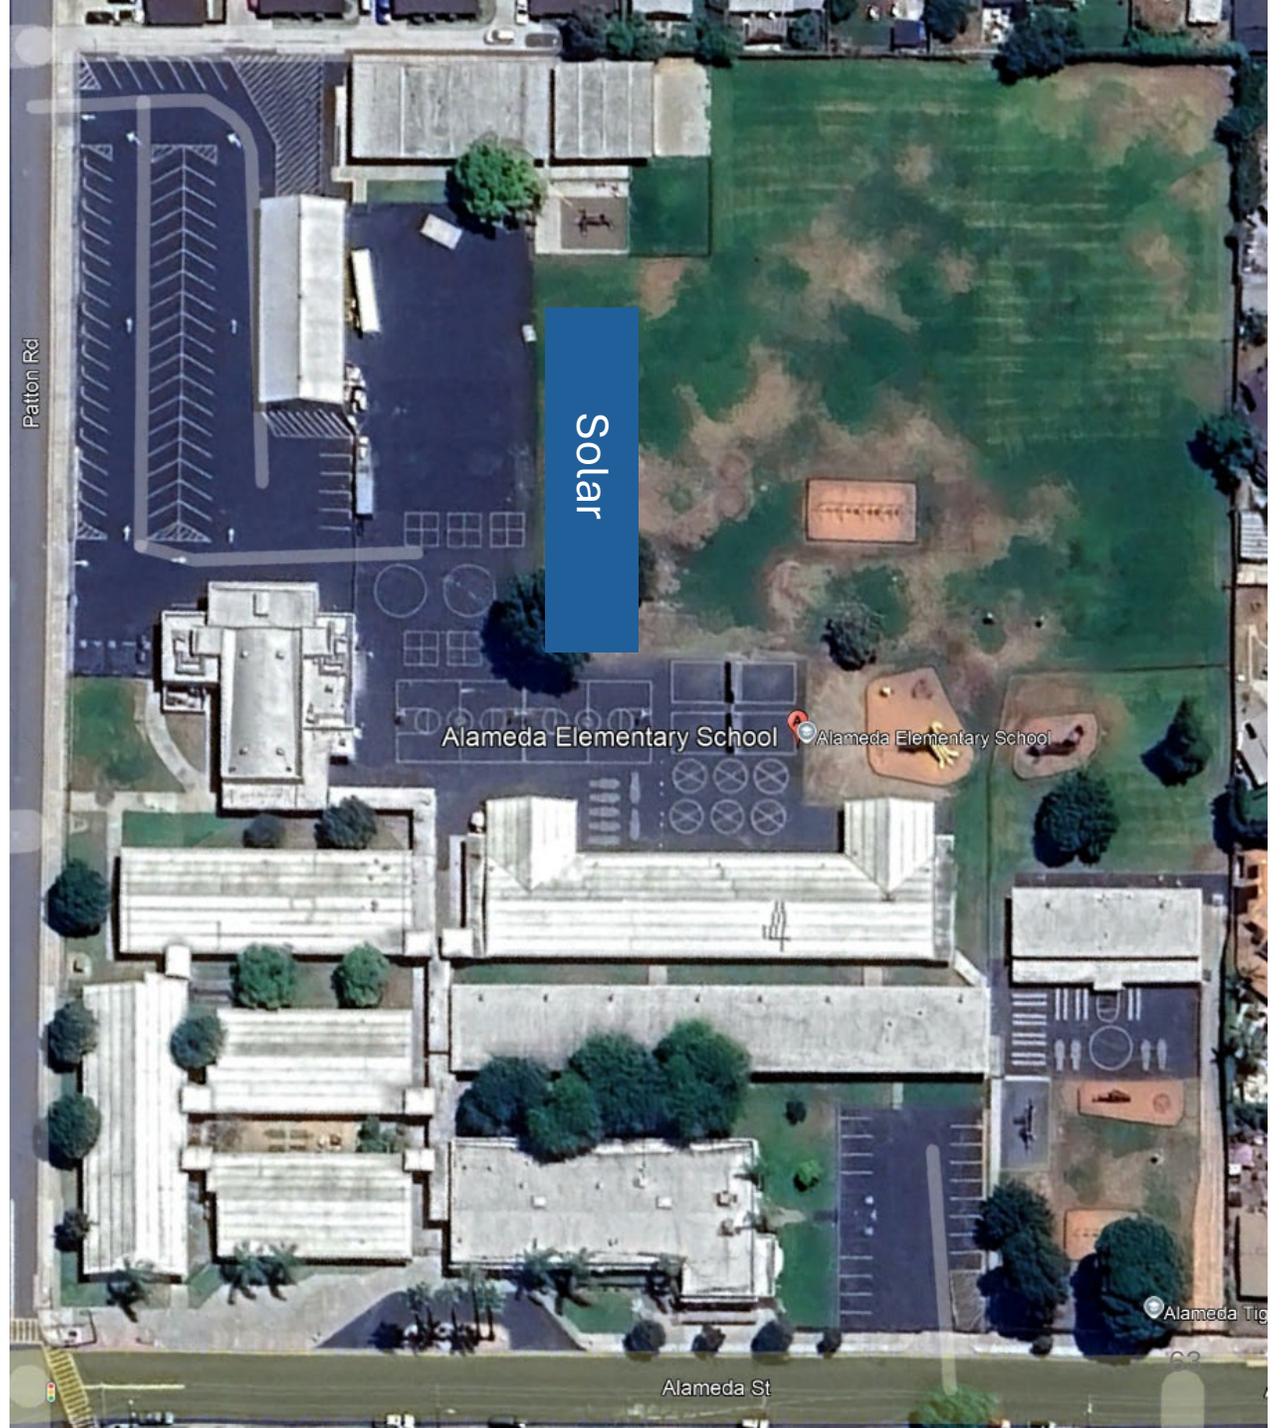

## ALAMEDA ELEMENTARY

### TK/K:

Current – 2TK/4K

29/30 – 3TK/4K

**2 TK SDC**


**5 Portables**

Remove 5 Portables & Warehouse

Pricing: TOTAL - \$19 million

### **TK/K Village ONLY**

- 9 Classrooms - \$16 million
- Site work/playground - \$3 million

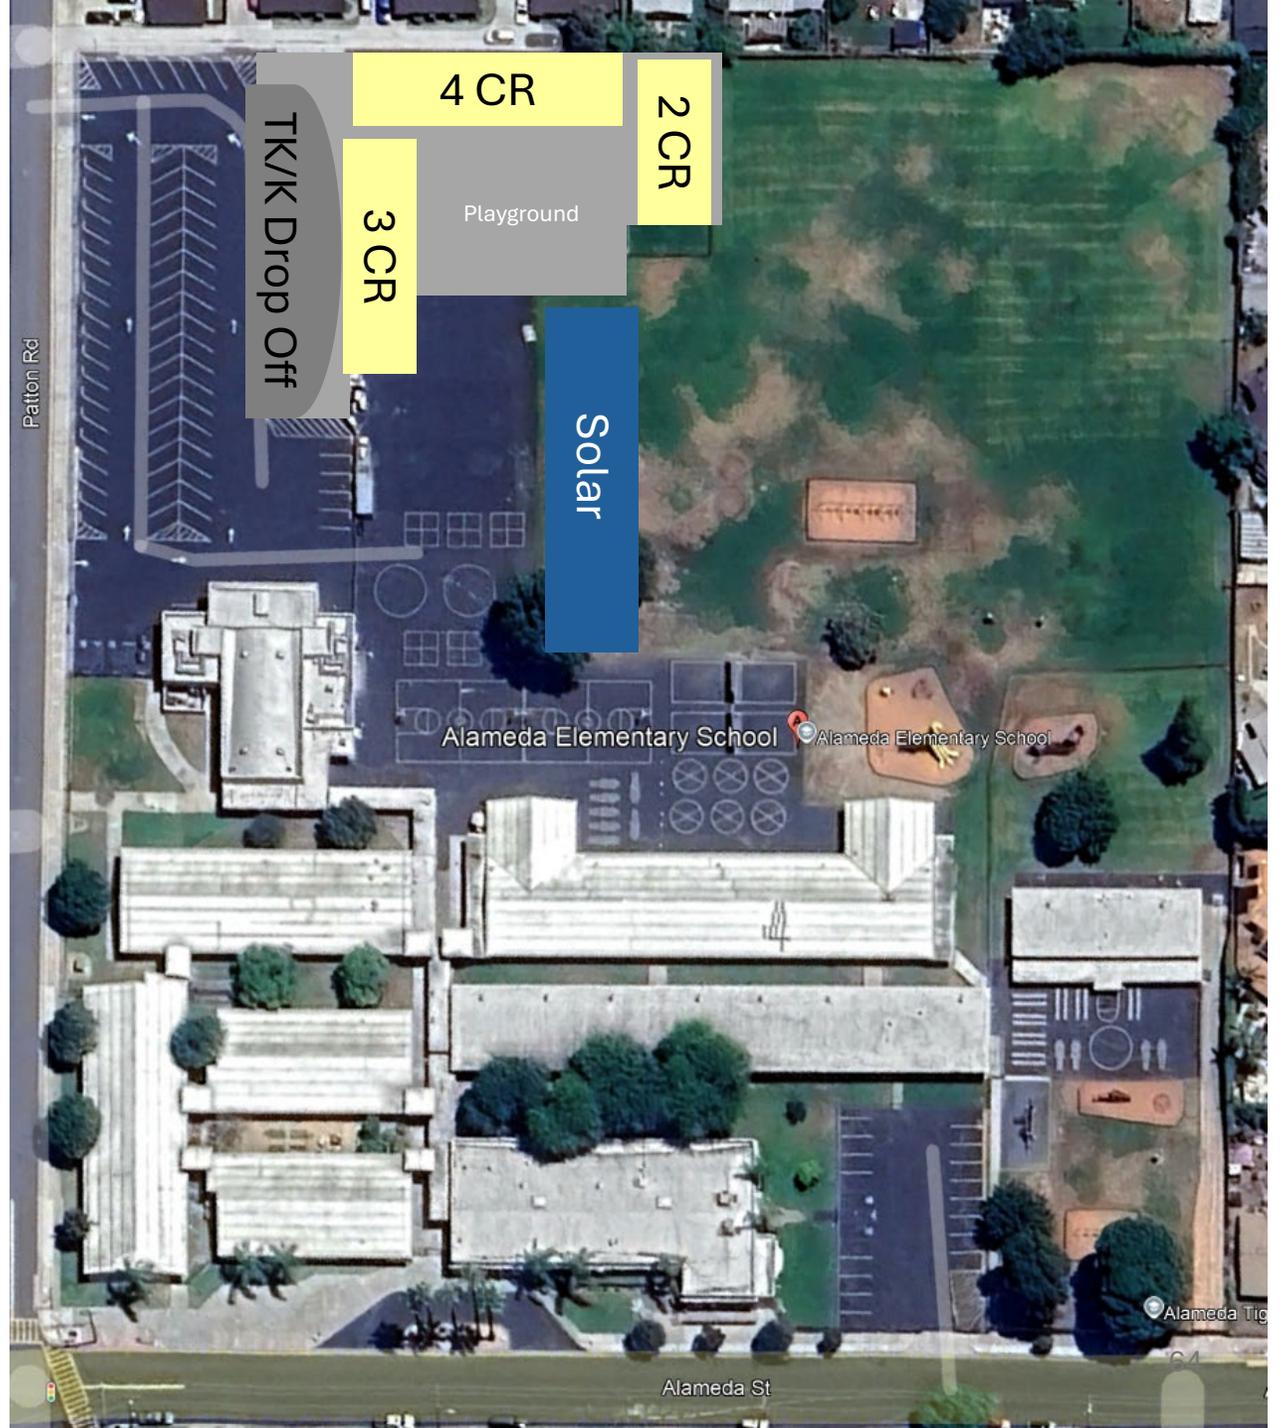



**Downey Unified**  
SCHOOL DISTRICT



# **Board Discussion & Phase II Site Selections**



# TK-K Complex Construction Timeline

	2026/27	2027/28	2028/29	2029/30	2030/31
<b>Phase II (3 Schools)</b>	<b>Design/DSA</b>	<b>Start</b>	<b>End</b>		
<b>Phase III (3 Schools)</b>	<b>Design/DSA</b>		<b>Start</b>	<b>End</b>	
<b>Phase IV (2 Schools)</b>	<b>Design/DSA</b>			<b>Start</b>	<b>End</b>



**Downey Unified**  
SCHOOL DISTRICT

**THANK YOU!**
