

PROJECT MANUAL



Bid No. 23/24-20
Various Site CAT6 Cabling for IP Phone Project
December 13, 2023

DOCUMENT 00 01 10

TABLE OF CONTENTS - CONTRACT DOCUMENTS

PROCUREMENT AND CONTRACTING REQUIREMENTS

Division 00	Section	Title
	00 01 01	Title Page
	00 01 10	Table of Contents (This Document)
	00 01 15	List of Drawings, Tables and Schedules
	00 11 16	Notice to Bidders / Invitation to Bid
	00 21 13	Instructions to Bidders
	00 31 19	Existing Information and Documentation Regarding Project Site (<u>NOT</u> part of the Contract Documents)

DOCUMENTS THAT BIDDER MUST SUBMIT AS PART OF ITS BID

00 41 13	Bid Form
00 43 13	Bid Bond (Security)
00 43 36	Designated Subcontractors List
00 43 40	Noncollusion Declaration
00 43 50	Iran Contracting Act Certification
00 45 00	Notice of Award
00 45 10	Agreement
00 45 40	Certifications to be Completed by Contractor
00 45 85	Criminal Background Investigation/Fingerprinting Certification
00 54 70	Storm Water Pollution Prevention Plan
00 61 14	Performance Bond
00 61 15	Payment Bond (Contractor's Labor and Material Bond)
00 63 40	Allowance Expenditure Directive Form
00 63 57	Proposed Change Order Form
00 63 63	Change Order Form
00 70 00	General Conditions
00 71 00	Special Conditions & Supplementary Conditions
00 91 13	Addenda - All addenda issued by District become part of the Contract.

SPECIFICATIONS – GENERAL REQUIREMENTS

Division 01	Section	Title
	01 11 00	Summary of Work
	01 12 10	Contract Forms and Submittals
	01 20 00	Price and Payment Procedures
	01 21 00	Allowances
	01 23 00	Alternates and Unit Pricing
	01 25 10	Product Options and Substitutions
	01 26 00	Contract Modification Procedures
	01 26 10	Requests for Information
	01 31 00	Coordination and Project Meetings
	01 32 16	Construction Schedule - Network Analysis
	01 33 00	Submittals
	01 40 00	Quality Requirements
	01 42 13	Abbreviations and Acronyms
	01 42 16	General Definitions and References
	01 45 29	Testing Laboratory Services
	01 50 00	Temporary Facilities and Controls
	01 52 10	Site Standards
	01 56 39	Temporary Tree and Plant Protection
	01 57 10	Storm Water Pollution Prevention Plan (SWPPP) – Construction
	01 60 00	Materials and Equipment
	01 66 10	Delivery, Storage and Handling
	01 73 00	Execution
	01 73 10	Cutting and Patching
	01 77 00	Contract Closeout and Final Cleaning
	01 78 23	Operation and Maintenance Data
	01 78 36	Warranties
	01 78 39	Record Documents
	01 91 00	Commissioning

END OF DOCUMENT

DOCUMENT 00 01 15

LIST OF DRAWINGS, TABLES AND SCHEDULES

DRAWINGS

N/A

WORK HOURS

Monday through Friday – 3:00 PM to 11:30 PM

Saturday – 7 AM to 4 PM

END OF DOCUMENT

NOTICE TO BIDDERS / INVITATION TO BID

1. Notice is hereby given that the governing board ("Board") of the **Downey Unified School District** ("District") will receive sealed bids to construct the following project:

Bid No. 23/24-20: Various Site CAT6 Cabling for IP Phone Project ("Project" or "Contract") located at locations below:

Alameda Elementary School, 8613 Alameda St., Downey, CA 90242
Carpenter Elementary School, 9439 Foster Rd., Downey, CA 90242
Gallatin Elementary School, 9513 Brookshire Ave., Downey, CA 90240
Gauldin Elementary School, 9724 Spry St., Downey, CA 90242
Imperial Elementary School, 8133 Imperial Hwy., Downey, CA 90242
Lewis Elementary School, 13220 Bellflower Blvd., Downey, CA 90242
Old River Elementary School, 11994 Old River School Rd., Downey, CA 90241
Pace Education Center, 9625 Van Ruiten St., Bellflower, CA 90706
Price Elementary School, 9525 Tweedy Ln., Downey, CA 90240
Rio Hondo Elementary School, 7731 Muller St., Downey, CA 90241
Rio San Gabriel Elementary School, 9338 Gotham St., Downey, CA 90241
Unsworth Elementary School, 9001 Lindsay St., Downey, CA 90240
Ward Elementary School, 8851 Adoree St., Downey, CA 90242
Williams Elementary School, 7530 Arnett St., Downey, CA 90241
Doty Middle School, 10301 Woodruff Ave., Downey, CA 90241
Sussman Middle School, 12500 Birchdale Ave., Downey, CA 90242
Columbus High School, 12330 Woodruff Ave., Downey, CA 90241
Downey High School, 11040 Brookshire Ave., Downey, CA 90241
Warren High School, 8141 De Palma St., Downey, CA 90241

2. Contractors must submit sealed bids on or before 10 AM on January 5, 2024 at the District Office Facilities Department, located at T-4, 11627 Brookshire Ave., Downey, CA 90241 at or after which time the District will open the bids and publicly read them aloud. Any claim by a Bidder of error in its bid must be made in compliance with Public Contract Code § 5100, et seq. Any bid that is submitted after this time shall be non-responsive and returned to the Bidder. The District is not responsible for Bids that are received after the deadline noted above.

3. The Project consists of:

Providing and installing CAT6 cables for IP phone system for various sites.

4. All bids shall be on the form provided by the District. Each bid must conform and be responsive to all pertinent Contract Documents, including, but not limited to, the Instructions to Bidders.
5. To bid on this Project, the Bidder is required to possess one or more of the following State of California Contractor Licenses: C-7
The Bidder's license(s) must be active and in good standing at the time of the bid opening and must remain so throughout the term of the Contract.
6. As security for its Bid, each Bidder shall provide with its Bid form
 - a bid bond issued by an admitted surety insurer on the form provided by the District,
 - cash, or
 - a cashier's check or a certified check, drawn to the order of the **Downey Unified School District** in the amount of ten percent (10%) of the total bid price. This bid security shall be a guarantee that the Bidder shall, within seven (7) calendar days after the date of the Notice of Award, enter into a contract with the District for the performance of the services as stipulated in the bid.

7. The successful Bidder shall be required to furnish a 100% Performance Bond and a 100% Payment Bond if it is awarded the contract for the Project.
8. The successful Bidder may substitute securities for any monies withheld by the District to ensure performance under the Contract, in accordance with the provisions of Public Contract Code § 22300.
9. The successful Bidder and its subcontractors shall pay all workers on the Project not less than the general prevailing rate of per diem wages and the general prevailing rate for holiday and overtime work as determined by the Director of the Department of Industrial Relations, State of California, for the type of work performed and the locality in which the work is to be performed within the boundaries of the District, pursuant to Labor Code § 1770 et seq. Prevailing wage rates are on file with the District and are available to any interested party on request or at www.dir.ca.gov/oprl/statistics_and_databases.html. Bidders and Bidders' subcontractors shall comply with the registration and qualification requirements pursuant to Labor Code §§ 1725.5 & 1771.1
10. A mandatory pre-bid conference and site visit will be held on December 28, 2023 at 9 AM starting at Alameda Elementary School, 8613 Alameda St., Downey, CA 90242 at the front of the school and then proceeding to other sites. All prospective Bidders are required to sign in at each school site. The Site Visit is expected to take approximately an hour. Failure to attend or tardiness will render bid ineligible.
11. Contract Documents are available on or after December 13, 2023.
12. The District's Board reserves the right to reject any and all bids and/or waive any irregularity in any bid received. If the District awards the Contract, the security of unsuccessful Bidder(s) shall be returned within sixty (60) days from the time the award is made. Unless otherwise required by law, no Bidder may withdraw its bid for ninety (90) days after the date of the bid opening.
13. The District shall award the Contract, if it awards it at all, to the lowest responsive responsible Bidder based on: The base bid amount only.

END OF DOCUMENT

DOCUMENT 00 21 13

INSTRUCTIONS TO BIDDERS

Bidders shall follow the instructions in this document, and shall submit all documents, forms, and information required for consideration of a Bid.

Downey Unified School District ("District") will evaluate information submitted by the apparent low Bidder and, if incomplete or unsatisfactory to District, Bidder's bid may be rejected at the sole discretion of District.

1. **Project.** Bids are requested for a general construction contract, or work described in general, for the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract")

2. **Submittal of Bids.** District will receive sealed Bids from Bidders as indicated in the Invitation to Bid and each Bidder shall ensure that its Bid contains all documents as required herein and is submitted by date and time shown in the Invitation to Bid.
 - a. Contractors must ensure the District receives its bid, sealed and marked with name and address of the Bidder, the Project name and number, the bid number and bid package (if applicable), and the date for opening bids.
3. **Bid Opening.** Bids will be opened at or after the time indicated for receipt of bids.
4. **Complete Bids.** Bidders must supply all information required by each Bid Document. Bids must be full and complete. District reserves the right in its sole discretion to reject any Bid as non-responsive as a result of any error or omission in the Bid. Each Bidder must complete and submit all of the following documents as its Bid:
 - Bid Form
 - Bid Bond or other security
 - Designated Subcontractors List
 - Noncollusion Declaration
 - Iran Contracting Act Certification
 - a. **Bid Form.** Bidders must submit Bids on the Bid Form and all other required District forms. Bids not submitted on the District's required forms shall be deemed non-responsive and shall not be considered. Additional sheets required to fully respond to requested information are permissible. Bidders shall not modify the Bid Form or qualify their Bids. Bidders shall not submit scanned, re-typed, word-processed, or otherwise recreated versions of the Bid Form or other District-provided documents.
 - b. **Bid Bond or Other Security.** Bidders must submit their Bid Form with cash, a cashier's check or a certified check payable to District, or a bid bond by an admitted surety insurer of not less than ten percent (10%) of their base Bid amount, including all additive alternates. Required form of corporate surety, Bid Bond, is provided by District and must be used and fully completed by Bidders choosing to provide a Bid Bond as security. The Surety on Bidders' Bid Bond must be an insurer admitted in the State of California and authorized to issue surety bonds in the State of California. Bids submitted without necessary bid security will be deemed non-responsive and will not be considered.
 - c. **Designated Subcontractors List.** Bidders must submit with the Bid the Designated Subcontractors List for those subcontractors who will perform any portion of Work, including labor, rendering of service, or specially fabricating and installing a portion of the Work or improvement according to detailed drawings contained in the plans and specifications, in excess of one half of one percent (0.5%) of the Bidder's total

Bid. Failure to fully complete and submit this list when required by law shall result in Bid being deemed non-responsive and the Bid will not be considered.

- d. **Noncollusion Declaration.** Bidders shall submit the Noncollusion Declaration with their Bids. Bids submitted without the Noncollusion Declaration shall be deemed non-responsive and will not be considered.
 - e. **Iran Contracting Act Certification.** Bidders shall submit the Iran Contracting Act Certification with their Bids. Bids submitted without the Iran Contracting Act Certification shall be deemed non-responsive and will not be considered.
5. **Erasures.** Bids shall be clearly written without erasure or deletions. District reserves the right to reject any Bid containing erasures or deletions.
6. **Prevailing Wages.** Pursuant to sections 1770 et seq. of the California Labor Code, Bidder and all Subcontractors under the Bidder shall pay all workers on all work performed pursuant to the Contract not less than the general prevailing rate of per diem wages and the general prevailing rate for holiday and overtime work as determined by the Director of the State of California Department of Industrial Relations (DIR) for the type of work performed and the locality in which the work is to be performed within the boundaries of the District. Copies of the general prevailing rates of per diem wages for each craft, classification, or type of worker needed to execute the Contract, as determined by the DIR are on file with the District and are available to any interested party on request or at www.dir.ca.gov/oprl/statistics_and_databases.html.
7. **Contractor Registration.** Bidder shall ensure that it and its Subcontractors comply with the registration and compliance monitoring provisions of Labor Code section 1771.4, including furnishing its CPRs to the Labor Commissioner, and are registered pursuant to Labor Code section 1725.5. Bidder and its subcontractors shall comply with Labor Code section 1725.5 to be qualified to bid on, be listed in a bid proposal, subject to the requirements of Section 4104 of the Public Contract Code, or engage in the performance of the Contract.
8. **Bidder Diligence.** Submission of Bid signifies careful examination of the Contract Documents and a complete understanding of the nature, extent, and location of Work to be performed. Bidders must complete the tasks listed below as a condition to bidding, and submission of Bid shall constitute the Bidder's express representation to District that Bidder has fully completed the following:
- a. Bidder has visited the Project Site, if required, and has examined thoroughly and understood the nature and extent of the Contract Documents, Work, Site, locality, actual conditions, as-built conditions, and all local conditions and federal, state and local laws, and regulations that in any manner may affect cost, progress, performance, or furnishing of Work or that relate to any aspect of the means, methods, techniques, sequences, or procedures of construction to be employed by Bidder and safety precautions and programs incident thereto;
 - b. Bidder has conducted or obtained and has understood all examinations, investigations, explorations, tests, reports, and studies that pertain to the subsurface conditions, as-built conditions, underground facilities, and all other physical conditions at or contiguous to the Site or otherwise that may affect the cost, progress, performance, or furnishing of Work, as Bidder considers necessary for the performance or furnishing of Work at the Contract Price, within the Contract Time, and in accordance with the other terms and conditions of Contract Documents, including specifically the provisions of the General Conditions. Bidder has notified the District if it contends that it requires additional examinations, investigations, explorations, tests, reports, studies, or similar information or data prior to submitting its bid;
 - c. Bidder has correlated its knowledge and the results of all observations, examinations, investigations, explorations, tests, reports, and studies with the terms and conditions of the Contract Documents;

- d. Bidder has given the District prompt written notice of all conflicts, errors, ambiguities, or discrepancies that it has discovered in or among the Contract Documents and the actual conditions, and the written resolution thereof by the District is acceptable to Bidder;
- e. Bidder has made a complete disclosure in writing to the District of all facts bearing upon any possible interest, direct or indirect, that Bidder believes any representative of the District or other officer or employee of the District presently has or will have in this Contract or in the performance thereof or in any portion of the profits thereof;
- f. Bidder must, prior to bidding, perform the work, investigations, research, and analysis required by the Instructions to Bidders and that Bidder represented in its Bid Form and the Agreement that it performed prior to bidding. Bidder is charged with all information and knowledge that a reasonable bidder would ascertain from having performed this required work, investigation, research, and analysis. Bid prices must include entire cost of all work “incidental” to completion of the Work.
- g. **Conditions Shown on the Contract Documents:** Information as to underground conditions, as-built conditions, or other conditions or obstructions, indicated in the Contract Documents, e.g., on Drawings or in Specifications, has been obtained with reasonable care, and has been recorded in good faith. However, District only warrants, and Bidder may only rely, on the accuracy of limited types of information.
 - (1) As to above-ground conditions or as-built conditions shown or indicated in the Contract Documents, there is no warranty, express or implied, or any representation express or implied, that this information is correctly shown or indicated. This information is verifiable by independent investigation and Bidder is required to make that verification as a condition to bidding. In submitting its Bid, Bidder shall rely on the results of its own independent investigation. In submitting its Bid, Bidder shall not rely on District-supplied information regarding above-ground conditions or as-built conditions.
 - (2) As to any subsurface condition shown or indicated in the Contract Documents, Bidder may rely only upon the general accuracy of actual reported depths, actual reported character of materials, actual reported soil types, actual reported water conditions, or actual obstructions shown or indicated. District is not responsible for the completeness of this information for bidding or construction; nor is District responsible in any way for any conclusions or opinions of Bidder drawn from that information; nor is District responsible for subsurface conditions that are not specifically shown if those subsurface conditions are reasonably determinable by above-ground conditions and observation or as-built conditions (e.g., subsurface soil conditions in areas contiguous to areas where an above-ground condition is shown; utility pipes between a manhole and a water source, etc.).
- h. **Conditions Shown in Reports and Drawings Supplied for Informational Purposes:** Reference is made to the document entitled Existing Information and Documentation Regarding Project Site, for identification of:
 - (1) Subsurface Conditions: Those reports of explorations and tests of subsurface conditions at or contiguous to the Project Site that have been utilized by Architect in preparing the Contract Documents; and
 - (2) Physical Conditions: Those drawings of physical conditions in or relating to existing surface or subsurface structures at or contiguous to the Project Site that has been utilized by Architect in preparing the Contract Documents.
 - (3) These reports and drawings are not Contract Documents and, except for any “technical” data regarding subsurface conditions specifically identified in Existing Information and Documentation Regarding Project Site, and underground facilities data, Bidder may not in any manner rely on the

information in these reports and drawings.

9. **As-Builts.** Bidders may examine any available “as-built” drawings of previous work by giving District reasonable advance notice. District will not be responsible for accuracy of “as-built” drawings. The document entitled Existing Information and Documentation Regarding Project Site applies to all supplied “as-built” drawings.
10. **Questions.** All questions about the meaning or intent of the Contract Documents are to be directed in writing to the District. Interpretations or clarifications considered necessary by the District in response to those questions will be issued in writing by Addenda faxed, mailed, or delivered to all parties recorded by the District as having received the Contract Documents. Questions received less than **SEVEN (7)** calendar days prior to the date for opening Bids may not be answered. Only questions answered by formal written Addenda will be binding. Oral and other interpretations or clarifications will be without legal effect.
11. **Addenda.** Addenda may also be issued to modify parts of the Contract Documents as deemed advisable by the District. Bidder must acknowledge each Addendum in its Bid Form by number or its Bid may be considered non-responsive. Each Addenda shall be part of the Contract Documents. A complete listing of Addenda may be obtained from the District.
12. **Substitution for Specified Items.** Bids shall be based on products and systems specified in the Contract Documents or listed by name in Addenda. All requests must comply with the requirements specified in the General Conditions, the Specifications and the following:
 - a. **Request for Substitution Prior to Bid.**
 - (1) District must receive any request for substitution a minimum of **FOURTEEN (14)** calendar days prior to the date of bid opening.
 - (2) **Information with Request.** Requests for substitutions shall contain sufficient information to assess acceptability of the product or system and impact to Project, including, without limitation, the requirements specified in the General Conditions and the Specifications. Insufficient information shall be grounds for rejection of substitution.
 - (3) The District’s denial of a substitution request prior to the date of bid opening shall be conclusive, requiring Bidders to list only approved items. The District is not responsible and/or liable in any way for a Bidder’s damages and/or claims related, in any way, to that Bidder’s basing its bid on any requested substitution that the District has not approved. Bidder’s Bid shall be deemed non-responsive if it identifies a product or manufacturer of a non-approved substitution.
 - (4) Approved substitutions shall be listed in Addenda.
 - (5) District reserves the right not to act upon submittals of substitutions until after the date of bid opening. If the District does not act on a substitution request prior to the date of bid opening, Bidders must bid based on products and systems specified in Contract Documents or listed by name in Addenda.
 - b. **Request for Substitution after Bid Award.** Substitutions may be requested after the Contract has been awarded only if indicated in and in accordance with requirements specified in the General Conditions, as may be modified in the Special Conditions.
13. **Alternates.** The Contract may include alternates. Alternates are defined as alternate products, materials, equipment, systems, methods, or major elements of the construction, that may, at the District’s option and under terms established in the Contract and pursuant to section 20103.8 of the Public Contract Code, be selected for the Work. The District shall award the Contract, if it awards it at all, to the lowest responsive

responsible bidder based on the criteria as indicated in the Invitation to Bid.

14. **Notice of Award.** The Bidder awarded the Contract shall execute and submit the following documents by 5:00 p.m. of the **SEVENTH (7TH)** calendar day following the date of the Notice of Award. Failure to properly and timely submit these documents entitles District to, among other remedies, make a claim against Bidder's Bid Bond or deposit Bidder's cash, cashier's check, or certified check. The proceeds thereof may be retained by District as liquidated damages, in District's sole discretion.
 - a. Agreement: To be executed by successful Bidder. Submit one (1) copy, bearing an original signature.
 - b. Performance Bond (100%): On the form provided in the Contract Documents and fully executed as indicated on the form.
 - c. Payment Bond (100%) (Contractor's Labor and Material Bond): On the form provided in the Contract Documents and fully executed as indicated on the form.
 - d. Insurance Certificates and Endorsements as required.
 - e. Certifications to be Completed by Contractor
 - f. Criminal Background Investigation/Fingerprinting Certification.
15. **Notice to Proceed.** District may issue a Notice to Proceed within **THREE (3)** months from the date of the Notice of Award. Upon receipt of the Notice to Proceed, Contractor shall complete the Work within the period of time indicated in the Contract Documents. It is further expressly understood by Contractor that Contractor shall not be entitled to any claim of additional compensation or additional time when the Notice to Proceed is issued within the 3-month period.
 - a. The District may postpone issuing the Notice to Proceed beyond the 3-month period, upon reasonable notice to Contractor.
 - b. If the Contractor believes that a postponement of issuance of the Notice to Proceed will cause a hardship to Contractor, the Contractor may, by written notice to District within **SEVEN (7)** calendar days after receipt by Contractor of District's notice of postponement, take one of the following actions:
 - (1) **Agree with the postponement.** This would be at no additional cost to the District.
 - (2) **Terminate the Contract.** District shall only be obligated to pay Contractor for any Work that Contractor had performed at the time of notification of postponement and that the District had in writing authorized Contractor to perform, if any, prior to issuing a Notice to Proceed.
 - (3) **Request additional compensation.** Contractor must submit detailed documentation demonstrating the need for that additional compensation, compared to the calculations and amounts that Contractor used to prepare its bid. If the Parties do not agree on an amount for the requested additional compensation, the Contractor can agree to the postponement without any additional compensation, or either Party may terminate the Contract.
 - c. If the Contract is terminated as a result of a notice of postponement, District shall have the authority to award the Contract to the next lowest responsive responsible Bidder.
16. **Bid Protests.** Any bid protest by any Bidder regarding any other bid on this Project must be submitted in writing to the District, before 5:00 p.m. of the **THIRD (3rd)** Business Day following the date of bid opening.
 - a. The protest must contain a complete statement of any and all bases for the protest.

- b. The protest must refer to the specific portions of all documents that form the bases for the protest, including the specific portion(s) of the bid(s) that the Bidder is protesting.
 - c. The protest must include the name, address and telephone number of the person representing the protesting party.
 - d. The party filing the protest must concurrently transmit a copy of the protest and any attached documentation to all other parties with a direct financial interest that may be adversely affected by the outcome of the protest, which must include all other Bidders or proposers who appear to have a reasonable prospect of receiving an award depending upon the outcome of the protest.
 - e. The procedure and time limits set forth in this paragraph are mandatory and are each Bidder's sole and exclusive remedy in the event of bid protest. Failure to comply with these procedures shall constitute a waiver of any right to further pursue the bid protest, including filing a Government Code Claim or legal proceedings.
17. **Rejection of Bids.** District reserves the right to reject any or all bids, including without limitation the right to reject any or all nonconforming, non-responsive, unbalanced, or conditional bids, to re-bid, and to reject the bid of any Bidder if District believes that it would not be in the best interest of the District to make an award to that Bidder, whether because the bid is not responsive or the Bidder is unqualified or of doubtful financial ability or fails to meet any other pertinent standard or criteria established by District. District also reserves the right to waive inconsequential deviations not involving price, time, or changes in the Work. For purposes of this paragraph, an "unbalanced bid" is one having nominal prices for work item(s) that represent substantive work and/or overly-enhanced prices for nominal work item(s).
18. **Bidder's Representative's Authority.** Each bid must be executed by an authorized representative of the Bidder. Bidders may be asked to provide documentation of that authority (e.g., an authenticated resolution of its Board of Directors, a power of attorney evidencing the capacity of the person signing the Bid Form to bind the Bidder to its bid, etc.).
19. **Bidder Responsibility.** Prior to the award of Contract, District reserves the right to consider the responsibility of the Bidder. District may conduct investigations as District deems necessary to assist in the evaluation of any bid and to establish the responsibility, including, without limitation, qualifications and financial ability of Bidders, proposed subcontractors, suppliers, and other persons and organizations to perform and furnish the Work in accordance with the Contract Documents to District's satisfaction within the Contract Time.

END OF DOCUMENT

DOCUMENT 00 31 19

EXISTING INFORMATION AND DOCUMENTATION REGARDING PROJECT SITE

1. Summary

This document describes existing conditions at or near the Project and use of information available regarding existing conditions. This document is **not** part of the Contract Documents. See General Conditions for definition(s) of terms used herein. Contractor is required to request from the District a copy of any reports that it believes are necessary to perform Contractor's Work in a safe, efficient and workman-like manner.

2. Reports and Information on Existing Conditions

- a. Documents providing a general description of the Site and conditions of the Work may have been collected by District, its consultants, contractors, and tenants. These documents may include previous contracts, contract specifications, tenant improvement contracts, as-built drawings, utility drawings, and information regarding underground facilities.
- b. Information regarding existing conditions may be inspected at the District offices or the Construction Manager's offices, if any, and copies may be obtained at cost of reproduction and handling upon Bidder's agreement to pay for such copies. These reports, documents, and other information are **not** part of the Contract Documents.
- c. Information regarding existing conditions may also be included in the Project Manual, but shall **not** be considered part of the Contract Documents.
- d. The reports and other data or information regarding existing conditions and underground facilities at or contiguous to the Project are the following:
 - (1) **Geotechnical Data.** Geotechnical data at or near the Project that is in the District's possession available for Contractor's review.
 - (2) **Hazardous Material Reports**
 - (3) **Asbestos and/or AHERA Reports.** Asbestos survey report, prepared for this Project and/or this Project site is attached in the supplementary conditions section of the Project Manual.

3. Use of Information

- a. Information regarding existing conditions was obtained only for use of District and its consultants, contractors, and tenants for planning and design and is **not** part of the Contract Documents.
- b. District does not warrant, and makes no representation regarding, the accuracy or thoroughness of any information regarding existing conditions. Bidder represents and agrees that in submitting a bid it is not relying on any information regarding existing conditions supplied by District.
- c. Under no circumstances shall District be deemed to warrant or represent existing above-ground conditions, as-built conditions, or other actual conditions, verifiable by independent investigation. These conditions are verifiable by Contractor by the performance of its own independent investigation that Contractor must perform as a condition to bidding, and Contractor should not and shall not rely on this information or any other information supplied by District regarding existing conditions.
- d. Any information shown or indicated in the reports and other data supplied herein with respect to existing underground facilities at or contiguous to the Project may be based upon information and data furnished to District by the District's employees and/or consultants or builders of such underground facilities or

others. District does not assume responsibility for the completeness of this information, and Bidder is solely responsible for any interpretation or conclusion drawn from this information.

- e. District shall be responsible only for the general accuracy of information regarding underground facilities, and only for those underground facilities that are owned by District, and only where Bidder has conducted the independent investigation required of it pursuant to the Instructions to Bidders, and discrepancies are not apparent.

4. Limited Reliance on Certain Information

- a. Reference is made herein for identification of:
 - (1) Reports of explorations and tests of subsurface conditions at or contiguous to the Site that have been utilized by District in preparation of the Contract Documents.
 - (2) Drawings of physical conditions in or relating to existing subsurface structures (except underground facilities) that are at or contiguous to the Site and have been utilized by District in preparation of the Contract Documents.
- b. Bidder may rely upon the general accuracy of the “technical data” contained in the reports and drawings identified above, but only insofar as it relates to subsurface conditions, provided Bidder has conducted the independent investigation required pursuant to Instructions to Bidders, and discrepancies are not apparent. The term “technical data” in the referenced reports and drawings shall be limited as follows:
 - (1) The term “technical data” shall include actual reported depths, reported quantities, reported soil types, reported soil conditions, and reported material, equipment or structures that were encountered during subsurface exploration. The term “technical data” does not include, and Bidder may not rely upon, any other data, interpretations, opinions or information shown or indicated in such drawings or reports that otherwise relate to subsurface conditions or described structures.
 - (2) The term “technical data” shall not include the location of underground facilities.
 - (3) Bidder may not rely on the completeness of reports and drawings for the purposes of bidding or construction. Bidder may rely upon the general accuracy of the “technical data” contained in such reports or drawings.
 - (4) Bidder is solely responsible for any interpretation or conclusion drawn from any “technical data” or any other data, interpretations, opinions, or information provided in the identified reports and drawings.

5. Investigations/Site Examinations

- a. Before submitting a Bid, each Bidder is responsible for conducting or obtaining any additional or supplementary examinations, investigations, explorations, tests, studies, and data concerning conditions (surface, subsurface, and underground facilities) at or contiguous to the Site or otherwise, that may affect cost, progress, performance, or furnishing of Work or that relate to any aspect of the means, methods, techniques, sequences, or procedures of construction to be employed by Bidder and safety precautions and programs incident thereto or that Bidder deems necessary to determine its Bid for performing and furnishing the Work in accordance with the time, price, and other terms and conditions of Contract Documents.
- b. On request, District will provide each Bidder access to the Site to conduct such examinations, investigations, explorations, tests, and studies, as each Bidder deems necessary for submission of a Bid. Bidders must fill all holes and clean up and restore the Site to its former condition upon completion of its

explorations, investigations, tests, and studies. Such investigations and Site examinations may be performed during any and all Site visits indicated in the Invitation to Bid and only under the provisions of the Contract Documents, including, but not limited to, proof of insurance and obligation to indemnify against claims arising from such work, and District's prior approval.

END OF DOCUMENT

DOCUMENT 00 41 13

BID FORM

To: Governing Board of **Downey Unified School District** ("District")

From: _____
(Proper Name of Bidder)

1. **Total Bid.** The undersigned declares that the Contract Documents including, without limitation, the Invitation to Bid, the Instructions to Bidders, and the Special Conditions have been read, and agrees and proposes to furnish all necessary labor, materials, and equipment to perform and furnish all work in accordance with the terms and conditions of the Contract Documents, including, without limitation, the Drawings and Specifications for the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract")

and will accept in full payment for that Work the following total lump sum amount, all taxes included:

TOTAL BASE BID

**NOTE: IF THERE ARE ALLOWANCES IDENTIFIED IN THIS BID FORM, DO \$ _____ Dollars
NOT INCLUDE ANY ALLOWANCE(S) AMOUNTS IN THESE BID AMOUNTS.**

2. **Allowance(s).** The Bidder's Base Bid shall **NOT** include the following potential Allowance(s). The District will add some or all of the following Allowance(s) amount(s) to the successful bidder's Contract, at the District's discretion. Contractor shall be permitted to invoice for Work under an Allowance in the identical structure as a Change Order.
3. **Contract Review.** The undersigned has reviewed the Work outlined in the Contract Documents and fully understands the scope of Work required in this bid, understands the construction and project management function(s) is described in the Contract Documents, and that each Bidder who is awarded a contract shall be in fact a prime contractor, not a subcontractor, to the District, and agrees that its bid, if accepted by the District, will be the basis for the Bidder to enter into a contract with the District in accordance with the intent of the Contract Documents.
4. **Requests for Clarification.** The undersigned has notified the District in writing of any discrepancies or omissions or of any doubt, questions, or ambiguities about the meaning of any of the Contract Documents, and has contacted the Construction Manager before bid date to verify the issuance of any clarifying Addenda.
5. **Contract Time.** The undersigned agrees to commence work under this Contract on the date established in the Contract Documents and to complete all work within the time specified in the Contract Documents.
6. **Contractual Provisions.** The undersigned hereby acknowledges and agrees to be bound by following provisions and all provisions in the Contract Documents:
- The liquidated damages clause of the General Conditions and Agreement.
 - The "Changes in the Work" provisions in the General Conditions that limit the permitted charges and mark-ups on change orders and on the amount of home office overhead that the successful

bidder can receive from the District.

- The "Claims" provisions in the General Conditions that delineate the required process to submit and process disputes and claims.
- The "COVID-19" provisions in the Contract Documents related to the Contractor's staffing requirements and its compliance with all applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with COVID-19, and/or any similar virus or derivative strain.

7. **Bid Open for 90 Days.** It is understood that the District reserves the right to reject this bid and that the bid shall remain open to acceptance and is irrevocable for a period of ninety (90) days.

8. **Attachments.** The following documents are attached hereto:

- The Bid Bond on the District's form or other security
- The Designated Subcontractors List
- The Noncollusion Declaration
- Iran Contracting Act Certification

9. **Addenda Acknowledgement.** Receipt and acceptance of the following addenda is hereby acknowledged:

No.____, Dated _____	No.____, Dated _____
No.____, Dated _____	No.____, Dated _____
No.____, Dated _____	No.____, Dated _____
No.____, Dated _____	No.____, Dated _____
☐ Or check here if <u>no</u> addenda were issued.	

10. **Bidder's License.** Bidder acknowledges that the license required for performance of the Work is as stated in the Invitation to Bid. Bidder certifies that it is, at the time of bidding, and shall be throughout the period of the contract, licensed by the State of California to do the type of work required under the terms of the Contract Documents. Bidder further certifies that it is regularly engaged in the general class and type of work called for in the Contract Documents.

11. **Labor Harmony.** The undersigned hereby certifies that Bidder is able to furnish labor that can work in harmony with all other elements of labor employed or to be employed on the Work.

12. **DIR Registration.** Bidder shall ensure that it and its Subcontractors comply with the registration and compliance monitoring provisions of Labor Code section 1771.4, including furnishing its CPRs to the Labor Commissioner, and are registered pursuant to Labor Code section 1725.5.

13. **General Acknowledgement.** The Bidder represents that it is competent, knowledgeable, and has special skills with respect to the nature, extent, and inherent conditions of the Work to be performed. Bidder further acknowledges that there are certain peculiar and inherent conditions existent in the construction of the Work that may create, during the Work, unusual or peculiar unsafe conditions hazardous to persons and property. Bidder expressly acknowledges that it is aware of such peculiar risks and that it has the skill and experience to foresee and to adopt protective measures to adequately and safely perform the Work with respect to such hazards.

14. False Claims Act. Bidder expressly acknowledges that it is aware that if a false claim is knowingly submitted (as the terms "claim" and "knowingly" are defined in the California False Claims Act, Cal. Gov. Code, §12650 et seq.), the District will be entitled to civil remedies set forth in the California False Claim Act. It may also be considered fraud and the Contractor may be subject to criminal prosecution.

Furthermore, Bidder hereby certifies to the District that all representations, certifications, and statements made by Bidder, as set forth in this bid form, are true and correct and are made under penalty of perjury.

Dated this _____ day of _____ 20 _____

Signature _____

Signed by (Print Name) _____

Title of Person Signing _____

Name of Bidder _____

Type of Organization _____

Address of Bidder _____

Taxpayer's Identification No. of Bidder _____

Telephone Number _____

Fax Number _____

E-mail _____ Web page _____

Bidder's DIR Registration No.: No.: _____

Contractor's License No(s): No.: _____ Class: _____ Expiration Date: _____

No.: _____ Class: _____ Expiration Date: _____

No.: _____ Class: _____ Expiration Date: _____

If Bidder is a corporation, provide the following:

Name of Corporation: _____

President: _____

Secretary: _____

Treasurer: _____

END OF DOCUMENT

DOCUMENT 00 43 13

BID BOND (SECURITY)

**(Note: If Bidder is providing a bid bond as its bid security,
Bidder must use this form, NOT a surety company form.)**

The undersigned, _____ as Principal ("Principal");

and _____ as Surety ("Surety"; a corporation organized and existing under and by virtue of the laws of the State of _____ and authorized to do business as a surety in the State of California) are held and firmly bound unto the **Downey Unified School District** ("District") as Oblgee, in the sum of \$ _____ Dollars, lawful money of the United States, for the payment to the District will and truly to be made pursuant to the provisions herein. Principal and Surety each of us, bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally.

THE CONDITION OF THIS OBLIGATION IS SUCH that whereas the Principal has submitted a bid to the District for all Work specifically described in the accompanying bid and if the District awards the contract to the Principal and, within the time and manner required under the Contract Documents, after the prescribed forms are presented to Principal for signature, the Principal enters into a written contract, in the prescribed form in accordance with the bid, and files two bonds (one guaranteeing faithful performance and the other guaranteeing payment for labor and materials as required by law), and meets all other conditions to the contract between the Principal and the Oblgee becoming effective, or if the Principal shall fully reimburse and save harmless the Oblgee from any damage sustained by the Oblgee through failure of the Principal to enter into the written contract and to file the required performance and labor and material bonds, and to meet all other conditions to the Contract between the Principal and the Oblgee becoming effective, then this obligation shall be null and void; otherwise, it shall be and remain in full force and effect and the Surety shall immediately issue full payment of the sum stated above to the Oblgee upon notification from the Oblgee that the Principal has not taken all steps to nullify or void this obligation.

Surety agrees that no change, extension of time, alteration or addition to the terms of the call for bids, or to the work to be performed thereunder, or the specifications accompanying the same, shall in any way affect its obligation under this bond, and it does hereby waive notice of any such change, extension of time, alteration or addition to the call for bids, or to the work, or to the specifications.

In the event suit is brought upon this bond by the Oblgee and judgment is recovered, the Surety shall pay all costs incurred by the Oblgee in that suit, including a reasonable attorneys' fee to be fixed by the Court.

If the District awards the bid, the security of unsuccessful bidder(s) shall be returned within sixty (60) days from the time the award is made. Unless otherwise required by law, no bidder may withdraw its bid for ninety (90) days after the date of the bid opening.

IN WITNESS WHEREOF, this instrument has been duly executed by the Principal and Surety above named, on

_____, 20_____.

Principal

By

Surety

By

Name of California Agent of Surety

Address of California Agent of Surety

Telephone Number of California Agent of Surety

Bidder must attach Power of Attorney and Certificate of Authority for Surety and a Notarial Acknowledgment for all Surety's signatures. The California Department of Insurance must authorize the Surety to be an admitted Surety Insurer.

END OF DOCUMENT

DOCUMENT 00 43 36

DESIGNATED SUBCONTRACTORS LIST

TO BE EXECUTED BY BIDDER AND SUBMITTED WITH BID

Various Sites CAT6 Cabling for IP Phones Project (“Project” or “Contract”)

1. **Listed.** Bidder must list hereinafter the name and location of each subcontractor who will be employed, and the scope of Work that each will perform if the Contract is awarded to the Bidder. Bidder acknowledges and agrees that under Public Contract Code section 4100, et seq., it must clearly identify the name and location of each subcontractor who will perform work or labor or render service to the Bidder in or about the construction of the Work in an amount in excess of one-half of one percent (1/2 of 1%) of Bidder’s total Bid.
2. **CSLB Number.** Bidder must provide the Contactor State License Board number (“**CSLB No.**”) for all listed subcontractors.
3. **DIR Number.** Bidder must provide the Department of Industrial Relations registration number (“**DIR No.**”) for all listed subcontractors.
4. **Same Scope.** If more than one subcontractor is named for the same scope of Work, state with specificity the particular scope or portion that each subcontractor will perform.
5. **No Vendors or Suppliers.** Bidder need not list entities that are only vendors or suppliers of materials.
6. **Not Listed.** As to any Work that Bidder fails to list that is in excess of one-half of one percent (1/2 of 1%) of Bidder’s total Bid, Bidder agrees that it is qualified to perform that scope of Work and will perform that scope of Work, or be subjected to penalty under applicable law.
7. **Alternate Work.** If alternate bids are called for and Bidder intends to use Subcontractors different from or in addition to those Subcontractors listed for work under the base Bid, Bidder must list Subcontractors that will perform Work in an amount in excess of one half of one percent (1/2 of 1%) of Bidder’s total Bid, including alternates.
8. **Bidders may correct inadvertent error(s) in listing subcontractors’ CSLB Nos. or DIR Nos. within twenty-four (24) hours after bid opening.**
9. **Additional Sheets.** If further space is required for the list of proposed subcontractors, additional sheets showing the required information, as indicated below, shall be attached hereto and made a part of this document and submitted with this form.

I certify and declare under penalty of perjury under the laws of the State of California that all the information listed on the following page(s) is complete, true, and correct.

Date: _____

Proper Name of Bidder: _____

Signature: _____

Print Name: _____

Title: _____

Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:

Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:

Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:
Subcontractor Name	Portion of Work (Scope)	Location of Business	CSLB No.:
			DIR No.:
			If DVBE, % of Work:

END OF DOCUMENT

DOCUMENT 00 43 40

NONCOLLUSION DECLARATION
Public Contract Code § 7106

TO BE EXECUTED BY BIDDER AND SUBMITTED WITH BID

The undersigned declares:

I am the _____ **[PRINT YOUR TITLE]**

of _____ **[PRINT FIRM NAME]**,

the party making the foregoing bid.

The bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation. The bid is genuine and not collusive or sham. The bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid. The bidder has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or to refrain from bidding. The bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder. All statements contained in the bid are true. The bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof, to effectuate a collusive or sham bid, and has not paid, and will not pay, any person or entity for such purpose.

Any person executing this declaration on behalf of a bidder that is a corporation, partnership, joint venture, limited liability company, limited liability partnership, or any other entity, hereby represents that he or she has full power to execute, and does execute, this declaration on behalf of the bidder.

I declare under penalty of perjury under the laws of the State of California that the foregoing is true and correct and that this declaration is executed on the following date:

Date: _____

Proper Name of Bidder: _____

City, State: _____

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

DOCUMENT 00 43 50

IRAN CONTRACTING ACT CERTIFICATION (Public Contract Code § 2204)

Various Sites CAT6 Cabling for IP Phones Project (“Project” or “Contract”)

Pursuant to Public Contract Code (PCC) section 2204, an Iran Contracting Act certification is required for solicitations of goods or services of one million dollars (\$1,000,000) or more.

Bidder shall complete **ONLY ONE** of the following three paragraphs.

- ☐ 1. Bidder’s Total Base Bid is less than one million dollars (\$1,000,000).

OR

- ☐ 2. Bidder’s Total Base Bid is one million dollars (\$1,000,000) or more, but Bidder is **not** on the current list of persons engaged in investment activities in Iran created by the California Department of General Services (“DGS”) pursuant to Public Contract Code § 2203(b), and Bidder is not a financial institution extending twenty million dollars (\$20,000,000) or more in credit to another person, for 45 days or more, if that other person will use the credit to provide goods or services in the energy sector in Iran and is identified on the current list of persons engaged in investment activities in Iran created by DGS.

OR

- ☐ 3. Bidder’s Total Base Bid is one million dollars (\$1,000,000) or more, but the District has given prior written permission to Bidder to submit a proposal pursuant to PCC 2203(c) or (d). **A copy of the written permission from the District is included with Bid.**

I certify that I am duly authorized to legally bind the Bidder to this certification, that the contents of this certification are true, and that this certification is made under the laws of the State of California.

Date: _____

Proper Name of Bidder: _____

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

DOCUMENT 00 45 00

NOTICE OF AWARD

Dated: _____, 20__

To: _____
("Contractor")

(Address)

From: Governing Board ("Board") of **Downey Unified School District** ("District")

Re: **Various Sites CAT6 Cabling for IP Phones Project** ("Project" or "Contract")

Contractor was awarded the Contract on _____, 20__, by action of the District's Board.

The Contract Price is \$ _____ **Dollars** and includes alternates
_____.

Three (3) copies of each of the Contract Documents (except Drawings) accompany the Notice of Award. Three (3) sets of the Drawings will be delivered separately or otherwise made available. Additional copies are available at cost of reproduction.

Contractor must comply with the following conditions precedent within **SEVEN (7)** calendar days of the date of this Notice of Award.

Contractor shall execute and submit the following Contract Documents by 5:00 p.m. of the **SEVENTH (7TH)** calendar day following the date of the Notice of Award. Failure to properly and timely submit the following Contract Documents entitles District to foreclose on Contractor's bid bond and award the contract to the next responsive, responsible bidder.

- a. Agreement: Submit four (4) copies, each bearing an original signature. **If Contractor is a corporation, Contractor must attach a certified copy of the corporation's by-laws, or the resolution of the Board of Directors of the corporation, authorizing the signatory to execute the Agreement and the bonds required by the Contract Documents.**
- b. Performance Bond (100%): Fully executed form provided in the Contract Documents.
- c. Payment Bond (100%) (Contractor's Labor and Material Bond): Fully executed form provided in the Contract Documents.
- d. Insurance Certificates and Endorsements as required.
- e. Certifications to be Completed by Contractor
- f. Criminal Background Investigation/Fingerprinting Certification.

Failure to comply with these conditions within the time specified will entitle District to consider Contractor's bid abandoned, to annul the Notice of Award, and to declare Contractor's Bid Security forfeited, as well as any other rights the District may have against Contractor.

District will return to Contractor one fully signed counterpart of the Agreement.

Downey Unified School District

SIGNATURE: _____

NAME: _____

TITLE: _____

END OF DOCUMENT

DOCUMENT 00 45 10

AGREEMENT

This agreement is made and entered into on _____, 202_____, by and between the **Downey Unified School District** ("District") and _____ ("Contractor") ("Agreement"). The District and the Contractor agree as follows:

1. **The Work:** Contractor shall furnish all tools, equipment, apparatus, facilities, labor, and material necessary to perform and complete in a good and workmanlike manner, the work of the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract" or "Work")

The Work shall be performed and completed as required in the Contract Documents as defined in the General Conditions including, without limitation, the Drawings and Specifications, under the direction and supervision of, and subject to, the approval of the District or its authorized representative.

2. **The Contract Documents:**

- a. The complete Contract consists of all Contract Documents as defined in the General Conditions and incorporated herein by this reference. All obligations of the District and Contractor are fully set forth and described in the Contract Documents. The Contract Documents are intended to cooperate so that Work called for in one and not mentioned in the other or vice versa is to be performed the same as if mentioned in all Contract Documents.
- b. **Interpretation of Contract Documents/Order of Precedence:** Questions concerning the intent, precedence, or meaning of the Contract Documents, including the Drawings or Specifications, shall be submitted to the District for interpretation. Inconsistencies in the Contract Documents shall be resolved by giving precedence in the following order:
- (i) District-approved modifications (e.g., Change Orders, Force Account Directives, etc.), beginning with the most recent (if any);
 - (ii) Agreement;
 - (iii) Special Conditions (if any);
 - (iv) Supplemental Conditions (if any);
 - (v) General Conditions;
 - (vi) Remaining Division 0 documents (Documents beginning with "00");
 - (vii) Division 1 Documents (Documents beginning with "01");
 - (viii) Division 2 through Division 49 documents (Technical Specifications);
 - (ix) Figured dimensions;
 - (x) Large-scale drawings;
 - (xi) Small-scale drawings.

In case of conflict, the greater quantity and/or higher standard of workmanship shall apply unless the District expressly in writing (e.g., via a Change Order) accepts a lesser quantity or lower quality of workmanship and the Contract Price is adjusted accordingly. The decision of the District in the matter shall be final.

3. **Integration / Modification.** The Contract Documents and any documents specifically incorporated by reference are completely integrated as the complete and exclusive statement of the terms of the Agreement. This Agreement supersedes all previous contracts, agreements, and / or communications, both oral and written, and constitutes the entire understanding of the District and Contractor. No extrinsic evidence whatsoever shall be admissible or used to explain or supplement the terms of the Contract, Contract

Documents, or any items incorporated by reference. No changes, amendments or alterations shall be effective unless in writing, signed by both Parties, and unless provided otherwise by the Contract Documents.

4. **Classification of Contractor's License:** Contractor hereby acknowledges that it currently holds valid Type C-39 issued by the State of California and Audio Enhancement and Extron certified and authorized dealer, Contractor's State Licensing Board, in accordance with division 3, chapter 9, of the Business and Professions Code and in the classification called for in the Contract Documents.
 5. **Time for Completion:** It is hereby understood and agreed that the Contractor shall complete the Work within one hundred sixty-five (165) consecutive calendar days ("**Contract Time**") from the date specified in the District's Notice to Proceed. The District shall not approve an early completion schedule by Contractor. A schedule showing the Work completed in less than the Contract Time indicated in the Contract, shall be considered to have Project Float.
 6. **Completion-Extension of Time:** If Contractor fails to complete the Work within the Contract Time, due allowance being made for the contingencies provided for herein, Contractor shall become liable to District for all loss and damage that District may suffer on account thereof. Contractor shall coordinate its Work with the work of all other contractors. The District shall not be liable for delays resulting from Contractor's failure to coordinate its Work with other contractors in a manner that allows for timely completion of Contractor's Work. Contractor shall be liable for delays to other contractors caused by Contractor's failure to coordinate its Work with the work of other contractors.
 7. **Liquidated Damages:** Time is of the essence for all Work to be performed. It is hereby understood and agreed that it is and will be difficult and/or impossible to ascertain and determine the actual damage that District will sustain in the event of and by reason of Contractor's delay; therefore, pursuant to Government Code section 53069.85 and Public Contract Code section 7203, Contractor shall forfeit and pay to District the following sum(s) as liquidated damages ("**Liquidated Damages**"):
 - **Project Completion: \$1,200.00 dollars** per day as Liquidated Damages for each and every day's delay beyond the Contract Time to complete all the Work.
- a. Each portion of the Liquidated Damages shall be calculated cumulatively. For example, if Contractor is late in completing two milestones and the entire Project, Contractor will forfeit and pay three separate Liquidated Damages amounts. It is hereby understood and agreed that neither the total cumulative Liquidate Damages amount nor any portion of the Liquidated Damage amount are penalties.
 - b. District may deduct Liquidated Damages from money due or that may become due Contractor under this Agreement. Contractor's forfeiture of Liquidated Damages to District, and District's right to retain Liquidated Damages, are as indicated in Government Code section 53069.85 and as indicated herein and in the General Conditions. Liquidated Damages are automatically and without notice of any kind forfeited and payable by Contractor upon the accrual of each day of delay. Neither District's failure or delay in deducting Liquidated Damages from payments otherwise due the Contractor, nor District's failure or delay in notifying Contractor of the forfeiture and payment of Liquidated Damages, shall be deemed a waiver of District's right to Liquidated Damages and/or the District's right to withhold Liquidated Damages from any amounts that would otherwise be payable to the Contractor.
 - c. Contractor and Surety shall be liable for and pay to District the entire amount of Liquidated Damages including any portion that exceeds the amount of the Contract Price then held, retained or controlled by District.
 - d. Liquidated Damages shall be in addition, and not in lieu of, District's right to charge Contractor for the District's cost of completing or correcting items of the Work.

8. **Contract Price:** In consideration of the foregoing covenants, promises, and agreements, Contractor offers, in the amounts stated below, to perform the Work according to the Contract Documents. District covenants, promises, and agrees that it will pay and cause to be paid to Contractor in full, and as the Contract Price the following amount(s):

\$ _____ Dollars
(“Contract Price”)

- a. The Contract Price shall be paid in lawful money of the United States pursuant to the payment provisions in the General Conditions.
- b. The District may, at its sole discretion, increase or decrease the Contract Price by unit prices or alternates contained in Contractor’s original bid. If the Bid for the Work included proposal(s) for Alternate Bid Item(s), during Contractor’s performance of the Work, the District may elect to add any such Alternate Bid Item(s) if the item did not form a basis for award of the Agreement or delete any such Alternate Bid Item(s) if that item formed a basis for award of the Agreement. If the District elects to add or delete an Alternate Bid Item(s) pursuant to the foregoing, the cost or credit for that Alternate Bid Item(s) shall be as set forth in the Contractor’s Bid, at the District’s discretion. If any Alternate Bid Item is added or deleted from the Work pursuant to the foregoing, the Contract Time shall be adjusted by the number of days allocated for the added or deleted Alternate Bid Item in the Contract Documents; if days are not allocated for any Alternate Bid Item added or deleted pursuant to the foregoing, the Contract Time shall be equitably adjusted.
9. **Insurance and Bonds:** Contractor shall provide all required certificates of insurance, and payment and performance bonds.
10. **Performance of Work:** If Contractor fails to perform the Work properly or fails to perform any provisions of this Contract, the District, may, pursuant to the General Conditions and without prejudice to any other remedy it may have, cure the deficiencies and deduct the cost thereof from the payment then or thereafter due Contractor.
11. **COVID-19.** Contractor is responsible for complying with all applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with COVID-19, and/or any similar virus or derivative strain. Contractor shall ensure it has supervisor employees onsite that are trained and knowledgeable of all of these requirements to ensure full compliance on Project Site(s).
12. **Authority of Architect, Project Inspector, and DSA:** Contractor hereby acknowledges that the Architect(s), the Project Inspector(s), and the Division of the State Architect have authority to approve and/or stop Work if Contractor’s Work does not comply with the requirements of the Contract Documents, Title 24 of the California Code of Regulations, and all applicable laws. Contractor shall be liable for any delay caused by its non-compliant Work.
13. **Assignment of Contract:** Neither the Contract, nor any part thereof, nor any moneys due or to become due thereunder, may be assigned by Contractor without the written approval of District, nor without the written consent of the Surety on Contractor’s Performance Bond (the “Surety”), unless the Surety has waived in writing its right to notice of assignment.
14. **Payment of Prevailing Wages:** Contractor and all Subcontractors under Contractor shall pay all workers on Work performed pursuant to this Contract not less than the general prevailing rate of per diem wages and the general prevailing rate for holiday and overtime work as determined by the Director of the Department of Industrial Relations, State of California, for the type of work performed and the locality in which the work is to be performed within the boundaries of the District, pursuant to sections 1770 et seq. of the California Labor Code.

15. Contractor & Subcontractor Registration: Contractor shall comply with the registration and compliance monitoring provisions of Labor Code section 1771.4, including complying with any applicable enforcement by the Department of Industrial Relations.

16. Authority of Contractor's Representatives: Contractor hereby certifies that the person who executes this Agreement has the authority and power to legally bind the Contractor. Contractor also certifies that each person(s) it employees on the Project at or above the level of project superintendent, has the authority to legally bind the Contractor.

17. Severability: If any term, covenant, condition, or provision of the Contract Documents is held by a court of competent jurisdiction to be invalid, void or unenforceable, the remainder of the provisions in the Contract Documents shall remain in full force and effect and shall in no way be affected, impaired, or invalidated thereby.

18. Notice: Any notice required by the Agreement shall be in writing, dated and signed by the party giving notice or by a duly authorized representative of that party. Notice shall be served and considered effective if given in one of the following manners and to the following persons and addresses:

- a. By personal delivery; considered delivered on the day of delivery.
- b. By overnight delivery service; considered delivered one (1) day after date deposited, as indicated by the delivery service.
- c. By depositing same in United States mail, enclosed in a sealed envelope; considered delivered three (3) days after date deposited, as indicated by the postmarked date.
- d. By registered or certified mail with postage prepaid, return receipt requested; considered delivered on the day the notice is signed for.

If to District

Downey Unified School District
11627 Brookshire Ave.
Downey, CA 90241
ATTN: Vince Madsen

If to Contractor:

_____, CA _____
ATTN: _____

IN WITNESS WHEREOF, accepted and agreed on the date indicated above:

Dated: _____, 20____

Dated: _____, 20____

Downey Unified School District

_____ **Contractor**

Signature: _____

Signature: _____

Print Name: _____

Print Name: _____

Print Title: _____

Print Title: _____

NOTE: If the Contractor is a corporation, Contractor must attach a certified copy of the corporation's by-laws, or of the resolution of the Board of Directors of the corporation, authorizing the above person to execute this Agreement and the bonds required by the Contract Documents.

END OF DOCUMENT

CERTIFICATIONS TO BE COMPLETED BY CONTRACTOR

THE UNDERSIGNED MUST CHECK EACH BOX AND EXECUTE THIS FORM AND HEREBY CERTIFIES TO THE GOVERNING BOARD OF THE DISTRICT THAT:

- The undersigned is a representative of the Contractor,
- The undersigned is familiar with the facts herein certified and acknowledged,
- The undersigned is authorized and qualified to execute this Agreement and these certifications on behalf of Contractor and that by executing this Agreement undersigned is certifying the following items.

☐ **Labor Code Sections 1860-1861 (Workers' Compensation).** In accordance with Labor Code section 3700, every contractor will be required to secure the payment of compensation to his or her employees. I acknowledge and certify under penalty of perjury that I am aware of the provisions of Section 3700 of the Labor Code which require every employer to be insured against liability for workers' compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this contract.

☐ **Government Code Sections 8355-8357 (Drug-Free Workplace).** I acknowledge and certify under penalty of perjury that I will provide a drug-free workplace by doing all of the following:

- (1) Publishing a statement notifying employees that the unlawful manufacture, distribution, dispensation, possession, or use of a controlled substance is prohibited in the person's or organization's workplace and specifying the actions that will be taken against employees for violations of the prohibition.
- (2) Establishing a drug-free awareness program to inform employees about all of the following:
 - (A) The dangers of drug abuse in the workplace.
 - (B) The person's or organization's policy of maintaining a drug-free workplace.
 - (C) Any available drug counseling, rehabilitation, and employee assistance programs.
 - (D) The penalties that may be imposed upon employees for drug abuse violations.
- (3) Requiring that each employee engaged in the performance of the contract or grant be given a copy of the statement required by subdivision (a) and that, as a condition of employment on the contract or grant, the employee agrees to abide by the terms of the statement.

I also acknowledge that this Contract may be subject to suspension of payments under the contract or grant or termination of the contract or grant, or both, and the contractor or grantee thereunder may be subject to debarment, in accordance with the requirements of the above-referenced statute, if the contracting or granting agency determines that any of the following has occurred:

- (1) The contractor or grantee has made a false certification under Section 8355.
- (2) The contractor or grantee violates the certification by failing to carry out the requirements of subdivisions (a) to (c), inclusive, of Section 8355.

I also acknowledge that the Department of General Services shall establish and maintain a list of individuals and organizations whose contracts or grants have been canceled due to failure to comply with the above-referenced statute. This list shall be updated monthly and published each month. No state agency shall award a contract or grant to a person or organization on the published list until that person or organization has complied with the above-referenced statute.

☐ **Tobacco-Free Environment.** Pursuant to, without limitation, 20 U.S.C. section 6083, Labor Code section 6400 et seq., Health & Safety Code section 104350 et seq. and District Board Policies, all District sites, including the Project site, are tobacco-free environments. Smoking and the use of tobacco products by all persons is prohibited on or in District property. District property includes school buildings, school grounds, school owned vehicles and vehicles owned by others while on District property.

I acknowledge and certify under penalty of perjury that I am aware of the District's policy regarding tobacco-free environments at District sites, including the Project site and acknowledge and certify that I will adhere to the requirements of that policy and not permit any of my firm's employees, agents, subcontractors, or my firm's subcontractors' employees or agents to use tobacco and/or smoke on the Project site. The District also prohibits electronic cigarettes, "vaping" or similar product uses on District sites.

☐ **No Hazardous Materials.** I acknowledge and certify under penalty of perjury that no Asbestos, or Asbestos-Containing Materials, polychlorinated biphenyl (PCB), or any material listed by the federal or state Environmental Protection Agency or federal or state health agencies as a hazardous material, or any other material defined as being hazardous under federal or state laws, rules, or regulations ("New Hazardous Material"), shall be furnished, installed, or incorporated in any way into the Project or in any tools, devices, clothing, or equipment used to affect any portion of Contractor's work on the Project for District. I have instructed our employees with respect to the above-mentioned standards, hazards, risks, and liabilities.

- (i) Asbestos and/or asbestos-containing material shall be defined as all items containing but not limited to chrysotile, crocidolite, amosite, anthophyllite, tremolite, and actinolite. Any or all material containing greater than one-tenth of one percent (.1%) asbestos shall be defined as asbestos-containing material. Any disputes involving the question of whether or not material is New Hazardous Material shall be settled by electron microscopy or other appropriate and recognized testing procedure, at the District's determination. The costs of any such tests shall be paid by Contractor if the material is found to be New Hazardous Material.
- (ii) All Work or materials found to be New Hazardous Material or Work or material installed with equipment containing "New Hazardous Material," will be immediately rejected and this Work will be removed at Contractor's expense at no additional cost to the District.

The Contractor must immediately notify the District within two (2) Business Days, if the Contractor finds and before it disturbs, any material that the Contractor believes may be hazardous waste, as defined in section 25117 of the Health and Safety Code, and requires removal to a Class I, Class II, or Class III disposal site in accordance with provisions of existing law.

☐ **Lead as a Health Hazard.** Lead poisoning is recognized as a serious environmental health hazard facing children today. Even at low levels of exposure, much lower than previously believed, lead can impair the development of a child's central nervous system, causing learning disabilities, and leading to serious behavioral problems. Lead enters the environment as tiny lead particles and lead dust disbursts when paint chips, chalks, peels, wears away over time, or is otherwise disturbed. Ingestion of lead dust is the most common pathway of childhood poisoning; lead dust gets on a child's hands and toys and then into a child's mouth through common hand-to-mouth activity. Exposures may result from construction or remodeling activities that disturb lead paint, from ordinary wear and tear of windows and doors, or from friction on other surfaces.

Ordinary construction and renovation or repainting activities carried out without lead-safe work practices can disturb lead-based paint and create significant hazards. Improper removal practices, such as dry scraping, sanding, or water blasting painted surfaces, are likely to generate high volumes of lead dust.

Because the Contractor and its employees will be providing services for the District, and because the Contractor's work may disturb lead-containing building materials, **Contractor is hereby notified** of the potential presence of lead-containing materials located within certain buildings utilized by the District. All school buildings built prior to

1993 are presumed to contain some lead-based paint until sampling proves otherwise.

(i) **Overview of California Law**

Education Code section 32240 et seq. is known as the Lead Safe Schools Protection Act. Under this act, the Department of Health Services ("DHS") is to conduct a sample survey of schools in the State of California for the purpose of developing risk factors to predict lead contamination in public schools. (Ed. Code, § 32241.)

Any school that undertakes any action to abate existing risk factors for lead is required to utilize trained and state-certified contractors, inspectors, and workers. (Ed. Code, § 32243, subd. (b).) Moreover, lead-based paint, lead plumbing, and solders, or other potential sources of lead contamination, shall not be utilized in the construction of any new school facility or the modernization or renovation of any existing school facility. (Ed. Code, § 32244.)

Both the Federal Occupational Safety and Health Administration ("Fed/OSHA") and the California Division of Occupational Safety and Health ("Cal/OSHA") have implemented safety orders applicable to all construction work where a contractor's employee may be occupationally exposed to lead.

The OSHA Regulations apply to all construction work where a contractor's employee may be occupationally exposed to lead. The OSHA Regulations contain specific and detailed requirements imposed on contractors subject to that regulation. The OSHA Regulations define construction work as work for construction, alteration, and/or repair, including painting and decorating. It includes, but is not limited to, the following:

- a. Demolition or salvage of structures where lead or materials containing lead are present;
- b. Removal or encapsulation of materials containing lead;
- c. New construction, alteration, repair, or renovation of structures, substrates, or portions thereof, that contain lead, or materials containing lead;
- d. Installation of products containing lead;
- e. Lead contamination/emergency cleanup;
- f. Transportation, disposal, storage, or containment of lead or materials containing lead on the site or location at which construction activities are performed; and
- g. Maintenance operations associated with the construction activities described in the subsection.

Because it is assumed by the District that all painted surfaces (interior as well as exterior) within the District contain some level of lead, it is imperative that the Contractor, its workers and subcontractors fully and adequately comply with all applicable laws, rules and regulations governing lead-based materials (including title 8, California Code of Regulations, section 1532. 1).

The Contractor must notify the District if any Work may result in the disturbance of lead-containing building materials. Any and all Work that may result in the disturbance of lead-containing building materials must be coordinated through the District. A signed copy of this Certification must be on file prior to beginning Work on the Project, along with all current insurance certificates.

(ii) **Renovation, Repair and Painting Rule, Section 402(c)(3) of the Toxic Substances Control Act**

In 2008, the U.S. Environmental Protection Agency, issued a rule pursuant to the authority of Section 402(c)(3)

of the Toxic Substances Control Act, requiring lead safe work practices to reduce exposure to lead hazards created by renovation, repair and painting activities that disturb lead-based paint (Renovation, Repair and Painting Rule). Renovations in homes, childcare facilities, and schools built prior to 1978 must be conducted by certified renovations firms, using renovators with accredited training, and following the work practice requirements to reduce human exposures to lead.

Contractor, its workers and subcontractors must fully and adequately comply with all applicable laws, rules and regulations governing lead-based materials, including those rules and regulations appearing within title 40 of the Code of Federal Regulations as part 745 (40 CFR 745).

The requirements apply to all contractors who disturb lead-based paint in a six-square-foot area or greater indoors or a 20-square-foot area outdoors. If a DPH-certified inspector or risk assessor determines that a home constructed before 1978 is lead-free, the federal certification is not required for anyone working on that particular building.

(iii) **Contractor's Liability**

If the Contractor fails to comply with any applicable laws, rules, or regulations, and that failure results in a site or worker contamination, the Contractor will be held solely responsible for all costs involved in any required corrective actions, and shall defend, indemnify, and hold harmless the District, pursuant to the indemnification provisions of the Contract, for all damages and other claims arising therefrom.

If lead disturbance is anticipated in the Work, only persons with appropriate accreditation, registrations, licenses, and training shall conduct this Work.

It shall be the responsibility of the Contractor to properly dispose of any and all waste products, including, but not limited to, paint chips, any collected residue, or any other visual material that may occur from the prepping of any painted surface. It will be the responsibility of the Contractor to provide the proper disposal of any hazardous waste by a certified hazardous waste hauler. This company shall be registered with the Department of Transportation (DOT) and shall be able to issue a current manifest number upon transporting any hazardous material from any school site within the District.

The Contractor shall provide the District with any sample results prior to beginning Work, during the Work, and after the completion of the Work. The District may request to examine, prior to the commencement of the Work, the lead training records of each employee of the Contractor.

I acknowledge and certify under penalty of perjury, that:

1. I have received notification of potential lead-based materials on the District's property;
 2. I am knowledgeable regarding and will comply with all applicable laws, rules, and regulations governing work with, and disposal of, lead.
-



Imported Materials. All soils, aggregate, or related materials ("Fill") that Contractor, a Subcontractor, agent or supplier, in any way, provides or delivers and/or supplies to the Project Site shall be free of any and all hazardous material as defined in section 25260 of the Health and Safety Code, shall satisfy the requirements of any environmental review of the Project performed pursuant to the statutes and guidelines of the California Environmental Quality Act, sections 21000 et seq. of the Public Resources Code ("CEQA"), and shall comply with the requirements of sections 17210 et seq. of the Education Code, including requirements for a Phase I environmental assessment acceptable to the State of California Department of Education and Department of Toxic Substances Control. I acknowledge that, to the furthest extent permitted by California law, the indemnification provisions in the Contract Documents apply to, without limitation, any claim(s) connected with providing, delivering, and/or supplying Fill.

☐ **Roofing Contract Financial Interest Certification (Public Contract Code § 3006)**

I, _____ [Your Name], _____ [Firm Name]
certify that I have not offered, given, or agreed to give, received, accepted, or agreed to accept, any gift, contribution, or any financial incentive whatsoever to or from any person in connection with a roof project contract or subcontract on the Project. As used in this certification, "person" means any natural person, business, partnership, corporation, union, committee, club, or other organization, entity, or group of individuals.

I, _____ [Your Name], _____ [Firm Name]
certify that I do not have, and throughout the duration of the Contract, I will not have, any financial relationship in connection with the performance of the Contract with any architect, engineer, roofing consultant, materials manufacturer, distributor, or vendor that is not disclosed below.

I, _____ [Your Name], _____ [Firm Name]
have the following financial relationships with an architect, engineer, roofing consultant, materials manufacturer, distributor, or vendor, or other person in connection with the following roof project contract:

Name of firm ("Firm"): _____
Mailing address: _____
Address of branch office used for this Project: _____
If subsidiary, name and address of parent company: _____

For Projects without substantive roofing components, check the following box and execute this certification:

☐ The Work on the Contract (1) does not include the replacement or repair of a roof or (2) is a repair of twenty five percent (25%) or less of the roof, (3) or is a repair project that has a total cost of twenty one thousand dollars (\$21,000) or less.

☐ **Russian Sanctions Certification**

On February 21, 2022, President Biden issued Executive Order 14065 (<https://www.whitehouse.gov/briefing-room/presidential-actions/2022/02/21/executive-order-on-blocking-property-of-certain-persons-and-prohibiting-certain-transactions-with-respect-to-continued-russian-efforts-to-undermine-the-sovereignty-and-territorial-integrity-of-ukraine/>; "Federal Order") imposing economic sanctions and prohibiting many activities including, but not limited to, investing in, importing to, exporting from, and contracting with, areas of Ukraine and in Russia. On March 4, 2022, California Governor Newsom issued Executive Order N-6-22 requiring state agencies to take steps to ensure any agency and entity under contract with state agencies comply with the Federal Order (<https://www.gov.ca.gov/wp-content/uploads/2022/03/3.4.22-Russia-Ukraine-Executive-Order.pdf>; "State Order").

The District requires the Contractor, as a vendor with the District, to comply with the economic sanctions imposed in response to Russia's actions in Ukraine, including the orders and sanctions identified on the U.S. Department of the Treasury website (<https://home.treasury.gov/policy-issues/financial-sanctions/sanctions-programs-and-country-information/ukraine-russia-related-sanctions>).

If your Firm's contract with the District has a cumulative value of \$5 million or more, your certification here constitutes your written response to the District, indicating:

(1) that your Firm is in compliance with the required economic sanctions of the Federal and State Orders;

(2) the steps your Firm has taken in response to Russia's actions in Ukraine, including, but not limited to, desisting from making new investments in, or engaging in financial transactions with, Russian entities, not

transferring technology to Russia or Russian entities, and directly providing support to the government and people of Ukraine.

I ACKNOWLEDGE AND CERTIFY UNDER PENALTY OF PERJURY THAT I AM DULY AUTHORIZED TO LEGALLY BIND THE CONTRACTOR TO ALL PROVISIONS AND ITEMS INCLUDED IN THESE CERTIFICATIONS, THAT THE CONTENTS OF THESE CERTIFICATIONS ARE TRUE, AND THAT THESE CERTIFICATIONS ARE MADE UNDER THE LAWS OF THE STATE OF CALIFORNIA.

Date: _____

Proper Name of Contractor: _____

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

CRIMINAL BACKGROUND INVESTIGATION / FINGERPRINTING CERTIFICATION

The undersigned does hereby certify to the governing board of the District that undersigned is a representative of the Contractor, is familiar with the facts herein certified, is authorized and qualified to execute this certificate on behalf of Contractor; and that the information in this Criminal Background Investigation / Fingerprinting Certification is true and correct.

1. **Education Code.** Contractor has taken at least one of the following actions (check all that apply):

☐ **All Workers Fingerprinted.** The Contractor has complied with the fingerprinting requirements of Education Code section 45125.1 with respect to all Contractor's employees and all of its subcontractors' employees who interact with pupils, outside of the immediate supervision and control of the pupil's parent or guardian or a school employee, has a valid criminal records summary as described in Education Code Section 44237 (Contractor shall "require each applicant for employment in a position requiring contact with minor pupils to submit two sets of fingerprints prepared for submittal by the employer to the Department of Justice for the purpose of obtaining criminal record summary information from the Department of Justice and the Federal Bureau of Investigation."). A complete and accurate list of Contractor's employees and of all of its subcontractors' employees who may interact with District pupils during the course and scope of the Contract is attached hereto; and/or

☐ **Physical Barrier.** Pursuant to Education Code section 45125.2, Contractor has installed or will install, prior to commencement of work, a physical barrier at the Project site, that will limit contact between Contractor's employees and District pupils at all times; and/or

☐ **Continual Supervision by Fingerprinted Employee.** Pursuant to Education Code section 45125.2, Contractor certifies that all employees will be under the continual supervision of, and monitored by, an employee of the Contractor who the California Department of Justice has ascertained has not been convicted of a violent or serious felony. The name and title of the employee who will be supervising Contractor's employees and its subcontractors' employees is:

Name: _____ **Title:** _____

☐ **Unoccupied Site.** The Work on the Contract is at an unoccupied school site and no employee and/or subcontractor or supplier of any tier of Contract shall come in contact with the District pupils.

2. **Megan's Law (Sex Offenders).** I have verified and will continue to verify that the employees of Contractor that will be on the Project site and the employees of the Subcontractor(s) that will be on the Project site are **not** listed on California's "Megan's Law" Website (<http://www.meganslaw.ca.gov/>).

Contractor's responsibility for background clearance extends to all of its employees, subcontractors, and employees of subcontractors coming into contact with District pupils regardless of whether they are designated as employees or acting as independent contractors of the Contractor.

Date: _____

Proper Name of Contractor: _____

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

DOCUMENT 00 61 14

PERFORMANCE BOND (100% of Contract Price)

(Note: Contractors must use this form, NOT a surety company form.)

WHEREAS, the governing board ("Board") of the **Downey Unified School District**, ("District") and

_____, ("Principal")

have entered into a contract for the furnishing of all materials and labor, services and transportation, necessary, convenient, and proper to perform the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract")

which Contract dated _____, 20____, and all of the Contract Documents attached to or forming a part of the Contract, are hereby referred to and made a part hereof, and

WHEREAS, the Principal is required under the terms of the Contract to furnish a bond for the faithful performance of the Contract;

NOW, THEREFORE, the Principal and _____ ("Surety") are held and firmly bound unto the District in the penal sum of:

\$ _____ **DOLLARS,**

lawful money of the United States, for payment to the District and will and truly be made pursuant to the provisions herein. Principal and Surety, each of us, bind ourselves, our heirs, executors, administrators, successors, and assigns jointly and severally to:

- Perform all the work required to complete the Project; and
- Pay to the District all damages the District incurs as a result of the Principal's failure to perform all the Work required to complete the Project.

In the event the Principal is declared by the District to be in breach or default in the performance of the Contract, then, after written notice from the District to the Surety, as provided for herein, the Surety shall either remedy the default or breach of the Principal or shall take charge of the Work of the Contract and complete the Contract with a Contractor other than the Principal at its own expense; provided, however, that the procedure by which the Surety undertakes to discharge its obligations under this Bond shall be subject to the advance written approval of the District.

The condition of the obligation is such that, if the above bounden Principal, his or its heirs, executors, administrators, successors, or assigns, shall in all things stand to and abide by, and well and truly keep and perform the covenants, conditions, and agreements in the Contract and any alteration thereof made as therein provided, on his or its part to be kept and performed at the time and in the intent and meaning, including all contractual guarantees and warranties of materials and workmanship, and shall indemnify and save harmless the District, its trustees, officers and agents, as therein stipulated, then this obligation shall become null and void, otherwise it shall be and remain in full force and effect.

As a condition precedent to the satisfactory completion of the Contract, the above obligation shall hold good for a period equal to the warranty and/or guarantee period of the Contract, during which time Surety's obligation shall continue if Contractor shall fail to make full, complete, and satisfactory repair, replace, and totally protect the District from loss or damage resulting from or caused by defective materials or faulty workmanship. The obligations of Surety hereunder shall continue so long as any obligation of Contractor remains. Nothing herein

shall limit the District's rights or the Contractor's or Surety's obligations under the Contract, law or equity, including, but not limited to, California Code of Civil Procedure section 337.15.

The Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration, or addition to the terms of the Contract or to the Work to be performed thereunder shall in any way affect its obligation on this bond, and it does hereby waive notice of any such change, extension of time, alteration, or addition to the Contract Documents or to the Work.

Any claims under this bond may be addressed to the Surety at the following address. This cannot be the Contractor's broker for this bond, but must be an employee of the Surety or the Surety's legal counsel:

Attention: _____

Telephone No.: (____) ____ - _____

Fax No.: (____) ____ - _____

E-mail Address: _____

IN WITNESS WHEREOF, two (2) identical counterparts of this instrument, each of which shall for all purposes be deemed an original thereof, have been duly executed by the Principal and Surety above named, on the _____ day of _____, 20____.

Principal

Surety

(Name of Principal)

(Name of Surety)

(Signature of Person with Authority)

(Signature of Person with Authority)

(Print Name)

(Print Name)

(Name of California Agent of Surety)

(Address of California Agent of Surety)

(Telephone Number of California Agent of Surety)

Contractor must attach a Notarial Acknowledgment for all Surety's signatures and a Power of Attorney and Certificate of Authority for Surety. The California Department of Insurance must authorize the Surety to be an admitted surety insurer.

END OF DOCUMENT

DOCUMENT 00 61 15

PAYMENT BOND -- Contractor's Labor & Material Bond (100% of Contract Price)

(Note: Contractors must use this form, NOT a surety company form.)

WHEREAS, the governing board ("Board") of the **Downey Unified School District**, ("District") and

_____, ("Principal")

have entered into a contract for the furnishing of all materials and labor, services and transportation, necessary, convenient, and proper to perform the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract")

which Contract dated _____, 20____, and all of the Contract Documents attached to or forming a part of the Contract, are hereby referred to and made a part hereof, and

WHEREAS, pursuant to law and the Contract, the Principal is required, before entering upon the performance of the work, to file a good and sufficient bond with the body by which the Contract is awarded in an amount equal to 100 percent (100%) of the Contract price, to secure the claims to which reference is made in the Civil Code of California, including section 9100, and the Labor Code of California, including section 1741.

NOW, THEREFORE, the Principal and _____ ("Surety") are held and firmly bound unto all laborers, material men, and other persons referred to in said statutes in the penal sum of:

\$ _____ **DOLLARS,**

lawful money of the United States, being a sum not less than the total amount payable by the terms of Contract, for the payment of which sum well and truly to be made pursuant to all applicable statutes and laws applicable to the provisions herein. Principal and Surety, each of us, bind ourselves, our heirs, executors, administrators, successors, or assigns, jointly and severally, to those applicable statutes and laws, and to the provisions herein.

The condition of this obligation is that if the Principal or any of his or its subcontractors, of the heirs, executors, administrators, successors, or assigns of any, all, or either of them shall fail to pay for any labor, materials, provisions, equipment, or other supplies, used in, upon, for or about the performance of the work contracted to be done, or for any work or labor thereon of any kind, or for amounts due under the Unemployment Insurance Act with respect to that work or labor, that the Surety will pay the same in an amount not exceeding the amount herein above set forth, and also in case suit is brought upon this bond, will pay a reasonable attorney's fee to be awarded and fixed by the Court, and to be taxed as costs and to be included in the judgment therein rendered.

It is hereby expressly stipulated and agreed that this bond shall inure to the benefit of any and all persons, companies, and corporations entitled to file claims under sections 9000 through 9566 of the Civil Code, so as to give a right of action to them or their assigns in any suit brought upon this bond.

Should the condition of this bond be fully performed, then this obligation shall become null and void; otherwise it shall be and remain in full force and affect.

The Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration, or addition to the terms of the Contract or to the Work to be performed thereunder shall in any way affect its obligation on this bond, and it does hereby waive notice of any such change, extension of time, alteration, or addition to the Contract Documents or to the Work.

IN WITNESS WHEREOF, two (2) identical counterparts of this instrument, each of which shall for all purposes be deemed an original thereof, have been duly executed by the Principal and Surety above named, on the _____ day of _____, 20____.

Principal

Surety

(Name of Principal)

(Name of Surety)

(Signature of Person with Authority)

(Signature of Person with Authority)

(Print Name)

(Print Name)

(Name of California Agent of Surety)

(Address of California Agent of Surety)

(Telephone Number of California Agent of Surety)

Contractor must attach a Notarial Acknowledgment for all Surety's signatures and a Power of Attorney and Certificate of Authority for Surety. The California Department of Insurance must authorize the Surety to be an admitted surety insurer.

END OF DOCUMENT

PROPOSED CHANGE ORDER FORM

Downey Unified School District

11627 Brookshire Avenue

Downey , CA 90241

PCO NO.:**Project:** _____**Date:** _____**Bid No.:** _____**DSA File No.:** _____**RFI #:** _____**DSA Appl. No.:** _____

Contractor hereby submits for District's review and evaluation this Proposed Change Order ("PCO"), submitted in accordance with and subject to the terms of the Contract Documents, including Sections 17.7 and 17.8 of the General Conditions. Any spaces left blank below are deemed no change to cost or time.

Contractor understands and acknowledges that documentation supporting Contractor's PCO must be attached and included for District review and evaluation. Contractor further understands and acknowledges that failure to include documentation sufficient to, in District's discretion, support some or all of the PCO, shall result in a rejected PCO.

	<u>WORK PERFORMED OTHER THAN BY CONTRACTOR</u>	<u>ADD</u>	<u>DEDUCT</u>
(a)	<u>Material</u> (attach suppliers' invoice or itemized quantity and unit cost plus sales tax)		
(b)	<u>Add Labor</u> (attach itemized hours and rates, fully encumbered)		
(c)	<u>Add Equipment</u> (attach suppliers' invoice)		
(d)	<u>Subtotal</u>		
(e)	<u>Add overhead and profit for any and all tiers of Subcontractor</u> , the total not to exceed ten percent (10%) of Item (d)		
(f)	<u>Subtotal</u>		
(g)	<u>Add Overhead and Profit for Contractor</u> , not to exceed five percent (5%) of Item (f)		
(h)	<u>Subtotal</u>		

DOWNEY UNIFIED SCHOOL DISTRICT

Various Sites Cabling for IP Phones

PROPOSED CHANGE ORDER FORM**DOCUMENT 00 63 57-4**

(i)	Add Bond and Insurance , not to exceed one and a half percent (1.5%) of Item (h)		
(j)	<u>TOTAL</u>		
(k)	<u>Time</u> (zero unless indicated; "TBD" not permitted)	____ Calendar Days	

[REMAINDER OF PAGE LEFT BLANK INTENTIONALLY]

	<u>WORK PERFORMED BY CONTRACTOR</u>	<u>ADD</u>	<u>DEDUCT</u>
(a)	<u>Material</u> (attach itemized quantity and unit cost plus sales tax)		
(b)	<u>Add Labor</u> (attach itemized hours and rates, fully encumbered)		
(c)	<u>Add Equipment</u> (attach suppliers' invoice)		
(d)	<u>Subtotal</u>		
(e)	<u>Add Overhead and Profit for Contractor</u> , not to exceed fifteen percent (15%) of Item (d)		
(f)	<u>Subtotal</u>		
(g)	<u>Add Bond and Insurance</u> , not to exceed one and a half percent (1.5%) of Item (f)		
(h)	<u>TOTAL</u>		
(i)	<u>Time</u> (zero unless indicated; "TBD" not permitted)	____ Calendar Days	

The undersigned Contractor approves the foregoing as to the changes, if any, to the Contract Price specified for each item, and as to the extension of time allowed, if any, for completion of the entire Work as stated herein, and agrees to furnish all labor, materials, and service, and perform all work necessary to complete any additional work specified for the consideration stated herein. Submission of sums which have no basis in fact or which Contractor knows are false are at the sole risk of Contractor and may be a violation of the False Claims Act set forth under Government Code section 12650 et seq. It is understood that the changes herein to the Contract shall only be effective when approved by the governing board of the District.

It is expressly understood that the value of the extra Work or changes expressly includes any and all of the Contractor's costs and expenses, direct and indirect, resulting from additional time required on the Project or resulting from delay to the Project including, without limitation, cumulative impacts. Contractor is not entitled to separately recover amounts for overhead or other indirect costs. Any costs, expenses, damages, or time extensions not included are deemed waived.

SUBMITTED BY:

Contractor:

[Name]

Date

END OF DOCUMENT

DOCUMENT 00 63 63

CHANGE ORDER FORM

Downey Unified School District
11627 Brookshire Avenue
Downey , CA 90241

CHANGE ORDER NO.:

CHANGE ORDER

Project: _____

Date: _____

Bid No.: _____

DSA File No.: _____

DSA Appl. No.: _____

The following parties agree to the terms of this Change Order:

Owner: _____

Contractor: _____

[Name / Address]

[Name / Address]

Architect: _____

Project Inspector: _____

[Name / Address]

[Name / Address]

Reference	Description	Cost	Days Ext.
PCO #	[Description of change]	\$	
Requested by:	[Requester]		
Performed by:	[Performer]		
Reason:	[Reason]		
PCO #	[Description of change]	\$	
Requested by:	[Requester]		
Performed by:	[Performer]		

Reason:	[Reason]		
PCO #	[Description of change]	\$	
Requested by:	[Requester]		
Performed by:	[Performer]		
Reason:	[Reason]		
Contract time will be adjusted as follows:		Original Contract Amount:	\$
Previous Completion Date: <u>[Date]</u>		Amount of Previously Approved Change Order(s):	\$
<u>[#]</u> Calendar Days Extension (zero unless otherwise indicated)		Amount of this Change Order:	\$
Current Completion Date: <u>[Date]</u>		Contract Amount:	\$

The undersigned Contractor approves the foregoing as to the changes, if any, to the Contract Price specified for each item, and as to the extension of time allowed, if any, for completion of the entire work as stated therein, and agrees to furnish all labor, materials and services and perform all work necessary to complete any additional work specified for the consideration stated therein. Submission of sums which have no basis in fact or which Contractor knows are false are at the sole risk of Contractor and may be a violation of the False Claims Act set forth under Government Code section 12650 et seq.

This change order is subject to approval by the governing board of this District and must be signed by the District. Until such time as this change order is approved by the District's governing board and executed by a duly authorized District representative, this change order is not effective and not binding.

It is expressly understood that the compensation and time, if any, granted herein represent a full accord and satisfaction for any and all time and cost impacts of the items herein, and Contractor waives any and all further compensation or time extension based on the items herein. The value of the extra work or changes expressly includes any and all of the Contractor's costs and expenses, and its subcontractors, both direct and indirect, resulting from additional time required on the project or resulting from delay to the project including without limitation, cumulative impacts. Any costs, expenses, damages or time extensions not included are deemed waived.

Signatures:

District:

Contractor:

[Name]

Date

[Name]

Date

Architect:

Project Inspector:

[Name]

Date

[Name]

Date

END OF DOCUMENT

DOCUMENT 00 65 10

NOTICE TO PROCEED

Dated: _____, 20__

To: _____
("Contractor")

(Address)

From: Governing Board ("Board") of **Downey Unified School District** ("District")

Re: **Various Sites CAT6 Cabling for IP Phones Project** ("Project" or "Contract")

Contractor is hereby notified that the Contract Time under the Contract will commence to run on _____, 20__. By that date, Contractor shall start performing its obligations under the Contract Documents. In accordance with the Agreement executed by Contractor, the Contract Time and Project Completion is _____, 20__.

Contractor must submit the following documents by 5:00 p.m. of the **TENTH (10TH)** calendar day following the date of this Notice to Proceed:

1. Contractor's preliminary schedule of construction.
2. Contractor's preliminary schedule of submittals, including Shop Drawings, Product Data, and Samples submittals.
3. Contractor's preliminary schedule of values for all of the Work.
4. Contractor's preliminary Contractor's Safety Plan specifically adapted for the Project.
5. A complete subcontractors list, including the name, address, telephone number, facsimile number, California State Contractor's License number, classification, and monetary value of all Subcontracts.

Thank you. We look forward to a successful Project.

Downey Unified School District

SIGNATURE: _____

NAME: _____

TITLE: _____

END OF DOCUMENT

DOCUMENT 00 65 36

WARRANTY AND GUARANTEE FORM

1. _____ ("Contractor")

hereby agrees that the _____ ("Work" of Contractor)

which Contractor has installed for the **Downey Unified School District** ("District") for the following project:

Various Sites CAT6 Cabling for IP Phones Project ("Project" or "Contract")

was performed in accordance with the requirements of the Contract Documents and that the Work as installed fulfills the requirements of the Contract Documents.

2. Contractor agrees to repair or replace all of the Work that may prove to be defective in workmanship or material and any other adjacent Work that may be displaced in connection with such replacement within a period of _____ **YEAR(S)** from the date of Completion as defined in the Contract, ordinary wear and tear and unusual abuse or neglect excepted. The date of completion is _____, 20____.
3. In the event Contractor fails to comply with the above-mentioned conditions within a reasonable period of time, as determined by District, but not later than **SEVEN (7)** calendar days after being notified in writing by District, Contractor authorizes District to proceed to repair or replace the defective Work at the expense of Contractor. Contractor shall pay the costs and charges therefor upon demand.

4. **Representatives to be contacted for service subject to the terms of Contract:**

NAME: _____

ADDRESS: _____

PHONE NO.: _____

EMAIL: _____

Date: _____

Proper Name of Contractor: _____

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

DOCUMENT 00 70 00

TABLE OF CONTENTS

GENERAL CONDITIONS

1.	CONTRACT TERMS AND DEFINITIONS	1
1.1.	Definitions	1
1.2.	Laws Concerning the Contract	5
1.3.	No Oral Agreements	5
1.4.	No Assignment	5
1.5.	Confidentiality	5
1.6.	Notice and Service Thereof	5
1.7.	No Waiver	5
1.8.	Substitutions for Specified Items	6
1.9.	Materials and Work	7
2.	DISTRICT	8
3.	ARCHITECT	9
4.	CONSTRUCTION MANAGER	9
5.	INSPECTOR, INSPECTIONS AND TESTS	9
5.1.	Project Inspector	9
5.2.	Tests and Inspections	10
5.3.	Costs for After Hours and/or Off Site Inspections	11
6.	CONTRACTOR	11
6.1.	Status of Contractor	11
6.2.	Contractor's Supervision	11
6.3.	Duty to Provide Fit Workers	12
6.4.	Personnel	13
6.5.	Prohibition on Harassment	14
6.6.	Conferences and Meetings.	14
6.7.	Purchase of Materials and Equipment	15
6.8.	Documents on Work	16
6.9.	Preservation of Records	17
6.10.	Integration of Work	17
6.11.	Obtaining of Permits and Licenses	17
6.12.	Work to Comply with Applicable Laws and Regulations	18
6.13.	Safety/Protection of Persons and Property	19
6.14.	Working Evenings and Weekends	22
6.15.	Noise and Dust Control	22
6.16.	Cleaning Up	23
7.	SUBCONTRACTORS	23
8.	OTHER CONTRACTS/CONTRACTORS	24
9.	DRAWINGS AND SPECIFICATIONS	25
9.8.	Ownership of Drawings	25
10.	CONTRACTOR'S SUBMITTALS AND SCHEDULES	26
10.1.	Schedules, Safety Plan and Complete Subcontractor List	26
10.2.	Monthly Progress Schedule(s)	29
10.3.	Material Safety Data Sheets (MSDS)	29
10.4.	Logistic Plan	29
10.5.	Information Included in Submittals.	29
10.6.	Verification of Submittal Information	30
10.7.	Contractor Responsibility for Deviations.	30

10.8.	No Performance of Work Without Architect Review.	30
10.9.	District and Architect Review of Submittals.....	30
10.10.	Deferred Approval Items.	30
10.11.	Contractor Responsibility for Deviations	31
11.	SITE ACCESS, CONDITIONS AND REQUIREMENTS.....	31
11.1.	Site Investigation	31
11.2.	Soils Investigation Report	31
11.3.	Access to Work	32
11.4.	Layout and Field Engineering.....	32
11.5.	Utilities for Construction	32
11.6.	Sanitary Facilities.....	32
11.7.	Surveys.....	32
11.8.	Regional Notification Center.....	32
11.9.	Existing Utility Lines.....	33
11.10.	Notification	33
11.11.	Hazardous Materials.....	33
11.12.	No Signs.....	33
12.	TRENCHES.....	34
12.1.	Trenches Greater Than Five Feet	34
12.2.	Excavation Safety	34
12.3.	No Tort Liability of District.....	34
12.4.	No Excavation without Permits	34
12.5.	Discovery of Hazardous Waste, Unusual Conditions and/or Unforeseen Conditions	34
13.	INSURANCE AND BONDS	35
13.1.	Insurance.....	35
13.2.	Contract Security – Bonds.....	38
14.	WARRANTY/GUARANTEE/INDEMNITY	38
14.1.	Warranty/Guarantee.....	38
14.2.	Indemnity	39
15.	TIME	40
15.1.	Notice to Proceed.....	40
15.2.	Hours of Work	40
15.3.	Progress and Completion.....	40
15.4.	Schedule	41
15.5.	Expeditious Completion.....	41
16.	EXTENSIONS OF TIME – LIQUIDATED DAMAGES	41
16.1.	Contractor’s Notice of Delay.....	41
16.2.	Excusable and Compensable Delay(s)	42
16.3.	Excusable and Non-Compensable Delay(s)	43
16.4.	Unexcused Delay(s) – Liquidated Damages.....	45
17.	CHANGES IN THE WORK.....	45
17.1.	No Changes Without Authorization	45
17.2.	Architect Authority.....	46
17.3.	Change Orders.....	46
17.4.	Unilateral Change Orders	47
17.5.	Force Account Directives	47
17.6.	Price Request.....	48
17.7.	Proposed Change Order.....	48
17.8.	Format for Proposed Change Order	50
17.9.	Change Order Certification	55
17.10.	Determination of Change Order Cost.....	55
17.11.	Deductive Change Orders	56

17.12.	Discounts, Rebates and Refunds.....	56
17.13.	Accounting Records	56
17.14.	Notice Required.....	56
17.15.	Applicability to Subcontractors.....	56
17.16.	Alteration to Change Order Language.....	56
17.17.	Failure of Contractor to Execute Change Order.....	57
18.	REQUEST FOR INFORMATION	57
19.	PAYMENTS.....	57
19.1.	Contract Price	57
19.2.	Applications for Progress Payments	58
19.3.	Progress Payments	60
19.4.	Decisions to Withhold Payment.....	62
19.5.	Subcontractor Payments	64
20.	COMPLETION OF THE WORK.....	64
20.1.	Completion.....	64
20.2.	Closeout Procedures.....	64
20.3.	Final Inspection	65
20.4.	Costs of Multiple Inspections.....	66
20.5.	Partial Occupancy or Use Prior to Completion	66
21.	FINAL PAYMENT AND RETENTION	67
21.1.	Final Payment.....	67
21.2.	Prerequisites for Final Payment.....	67
21.3.	Retention	68
21.4.	Substitution of Securities.....	68
21.5.	Claims Asserted After Final Payment	68
22.	UNCOVERING WORK, CORRECTION OF WORK AND RIGHT TO TAKEOVER WORK	68
22.1.	Uncovering of Work.....	68
22.2.	Rejection of Work.....	69
22.3.	Nonconforming Work	69
22.4.	Correction of Work	69
22.5.	District's Right to Takeover Work	69
23.	TERMINATION AND SUSPENSION	70
23.1.	District's Right to Terminate Contractor for Cause.....	70
23.2.	Emergency Termination of Public Contracts Act of 1949.....	72
23.3.	Termination of Contractor for Convenience	73
23.4.	Suspension of Work.....	73
23.5.	Scope Reduction.....	73
24.	CLAIMS RESOLUTION	73
24.1.	Exclusive Remedy.	74
24.2.	Performance during Claim Resolution Process.....	74
24.3.	Waiver.....	74
24.4.	Intention.	74
24.5.	Other Provisions.	74
24.6.	Claim Presentation	74
24.7.	Documentation of Resolution.....	79
24.8.	Claim Resolution Process – Non-Applicability.	79
25.	LABOR, WAGE & HOUR, APPRENTICE AND RELATED PROVISIONS	80
25.1.	Contractor & Subcontractor Registration	80
25.2.	Wage Rates, Travel and Subsistence	80
25.3.	Hours of Work	81
25.4.	Payroll Records.....	82
25.5.	Apprentices	84

25.6.	Non-Discrimination	85
25.7.	Labor First Aid	85
26.	MISCELLANEOUS.....	85
26.1.	Assignment of Antitrust Actions	85
26.2.	Excise Taxes.....	86
26.3.	Taxes	86
26.4.	Shipments	86
26.5.	Compliance with Government Reporting Requirements.....	86

1. CONTRACT TERMS AND DEFINITIONS

1.1. Definitions

Wherever used in the Contract Documents, the following terms shall have the meanings indicated, which shall be applicable to both the singular and plural thereof:

1.1.1. Adverse Weather: Weather that satisfies all of the following conditions: (1) unusually severe precipitation, sleet, snow, hail, heat, or cold conditions in excess of the norm for the location and time of year it occurred, (2) unanticipated, and (3) occurring at the Project Site.

1.1.2. Allowance(s): Amount(s) stated in the Agreement for specific scopes of work for which Contractor may, upon District's written approval, bill its time, materials, and other items in the identical structure as a Change Order.

1.1.3. Approval, Approved, and/or Accepted: Refer to written authorization, unless stated otherwise.

1.1.4. Architect: The individual, partnership, corporation, joint venture, or any combination thereof, named as Architect that has the rights and authority assigned to the Architect in the Contract Documents. The term Architect means the District's Architect on this Project or the Architect's authorized representative. If no Architect is used on the Project, then all references in the Contract Documents to Architect shall be read to refer to District.

1.1.5. As-Built Drawings: A reproducible full-size sets of drawings to be prepared on a monthly basis, and upon Project Completion, pursuant to the Contract Documents, that reflect changes made during the performance of the Work, recording differences between the original design of the Work and the Work as constructed.

1.1.6. Bidder: A contractor who provides a bid to the District to perform the Work of the Contract.

1.1.7. Change Order: A written order to the Contractor authorizing an addition to, deletion from, or revision in the Work, and/or authorizing an adjustment in the Contract Price or Contract Time. If a Change Order is required to be approved by DSA, the District may call it a Construction Change Document.

1.1.8. Completion: When the entire Work shall have been completed, including all punch list items, as further detailed in the "Completion of the Project" Section herein. Final DSA approval of the Project is not required for Completion. There is no "Substantial Completion" or "Beneficial Occupancy" for this Project, although the District may occupy the Project prior to completion as permitted herein.

1.1.9. Construction Manager: The individual, partnership, corporation, joint venture, or any combination thereof, or its authorized representative, named as such by the District. If no Construction Manager is used on the Project, then all references in the Contract Documents to Construction Manager shall be read to refer to District.

1.1.10. Construction Schedule: The progress schedule of construction of the Project as provided by Contractor and approved by District.

1.1.11. Contract, Contract Documents: The Contract consists exclusively of the documents evidencing the agreement of the District and Contractor, identified as the Contract Documents. The Contract Documents consist of the following documents:

1.1.11.1. Notice to Bidders / Invitation to Bid

- 1.1.11.2. Instructions to Bidders
- 1.1.11.3. Bid Form
- 1.1.11.4. Bid Bond
- 1.1.11.5. Designated Subcontractors List
- 1.1.11.6. Noncollusion Declaration
- 1.1.11.7. Iran Contracting Act Certification
- 1.1.11.8. Certifications to be Completed by Contractor
- 1.1.11.9. Disabled Veteran's Business Enterprise Participation Certification
- 1.1.11.10. Criminal Background Investigation/Fingerprinting Certification
- 1.1.11.11. Notice of Award
- 1.1.11.12. Agreement
- 1.1.11.13. Storm Water Pollution Prevention Plan (if applicable)
- 1.1.11.14. Notice to Proceed
- 1.1.11.15. Performance Bond
- 1.1.11.16. Payment Bond (Contractor's Labor and Material Bond)
- 1.1.11.17. District Contract Forms (if applicable)
- 1.1.11.18. District Closeout Forms (if applicable)
- 1.1.11.19. Warranty and Guarantee Form
- 1.1.11.20. General Conditions
- 1.1.11.21. Special Conditions
- 1.1.11.22. Project Plans, Specifications, Technical Specifications, and Drawings
- 1.1.11.23. Addenda to any of the above documents
- 1.1.11.24. Schedules if approved in writing by the District
- 1.1.11.25. Change Orders or written modifications to the above documents if approved in writing by the District

1.1.12. Contract Price: The total monies payable to the Contractor under the terms and conditions of the Contract Documents.

1.1.13. Contract Time: The time period stated in the Agreement for the Completion of the Work.

1.1.14. Contractor: The licensed person, entity, or entities identified in the Agreement as contracting to

perform the Work.

1.1.15. Daily Job Report(s): Daily Project reports prepared by the Contractor's employee(s) who are present on Site, which shall include the information required herein.

1.1.16. Day(s): Unless otherwise designated, day(s) means calendar day(s). **"Business Day(s)"** shall mean days except Saturday, Sunday, a day that is federally-recognized holiday, or a day that is a California-recognized holiday.

1.1.17. Defective or Nonconforming Work. Defective or nonconforming Work is any Work which is unsatisfactory, faulty or deficient by: (a) not conforming to the requirements of the Contract Documents; (b) not conforming to the standards of workmanship of the applicable trade; (c) not being in compliance with the requirements of any inspection, reference, standard, test, or approval required by the Contract Documents; or (d) damage to Work occurring prior to Completion.

1.1.18. District: The public agency or the school district for which the Work is performed.

1.1.19. Drawings: (or "Plans") The graphic and pictorial portions of the Contract Documents showing the design, location, scope and dimensions of the Work, generally including plans, elevations, sections, details, schedules, sequence of operation, and diagrams.

1.1.20. DSA: Division of the State Architect.

1.1.21. Force Account Directive: A process that may be used when the District and the Contractor cannot agree on a price for a specific scope of work or before Contractor prepares a price for the scope of work and Contractor is directed in writing by the District to perform on a time and materials basis.

1.1.22. Premises: The real property owned by the District on which the Project Site is located. For example, if the Project is only being performed on a portion of a school, the Site is only the area where the Project is located (the Project Site), and the Premises is the entire school site.

1.1.23. Product(s): New material, machinery, components, equipment, fixtures and systems forming the Work, including existing materials or components required and approved by the District for reuse.

1.1.24. Product Data: Illustrations, standard schedules, performance charts, instructions, brochures, diagrams, and other information furnished by Contractor to illustrate a material, product, or system for a scope of the Work.

1.1.25. Project: The planned undertaking as provided for in the Contract Documents.

1.1.26. Project Inspector: (or "Inspector") Individual(s) retained by the District in accordance with title 24 of the California Code of Regulations to monitor and inspect the Project. If no Project Inspector is used on the Project, then all references in the Contract Documents to Project Inspector shall be read to refer to District.

1.1.27. Program Manager: The individual, partnership, corporation, joint venture, or any combination thereof, or its authorized representative, named as such by the District. If no Program Manager is designated for the Project then all references to Program Manager shall refer to District.

1.1.28. Proposed Change Order: A written request prepared by the Contractor requesting that the District and the Architect issue a Change Order based upon a proposed change to the Work.

1.1.29. Provide: Shall include "provide complete in place," that is, "furnish and install," and "provide complete and functioning as intended in place" unless specifically stated otherwise.

1.1.30. Request for Information: (or "RFI") A written request prepared by the Contractor requesting that the Architect provide additional information necessary to clarify or amplify an item in the Contract Documents that the Contractor believes is not clearly shown or called for in the Drawings or Specifications or other portions of the Contract Documents, or to address issues that have arisen under field conditions.

1.1.31. Request for Substitution: A request by Contractor to substitute an equal or superior material, product, thing, or service for a specific material, product, thing, or service that has been designated in the Contract Documents by a specific brand or trade name.

1.1.32. Safety Orders: Written and/or verbal orders for construction issued by the California Division of Industrial Safety ("CalOSHA") or by the United States Occupational Safety and Health Administration ("OSHA").

1.1.33. Safety Plan: Contractor's safety plan specifically adapted for the Project. Contractor's Safety Plan shall comply with all provisions regarding Project safety, including all applicable provisions in these General Conditions.

1.1.34. Samples: Physical examples that illustrate materials, products, equipment, finishes, colors, or workmanship and that, when approved in accordance with the Contract Documents, establish standards by which portions of the Work will be judged.

1.1.35. Shop Drawings: All drawings, prints, diagrams, illustrations, brochures, schedules, and other data that are prepared by the Contractor, a subcontractor, manufacturer, supplier, or distributor, that illustrate how specific portions of the Work shall be fabricated or installed.

1.1.36. Site: The Project site as shown on the Drawings.

1.1.37. Specifications: That portion of the Contract Documents, Division 1 through Division 17, and all technical sections, and addenda to all of these, if any, consisting of written descriptions and requirements of a technical nature of materials, equipment, construction methods and systems, standards, and workmanship.

1.1.38. Subcontractor: A contractor and/or supplier who is under contract with the Contractor or with any other subcontractor, regardless of tier, to perform a portion of the Work.

1.1.39. Submittal Schedule: The schedule of submittals as provided by Contractor and approved by District.

1.1.40. Surety: The person, firm, or corporation that executes as surety the Contractor's Performance Bond and Payment Bond, and must be a California admitted surety insurer as defined in the Code of Civil Procedure section 995.120.

1.1.41. SWPPP: The District's Storm Water Pollution Prevention Plan.

1.1.42. Terms. The term "provide" means "provide complete in place" or to "furnish and install" such item. Unless otherwise provided in the Contract Documents, the terms "approved;" "directed;" "satisfactory;" "accepted;" "acceptable;" "proper;" "required;" "necessary" and "equal" shall mean as approved, directed, satisfactory, accepted, acceptable, proper, required, necessary and equal, in the opinion of the District. The term "typical" as used in the Drawings shall require the installation or furnishing of such item(s) of the Work designated as "typical" in all other areas similarly marked as "typical"; Work in such other areas shall conform to that shown as "typical" or as reasonably inferable therefrom.

1.1.43. Unilateral Change Order: A written order prepared and issued by the District, the Construction

Manager, and/or the Architect and signed by the District and the Architect, directing a change in the Work. **A Unilateral Change Order is NOT a Construction Change Document (which is defined above as a Change Order that DSA must approve).**

1.1.44. Work: All labor, materials, equipment, components, appliances, supervision, coordination, and services required by, or reasonably inferred from, the Contract Documents, that are necessary for the construction and Completion of the Project.

1.2. Laws Concerning the Contract

Contract is subject to all provisions of the Constitution and laws of California and the United States, governing, controlling, or affecting District, or the property, funds, operations, or powers of District, and such provisions are by this reference made a part hereof. Any provision required by law to be included in this Contract shall be deemed to be inserted.

1.3. No Oral Agreements

No oral agreement or conversation with any officer, agent, or employee of District, either before or after execution of Contract, shall affect or modify any of the terms or obligations contained in the Contract Documents.

1.4. No Assignment

Contractor shall not assign the Contract or any part thereof including, without limitation, any services or money to become due without the prior written consent of the District. Assignment without District's prior written consent shall be null and void. Any assignment of money due or to be come due under the Contract shall be subject to a prior lien for services rendered or material supplied for Work performed in favor of all persons, firms, or corporations rendering services or supplying material to the extent that claims are filed pursuant to the Civil Code, Code of Civil Procedure, Government Code, Labor Code, and/or Public Contract Code, and shall also be subject to deductions for Liquidated Damages or withholding of payments as determined by District in accordance with the Contract. Contractor shall not assign or transfer in any manner to a Subcontractor or supplier the right to prosecute or maintain an action against the District.

1.5. Confidentiality

Contractor shall maintain the confidentiality of all information, documents, programs, procedures and all other items that Contractor encounters while performing the Work. This requirement shall be ongoing and shall survive the expiration or termination of the Contract and specifically includes, without limitation, all student, parent, and employee disciplinary information and health information.

1.6. Notice and Service Thereof

Any notice required by the Contract shall be in writing, dated and signed by the party giving notice or by a duly authorized representative of that party and pursuant to the provisions in the Agreement.

1.7. No Waiver

The failure of District in any one or more instances to insist upon strict performance of any term of the Contract or to exercise any District option shall not be construed as a waiver or relinquishment of the right to assert or rely upon any such term or option on a future occasion. No action or failure to act by the District, Architect, or Construction Manager shall constitute a waiver of any right or duty afforded the District under the Contract, nor shall any action or failure to act constitute an approval of or acquiescence in any breach hereunder, except as may be specifically agreed in writing.

1.8. Substitutions for Specified Items

1.8.1. Requests for substitutions prior to award of the Contract shall be submitted within the time period indicated in the Instructions to Bidders.

1.8.2. Requests for substitutions after award of the Contract shall be submitted within **THIRTY-FIVE (35)** days of the date of the Notice of Award. This time period may be extended by the District only, in its sole discretion.

1.8.3. Whenever in the Specifications any materials, process, or article is indicated or specified by grade, patent, or proprietary name, or by name of manufacturer, that Specification shall be deemed to be followed by the words “or equal.” Contractor may, unless otherwise stated, offer any material, process, or article that shall be substantially equal or better in every respect to that so indicated or specified.

1.8.3.1. If the material, process, or article offered by Contractor is not, in the opinion of the District, substantially equal or better in every respect to that specified, then Contractor shall furnish the material, process, or article specified in the Specifications without any additional compensation or change order.

1.8.3.2. This provision shall not be applicable with respect to any material, product, thing or service for which District made findings and gave notice in accordance with Public Contract Code section 3400(b); therefore, Contractor shall not be entitled to request a substitution with respect to those materials, products or services.

1.8.4. A request for a substitution shall be in writing and shall include:

1.8.4.1. All variations of the proposed substitute from the material specified including, but not limited to, principles of operation, materials, or construction finish, thickness or gauge of materials, dimensions, weight, and tolerances;

1.8.4.2. Available maintenance, repair or replacement services;

1.8.4.3. Increases or decreases in operating, maintenance, repair, replacement, and spare parts costs;

1.8.4.4. Whether or not acceptance of the substitute will require other changes in the Work (or in work performed by the District or others under Contract with the District); and

1.8.4.5. The time impact on any part of the Work resulting directly or indirectly from acceptance of the proposed substitute.

1.8.5. No substitutions shall be made until approved, in writing, by the District. The burden of proof as to equality of any material, process, or article shall rest with Contractor. The Contractor warrants that if substitutes are approved:

1.8.5.1. The proposed substitute is equal or superior in all respects to that specified, and that such proposed substitute is suitable and fit for the intended purpose and will perform adequately the function and achieve the results called for by the general design and the Contract Documents;

1.8.5.2. The Contractor provides the same warranties and guarantees for the substitute that would be provided for that specified;

1.8.5.3. The Contractor shall be fully responsible for the installation of the substitute and any changes in the Work required, either directly or indirectly, because of the acceptance of such substitute, with no increase in Contract Price or Contract Time. Incidental changes or extra component parts required to accommodate the substitute will be made by the Contractor without a change in the Contract Price or Contract Time;

1.8.5.4. The Contractor shall be responsible for any re-design costs occasioned by District's acceptance and/or approval of any substitute; and

1.8.5.5. The Contractor shall, in the event that a substitute is less costly than that specified, credit the District with one hundred percent (100%) of the net difference between the substitute and the originally specified material. In this event, the Contractor agrees to execute a deductive Change Order to reflect that credit.

1.8.6. In the event Contractor furnishes a material, process, or article more expensive than that specified, the difference in the cost of that material, process, or article so furnished shall be borne by Contractor.

1.8.7. In no event shall the District be liable for any increase in Contract Price or Contract Time due to any claimed delay in the evaluation of any proposed substitute or in the acceptance or rejection of any proposed substitute.

1.8.8. If the District approves a substitution after the award of the Contract, the District shall memorialize that approval in a Change Order or other applicable Contract modification process.

1.9. Materials and Work

1.9.1. Except as otherwise stated in the Contract, Contractor shall provide and pay for all materials, labor, tools, equipment, transportation, supervision, temporary constructions of every nature, and all other services, management, and facilities of every nature whatsoever necessary to execute and complete the Contract within the Contract Time.

1.9.2. Unless otherwise specified, all materials shall be new and the best of their respective kinds and grades as noted or specified, and workmanship shall be of good quality.

1.9.3. Materials shall be furnished in sufficient quantities and at such times as to ensure uninterrupted progress of Work and shall be stored properly and protected as required.

1.9.4. For all materials and equipment specified or indicated in the Drawings, the Contractor shall provide all labor, materials, equipment, and services necessary for complete assemblies and complete working systems, functioning as intended. Incidental items not indicated on Drawings, nor mentioned in the Specifications, that can legitimately and reasonably be inferred to belong to the Work described, or be necessary in good practice to provide a complete assembly or system, shall be furnished as though itemized here in every detail. In all instances, material and equipment shall be installed in strict accordance with each manufacturer's most recent published recommendations and specifications.

1.9.5. Contractor shall, after award of Contract by District and after relevant submittals have been approved, place orders for materials and/or equipment as specified so that delivery of same may be made without delays to the Work. Contractor shall, upon demand from District, present documentary evidence showing that orders have been placed.

1.9.6. District reserves the right but has no obligation, for any neglect in complying with the above instructions, to place orders for such materials and/or equipment as it may deem advisable in order that the Work may be completed at the date specified in the Agreement, and all expenses incidental to the

procuring of said materials and/or equipment shall be paid for by Contractor or withheld from payment(s) to Contractor.

1.9.7. Contractor warrants good title to all material, supplies, and equipment installed or incorporated in Work and agrees upon Completion of all Work to deliver the Site to District, together with all improvements and appurtenances constructed or placed thereon by it, and free from any claims, liens, or charges. Contractor further agrees that neither it nor any person, firm, or corporation furnishing any materials or labor for any Work shall have any right to lien any portion of the Premises or any improvement or appurtenance thereon, except that Contractor may install metering devices or other equipment of utility companies or of political subdivision, title to which is commonly retained by utility company or political subdivision. In the event of installation of any such metering device or equipment, Contractor shall advise District as to owner thereof.

1.9.8. Nothing contained in this Article, however, shall defeat or impair the rights of persons furnishing materials or labor under any bond given by Contractor for their protection or any rights under law permitting such protection or any rights under law permitting such persons to look to funds due Contractor in hands of District (e.g., stop payment notices). This provision shall be inserted in all subcontracts and material contracts and notice of its provisions shall be given to all persons furnishing material for work when no formal contract is entered into for such material.

1.9.9. Title to new materials and/or equipment for the Work and attendant liability for its protection and safety shall remain with Contractor until incorporated in the Work of this Contract and accepted by District. No part of any materials and/or equipment shall be removed from its place of storage except for immediate installation in the Work. Contractor shall keep an accurate inventory of all materials and/or equipment in a manner satisfactory to District or its authorized representative and shall, at the District's request, forward it to the District.

1.9.10. Contractor certifies that it shall comply with the recycled product requirements of Public Contract Code section 22150, et seq., including, without limitation, section 22154 which states, "All businesses shall certify in writing to the contracting officer, or his or her representative, the minimum, if not exact, percentage of postconsumer material in the products, materials, goods, or supplies being offered or sold to any local public entity."

2. DISTRICT

2.1. The governing board of the District or its designees will act for the District in all matters pertaining to the Contract.

2.2. The District may, at any time,

2.2.1. Direct the Contractor to communicate with or provide notice to the Construction Manager or the Architect on matters for which the Contract Documents indicate the Contractor will communicate with or provide notice to the District; and/or

2.2.2. Direct the Construction Manager or the Architect to communicate with or direct the Contractor on matters for which the Contract Documents indicate the District will communicate with or direct the Contractor.

2.3. District's Rights if Contractor Fails to Perform. If the District at any time believes that the Contractor is behind schedule, is failing to construct the Project pursuant to the Contract Documents or is otherwise failing to perform any provisions of this Contract, the District, after **FORTY-EIGHT (48)** hours written notice to the Contractor, may take any action necessary or beneficial to the District to complete the Project, takeover the Work of the Contract, terminate or suspend the Contract as indicated herein, or any combination or portion of those actions. The Contractor and the Surety shall be liable to the District for

any cost incurred by the District in those actions and the District has the right to deduct the cost thereof from any payment then or thereafter due the Contractor.

3. ARCHITECT

- 3.1.** Architect shall have the authority to act on behalf of District to the extent expressly provided in the Contract Documents and to the extent determined by District to, among other things, observe the progress and quality of the Work on behalf of the District.
- 3.2.** Architect shall have authority to reject materials, workmanship, and/or the Work whenever rejection may be necessary, in Architect's reasonable opinion, to insure the proper execution of the Contract and if Work is defective or does not conform to the requirements of the Contract Documents. Whenever the Architect considers it necessary or advisable, for implementation of the intent of the Contract Documents, the Architect will have authority to require additional inspections or testing of the Work, whether or not such Work is fabricated, installed or completed. Neither this authority of the Architect nor a decision made in good faith by the Architect to exercise or not to exercise that authority shall give rise to a duty or responsibility to the Contractor, Subcontractors, material suppliers, their agents or employees, or other persons performing portions of the Work.
- 3.3.** Architect shall, with the District and on behalf of the District, determine the amount, quality, acceptability, and fitness of all parts of the Work, and interpret the Specifications, Drawings, and shall, with the District, interpret all other Contract Documents.
- 3.4.** Architect shall have all authority and responsibility established by law, including title 24 of the California Code of Regulations.
- 3.5.** Contractor shall provide District and the Construction Manager with a copy of all written communication between Contractor and Architect at the same time as that communication is made to Architect, including, without limitation, all RFIs, correspondence, submittals, claims, and proposed change orders.

4. CONSTRUCTION MANAGER

- 4.1.** If a Construction Manager is used on this Project, the Construction Manager will provide administration of the Contract on the District's behalf. After execution of the Contract and Notice to Proceed, all correspondence and/or instructions from Contractor and/or District shall be forwarded through the Construction Manager. The Construction Manager will not be responsible for and will not have control or charge of construction means, methods, techniques, sequences, or procedures or for safety precautions in connection with the Work, which shall all remain the Contractor's responsibility.
- 4.2.** Construction Manager, however, will have authority to reject materials and/or workmanship not conforming to the Contract Documents, as determined by the District, the Architect, and/or the Project Inspector. Construction Manager shall also have the authority to require special inspection or testing of any portion of the Work, whether it has been fabricated, installed, or fully completed. Any decision made by Construction Manager, in good faith, shall not give rise to any duty or responsibility of the Construction Manager to the Contractor, any Subcontractor, their agents, employees, or other persons performing any of the Work. Construction Manager shall have free access to all parts of Work at any time.
- 4.3.** If the District does not use a Construction Manager on this Project, all references to Construction Manager or CM shall be read as District.

5. INSPECTOR, INSPECTIONS AND TESTS

5.1. Project Inspector

5.1.1. One or more Project Inspector(s), including special Project Inspector(s), as required, will be assigned to the Work by District, in accordance with requirements of title 24, part 1, of the California Code of Regulations, to enforce the building code and monitor compliance with Plans and Specifications for the Project previously approved by the DSA. Duties of Project Inspector(s) are specifically defined in section 4-342 of said part 1 of title 24.

5.1.2. No Work shall be carried on except with the knowledge and under the inspection of the Project Inspector(s). The Project Inspector(s) shall have free access to all parts of Work at any time. Contractor shall furnish Project Inspector(s) reasonable opportunities for obtaining such information as may be necessary to keep Project Inspector(s) fully informed respecting progress and manner of work and character of materials. Inspection of Work shall not relieve Contractor from the obligation to fulfill the Contract. Project Inspector(s) and the DSA are authorized to stop work whenever the Contractor and/or its Subcontractor(s) are not complying with the Contract Documents. Any work stoppage by the Project Inspector(s) and/or DSA shall be without liability to the District. Contractor shall instruct its Subcontractors and employees accordingly.

5.1.3. If Contractor and/or any Subcontractor requests that the Project Inspector(s) perform any inspection off-site, this shall only be done if it is allowable pursuant to applicable regulations and DSA, if the Project Inspector(s) agree to do so, and at the expense of the Contractor.

5.1.4. Limitations on Project Inspector Authority. The Project Inspector does not have authority to interpret the Contract Documents or to modify the Work depicted in the Contract Documents. No Work inconsistent with the Contract Documents shall be performed solely on the basis of the direction of the Project Inspector, and the Contractor shall be liable to the District for the consequences of all Work performed on such basis.

5.2. Tests and Inspections

5.2.1. Tests and Inspections shall comply with title 24, part 1, California Code of Regulations, group 1, article 5, section 4-335, and with the provisions of the Specifications.

5.2.2. If the Contract Documents, laws, ordinances or any public authority with jurisdiction over the Work requires the Work, or any portion thereof, to be specially tested, inspected or approved, the Contractor shall give the Architect, the Construction Manager and the Project Inspector written notice of the readiness of such Work for observation, testing or inspection at least seventy-two (72) hours prior to the time for the conducting of such test, inspection or observation. If inspection, testing or observation is by authority other than the District, the Contractor shall inform the Project Inspector and the Construction Manager not less than seventy-two (72) hours prior to the date fixed for such inspection, test or observation. The Contractor shall not cover up any portion of the Work subject to tests, inspections or observations prior to the completion and satisfaction of the requirements of such test, inspection or observation. In the event that any portion of the Work subject to tests, inspection or approval shall be covered up by Contractor prior to completion and satisfaction of the requirements of such tests, inspection or approval, Contractor shall be responsible for the uncovering of such portion of the Work as is necessary for performing such tests, inspection or approval without adjustment of the Contract Price or the Contract Time on account thereof.

5.2.3. The District will select an independent testing laboratory to conduct the tests. Selection of the materials required to be tested shall be by the laboratory or the District's representative and not by the Contractor. The Contractor shall notify the District's representative a sufficient time in advance of its readiness for required observation or inspection.

5.2.4. The Contractor shall notify the District's representative a sufficient time in advance of the manufacture of material to be supplied under the Contract Documents, that must by terms of the Contract Documents be tested, in order that the District may arrange for the testing of same at the source

of supply. This notice shall be, at a minimum, seventy-two (72) hours prior to the manufacture of the material that must be tested.

5.2.5. Any material shipped by the Contractor from the source of supply prior to having satisfactorily passed required testing and inspection or prior to the receipt of notice from the representative that testing and inspection will not be required, shall not be incorporated into and/or onto the Project.

5.2.6. The District will select and pay testing laboratory costs for all tests and inspections. Costs of tests of any materials found to be not in compliance with the Contract Documents shall be paid for by the District and reimbursed by the Contractor or deducted from the Contract Price.

5.3. Costs for After Hours and/or Off Site Inspections

5.3.1. If the Contractor performs Work outside the Inspector's regular working hours, over a period of more than eight (8) hours per day by any single person, on weekends/holidays or requests the Inspector to perform inspections off Site, then the costs of any inspections required outside regular working hours, over a period of more than eight (8) hours per day by any single person, on weekends/holidays or off Site, shall be borne by the Contractor and may be invoiced to the Contractor by the District or the District may deduct those expenses from the next Progress Payment.

6. CONTRACTOR

Contractor shall construct the Work for the Contract price including any adjustment(s) to the Contract Price pursuant to provisions herein regarding changes to the Contract Price. Except as otherwise noted, Contractor shall provide and pay for all labor, materials, equipment, permits, fees, licenses, facilities, transportation, taxes, and services necessary for the proper execution and Completion of the Work, except as indicated herein.

6.1. Status of Contractor

6.1.1. Contractor is and shall at all times be deemed to be an independent contractor and shall be wholly responsible for the manner in which it and its Subcontractors perform the services required of it by the Contract Documents. Nothing herein contained shall be construed as creating the relationship of employer and employee, or principal and agent, between the District, or any of the District's employees or agents, and Contractor or any of Contractor's Subcontractors, agents or employees. Contractor assumes exclusively the responsibility for the acts of its employees as they relate to the services to be provided during the course and scope of their employment. Contractor, its Subcontractors, agents, and its employees shall not be entitled to any rights or privileges of District employees. District shall be permitted to monitor the Contractor's activities to determine compliance with the terms of the Contract.

6.1.2. As required by law, Contractor and all Subcontractors shall be properly licensed and regulated by the Contractor's State License Board, located at 9821 Business Park Drive, , Sacramento, California 95827, with a mailing address of Post Office Box 26000, Sacramento, California, and with a website at <http://www.cslb.ca.gov>.

6.2. Contractor's Supervision

6.2.1. During progress of the Work, Contractor shall keep on the Premises, and at all other locations where any Work related to the Contract is being performed, a competent project manager and construction superintendent who are employees of the Contractor, to whom the District does not object and at least one of whom shall be fluent in English, written and verbal.

6.2.2. The project manager and construction superintendent shall both speak fluently the predominant language of the Contractor's employees.

6.2.3. Before commencing the Work, Contractor shall give written notice to District of the name of its project manager and construction superintendent. Neither the Contractor's project manager nor construction superintendent shall be changed except with prior written notice to District, unless the Contractor's project manager and/or construction superintendent proves to be unsatisfactory to Contractor, District, any of the District's employees, agents, the Construction Manager, or the Architect, in which case, Contractor shall notify District in writing. District retains the right to reasonably refuse Contractor's replacement personnel. The Contractor's project manager and construction superintendent shall each represent Contractor, and all directions given to Contractor's project manager and/or construction superintendent shall be as binding as if given to Contractor.

6.2.4. Contractor shall give efficient supervision to Work, using its best skill and attention. Contractor shall carefully study and compare all Contract Documents, Drawings, Specifications, and other instructions and shall at once report to District, Construction Manager, and Architect any error, inconsistency, or omission that Contractor or its employees and Subcontractors may discover, in writing, with a copy to District's Project Inspector(s). The Contractor shall have responsibility for discovery of errors, inconsistencies, or omissions.

6.2.5. The Contractor's project manager shall devote sufficient time to the Project on site, and in the Contractor's home office to pre-plan activities to meet the Construction Schedule and fulfill all Contract obligations. This includes making timely submittals, issuing and disseminating necessary RFI's, promptly processing and distributing bulletins, change orders and payments, keeping required logs current etc. If any of these activities fall behind contract requirements or dates necessary to complete the Project on time, the Contractor must provide a full time project manager on the Project Site dedicated solely to the Project, until the deficiencies are corrected.

6.2.6. The Contractor shall verify all indicated dimensions before ordering materials or equipment, or before performing Work. The Contractor shall take field measurements, verify field conditions, and shall carefully compare such field measurements and conditions and other information known to the Contractor with the Project Documents before commencing work. Errors, inconsistencies or omissions discovered shall be immediately reported to the District. Upon commencement of any item of Work, the Contractor shall be responsible for dimensions related to the Work and shall make any corrections necessary to make Work properly fit at no additional cost to District. This responsibility for verification of dimensions is a non-delegable duty and may not be delegated to subcontractors or agents.

6.2.7. Omissions from the Drawings or Specifications, or the misdescription of details of Work which are manifestly necessary to carry out the intent of the Drawings and Specifications, or which are customarily performed, shall not relieve the Contractor from performing such omitted or misdescribed Work, but they shall be performed as if fully and correctly set forth and described in the Drawings and Specifications.

6.2.8. The Contractor shall be solely responsible for the means, methods, techniques, sequences, and procedures of construction. The Contractor shall be responsible to see that the finished Work complies accurately with the Contract Documents.

6.3. Duty to Provide Fit Workers

6.3.1. Contractor and Subcontractor(s) shall at all times enforce strict discipline and good order among their employees and shall not employ or work any unfit person or anyone not skilled in work assigned to that person. It shall be the responsibility of Contractor to ensure compliance with this requirement. District may require Contractor to permanently remove unfit persons from Project Site.

6.3.2. COVID-19. Contractor shall ensure that all its employees and employees of its subcontractors shall comply with all applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with COVID-19, and/or any

similar virus or derivative strain.

6.3.3. Any person in the employ of Contractor or Subcontractor(s) whom District may deem incompetent or unfit shall be excluded from working on the Project and shall not again be employed on the Project except with the prior written consent of District.

6.3.4. The Contractor shall furnish labor that can work in harmony with all other elements of labor employed or to be employed in the Work.

6.3.5. If Contractor intends to make any change in the name or legal nature of the Contractor's entity, Contractor must first notify the District. The District shall determine if Contractor's intended change is permissible while performing the Contract.

6.3.6. Compliance with Immigration Reform and Control Act of 1986. As required by law, Contractor and all Subcontractors shall employ individuals for the Work in conformity with the Immigration Reform and Control Act of 1986, 8 USC §§1101 et seq.

6.4. Personnel

6.4.1. Contractor, Contractor's employees, Subcontractors, Subcontractors' employees, or any person associated with the Work shall conduct themselves in a manner appropriate for a school site. The District will not permit any (1) verbal or physical contact with neighbors, students, and faculty; (2) profanity, or inappropriate attire or behavior; (3) photographing, videoing, or audio recording of any neighbors, students, and faculty or any posting of any photographs, videos, or audio recordings of any neighbors, students, and faculty on any internet site, social media platform of any kind, regardless of source of any photograph, video, or audio recording. District may require Contractor to permanently remove noncomplying persons from Project Site.

6.4.2. The Contractor shall employ a full-time superintendent and necessary assistants who shall have complete authority to represent and act on behalf on the Contractor on all matters pertaining to the Work. The superintendent shall be competent and have a minimum of five (5) years' experience in construction supervision on projects of similar scale and complexity. The superintendent shall be satisfactory to the District and, if not satisfactory, shall be replaced by the Contractor with one that is acceptable to the District. The superintendent shall not be changed without the written consent of the District unless the superintendent ceases to be employed by the Contractor.

6.4.3. The Contractor shall employ a competent estimator and necessary assistants, or contract for sufficient services of an estimating consultant and to process proposed change orders. The estimator shall have a minimum of five (5) years' experience in estimating. The estimator shall be satisfactory to the District and, if not satisfactory, shall be replaced by the Contractor with one that is acceptable. The Contractor shall submit PCO's requested by the District within fourteen (14) calendar days.

6.4.4. The Contractor shall employ a competent scheduler and necessary assistants, or contract for sufficient services of a scheduling consultant. The scheduler shall have a minimum of five (5) years' experience in scheduling. The scheduler shall be satisfactory to the District and, if not satisfactory, shall be replaced by the Contractor with one that is acceptable.

6.4.5. Contractor shall at all times enforce strict discipline and good order among Contractor's employees, and shall not employ on the Project any unfit person or anyone not skilled in the task assigned.

6.4.6. If Contractor or any Subcontractor on the Project site fails to comply with any provision herein, the District may have the offending person(s) immediately removed from the Site, and the person(s) shall be replaced within three (3) days, at no additional expense to the District. Contractor, on behalf of it and

its Subcontractors, hereby waives any claim that the provisions of this paragraph or the enforcement thereof interferes, or has the potential to interfere, with its right to control the means and methods of its performance and duties under this Contract.

6.5. Prohibition on Harassment

6.5.1. In addition to the non-discrimination requirements in the Contract Documents, the Contractor and all Subcontractors must comply with these provisions prohibiting harassment at the Site. The District is committed to providing a campus and workplace free of sexual harassment and harassment based on factors such as race, color religion, national origin, ancestry, age, medical condition, marital status, disability or veteran status. Harassment includes without limitation, verbal, physical or visual conduct which creates an intimidating, offensive or hostile environment such as racial slurs; ethnic jokes; posting of offensive statements, posters or cartoons or similar conduct. Sexual harassment includes without limitation the solicitation of sexual favors, unwelcome sexual advances, or other verbal, visual or physical conduct of a sexual nature.

6.5.2. Contractor shall take all reasonable steps to prevent harassment from occurring, including without limitation affirmatively raising the subject of harassment among its employees, expressing strong disapproval of any form of harassment, developing appropriate sanctions, informing employees of their right to raise and how to raise the issue of harassment and informing complainants of the outcome of an investigation into a harassment claim.

6.5.3. Contractor shall not permit any person, whether employed by Contractor or a Subcontractor or any other person or entity, performing any Work at or about the Site to engage in any prohibited form of harassment. Any person performing or providing Work on or about the Site engaging in a prohibited form of harassment directed to any student, faculty member or staff of the District or directed to any other person on or about the Site shall be subject to immediate removal and shall be prohibited thereafter from providing or performing any portion of the Work. Upon the District's receipt of any notice or complaint that any person employed directly or indirectly by Contractor on any Subcontractor in performing or providing the Work has engaged in a prohibited form of harassment, the District will promptly undertake an investigation of such notice or complaint. In the event that the District, after such investigation, reasonably determines that a prohibited form of harassment has occurred, the District shall promptly notify the Contractor of the same and direct that the person engaging in such conduct be immediately removed from the Site. Unless the District's determination that a prohibited form of harassment has occurred is grossly negligent or without reasonable cause, District shall have no liability for directing the removal of any person determined to have engaged in a prohibited form of harassment nor shall the Contract Price or the Contract Time be adjusted on account thereof. The indemnity provisions of the Contract Documents apply to any assertion by any person dismissed from performing or providing work at the direction of the District pursuant to this provision; or (ii) the assertion by any person that any person directly or indirectly under the employment or direction of the Contractor has engaged in a prohibited form of harassment directed to or affecting such person. The obligations of the Contractor and the Surety under the preceding sentence are in addition to, and not in lieu of, any other obligation of defense, indemnity and hold harmless whether arising under the Contract Documents, at law or otherwise; these obligations survive completion of the Work or the termination of the Contract.

6.6. Conferences and Meetings.

6.6.1. In addition to the conference and meeting requirements in the Specifications, Contractor's supervisory personnel for the Work and the Contractor's management personnel shall attend all required meetings as required by the Contract Documents or as requested by the District. The Contractor's personnel participating in conferences and meetings relating to the Work shall be authorized to act on behalf of the Contractor and to bind the Contractor. The Contractor is solely responsible for arranging for the attendance by Subcontractors and Material Suppliers at meetings and conferences relating to the Work as necessary, appropriate or as requested by the District.

6.6.2. Preconstruction Conference. The Contractor's representatives (and representatives of Subcontractors as requested by the District) shall attend a preconstruction conference at such time and place as designated by the District. The preconstruction conference will generally address the requirements of the Work and Contract Documents, and to establish construction procedures. Subject matters of the preconstruction conference will include as appropriate: (a) administrative matters, including an overview of the respective responsibilities of the District, Architect, Construction Manager, Contractor, Subcontractors, Project Inspector, and others performing any part of the Work or services relating to the Work; (b) Submittals; (c) Changes; (d) employment practices, including Certified Payroll preparation and submission and prevailing wage rate responsibilities of the Contractor and Subcontractors; (e) Progress Schedule development and maintenance; (f) development of Schedule of Values and payment procedures; (g) implementation of BIM, if applicable; (h) communication procedures, including the handling of Requests for Information; (i) emergency and safety procedures; (j) Site visitor policies; (k) conduct of Contractor/Subcontractor personnel at the Site; and (l) Completion, Punchlist and closeout procedures.

6.6.3. Progress Meetings. Progress meetings will be conducted on regular intervals (weekly unless otherwise expressly indicated elsewhere in the Contract Documents). The Contractor's representatives and representatives of Subcontractors (as requested by the District) shall attend progress meetings. Progress Meetings will be chaired by the District or the Construction Manager and will generally include as agenda items: Site safety, field issues, coordination of Work, construction progress and impacts to timely Completion, if any. The purposes of the progress meetings include: a formal and regular forum for discussion of the status and progress of the Work by all Project participants, a review of progress or resolution of previously raised issues and action items assigned to the Project participants, and reviews of the Progress schedule and submittals. Contractor shall prepare and submit at each progress meeting a three (3) week look-ahead schedule identifying all planned activities for the next three (3) weeks and any deviations from activities in the current Construction Schedule.

6.6.4. Special Meetings. As deemed necessary or appropriate by the District, special meetings will be conducted with the participation of the Contractor, Subcontractors and other Project participants as requested by the District.

6.6.5. Minutes of Meetings. following conclusion of the preconstruction conference, progress meetings and special meetings, the Architect or the Construction Manager will prepare and distribute minutes reflecting the items addressed and actions taken at a meeting or conference. Unless the Contractor notifies the Architect and the Construction Manager in writing of objections or corrections to minutes prepared hereunder within five (5) days of the date of distribution of the minutes, the minutes as distributed shall constitute the official record of the meeting or conference. No objections or corrections of any Subcontractor or Material Supplier shall be submitted directly to the Architect or the Construction Manager; such objections or corrections shall be submitted to the Architect and the Construction Manager through the Contractor. If the Contractor timely interposes objections or notes corrections, the resolution of such matters shall be addressed at the next scheduled progress meeting.

6.7. Purchase of Materials and Equipment

6.7.1. The Contractor is required to order and obtain materials and equipment sufficiently in advance of its Work at no additional cost or advance payment from District to ensure against price escalations or delays. All materials and equipment shall be stored on-Site and secured by Contractor unless otherwise approved in writing by the District.

6.7.2. Off-Site Storage of Materials and Equipment Only Upon District's Written Consent. If Contractor intends to store materials and/or equipment off site after District has paid for those materials and/or equipment, Contractor must first obtain the District's express, written consent. If Contractor receives District's consent to store materials and/or equipment off site ("Stored Materials"), Contractor shall comply with all of the following:

6.7.2.1. Property of Others Insurance. Contractor shall procure and maintain, during the entire time Stored Materials are in off-site storage, insurance coverage acceptable to the District that shall protect Contractor and District from all claims for Stored Materials that are lost, stolen, or damaged. The District shall be named as a loss payee for this insurance coverage. The insurance coverage shall include a "loss payable endorsement" stating that all amounts payable will be paid as a joint-check to the Contractor and District. If approved in advance by District, this required insurance may be obtained by an "Employee Theft Protection Insurance Policy" or an "Employee Theft Protection Bond."

6.7.2.2. Payment for Stored Materials. District shall only make payment to Contractor for Stored Materials if agreed upon in advance, in writing, by the District and provided that Contractor submits an itemized list of all Stored Materials with Contractor's Application for Payment. Contractor's itemized list of all Stored Materials shall be supported by all of the following:

6.7.2.2.1. Itemized breakdown of the Stored Materials for the purpose of requesting partial payment, identifying the serial numbers and exact storage location of each piece of equipment and material; and

6.7.2.2.2. Verified invoices for the Stored Materials; and

6.7.2.2.3. Original copy of Property of Others Insurance, Employee Theft Protection Insurance Policy, or an Employee Theft Protection Bond based on the type of insurance required by the District. These documents shall include certificates and endorsements stating the coverage and that the District is a loss payee or obligee, as appropriate.

6.7.2.2.4. An express, signed document from Contractor indicating that the District may, at any time and at its sole discretion, have unhindered and unqualified access to all Stored Materials and to remove the Stored Materials.

6.8. Documents on Work

6.8.1. Contractor shall at all times keep on the Work Site, or at another location as the District may authorize in writing, one legible copy of all Contract Documents, including Addenda and Change Orders, and current titles 19 and 24 of the California Code of Regulations, the specified edition(s) of the California Building Standards Code (electronic versions are acceptable), all approved Drawings, Plans, Schedules, and Specifications, and all codes and documents referred to in the Specifications, and made part thereof. These documents shall be kept in good order and available to District, Construction Manager, Architect, Architect's representatives, the Project Inspector(s), and all authorities having jurisdiction. Contractor shall be acquainted with and comply with the provisions of these titles as they relate to this Project. (See particularly the duties of Contractor, title 24, part 1, California Code of Regulations, section 4-343.) Contractor shall also be acquainted with and comply with all California Code of Regulations provisions relating to conditions on this Project, particularly titles 8 and 17. Contractor shall coordinate with Architect and Construction Manager and shall submit its verified report(s) according to the requirements of title 24.

6.8.2. Daily Job Reports.

6.8.2.1. Contractor shall maintain, at a minimum, at least one (1) set of Daily Job Reports on the Project. These must be prepared by the Contractor's employee(s) who are present on Site, and must include, at a minimum, the following information:

6.8.2.1.1. A brief description of all Work performed on that day.

- 6.8.2.1.2.** A summary of all other pertinent events and/or occurrences on that day.
- 6.8.2.1.3.** The weather conditions on that day.
- 6.8.2.1.4.** A list of all Subcontractor(s) working on that day,
- 6.8.2.1.5.** A list of each Contractor employee working on that day and the total hours worked for each employee.
- 6.8.2.1.6.** A complete list of all equipment on Site that day, whether in use or not.
- 6.8.2.1.7.** A complete list of all materials, supplies, and equipment delivered on that day.
- 6.8.2.1.8.** A complete list of all inspections and tests performed on that day.

6.8.2.2. Each day Contractor shall provide a copy of the previous day's Daily Job Report to the District or the District's Construction Manager.

6.9. Preservation of Records

District shall have the right to examine and audit all Daily Job Reports or other Project records of Contractor's project manager(s), project superintendent(s), and/or project foreperson(s), all certified payroll records and/or related documents including, without limitation, payroll, payment, timekeeping and tracking documents; all books, estimates, records, contracts, documents, bid documents, bid cost data, subcontract job cost reports, and other data of the Contractor, any Subcontractor, and/or supplier, including computations and projections related to bidding, negotiating, pricing, or performing the Work or Contract modification, in order to evaluate the accuracy, completeness, and currency of the cost, manpower, coordination, supervision, or pricing data at no additional cost to the District. These documents may be duplicative and/or be in addition to any Bid Documents held in escrow by the District. Contractor shall make available at its office at all reasonable times the materials described in this paragraph for the examination, audit, or reproduction until three (3) years after final payment under this Contract. Notwithstanding the provisions above, Contractor shall provide any records requested by any governmental agency, if available, after the time set forth above.

6.10. Integration of Work

6.10.1. Contractor shall do all cutting, fitting, patching, and preparation of Work as required to make its several parts come together properly, to fit it to receive or be received by work of other contractors, and to coordinate tolerances to various pieces of work, showing upon, or reasonably implied by, the Drawings and Specifications for the completed structure, and shall conform them as District and/or Architect may direct.

6.10.2. All cost caused by defective or ill-timed Work shall be borne by Contractor, inclusive of repair work.

6.10.3. Contractor shall not endanger any work performed by it or anyone else by cutting, excavating, or otherwise altering work and shall not cut or alter work of any other contractor except with written consent of District.

6.11. Obtaining of Permits and Licenses

6.11.1. Contractor shall secure and pay for all permits, licenses, and certificates. Contractor must review the Special Conditions for any changes or exceptions to this provision.

6.12. Work to Comply with Applicable Laws and Regulations

6.12.1. Contractor shall give all notices and comply with all applicable laws, ordinances, rules, and regulations relating to the Work, including the specific laws, ordinances, rules, and regulations as indicated and specified in the Contract Documents and identified below, including but not limited to the appropriate statutes and administrative code sections. If Contractor observes that Drawings and Specifications are at variance therewith, or should Contractor become aware of the development of conditions not covered by Contract Documents that will result in finished Work being at variance therewith, Contractor shall promptly notify District in writing and any changes deemed necessary by District shall be made as provided in Contract for changes in Work.

6.12.1.1. National Electrical Safety Code, U. S. Department of Commerce

6.12.1.2. National Board of Fire Underwriters' Regulations

6.12.1.3. California Building Standards Code , latest addition, and the California Code of Regulations, Title 24, including amendments

6.12.1.4. Manual of Accident Prevention in Construction, latest edition, published by A.G.C. of America

6.12.1.5. Industrial Accident Commission's Safety Orders, State of California

6.12.1.6. Regulations of the State Fire Marshall (title 19, California Code of Regulations) and Pertinent Local Fire Safety Codes

6.12.1.7. Americans with Disabilities Act

6.12.1.8. Education Code of the State of California

6.12.1.9. Government Code of the State of California

6.12.1.10. Labor Code of the State of California, division 2, part 7, Public Works and Public Agencies

6.12.1.11. Public Contract Code of the State of California

6.12.1.12. California Art Preservation Act

6.12.1.13. U. S. Copyright Act

6.12.1.14. U. S. Visual Artists Rights Act

6.12.2. Contractor shall comply will all applicable mitigation measures, if any, adopted by any public agency with respect to this Project pursuant to the California Environmental Quality Act ("CEQA") (Public Resources Code sections 21000 et. seq.) (Also see the Special Conditions.)

6.12.3. If Contractor performs any Work that it knew, or through exercise of reasonable care should have known, to be contrary to any applicable laws, ordinance, rules, or regulations, Contractor shall bear all costs arising therefrom.

6.12.4. Where Specifications or Drawings state that materials, processes, or procedures must be approved by the DSA, State Fire Marshall, or other body or agency, Contractor shall be responsible for satisfying requirements of such bodies or agencies.

6.13. Safety/Protection of Persons and Property

6.13.1. Contractor will be solely and completely responsible for conditions of the Work Site, including safety of all persons and property during performance of the Work. This requirement will apply continuously and not be limited to normal working hours.

6.13.2. COVID-19. Contractor is responsible for complying with all applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with COVID-19, and/or any similar virus or derivative strain. Contractor shall ensure it has supervisor employees onsite that are trained and knowledgeable of all of these requirements to ensure full compliance on Project Site(s).

6.13.3. The wearing of hard hats will be mandatory at all times for all personnel on Site. Contractor shall supply sufficient hard hats to properly equip all employees and visitors.

6.13.4. Any construction review of the Contractor's performance is not intended to include review of the adequacy of the Contractor's safety measures in, on, or near the Work Site.

6.13.5. Implementation and maintenance of safety programs shall be the sole responsibility of the Contractor.

6.13.6. Contractor shall furnish to the District a copy of the Contractor's safety plan within the time frame indicated in the Contract Documents and specifically adapted for the Project.

6.13.7. Contractor shall be responsible for all damages to persons or property that occur as a result of its fault or negligence in connection with the performance of the Contract and shall take all necessary measures and be responsible for the proper care and completion and final acceptance by District. All Work shall be solely at Contractor's risk with the exception of damage to the Work caused by "acts of God" as defined in Public Contract Code section 7105.

6.13.8. Contractor shall take, and require Subcontractors to take, all necessary precautions for safety of workers on the Project and shall comply with all applicable federal, state, local, and other safety laws, standards, orders, rules, regulations, and building codes to prevent accidents or injury to persons on, about, or adjacent to premises where Work is being performed and to provide a safe and healthful place of employment. Contractor shall furnish, erect, and properly maintain at all times, all necessary safety devices, safeguards, construction canopies, signs, nets, barriers, lights, and watchmen for protection of workers and the public and shall post danger signs warning against hazards created by such features in the course of construction.

6.13.9. Hazards Control. Contractor shall store volatile wastes in covered metal containers and remove them from the Site daily. Contractor shall prevent accumulation of wastes that create hazardous conditions. Contractor shall provide adequate ventilation during use of volatile or noxious substances.

6.13.10. Contractor shall designate a responsible member of its organization on the Project, whose duty shall be to post information regarding protection and obligations of workers and other notices required under occupational safety and health laws, to comply with reporting and other occupational safety requirements, and to protect the life, safety, and health of workers. Name and position of person so designated shall be reported to District by Contractor.

6.13.11. Contractor shall correct any violations of safety laws, rules, orders, standards, or regulations. Upon the issuance of a citation or notice of violation by the Division of Occupational Safety and Health, Contractor shall correct such violation promptly.

6.13.12. Storm Water. Contractor shall comply with the District's Storm Water Pollution Prevention Plan

(SWPPP) and, if indicated in the Special Conditions, shall be the District's Qualified SWPPP Practitioner, at no additional cost to the District.

6.13.13. In an emergency affecting safety of life or of work or of adjoining property, Contractor, without special instruction or authorization, shall act, at its discretion, to prevent such threatened loss or injury. Any compensation claimed by Contractor on account of emergency work shall be determined by agreement.

6.13.14. All salvage materials will become the property of the Contractor and shall be removed from the Site unless otherwise called for in the Contract Documents. The District reserves the right to designate certain items of value that shall be turned over to the District.

6.13.15. All connections to public utilities and/or existing on-site services shall be made and maintained in such a manner as to not interfere with the continuing use of same by the District during the entire progress of the Work.

6.13.16. Contractor shall provide such heat, covering, and enclosures as are necessary to protect all Work, materials, equipment, appliances, and tools against damage by weather conditions, such as extreme heat, cold, rain, snow, dry winds, flooding, or dampness.

6.13.17. Contractor shall protect and preserve the Work from all damage or accident, providing temporary roofs, window and door coverings, boxing, or other construction as needed. Contractor shall be responsible for existing structures, walks, roads, trees, landscaping, materials, equipment, furnishings, and/or improvements in working areas; and shall provide adequate protection therefor. If temporary removal is necessary of any of the above items, or damage occurs due to the Work, the Contractor shall replace same at its expense with same kind, quality, and size of Work or item damaged. This shall include any adjoining property of the District and others.

6.13.18. Contractor shall take adequate precautions to protect existing roads, sidewalks, curbs, pavements, utilities, adjoining property, and structures (including, without limitation, protection from settlement or loss of lateral support), and to avoid damage thereto, and repair any damage thereto caused by construction operations.

6.13.19. Contractor shall confine apparatus, the storage of materials, and the operations of workers to limits indicated by law, ordinances, permits, or directions of the District, and shall not interfere with the Work or unreasonably encumber Premises or overload any structure with materials. Contractor shall enforce all instructions of District and Architect regarding signs, advertising, fires, and require that all workers comply with all regulations while on Project Site.

6.13.20. Contractor shall take care to prevent disturbing or covering any survey markers, monuments, or other devices marking property boundaries or corners. If such markers are disturbed, Contractor shall have a civil engineer, registered as a professional engineer in California, replace them at no cost to District.

6.13.21. In the event that the Contractor enters into any agreement with owners of any adjacent property to enter upon the adjacent property for the purpose of performing the Work, Contractor shall fully indemnify, defend, and hold harmless each person, entity, firm, or agency that owns or has any interest in adjacent property. The form and content of the agreement of indemnification shall be approved by the District prior to entering the adjacent property. The Contractor shall also indemnify the District as provided in the indemnification provision herein. These provisions shall be in addition to any other requirements of the owners of the adjacent property.

6.13.22. Infectious Disease Compliance Provisions

6.13.22.1. Compliance with Orders. Contractor and its Subcontractors, agents and employees thereof, are responsible for complying with all applicable and existing federal, State, and/or local statutes, orders, rules, regulations, ordinances, and/or directives in any way relating to construction site safety, the Work, the Project, and Site, in connection with any infectious and communicable disease in any form, whether bacterial or viral, including, without limitation, MSRA, influenza, COVID-19, and/or any similar virus or derivative strain ("**Infectious Disease(s)**"). Contractor shall ensure it has supervisor employees onsite that are trained and knowledgeable of all these requirements to ensure full compliance on Site and the Work. Contractor's obligations hereunder shall include, without limitation providing personal protective equipment ("PPE") to its employees and to ensure that its subcontractors provide PPE equipment to its employees to prevent the spread of an Infectious Disease at the Project Site(s).

6.13.22.2. Infectious Disease and Contract Time. Contractor agrees that the Contract Time is based on Contractor's full compliance with all applicable and existing federal, State, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety, the Work, the Project, and the Site in connection with an Infectious Disease. Any dispute concerning the Contract Time in connection with any delay associated with an Infectious Disease shall be resolved pursuant to the Claims procedures in these General Conditions.

6.13.22.3. Infectious Disease Release. Contractor acknowledges that it is voluntarily and freely entering into the Contract for this Project and deciding to perform the Work which will require Contractor to enter upon and into the Site and that Contractor use of the Site includes the possible exposure to and illness from an Infectious Disease. Contractor further acknowledges the dangers involved and with full knowledge of these dangers, voluntarily agrees to assume all risks of bodily injury, death, or property damage, whether those risks are known or unknown. Contractor hereby releases District, its agents, representatives, officers, consultants, employees, trustees, and volunteers from any and all liabilities, causes of action, lawsuits, claims, demands, or damages of any kind whatsoever that Contractor, its staff, participants, relatives, children, spouse, partner, household members, family members, employees, guests, invitees, volunteers, agents, consultants, Subcontractors, and any other person tracing exposure or illness to Contractor, now have, or may have in the future, for injury, trauma, illness, loss, unwanted contact, harassment, disability, death or property damages related to being exposed to or contracting an Infectious Disease while using the Site for the performance of the Work. Contractor shall include this paragraph in all subcontracts with Subcontractors.

6.13.22.4. Contractor shall ensure it has supervisor employees onsite that are trained and knowledgeable of all of these requirements to ensure full compliance on Project Site(s).

6.13.22.5. Any cost to comply with these "Infectious Disease Compliance Provisions" shall be at Contractor's sole expense and expense, but may be included in the Contract Price.

6.13.23. Photos, Videos and Use of Drones.

6.13.23.1. Contractor may photograph or video the progress of the Work and shall provide all of those photos and videos to the District at the District's request. Contractor may utilize drones or similar aerial equipment to photograph, video or monitor the progress of the Work and for security purposes, but Contractor must comply with all legal requirements of the federal government, the State of California, and the County and City in which the Project is located, applicable to the use of drones or similar aerial equipment. In addition, Contractor shall ensure that no photographs, videos or digital recordings of any kind are taken of District students or staff.

6.13.23.2. If Contractor utilizes drones or any other unmanned aircraft during construction operations, Contractor must either ensure its insurance coverage includes

unmanned aircraft operations or procure and maintain a separate aircraft liability policy to cover unmanned aircraft operations.

6.14. Working Evenings and Weekends

Contractor may be required to work evenings and/or weekends at no additional cost to the District. Contractor shall give the District seventy-two (72) hours' notice prior to performing any evening and/or weekend work. Contractor shall perform all evening and/or weekend work only upon District's written approval and in compliance with all applicable rules, regulations, laws, and local ordinances including, without limitation, all noise and light limitations. Contractor shall reimburse the District for any Inspector and custodial charges necessitated by the Contractor's evening and/or weekend work.

6.15. Noise and Dust Control

6.15.1. In addition to the noise control, dust control and related requirements in the Specifications, Contractor shall control the noise and dust at the Site as indicated here.

6.15.2. Noise Control. The Contractor shall install noise reducing devices on construction equipment. Contractor shall comply with the requirements of the city and county having jurisdiction with regard to noise ordinances governing construction sites and activities. Construction equipment noise at the Site shall be limited as required by applicable law, rule or regulation. If classes are in session at any point during the progress of the Work, and, in the District's reasonable discretion, the noise from any Work disrupts or disturbs the students or faculty or the normal operation of the school at the Site, at the District's request, the Contractor shall schedule the performance of that Work around normal school hours or make other arrangements so that the Work does not cause disruption or disturbance. In no event shall those arrangements result in adjustment of the Contract Price or the Contract Time.

6.15.3. Dust Control. The Contractor shall be fully and solely responsible for maintaining and upkeeping all areas of the Site and adjoining areas, outdoors and indoors, free from flying debris, grinding powder, sawdust, dirt and dust as well as any other product, product waste or work waste, that by becoming airborne may cause respiratory inconveniences to persons, particularly to students and District personnel. Additionally, the Contractor shall take specific care to avoid deposits of airborne dust or airborne elements. Those protection devices, systems or methods shall be in accordance with the regulations set forth by the EPA and OSHA, and other applicable law, rule or regulation. Additionally, the Contractor shall be responsible to regularly and routinely clean up and remove any and all deposits of dust and other elements. Damage and/or any liability derived from the Contractor's failure to comply with these requirements shall be exclusively at the cost of the Contractor, including, without limitation, any and all penalties that may be incurred for violations of applicable law, rule or regulation, and any amounts expended by the District to pay such damages shall be due and payable to the District on demand. Contractor shall replace any damages property or part thereof and professionally clean any and all items that become covered or partially covered to any degree by dust or other airborne elements. If classes are in session at any point during the progress of Work, and, in the District's reasonable discretion, flying debris, grinding powder, sawdust, dirt or dust from any Work disrupts or disturbs the students or faculty or the normal operation of the school, at the District's request, the Contractor shall schedule the performance of all that Work around normal school hours and make other arrangements so that the Work does not cause disruption or disturbance. In no event shall those arrangements result in adjustment of the Contract Price or the Contract Time.

6.15.4. Contractor Failure to Comply. If the Contractor fails to comply with the requirements for dust control, noise control, or any other maintenance or clean up requirement of the Contract Documents, the District, Architect, Project Inspector, or Construction Manager shall notify the Contractor in writing and the Contractor shall take immediate action. Should the Contractor fail to respond with immediate and responsive action and not later than twenty-four (24) hours from that notification, the District shall have the absolute right to proceed as it may deem necessary to remedy such matter. Any and all costs incurred

by the District in connection with those actions shall be the sole responsibility of, and be borne by, the Contractor; the District may deduct those amounts from the Contract Price then or thereafter due the Contractor.

6.16. Cleaning Up

6.16.1. The Contractor shall provide all services, labor, materials, and equipment necessary for protecting the Work, all school occupants, furnishings, equipment, and building structure from damage until its Completion and final acceptance by District. Dust barriers shall be provided to isolate dust and dirt from construction operations. At Completion of the Work and portions thereof, Contractor shall clean to the original state any areas beyond the Work area that become dust laden as a result of the Work. The Contractor must erect the necessary warning signs and barricades to ensure the safety of all school occupants. The Contractor at all times must maintain good housekeeping practices to reduce the risk of fire damage and must make a fire extinguisher, fire blanket, and/or fire watch, as applicable, available at each location where cutting, braising, soldering, and/or welding is being performed or where there is an increased risk of fire.

6.16.2. Contractor at all times shall keep Premises free from debris such as waste, rubbish, and excess materials and equipment caused by the Work. Contractor shall not leave debris under, in, or about the Premises, but shall promptly remove same from the Premises on a daily basis. If Contractor fails to clean up, District may do so and the cost thereof shall be charged to Contractor. If Contract is for work on an existing facility, Contractor shall also perform specific clean-up on or about the Premises upon request by the District as it deems necessary for the continuing education process. Contractor shall comply with all related provisions of the Specifications.

6.16.3. If the Construction Manager, Architect, or District observes the accumulation of trash and debris, the District will give the Contractor a 24-hour written notice to mitigate the condition.

6.16.4. Should the Contractor fail to perform the required clean-up, or should the clean-up be deemed unsatisfactory by the District, the District will then perform the clean-up. All cost associated with the clean-up work (including all travel, payroll burden, and costs for supervision) will be deducted from the Contract Price, or District may withhold those amounts from payment(s) to Contractor.

7. SUBCONTRACTORS

7.1. Contractor shall provide the District with information for all Subcontracts as required in the Contractor's Submittals and Schedules Section.

7.2. No contractual relationship exists between the District and any Subcontractor, supplier, or sub-subcontractor by reason of the Contract.

7.3. Contractor agrees to bind every Subcontractor by terms of the Contract as far as those terms are applicable to Subcontractor's work. If Contractor shall subcontract any part of the Contract, Contractor shall be as fully responsible to District for acts and omissions of any Subcontractor and of persons either directly or indirectly employed by any Subcontractor, as it is for acts and omissions of persons directly employed by Contractor. The divisions or sections of the Specifications are not intended to control the Contractor in dividing the Work among Subcontractors or limit the work performed by any trade.

7.4. District's consent to, or approval of, or failure to object to, any Subcontractor under the Contract shall not in any way relieve Contractor of any obligations under the Contract and no such consent shall be deemed to waive any provisions of the Contract.

7.5. Contractor acknowledges sections 4100 through 4114 of the Public Contract Code of the State of California, as regards subletting and subcontracting, and shall comply with all applicable requirements

therein. In addition, Contractor acknowledges sections 1720 through 1861 of the Labor Code of the State of California, as regards the payment of prevailing wages and related issues, and shall comply with all applicable requirements therein all including, without limitation, section 1775 and the Contractor's and Subcontractors' obligations and liability for violations of prevailing wage law and other applicable laws.

- 7.6.** No Contractor whose Bid is accepted shall, without consent of the awarding authority and in full compliance with section 4100, et seq, of the Public Contract Code, including, without limitation, sections 4107, 4107.5, and 4109 of the Public Contract Code, either:

7.6.1. Substitute any person as a Subcontractor in place of the Subcontractor designated in the original Bid; or

7.6.2. Permit any Subcontract to be assigned or transferred, or allow any portion of the Work to be performed by anyone other than the original Subcontractor listed in the Bid; or

7.6.3. Sublet or subcontract any portion of the Work in excess of one-half of one percent (1/2 of 1%) of the Contractor's total bid as to which his original bid did not designate a Subcontractor.

- 7.7.** The Contractor shall be responsible for the coordination of the trades, Subcontractors, sub-subcontractors, and material or equipment suppliers working on the Project.

- 7.8.** Contractor is solely responsible for settling any differences between the Contractor and its Subcontractor(s) or between Subcontractors.

- 7.9.** Contractor must include in all of its subcontracts the assignment provisions as indicated in the Termination section of these General Conditions.

8. OTHER CONTRACTS/CONTRACTORS

- 8.1.** District reserves the right to let other contracts, and/or to perform work with its own forces, in connection with other portions of the Project or other construction or operations at or about the Site. Contractor shall afford other contractors reasonable opportunity for introduction and storage of their materials and execution of their work and shall properly coordinate and connect Contractor's Work with the work of other contractors.

- 8.2.** In addition to Contractor's obligation to protect its own Work, Contractor shall protect the work of any other contractor that Contractor encounters while working on the Site.

- 8.3.** If any part of Contractor's Work depends for proper execution or results upon work of District or any other contractor, Contractor shall inspect and promptly report to the District in writing before proceeding with its Work any defects in District's or any other contractor's work that render Contractor's Work unsuitable for proper execution and results. Contractor shall be held accountable for damages to District for District's or any other contractor's work that Contractor failed to inspect or should have inspected. Contractor's failure to inspect and report shall constitute Contractor's acceptance of all District's or any other contractor's work as fit and proper for reception of Contractor's Work, except as to defects that may develop in District's or any other contractor's work after execution of Contractor's Work.

- 8.4.** To ensure proper execution of its subsequent work, Contractor shall measure and inspect work already in place and shall at once report to the District in writing any discrepancy between that executed work and the Contract Documents.

- 8.5.** Contractor shall ascertain to its own satisfaction the scope of the Project and nature of District's or any other contracts that have been or may be awarded by District in completion of the Project to the end that

Contractor may perform this Contract in light of the other contracts, if any.

- 8.6.** Nothing herein contained shall be interpreted as granting to Contractor exclusive occupancy of the Site, the Premises, or of the Project. The District shall have complete access to the Project Site for any reasonable purpose at all times. Contractor shall not cause any unnecessary hindrance or delay to the use and/or school operation(s) of the Premises and/or to District or any other contractor working on the Project. If simultaneous execution of any contract or school operation is likely to cause interference with performance of Contractor's Contract, Contractor shall coordinate with those contractor(s), person(s), and/or entity(s) and shall notify the District of the resolution.

9. DRAWINGS AND SPECIFICATIONS

- 9.1.** A complete list of all Drawings that form a part of the Contract is to be found as an index on the Drawings themselves, and/or may be provided to the Contractor and/or in the Table of Contents.
- 9.2.** Materials or Work described in words that so applied have a well-known technical or trade meaning shall be deemed to refer to recognized standards, unless noted otherwise.
- 9.3.** Trade Name or Trade Term. It is not the intention of the Contract to go into detailed descriptions of any materials and/or methods commonly known to the trade under "trade name" or "trade term." The mere mention or notation of "trade name" or "trade term" shall be considered sufficient notice to Contractor that it will be required to complete the work so named, complete, finished, and operable, with all its appurtenances, according to the best practices of the trade.
- 9.4.** The naming of any material and/or equipment shall mean furnishing and installing of same, including all incidental and accessory items thereto and/or labor therefor, as per best practices of the trade(s) involved, unless specifically noted otherwise.
- 9.5.** Contract Documents are complementary, and what is called for by one shall be binding as if called for by all. As such, Drawings and Specifications are intended to be fully cooperative and to agree. However, if Contractor observes that Drawings and Specifications are in conflict, Contractor shall promptly notify District and Architect in writing, and any necessary changes shall be made as provided in the Contract Documents.
- 9.6.** In the case of discrepancy or ambiguity in the Contract Documents, the order of precedence in the Agreement shall prevail. However, in the case of discrepancy or ambiguity solely between and among the Drawings and Specifications, the discrepancy or ambiguity shall be resolved in favor of the interpretation that will provide District with the functionally complete and operable Project described in the Drawings and Specifications. In case of ambiguity, conflict, or lack of information, District will furnish clarifications with reasonable promptness.
- 9.7.** Drawings and Specifications are intended to comply with all laws, ordinances, rules, and regulations of constituted authorities having jurisdiction, and where referred to in the Contract Documents, the laws, ordinances, rules, and regulations shall be considered as a part of the Contract within the limits specified. Contractor shall bear all expense of correcting work done contrary to said laws, ordinances, rules, and regulations.
- 9.8. Ownership of Drawings**
- 9.8.1.** All copies of the Drawings, Designs, Specifications, and copies of other incidental architectural and engineering work, or copies of other Contract Documents furnished by District, are the property of District. They are not to be used by Contractor in other work and, with the exception of signed sets of Contract Documents, are to be returned to District on request at Completion of Work, or may be used by District as it may require without any additional costs to District. Neither the Contractor nor any

Subcontractor, or material or equipment supplier shall own or claim a copyright in the Drawings, Specifications, and other documents prepared by the Architect. District hereby grants the Contractor, Subcontractors, sub-subcontractors, and material or equipment suppliers a limited license to use applicable portions of the Drawings prepared for the Project in the execution of their Work under the Contract Documents.

10. CONTRACTOR'S SUBMITTALS AND SCHEDULES

Contractor's submittals shall comply with the provisions and requirements of the Specifications including, without limitation Submittals. No submittal, unless approved in writing by the District as acceptable and complete, shall be a Contract Document.

10.1. Schedules, Safety Plan and Complete Subcontractor List

10.1.1. Within **TEN (10)** calendar days after the date of the Notice to Proceed (unless otherwise specified in the Notice to Proceed or in the Special Conditions), Contractor shall prepare and submit to the District for review, in a form supported by sufficient data to substantiate its accuracy as the District may require:

10.1.1.1. Schedule of Work. Contractor shall provide a preliminary schedule of construction indicating the starting and completion dates of the various stages of the Work, including any information and following any form as may be specified in the Specifications. Once approved by District, this shall become the Construction Schedule. This schedule shall include and identify all tasks that are on the Project's critical path with a specific determination of the start and completion of each critical path task, all contract milestones and each milestone's completion date(s) as may be required by the District, and the date of Project Completion.

10.1.1.1.1. Proposed Advanced Schedule. The District is not required to accept an early completion ("advanced") schedule; i.e., one that shows early completion dates for the Contract completion or milestones. Contractor shall not be entitled to extra compensation if the District allows the Contractor to proceed performing the Contract on an earlier ("advanced") schedule and Contractor completes the Project, for whatever reason, beyond the date shown in that earlier ("advanced") schedule, but within the Time for Completion indicated in the Contract. A schedule showing the work completed in less than the Time for Completion indicated in the Contract, shall be considered to have Project Float.

10.1.1.1.2. Float or Slack in the Schedule. Float or slack is the amount of time between the early start date and the late start date, or the early finish date and the late finish date, of any of the activities in the schedule. Float or slack is not for the exclusive use of or benefit of either the District or the Contractor, but its use shall be determined solely by the District.

10.1.1.2. Schedule of Submittals. The Contractor shall provide a preliminary schedule of submittals, including Shop Drawings, Product Data, and Samples submittals. Once approved by District, this shall become the Submittal Schedule. All submittals shall be forwarded to the District by the date indicated on the approved Submittal Schedule, unless an earlier date is necessary to maintain the Construction Schedule, in which case those submittals shall be forwarded to the District so as not to delay the Construction Schedule.

10.1.1.3. Schedule of Values. The Contractor shall provide a preliminary schedule of values for all component parts of the Work for which progress payments may be requested. The schedule of values must include quantities and prices of items totaling the Contract Price and must subdivide the Work into component parts in sufficient detail to serve as the basis for progress payments during construction. The preliminary schedule of values should include, at a minimum, the following information and the following structure:

10.1.1.3.1. Divided into at least the following categories:

- 10.1.1.3.1.1.** Overhead and profit;
- 10.1.1.3.1.2.** Supervision;
- 10.1.1.3.1.3.** General conditions;
- 10.1.1.3.1.4.** Layout;
- 10.1.1.3.1.5.** Mobilization;
- 10.1.1.3.1.6.** Submittals;
- 10.1.1.3.1.7.** Bonds and insurance;
- 10.1.1.3.1.8.** Closeout documentation;
- 10.1.1.3.1.9.** Demolition;
- 10.1.1.3.1.10.** Installation;
- 10.1.1.3.1.11.** Rough-in;
- 10.1.1.3.1.12.** Finishes;
- 10.1.1.3.1.13.** Testing;
- 10.1.1.3.1.14.** Punch List and acceptance.

10.1.1.3.2. Divided by each of the following areas:

- 10.1.1.3.2.1.** Site work;
- 10.1.1.3.2.2.** By each building;
- 10.1.1.3.2.3.** By each floor.

10.1.1.3.3. The preliminary schedule of values shall not provide for values any greater than the following percentages of the Contract value:

- 10.1.1.3.3.1.** Mobilization and layout combined to equal not more than 1%;
- 10.1.1.3.3.2.** Submittals, samples and shop drawings combined to equal not more than 3%;
- 10.1.1.3.3.3.** Bonds and insurance combined to equal not more than 2%.

10.1.1.3.4. Closeout Documentation. Closeout Documentation shall have a value in the preliminary schedule of not less than 5%. The value for Closeout Documentation shall be in addition to and shall not be a part of the Contract retention.

10.1.1.3.5. All items on the Schedule of Values must have a specific completion date on the Construction Schedule, or District has approved the Construction Schedule and the Construction Schedule is fully cost-loaded and resource-loaded, unless waived by the District in writing, and detailed as required by the Contract Documents

10.1.1.3.6. Contractor shall certify that the preliminary schedule of values as submitted to the District is accurate and reflects the costs as developed in preparing Contractor's bid. The preliminary schedule of values shall be subject to the District's review and approval of the form and content thereof. In the event that the District objects to any portion of the preliminary schedule of values, the District shall notify the Contractor, in writing, of the District's objection(s) to the preliminary schedule of values. Within five (5) calendar days of the date of the District's written objection(s), Contractor shall submit a revised preliminary schedule of values to the District for review and approval. The foregoing procedure for the preparation, review and approval of the preliminary schedule of values shall continue until the District has approved the entirety of the preliminary schedule of values.

10.1.1.3.7. Once the preliminary schedule of values is approved by the District, this shall become the Schedule of Values. The Schedule of Values shall not be thereafter modified or amended by the Contractor without the prior written consent and approval of the District,

which may be granted or withheld in the sole discretion of the District.

10.1.1.3.8. Notwithstanding any provision of the Contract Documents to the contrary, payment of the Contractor's overhead, supervision, general conditions costs, and profit, as reflected in the Schedule of Values, shall be paid by the District in installments, based on percentage complete, with the disbursement of Progress Payments and the Final Payment.

10.1.1.3.9. The Contractor shall not "front-load" the Schedule of Values with false dollar amounts for activities to be performed in the early stages of the Project. The District may, in its sole discretion, utilize the costs listed in the Schedule of Values as the true cost of items to be deducted from the Contract Price through credit or deductive Change Order. The values for each line item shall include the amount of overhead and profit applicable to each item of work and shall include, at a minimum, a breakdown between rough and finish Work for the basic trades as well as individual dollar figures for large dollar equipment and materials to be installed or furnished for the Project. No individual line item or scope of work in the Schedule of Values shall exceed \$50,000, except with the express, written consent of the District. Exceptions will be given by the District for a single item of Equipment for which the true cost exceeds \$50,000. The Schedule of Values shall be subject to the District's review and approval of the form and content thereof. Upon request, Contractor shall provide District with data and documentation substantiating the accuracy of the proposed line items. In the event that the District shall reasonably object to any portion of the Schedule of Values, within ten (10) days of the District's receipt of the Schedule of Values, the District shall notify the Contractor, in writing of the District's objection(s) to the Schedule of Values together with any request for substantiating data or documentation. Within five (5) days of the date of the District's written objection(s) and request for substantiating data and documentation, Contractor shall submit a revised Schedule of Values to the District for review and approval together with the requested data and documentation. The foregoing procedure for the preparation, review and approval of the Schedule of Values shall continue until the District has approved of the entirety of the Schedule of Values. Once the Schedule of Values is approved by the District, the Schedule of Values shall not be thereafter modified or amended by the Contractor without the prior consent and approval of the District, which may be granted or withheld in the sole reasonable discretion of the District. Notwithstanding any provision of the Contract Documents to the contrary, payment of the Contractor's overhead, supervision and general conditions costs and profit, as such items are reflected in the Schedule of Values, shall be made incrementally as included in the activities included in the Approved Construction Schedule.

10.1.1.4. Safety Plan. The Contractor shall provide a preliminary Contractor's Safety Plan specifically adapted for the Project. Contractor's Safety Plan shall comply with the following requirements:

10.1.1.4.1. All applicable requirements of California Division of Industrial Safety ("CalOSHA") and/or of the United States Occupational Safety and Health Administration ("OSHA").

10.1.1.4.2. All provisions regarding Project safety, including all applicable provisions in these General Conditions.

10.1.1.4.3. Contractor's Safety Plan shall be prepared in both English and in the predominant language(s) of the Contractor's and its Subcontractors' employees.

10.1.1.5. Complete Subcontractor List. Contractor shall provide a preliminary Subcontractor List stating the name, address, telephone number, facsimile number, email address, California State Contractors License number, Department of Industrial Relations

registration number, classification, and monetary value of all Subcontracts for parties furnishing labor, material, or equipment for the Project.

10.1.2. Contractor must provide all schedules both in hard copy and electronically, in a format (e.g., Microsoft Project, Primavera, or substantially similar product) approved in advance by the District.

10.1.3. The District will review the schedules submitted and the Contractor shall make changes and corrections in the schedules as requested by the District and resubmit the schedules until approved by the District.

10.1.4. The District shall have the right at any time to revise the Schedule of Values if, in the District's sole opinion, the Schedule of Values does not accurately reflect the value of the Work performed.

10.1.5. All submittals and schedules must be approved by the District before Contractor can rely on them as a basis for payment.

10.2. Monthly Progress Schedule(s)

10.2.1. Contractor shall provide Monthly Progress Schedule(s) to the District. A Monthly Progress Schedule shall update the approved Construction Schedule or the last Monthly Progress Schedule, showing all work completed and to be completed. The Monthly Progress Schedule shall be sent to the District and shall be in a format acceptable to the District and contain a written narrative of the progress of work that month and any changes, delays, or events that may affect the work. The process for District approval of the Monthly Progress Schedule shall be the same as the process for approval of the Construction Schedule.

10.2.2. Contractor shall also submit Monthly Progress Schedule(s) with all payment applications.

10.3. Material Safety Data Sheets (MSDS)

Contractor is required to ensure Material Safety Data Sheets are available in a readily accessible place at the Work Site for any material requiring a Material Safety Data Sheet per the Federal "Hazard Communication" standard, or employees right to know law. The Contractor is also required to ensure proper labeling on substances brought onto the Project Site and that any person working with the material or within the general area of the material is informed of the hazards of the substance and follows proper handling and protection procedures. Two additional copies of the Material Safety Data Sheets shall also be submitted directly to the District.

10.4. Logistic Plan

Contractor shall provide a staging and logistics plan identifying laydown areas, loading and unloading areas, crane locations, fence locations, temporary utility connections, trailer locations, and emergency evacuation meeting area. This Logistics Plan must be approved by the District prior to the Contractor mobilizing on the Site.

10.5. Information Included in Submittals.

All Submittals shall be accompanied by a written transmittal and each set of plans shall carry a "wet stamp" or other writing by the Contractor providing an identification of the portion of the Drawings or the Specifications pertaining to the Submittal, with each Submittal numbered consecutively for ease of reference along with the following information: (i) date of submission; (ii) Project name; (iii) name of submitting Subcontractor; and (iv) if applicable, the revision number. The foregoing information is in addition to, and not in lieu of, any other information required for the District's review, evaluation and approval of the Contractor's Submittals. Each Submittal shall be complete with its required number of

copies, no piecemeal documentation is allowed. Any Submittal not bearing the required wet stamp as stated herein, shall be rejected until the appropriate wet stamp information is provided on each submittal.

10.6. Verification of Submittal Information.

By approving and submission of Submittals, the Contractor represents to the District and Architect that the Contractor has determined and verified materials, field measurements, field construction criteria, catalog numbers and similar data related thereto and has checked and coordinated the information contained within such Submittals with the requirements of the Work and of the Contract Documents. Each Submittal shall include the following certification duly executed by the Contractor's superintendent or project manager for the Work: "The Contractor has reviewed and approved the field dimensions and construction criteria of the attached Submittal. The Contractor has verified that the Submittal is complete and includes notations of any portion of the Work depicted in the Submittal which is not in strict conformity with the Contract Documents. The information in the attached Submittal has been reviewed and coordinated by the Contractor with information included in other Submittals."

10.7. Contractor Responsibility for Deviations.

The Contractor shall not be relieved of responsibility for correcting deviations from the requirements of the Contract Documents by the District's and Architect's review of Submittals unless the Contractor has specifically informed the District in writing of such deviation at the time of submission of the Submittal and the District has given written approval to the specific deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Submittals by the District's and Architect's review or comments thereon.

10.8. No Performance of Work Without Architect Review.

The Contractor shall perform no portion of the Work requiring the District's and Architect's review of Submittals until the District and Architect have completed their review and returned the Submittal to the Contractor indicating "No Exception Taken" to that Submittal. The Contractor shall not perform any portion of the Work forming a part of a Submittal or which is affected by a related Submittal until the entirety of the Submittal or other related Submittal has been fully processed. All Work shall be in accordance with the final action taken by the District and the Architect review in review of Submittals and other applicable portions of the Contract Documents.

10.9. District and Architect Review of Submittals.

The purpose of the District's and Architect's review of Submittals and the time for the District's and Architect's return of Submittals to the Contractor shall be as set forth elsewhere in the Contract Documents. If the District and/or Architect return a Submittal as rejected or requiring correction(s) with re-submission, the Contractor, so as not to delay the progress of the Work, shall promptly thereafter resubmit a Submittal conforming to the requirements of the Contract Documents; the resubmitted Submittal shall indicate the portions thereof modified in accordance with the District's and Architect's direction. When professional certification of performance criteria of materials, systems or equipment is required by the Contract Documents, the District shall be entitled to rely upon the accuracy and completeness of the Contractor's calculations and certifications accompanying Submittals. The District's and Architect's review of the Submittals is for the limited purposes described in the Contract Documents. The District and Architect will review each Submittal twice. Should additional Submittals be required as a result of failure of the Contractor to address comments, the Contractor will pay for the Architect's services on a time and material basis for each subsequent review.

10.10. Deferred Approval Items.

In the event that any portion of the Work is designated in the Contract Documents as a "Deferred Approval" item from DSA, Contractor shall be solely and exclusively responsible for the preparation of Submittals for such item(s) in a timely manner so as not to delay or hinder the completion of the Work within the Contract Time. All work, labor, materials, equipment or services necessary to complete the design, engineering and permitting/approval of the Deferred Approval items shall be provided by the Contractor without adjustment of the Contract Price or the Contract Time.

10.11. Contractor Responsibility for Deviations

The Contractor shall not be relieved of responsibility for correcting deviations from the requirements of the Contract Documents by the District's or Architect's review of Submittals unless the Contractor has specifically informed the District and the Architect in writing of such deviation at the time of submission of the Submittal and the District and the Architect have given written approval to the specific deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Submittals by the District's or the Architect's review or comments thereon.

11. SITE ACCESS, CONDITIONS AND REQUIREMENTS

11.1. Site Investigation

Before bidding on the Work, Contractor shall make a careful investigation of the Site and thoroughly familiarize itself with the requirements of the Contract. By the act of submitting a bid for the Work included in the Contract, Contractor shall be deemed to have made a complete study and investigation, and to be familiar with and accepted the existing conditions of the Site.

11.2. Soils Investigation Report

11.2.1. When a soils investigation report obtained from test holes at Site is available, that report shall be available to the Contractor but shall not be a part of the Contract. Any information obtained from that report or any information given on Drawings as to subsurface soil condition or to elevations of existing grades or elevations of underlying rock is approximate only, is not guaranteed, does not form a part of the Contract, and Contractor may not rely thereon. By submitting its bid, Contractor acknowledges that it made visual examination of Site and made whatever tests Contractor deems appropriate to determine underground condition of soil.

11.2.2. If a soils report is identified in the Contract Documents, it is not a Contract Document. Further, no representation is made by District that information provided is adequate for purposes of construction of the Project. District disclaims responsibility for any and all interpretations made by the Contractor of any soil or subsurface condition for information, such as soil-bearing values, rock profiles, presence and scope of boulders and cobbles, soil stability and the presence or level and extent of underground water.

11.2.3. The Contractor shall determine the means, methods, techniques and sequences necessary to achieve required soil contours and characteristics of all completed Work.

11.2.4. If after execution of the Contract, the Contractor encounters conditions at the Site than are materially different from those customarily encountered at or near the Premises, any request by the Contractor for additional funds or additional time, shall be governed by provisions of the Contract Documents for Changes in the Work related to unforeseen conditions.

11.2.5. Contractor agrees that no claim against District will be made by Contractor for damages and hereby waives any rights to damages if, during progress of Work, Contractor encounters subsurface or latent conditions at Site materially differing from those shown on Drawings or indicated in Specifications, or for unknown conditions of an unusual nature that differ materially from those ordinarily encountered in the work of the character provided for in Plans and Specifications, except as indicated in the provisions

of these General Conditions regarding trenches, trenching, and/or existing utility lines.

11.3. Access to Work

District and its representatives shall at all times have access to Work wherever it is in preparation or progress, including storage and fabrication. Contractor shall provide safe and proper facilities for access so that District's representatives may perform their functions.

11.4. Layout and Field Engineering

11.4.1. All field engineering required for layout of this Work and establishing grades for earthwork operations shall be furnished by Contractor at its expense. This Work shall be done by a qualified, California-registered civil engineer approved in writing by District and Architect. Any required Record and/or As-Built Drawings of Site development shall be prepared by the approved civil engineer.

11.4.2. Contractor shall be responsible for having ascertained pertinent local conditions such as location, accessibility, and general character of the Site and for having satisfied itself as to the conditions under which the Work is to be performed. District shall not be liable for any claim for allowances because of Contractor's error or negligence in acquainting itself with the conditions at the Site.

11.4.3. Contractor shall protect and preserve established benchmarks and monuments and shall make no changes in locations without the prior written approval of District. Contractor shall replace any benchmarks or monuments that are lost or destroyed subsequent to proper notification of District and with District's approval.

11.5. Utilities for Construction

Utilities necessary to complete the Work and to completely perform all of the Contractors' obligations shall be obtained by the Contractor without adjustment of the Contract Price. The Contractor shall furnish and install necessary or appropriate temporary distributions of utilities, including utilities furnished by the District. Any such temporary distributions shall be removed by the Contractor upon completion of the Work. The costs of all such utility services, including the installation and removal of temporary distributions thereof, shall be borne by the Contractor and included in the Contract Price. Also refer to other utility requirements as indicated in the Specifications.

11.6. Sanitary Facilities

At all times during Work at the Site, the Contractor shall obtain and maintain temporary sanitary facilities in conformity with applicable law, rule or regulation. The Contractor shall maintain temporary sanitary facilities in a neat and clean manner with sufficient toilet room supplies. Personnel engaged in the Work are not permitted to use toilet facilities at the Site. Also refer to other Sanitary facility requirements as indicated in the Specifications.

11.7. Surveys

Contractor shall provide surveys done by a California-licensed civil engineer surveyor to determine locations of construction, grading, and site work as required to perform the Work.

11.8. Regional Notification Center

Contractor, except in an emergency, shall contact the appropriate regional notification center at least two (2) days prior to commencing any excavation if the excavation will be conducted in an area or in a private easement that is known, or reasonably should be known, to contain subsurface installations other than the underground facilities owned or operated by the District, and obtain an inquiry identification number from that notification center. No excavation shall be commenced and/or carried out by the Contractor

unless an inquiry identification number has been assigned to the Contractor or any Subcontractor and the Contractor has given the District the identification number. Any damages arising from Contractor's failure to make appropriate notification shall be at the sole risk and expense of the Contractor. Any delays caused by failure to make appropriate notification shall be at the sole risk of the Contractor and shall not be considered for an extension of the Contract time.

11.9. Existing Utility Lines

11.9.1. Pursuant to Government Code section 4215, District assumes the responsibility for removal, relocation, and protection of main or trunk utility lines and facilities located on the construction Site at the time of commencement of construction under the Contract with respect to any such utility facilities that are not identified in the Plans and Specifications. Contractor shall not be assessed for liquidated damages for delay in completion of the Project caused by failure of District or the owner of a utility to provide for removal or relocation of such utility facilities.

11.9.2. Locations of existing utilities provided by District shall not be considered exact, but approximate within reasonable margin and shall not relieve Contractor of responsibilities to exercise reasonable care nor costs of repair due to Contractor's failure to do so. District shall compensate Contractor for the costs of locating, repairing damage not due to the failure of Contractor to exercise reasonable care, and removing or relocating such utility facilities not indicated in the Plans and Specifications with reasonable accuracy, and for equipment necessarily idle during such work.

11.9.3. No provision herein shall be construed to preclude assessment against Contractor for any other delays in completion of the Work. Nothing in this Article shall be deemed to require District to indicate the presence of existing service laterals, appurtenances, or other utility lines, within the exception of main or trunk utility lines, whenever the presence of these utilities on the Site can be inferred from the presence of other visible facilities, such as buildings, meter junction boxes, on or adjacent to the Site.

11.9.4. If Contractor, while performing Work, discovers utility facilities not identified by District in Contract Plans and Specifications, Contractor shall immediately, but in no case longer than two (2) Business Days, notify the District and the utility in writing. The cost of repair for damage to above-mentioned visible facilities without prior written notification to the District shall be borne by the Contractor.

11.10. Notification

Contractor understands, acknowledges and agrees that the purpose for prompt notification to the District pursuant to these provisions is to allow the District to investigate the condition(s) so that the District shall have the opportunity to decide how the District desires to proceed as a result of the condition(s). Accordingly, failure of Contractor to promptly notify the District in writing, pursuant to the applicable provisions of these General Conditions, shall constitute Contractor's waiver of any claim for damages or delay incurred as a result of the condition(s).

11.11. Hazardous Materials

Contractor shall comply with all provisions and requirements of the Contract Documents related to hazardous materials including, without limitation, certifications related to hazardous materials in the document entitled Certifications to be Completed by Contractor.

11.12. No Signs

Neither the Contractor nor any other person or entity shall display any signs not required by law or the Contract Documents at the Site, fences trailers, offices, or elsewhere on the Site without specific prior written approval of the District.

12. TRENCHES

12.1. Trenches Greater Than Five Feet

Pursuant to Labor Code section 6705, if the Contract Price exceeds \$25,000 and involves the excavation of any trench or trenches five (5) feet or more in depth, the Contractor shall, in advance of excavation, promptly submit to the District and/or a registered civil or structural engineer employed by the District or Architect, a detailed plan showing the design of shoring for protection from the hazard of caving ground during the excavation of such trench or trenches.

12.2. Excavation Safety

If such plan varies from the Shoring System Standards established by the Construction Safety Orders, the plan shall be prepared by a registered civil or structural engineer, but in no case shall such plan be less effective than that required by the Construction Safety Orders. No excavation of such trench or trenches shall be commenced until said plan has been accepted by the District or by the person to whom authority to accept has been delegated by the District.

12.3. No Tort Liability of District

Pursuant to Labor Code section 6705, nothing in this Article shall impose tort liability upon the District or any of its employees.

12.4. No Excavation without Permits

The Contractor shall not commence any excavation Work until it has secured all necessary permits including the required CAL OSHA excavation/shoring permit. Any permits shall be prominently displayed on the Site prior to the commencement of any excavation.

12.5. Discovery of Hazardous Waste, Unusual Conditions and/or Unforeseen Conditions

12.5.1. Pursuant to Public Contract Code section 7104, if the Work involves digging trenches or other excavations that extend deeper than four (4) feet below the surface, the Contractor shall immediately, but in no case longer than two (2) Business Days, and before the following conditions are disturbed, notify the District, in writing, of any:

12.5.1.1. Material that the Contractor believes may be material that is hazardous waste, as defined in section 25117 of the Health and Safety Code, and requires removal to a Class I, Class II, or Class III disposal site in accordance with provisions of existing law.

12.5.1.2. Subsurface or latent physical conditions at the Site differing from those indicated.

12.5.1.3. Unknown physical conditions at the Site of any unusual nature, different materially from those ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract.

12.5.2. The District shall promptly investigate the conditions, and if it finds that the conditions do materially so differ, or do involve hazardous waste, and cause a decrease or increase in the Contractor's cost of, or the time required for, performance of any part of the Work, shall issue a Change Order under the procedures described herein.

12.5.3. In the event that a dispute arises between District and the Contractor whether the conditions materially differ, or involve hazardous waste, or cause a decrease or increase in the Contractor's cost of,

or time required for, performance of any part of the Work, the Contractor shall not be excused from any scheduled Completion date provided for by the Contract, but shall proceed with all work to be performed under the Contract. The Contractor shall retain any and all rights provided by the Contract or by law that pertain to the resolution of disputes and protests, which include the requirement that Contractor complies with the notice and PCO provisions of the Contract Documents. Contractor's failure to submit a proposed change order pursuant to the terms of the Contract Documents shall be deemed a waiver of Contractor's right to an adjustment of the Contract Price of Contract Time.

13. INSURANCE AND BONDS

13.1. Insurance

Unless different provisions and/or limits are indicated in the Special Conditions, all insurance required of Contractor and/or its Subcontractor(s) shall be in the amounts indicated herein and include the provisions set forth herein.

13.1.1. Commercial General Liability and Automobile Liability Insurance

13.1.1.1. Contractor shall procure and maintain, during the life of the Contract, Commercial General Liability Insurance and Automobile Liability Insurance that shall protect Contractor, District, State, Construction Manager(s), Project Inspector(s), and Architect(s) from all claims for bodily injury, property damage, personal injury, death, advertising injury, and medical payments arising from operations under the Contract. This coverage shall be provided in a form at least as broad as the Insurance Services Office (ISO) standard form. Contractor shall ensure that Products Liability and Completed Operations coverage, Fire Damage Liability, and any Auto including owned, non-owned, and hired, are included within the above policies and at the required limits, or Contractor shall procure and maintain these coverages separately.

13.1.1.2. Contractor's deductible or self-insured retention for its Commercial General Liability Insurance policy shall not exceed \$25,000 unless approved in writing by District.

13.1.2. Umbrella Liability Insurance

13.1.2.1. Contractor shall procure and maintain, during the life of the Contract, an Excess Liability and/or Umbrella Liability Insurance Policy. Any Umbrella Liability Insurance Policy shall protect Contractor, District, State, Construction Manager(s), Program Manager(s), and Architect(s) in the amounts indicated herein, and shall comply with all requirements for Commercial General Liability and Automobile Liability, Employers' Liability Insurance, and Sexual Molestation and Abuse Liability. This coverage shall be provided in a form at least as broad as the Insurance Services Office (ISO) standard form.

13.1.2.2. There shall be no gap between the per occurrence amount of any underlying policy and the start of the coverage under the Umbrella Liability Insurance Policy.

13.1.2.3. Whether this Excess Liability and/or Umbrella Liability Insurance Policy is written on a "follow form" or "stand alone" form, the coverages shall equal or greater than the Contractor's Commercial General Liability and Automobile Liability, Employers' Liability Insurance, and Sexual Molestation and Abuse Liability with no exclusions that reduce or eliminate coverage items.

13.1.3. Subcontractor(s): Contractor shall require its Subcontractor(s), if any, to procure and maintain Commercial General Liability Insurance, Automobile Liability Insurance, and Umbrella Liability Insurance with minimum limits equal to at least fifty percent (50%) of the amounts required of the Contractor.

13.1.4. Workers' Compensation and Employers' Liability Insurance

13.1.4.1. In accordance with provisions of section 3700 of the California Labor Code, the Contractor and every Subcontractor shall be required to secure the payment of compensation to its employees.

13.1.4.2. Contractor shall procure and maintain, during the life of this Contract, Workers' Compensation Insurance and Employers' Liability Insurance for all of its employees engaged in Work under the Contract, on/or at the Site of the Project. This coverage shall cover, at a minimum, medical and surgical treatment, disability benefits, rehabilitation therapy, and survivors' death benefits. Contractor shall require its Subcontractor(s), if any, to procure and maintain Workers' Compensation Insurance and Employers' Liability Insurance for all employees of Subcontractor(s). Any class of employee or employees not covered by a Subcontractor's insurance shall be covered by Contractor's insurance. If any class of employee or employees engaged in Work under the Contract, on or at the Site of the Project, are not protected under the Workers' Compensation Insurance, Contractor shall provide, or shall cause a Subcontractor to provide, adequate insurance coverage for the protection of any employee(s) not otherwise protected before any of those employee(s) commence work.

13.1.5. Sexual Molestation and Abuse Liability Insurance. Contractor shall procure and maintain, during the life of this Contract, sexual molestation and abuse insurance. Contractor shall require its Subcontractor(s), if any, to procure and maintain sexual molestation and abuse insurance for all employees of Subcontractor(s). Any class of employee or employees not covered by a Subcontractor's insurance shall be covered by Contractor's insurance. If any class of employee or employees engaged in Work under the Contract, on or at the Site of the Project, are not covered under the sexual molestation and abuse insurance, Contractor shall provide, or shall cause a Subcontractor to provide, adequate insurance coverage to cover any employee(s) not otherwise covered before any of those employee(s) commence work.

13.1.6. Builder's Risk Insurance: Builder's Risk "All Risk" Insurance (NO Earthquake or Flood).

13.1.6.1. Contractor (Builder) shall procure and maintain, during the life of this Contract, Builder's Risk (Course of Construction), or similar first party property coverage acceptable to the District, issued on a replacement cost value basis. The cost shall be consistent with the total replacement cost of all insurable Work included within the Contract Documents.

13.1.6.2. Coverage is to insure against all risks of accidental physical loss and shall include without limitation the perils of vandalism and/or malicious mischief (both without any limitation regarding vacancy or occupancy), sprinkler leakage, water damage, mold, civil authority, theft, sonic disturbance, collapse, wind, fire, war, terrorism, lightning, smoke, and rioting. Coverage shall include debris removal, demolition, increased costs due to enforcement of all applicable ordinances and/or laws in the repair and replacement of damaged and undamaged portions of the property, and reasonable costs for the Architect's and engineering services and expenses required as a result of any insured loss upon the Work and Project, including completed Work and Work in progress, to the full insurable value thereof.

13.1.6.3. Coverage shall be maintained until final payment has been made as provided under the Contract or until no person or entity other than the District has an insurable interest in the property to be covered, whichever is later. This insurance shall cover as insureds the District, Contractor, all Subcontractors of every tier on the Project, and all vendors and suppliers. Coverage must also be maintained for any materials stored offsite that will be incorporated into the Project.

13.1.6.4. The deductible for this insurance shall be paid by Contractor.

13.1.6.5. Contractor must review the Special Conditions to confirm the scope of this requirement and if the District has modified this provision.

13.1.7. Proof of Carriage of Insurance and Other Requirements: Endorsements and Certificates

13.1.7.1. Contractor shall not commence Work nor shall it allow any Subcontractor to commence Work under the Contract, until Contractor and its Subcontractor(s) have procured all required insurance and Contractor has delivered in duplicate to the District complete endorsements (or entire insurance policies) and certificates indicating the required coverages have been obtained, and the District has approved these documents.

13.1.7.2. Endorsements, certificates, and insurance policies shall include the following:

13.1.7.2.1. A clause stating:

13.1.7.2.1.1. “This policy shall not be amended, canceled or modified and the coverage amounts shall not be reduced until notice has been mailed to District, Architect, and Construction Manager stating date of amendment, modification, cancellation or reduction. Date of amendment, modification, cancellation or reduction may not be less than thirty (30) days after date of mailing notice.”

13.1.7.2.1.2. In lieu of receiving an endorsement with this clause, the District may, at its sole discretion, accept written notification from Contractor and its insurer to the District of any amendments, modifications, cancellations or reduction in coverage, not less than thirty (30) days prior to such coverage changes occur.

13.1.7.2.2. Language stating in particular those insured, extent of insurance, location and operation to which insurance applies, expiration date, to whom cancellation and reduction notice will be sent, and length of notice period.

13.1.7.3. All endorsements, certificates and insurance policies shall state that District, its trustees, employees and agents, the State of California, Construction Manager(s), Program Manager(s), Inspector(s) and Architect(s) are named additional insureds under all policies except Workers’ Compensation Insurance and Employers’ Liability Insurance.

13.1.7.4. Contractor’s and Subcontractors’ insurance policy(s) shall be primary and non-contributory to any insurance or self-insurance maintained by District, its trustees, employees and/or agents, the State of California, Construction Manager(s), Program Manager(s), Inspector(s), and/or Architect(s).

13.1.7.5. All endorsements shall waive any right to subrogation against any of the named additional insureds.

13.1.7.6. All policies shall be written on an occurrence form.

13.1.7.7. Unless otherwise stated in the Special Conditions, all of Contractor’s insurance shall be placed with insurers **ADMITTED** in California with a current A.M. Best's rating of no less than A— or A:VII.

13.1.7.8. The insurance requirements set forth herein shall in no way limit the Contractor’s liability arising out or relating to the performance of the Work or related activities.

13.1.7.9. Failure of Contractor and/or its Subcontractor(s) to comply with the insurance requirements herein shall be deemed a material breach of the Agreement.

13.1.8. Insurance Policy Limits

Unless different limits are indicated in the Special Conditions, the limits of insurance shall not be less than the following amounts:

Commercial General Liability	Includes: Bodily Injury, Property Damage, Personal & Advertising Injury, Product Liability and Completed Operations	\$2,000,000 each occurrence; \$4,000,000 general aggregate
Automobile Liability – <u>Any</u> Auto	Combined Single Limit	\$1,000,000 per occurrence
Excess Liability (Umbrella)		\$1,000,000 per occurrence; \$6,000,000 aggregate
Workers Compensation		Statutory limits pursuant to State law
Employers' Liability		\$2,000,000 each incident, each disease; \$2,000,000 policy limit
Sexual Abuse / Molestation		\$1,000,000 each incident; \$2,000,000 policy limit
Builder's Risk (Course of Construction)		Issued for the value and scope of Work indicated herein.
Property of Others	Combined Single Limit General Aggregate	Issued for the value and scope of Work stored off-site.

13.2. Contract Security – Bonds

13.2.1. Contractor shall furnish two surety bonds issued by a California admitted surety insurer as follows:

13.2.1.1. Performance Bond: A bond in an amount at least equal to one hundred percent (100%) of Contract Price as security for faithful performance of this Contract.

13.2.1.2. Payment Bond: A bond in an amount at least equal to one hundred percent (100%) of the Contract Price as security for payment of persons performing labor and/or furnishing materials in connection with the Contract.

13.2.2. Cost of bonds shall be included in the Bid and Contract Price.

13.2.3. All bonds related to the Project shall be in the forms set forth in the Contract Documents and shall comply with all requirements of the Contract Documents, including, without limitation, the bond forms.

14. WARRANTY/GUARANTEE/INDEMNITY

14.1. Warranty/Guarantee

14.1.1. Contractor shall obtain and preserve for the benefit of the District, manufacturer's warranties on materials, fixtures, and equipment incorporated into the Work. All manufacturer, material, and fixture warranties shall commence at Project Completion. Contractor shall ensure that all warranties are maintained for the benefit of the District, regardless of the who the manufacturer is, who the installing Subcontractor was, if any, etc. While the District will fully expect the Contractor to manage all warranty

work through all applicable warranty periods, the District must have that same ability if the Contractor fails to perform its warranty obligations as required.

14.1.2. In addition to guarantees required elsewhere, Contractor shall, and hereby does guarantee and warrant all Work against all defects for a period of **ONE (1)** year after the later of the following dates:

14.1.2.1. The date of completion as defined in Public Contract Code section 7107, subdivision (c),

14.1.2.2. The commissioning date for the Project, if any.

14.1.3. At the District's sole option, Contractor shall repair or replace any and all of that Work, together with any other Work that may be displaced in so doing, that may prove defective in workmanship and/or materials within a **ONE (1)** year period from date of Completion as defined above without expense whatsoever to District. In the event of failure of Contractor and/or Surety to commence and pursue with diligence said replacements or repairs within **TEN (10)** days after being notified in writing, Contractor and Surety hereby acknowledge and agree that District is authorized to proceed to have defects repaired and made good at expense of Contractor and/or Surety who hereby agree to pay costs and charges therefore immediately on demand.

14.1.4. If, in the opinion of District, defective work creates a dangerous condition or requires immediate correction or attention to prevent further loss to District or to prevent interruption of operations of District, District will attempt to give the notice required above. If Contractor or Surety cannot be contacted or neither complies with District's request for correction within a reasonable time as determined by District, District may, notwithstanding the above provision, proceed to make all corrections and/or provide attentions the District believes are necessary. The costs of correction or attention shall be charged against Contractor and Surety of the guarantees provided in this Article or elsewhere in the Contract Documents.

14.1.5. The above provisions do not in any way limit the guarantees on any items for which a longer guarantee is specified or on any items for which a manufacturer gives a guarantee for a longer period. Contractor shall furnish to District all appropriate guarantee or warranty certificates as indicated in the Specifications or upon request by District.

14.1.6. Nothing herein shall limit any other rights or remedies available to District.

14.2. Indemnity

14.2.1. To the furthest extent permitted by California law, Contractor shall indemnify, defend with legal counsel reasonably acceptable to the District, keep and hold harmless the District and its consultants, the Architect and its consultants, the Construction Manager and its consultants, separate contractors, and their respective board members, officers, representatives, contractors, agents, and employees, in both individual and official capacities ("Indemnitees"), against all suits, claims, damages, losses, and expenses, including but not limited to attorney's fees, caused by, arising out of, resulting from, or incidental to, the performance of the Work by Contractor, its Subcontractors, vendors, or suppliers, including, without limitation, any such suit, claim, damage, loss, or expense attributable to, without limitation, bodily injury, sickness, disease, death, alleged patent violation or copyright infringement, or to injury to or destruction of tangible property (including damage to the Work itself) including the loss of use resulting therefrom, except to the extent caused by the sole negligence, active negligence, or willful misconduct of the Indemnitees, and/or to any extent that would render these provisions void or unenforceable. This agreement and obligation of Contractor shall not be construed to negate, abridge, or otherwise reduce any right or obligation of indemnity that would otherwise exist as to any party or person described herein. This indemnification, defense, and hold harmless obligation includes, without limitation:

14.2.1.1. Any failure or alleged failure by Contractor to comply with any provision of law, any failure or alleged failure to timely and properly fulfill all of its obligations under the Contract Documents in strict accordance with their terms, and without limitation, any stop payment notice actions or liens, including liens by the California Department of Labor Standards Enforcement.

14.2.1.2. Any claim arising (including bid protests) from any errors or mistakes in Contractor's bid documents provided to Subcontractors.

14.2.2. Contractor shall give prompt notice to the District in the event of any injury (including death), loss, or damage included herein. Without limitation of the provisions herein, if Contractor's agreement to indemnify, defend, and hold harmless the Indemnitees as provided herein against liability for damage arising out of bodily injury to persons or damage to property caused by or resulting from the negligence of any of the Indemnitees shall to any extent be or be determined to be void or unenforceable, it is the intention of the parties that these circumstances shall not otherwise affect the validity or enforceability of Contractor's agreement to indemnify, defend, and hold harmless the rest of the Indemnitees, as provided herein, and in the case of any such suits, claims, damages, losses, or expenses caused in part by the default, negligence, or act or omission of Contractor, any Subcontractor, anyone directly or indirectly employed by any of them or anyone for whose acts any of them may be liable, and in part by any of the Indemnitees, Contractor shall be and remain fully liable on its agreements and obligations herein to the full extent permitted by law.

14.2.3. In any and all claims against any of the Indemnitees by any employee of Contractor, any Subcontractor, anyone directly or indirectly employed by any of them or anyone for whose acts any of them may be liable, Contractor's indemnification obligation herein shall not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Contractor or any Subcontractor under workers' compensation acts, disability benefit acts, or other employee benefit acts.

14.2.4. The defense and indemnification obligations hereunder shall survive the Completion of Work, including the warranty/guarantee period, and/or the termination of the Agreement.

15. TIME

15.1. Notice to Proceed

District may issue a Notice to Proceed as indicated in the Instructions to Bidders or will otherwise instruct the Contractor to begin performing the Work of the Project.

15.2. Hours of Work

Work shall be performed during regular working hours as permitted by the appropriate governmental agency except that in the event of an emergency, or when required to complete the Work in accordance with job progress, Work may be performed outside of regular working hours with the advance written consent of the District and approval of any required governmental agencies. Contractor and Subcontractors shall continuously furnish sufficient forces to ensure the performance of the Work in accordance with the Construction Schedule. In no event will the District be responsible for the costs of Work performed outside of regular working hours, including, without limitation, overtime or weekend Work, unless expressly agreed to by the District in writing and approved in a Change Order.

15.3. Progress and Completion

15.3.1. Time of the Essence

Time limits stated in the Contract Documents are of the essence to the Contract. By executing the Agreement, Contractor confirms that the Contract Time is a reasonable period for performing the Work.

15.3.2. No Commencement Without Insurance

15.3.2.1. Contractor shall not commence operations on the Project or elsewhere prior to the effective date of insurance and bonds. The date of commencement of the Work shall not be changed by the effective date of such insurance. If Contractor commences Work without insurance and bonds, all Work is performed at Contractor's peril and shall not be compensable until and unless Contractor secures bonds and insurance pursuant to the terms of the Contract Documents and subject to District's claim for damages.

15.4. Schedule

Contractor shall provide to District, Construction Manager, and Architect a schedule in conformance with the Contract Documents and as required in the Notice to Proceed and the Contractor's Submittals and Schedules section of these General Conditions.

15.5. Expeditious Completion

The Contractor shall proceed expeditiously with adequate forces and shall achieve Completion within the Contract Time.

16. EXTENSIONS OF TIME – LIQUIDATED DAMAGES

16.1. Contractor's Notice of Delay

16.1.1. In addition to the requirements indicated in this subsection, Contractor shall submit any request for an adjustment of the Contract Price or the Contract Time through the Change Order provisions in these General Conditions.

16.1.2. Contractor shall, within **FIVE (5)** calendar days of any delay impacting the critical path in completing the Work, notify District in writing of the causes of the delay including documentation and facts explaining the delay.

16.1.3. Any request by Contractor for an adjustment of the Contract Price or the Contract Time for a delay shall be submitted in accordance with the provisions in the Contract Documents governing changes in Work. When requesting time, requests must be submitted with full justification and documentation. Such justification must be based on the official Construction Schedule as updated at the time of occurrence of the delay or execution of Work related to any changes to the Scope of Work.

16.1.4. Any claim for delay must include the following information as support, without limitation:

16.1.4.1. Duration. The duration of the activity relating to the changes in the Work and the resources (manpower, equipment, material, etc.) required to perform the activities within the stated duration.

16.1.4.2. Schedule Analysis. A detailed schedule analysis articulating the cause of any delay and explaining the delay's impact to critical path and each activity of the Project. This analysis may be in the form of a time impact analysis. The time impact analysis shall provide all documentation and justification necessary to substantiate the requested extension. All supporting documentation shall be based on the then current Monthly Progress Schedule.

16.1.4.3. Logical Ties / Fragnets. Specific logical ties to the Contract Schedule for the proposed changes and/or delay showing the activity/activities in the Construction Schedule that are affected by the change and/or delay. (A portion of any delay of seven (7) days or more must be provided.) Include a “fragnet” analysis for the portion of the schedule and the activities the Contractor contends are impacted by the delay.

16.1.4.4. Updated Construction Schedule. A recovery or updated Construction Schedule must be submitted.

16.1.5. District shall review the facts and extent of any noticed delay and may grant Contract Time extension(s) of time for completing Work when, in the District’s judgment, the findings of fact justify an extension.

16.1.6. Extension(s) of time shall apply only to that portion of Work affected by delay, and shall not apply to other portions of Work not so affected.

16.1.7. An extension of time may only be granted if Contractor has timely submitted the updated Construction Schedule as required herein.

16.1.8. Following submission of a notice of delay, the District may determine whether the delay is to be considered:

16.1.8.1. Excusable and Compensable, Excusable and Non-Compensable, or Unexcused;

16.1.8.2. How long the delay continues; and

16.1.8.3. To what extent the prosecution and Completion of the Work might be delayed thereby.

16.1.9. Contractor’s failure to request adjustment(s) of the Contract Time in strict conformity with applicable provisions of the Contract Documents shall be deemed Contractor’s waiver of its right to assert a claim for a delay.

16.1.10. Limitations Upon Adjustment of Contract Time on Account of Delays. Any adjustment of the Contract Time on account of an Excusable Delay or a Compensable Delay shall be limited as set forth herein. No adjustment of the Contract Time shall be made on account of any Excusable Delays or Compensable Delays unless those delay(s) actually and directly impact Work or Work activities on the critical path of the then current and updated approved Construction Schedule as of the date on which a delay first occurs. The District shall not be deemed in breach of, or otherwise in default of any obligation hereunder, if the District shall deny a request by the Contractor for an adjustment of the Contract Time for any delay that does not actually and directly impact Work on the then current and updated approved Construction Schedule. In submitting a request for an adjustment of Contract Time, and as a condition precedent to the District’s review of that request, Contractor shall insert into the then current and updated approved Construction Schedule a “fragnet” analysis representing the event that Contractor claims to result in delay to the critical path as depicted in the updated approved Construction Schedule. If an Excusable Delay and a Compensable Delay occur concurrently, the maximum extension of the Contract Time shall be the number of days from the commencement of the first delay to the cessation of the delay that ends last. If an Unexcused Delay occurs concurrently with either an Excusable Delay or a Compensable Delay, the maximum extension of the Contract Time shall be the number of days, if any, which the Excusable Delay or the Compensable Delay exceeds the period of time of the Unexcused Delay.

16.2. Excusable and Compensable Delay(s)

16.2.1. Contractor is not entitled to additional compensation for any delay, even a delay caused by

Adverse Weather or an Excusable Delay, unless all of the following conditions are met (“**Excusable and Compensable Delay**”):

- 16.2.1.1.** The District is responsible for the delay;
- 16.2.1.2.** The delay is unreasonable under the circumstances involved and impacts the critical path of the Work and extends the most current Contract Completion date;
- 16.2.1.3.** The delay was not within the contemplation of District and Contractor;
- 16.2.1.4.** Contractor complies with the Change Order procedures, and if necessary, the Claims procedures of the Contract Documents;
- 16.2.1.5.** The delay could not have been avoided or mitigated by the Contractor's care, prudence, foresight, and diligence;
- 16.2.1.6.** The delay extends the most current Contract Completion date; and
- 16.2.1.7.** The delay is not concurrent with a Contractor-caused delay or other type of Excusable Delay.

16.2.2. In accordance with California Public Contract Code section 7102, if the Contractor’s progress is delayed by the events described in the preceding subsection, Contractor shall not be precluded from the recovery of damages directly and proximately resulting therefrom. In that event, Contractor’s damages, if any, shall be limited to direct, actual and unavoidable additional costs of labor, materials or construction equipment directly resulting from that delay, and shall exclude special, indirect or consequential damages. In no event shall Contractor seek costs or damages for delays, interruptions, hindrances or disruptions to the Work for on-Site or off-Site costs or damages based upon formulas, e.g. Eichleay or other formula. Except as expressly provided for herein, Contractor shall not have any other claim, demand or right to adjustment of the Contract Price arising out of delay, interruption, hindrance or disruption to the progress of the Work. Adjustments to the Contract Price and the Contract Time, if any, on account of Changes to the Work or Suspension of the Work shall be governed by the applicable provisions of the Contract Documents, including without limitation, the “Changes in the Work” section and the percentages in the “Format for Proposed Change” section of these General Conditions.

16.3. Excusable and Non-Compensable Delay(s)

16.3.1. An "Excusable Delay" shall mean an interruption of the Work beyond the reasonable control of the Contractor and that:

- 16.3.1.1.** Could have not been avoided by the Contractor exercising care, prudence, foresight, and diligence, and
- 16.3.1.2.** Actually extended the most current Project Completion date.

16.3.2. The Contractor may be entitled to an extension of the Project Completion date if there is an Excusable Delay, but the Contractor shall not be entitled to additional compensation for an Excusable Delay.

16.3.3. Force Majeure.

- 16.3.3.1.** Excusable Delays are limited to interruptions that satisfy the above requirements and that are acts of God; acts of a public enemy; fires; floods; windstorms; tornadoes; earthquakes; wars; riots; insurrections; epidemics; pandemics; quarantine

restrictions; strikes; lockouts; fuel shortages; freight embargoes; and Adverse Weather that satisfies the requirements herein ("**Force Majeure Events**").

16.3.3.2. If an Infectious Disease impacts the progress of the Work and Contractor demonstrates that the event satisfies the conditions of the Contract Documents for an adjustment to the Contract Time, it will be considered a Force Majeure Event.

16.3.3.3. In addition to any other requirement of the Contract Documents, Contractor shall not be entitled to any adjustment to the Contract Time unless Contractor submits a PCO and the District has issued a Change Order pursuant to the "Changes in the Work" provisions herein. If the Parties cannot in good faith and reasonably agree to an increase in the Contract Time, the Parties agree that dispute will be resolved pursuant to the Claims Resolution Process herein.

16.3.4. Contractor is aware that governmental agencies and utilities, including, without limitation, the Division of the State Architect, the Department of General Services, gas companies, electrical utility companies, water districts, and other agencies may have to approve Contractor-prepared drawings or approve a proposed installation. Contractor shall include in its bid, time for possible review of its drawings and for reasonable delays and damages that may be caused by such agencies. Contractor is not entitled to make a claim for damages or delays or an Excusable Delay arising from the review of Contractor's drawings or other approvals from the Division of the State Architect, the Department of General Services, gas companies, electrical utility companies, water districts, and other agencies.

16.3.5. Neither the financial resources of the Contractor or any person or entity directly or indirectly engaged by the Contractor in performance of any portion of the Work shall be deemed conditions beyond the control of the Contractor. If an event of Excusable Delay occurs, the Contract Time shall be subject to adjustment hereunder only if the Contractor establishes: (i) full compliance with all applicable provisions of the Contract Documents relative to the method, manner and time for Contractor's notice and request for adjustment of the Contract Time; (ii) that the event(s) forming the basis for Contractor's request to adjust the Contract Time are outside the reasonable control and without any fault or neglect of the Contractor or any person or entity directly or indirectly engaged by Contractor in performance of any portion of the Work; and (iii) that the event(s) forming the basis for Contractor's request to adjust the Contract Time directly and adversely impacted the critical path of the Work as indicated in the approved Construction Schedule or the most recent updated approved Construction Schedule relative to the date(s) of the claimed event(s) of Excusable Delay.

16.3.6. Computation of Time / Adverse Weather

16.3.6.1. The Contractor will only be allowed a time extension for Adverse Weather conditions if requested by Contractor within five (5) calendar days of the Adverse Weather event, and only if **all** of the following conditions are met – thereby making the resulting delay an Excusable Delay.

16.3.6.1.1. The weather conditions constitute Adverse Weather, as defined herein and further specified in the Special Conditions;

16.3.6.1.2. Contractor can verify that the Adverse Weather caused delays in excess of five (5) hours of the indicated labor required to complete the scheduled tasks of Work on the day affected by the Adverse Weather;

16.3.6.1.3. The Contractor's crew is dismissed as a result of the Adverse Weather; and

16.3.6.1.4. The number of days of delay exceed those indicated in the Special Conditions.

16.3.6.2. A day-for-day extension will only be allowed for those days in excess of those indicated in the Special Conditions and only if the tasks of Work on the day affected by the Adverse Weather were tasks required to be performed on that day to maintain the critical path of the Construction Schedule.

16.3.6.3. The Contractor shall work seven (7) days per week, if necessary, irrespective of inclement weather, to maintain access and the Construction Schedule, and to protect the Work under construction from the effects of Adverse Weather, all at no further cost to the District.

16.3.6.4. The Contract Time has been determined with consideration given to the average climate weather conditions prevailing in the County in which the Project is located.

16.4. Unexcused Delay(s) – Liquidated Damages

16.4.1. Unexcused delays refer to any delay to the progress of the Work caused by events or factors other than those specifically identified in the “Excusable and Compensable Delay(s)” or the “Excusable and Non-Compensable Delay(s)” sections above (“**Unexcused Delays**”). Neither the Contract Price nor the Contract Time shall be adjusted on account of Unexcused Delays.

16.4.2. Contractor and District hereby agree that the exact amount of damages for failure to complete the Work within the time specified is extremely difficult or impossible to determine. If the Work is not completed within the time specified in the Contract Documents, it is understood that the District will suffer damage. It being impractical and unfeasible to determine the amount of actual damage, it is agreed the Contractor shall forfeit and pay to District as fixed and liquidated damages, and not as a penalty, the amount set forth in the Agreement for each calendar day of delay in Completion. Contractor and its Surety shall be liable for the amount thereof pursuant to Government Code section 53069.85.

16.4.3. Contractor shall not forfeit or pay liquidated damages for an Excusable Delay or an Excusable and Compensable Delay.

17. CHANGES IN THE WORK

17.1. No Changes Without Authorization

17.1.1. There shall be no change whatsoever in the Drawings, Specifications, or in the Work without an executed Change Order, a written Unilateral Change Order, or a written Force Account Directive authorized by the District as herein provided. District shall not be liable for the cost of any extra work, any changes to the Contract Time, or any substitutions, changes, additions, omissions, or deviations from the Drawings and Specifications unless the District's governing board has authorized the same and the cost thereof has been approved in writing by an executed Change Order, a written Unilateral Change Order, or a written Force Account Directive.

17.1.2. Verbal Order of Change in the Work. Any verbal order, direction, instruction, interpretation, or determination from the District, the Project Inspector or the Architect which in the opinion of the Contractor causes any change to the scope of the Work, or otherwise requires an adjustment to the Contract Price or the Contract Time, shall be treated as a Change only if the Contractor gives the Architect written notice within three (3) Business Days of the order, directions, instructions, interpretation or determination and prior to acting in accordance therewith. Time is of the essence in Contractor's written notice pursuant to the preceding sentence so that the District can promptly investigate and consider alternative measures to address the order, direction, instruction, interpretation or determination giving rise to Contractor's notice. Accordingly, Contractor acknowledges that its failure, for any reason, to give written notice within three (3) Business Days of any verbal order, direction, instruction, interpretation or determination shall be deemed Contractor's waiver of any right to assert or claim any entitlement to an adjustment of the Contract Time or the Contract Price on account of that verbal order, direction,

instruction, interpretation or determination. The written notice shall state the date, circumstances, extent of adjustment to the Contract Price or the Contract Time, if any, requested, and the source of the verbal order, directions, instructions, interpretation or determination that the Contractor regards as a Change. Unless the Contractor acts in strict accordance with this procedure, any verbal order, direction, instruction, interpretation or determination shall not be treated as a Change and the Contractor hereby waives any claim for any adjustment to the Contract Price or the Contract Time on account thereof.

17.1.3. The Surety, in executing and providing the Performance Bond and the Payment Bond, shall be deemed to have expressly agreed to any change to the Contract and to any extension of time made by reason thereof.

17.1.4. No extension of time for performance of the Work shall be allowed hereunder unless claim for such extension is made at the time changes in the Work are ordered, and such time duly adjusted in writing in the Change Order, Unilateral Change Order, or Force Account Directive. The provisions of the Contract Documents shall apply to all such changes, additions, and omissions with the same effect as if originally embodied in the Drawings and Specifications.

17.1.5. Contractor shall perform immediately all work that has been authorized by a fully executed Change Order, Unilateral Change Order, or Force Account Directive. Contractor shall be fully responsible for any and all delays and/or expenses caused by Contractor's failure to expeditiously perform this Work and Contractor's failure or refusal to so proceed with that Work may be deemed to be Contractor's default of a material obligation of the Contractor under the Contract Documents.

17.1.6. Should any Change Order result in an increase in the Contract Price, the cost of that Change Order shall be agreed to, in writing, in advance by Contractor and District and be subject to the monetary limitations set forth in Public Contract Code section 20118.4. In the event that Contractor proceeds with any change in Work without a Change Order executed by the District, Unilateral Change Order, or Force Account Directive, Contractor waives any claim of additional compensation or time for that additional work.

17.1.7. Contractor understands, acknowledges, and agrees that the reason for District authorization is so that District may have an opportunity to analyze the Work and decide whether the District shall proceed with the Change Order or alter the Project so that a change in Work becomes unnecessary.

17.1.8. In an emergency affecting safety of life or of work or of adjoining property, Contractor, without special instruction or authorization, shall act, at its discretion, to prevent all threatened loss or injury. Any compensation or time claimed by Contractor on account of emergency work shall be determined as indicated herein as a PCO.

17.2. Architect Authority

The Architect will have authority to order minor changes in the Work not involving any adjustment in the Contract Price, or an extension of the Contract Time, or a change that is inconsistent with the intent of the Contract Documents. These changes shall be effected by written Change Order, Unilateral Change Order, or by Architect's response(s) to RFI(s).

17.3. Change Orders

17.3.1. A Change Order is a written instrument prepared and issued by the District and/or the Architect and signed by the District (as authorized by the District's governing board), the Contractor, the Architect, and approved by the Project Inspector (if necessary) and DSA (if necessary), stating their agreement regarding all of the following:

17.3.1.1. A description of a change in the Work;

17.3.1.2. The amount of the adjustment in the Contract Price, if any; and

17.3.1.3. The extent of the adjustment in the Contract Time, if any.

17.3.2. If a Change Order is required to be approved by DSA, the District may call it a Construction Change Document.

17.3.3. If the District approves a Change, the District or the Architect shall provide a written Change Order to the Contractor describing the Change and setting forth the adjustment to the Contract Time and the Contract Price, if any, on account of that Change. All Change Orders shall be full payment and final settlement of all rights for direct, indirect and consequential costs, including without limitation, costs of delays or impacts related to, or arising out of, items covered and affected by the Change Order, as well as any adjustments to the Contract Time. Any demand or request for an adjustment to the Contract Time or the Contract Price relating to any Change incorporated into a Change Order not presented by the Contractor for inclusion in the Change Order shall be deemed waived. The Contractor shall execute the Change Order prepared pursuant to the foregoing. After the Change Order has been prepared and forwarded to the Contractor for execution, the Contractor shall not modify or amend the form or content of such Change Order, or any portion thereof.

17.4. Unilateral Change Orders

17.4.1. A Unilateral Change Order is a written order prepared and issued by the District, the Construction Manager, and/or the Architect and signed by the District, directing a change in the Work. The District may as provided by law, by Unilateral Change Order and without invalidating the Contract, order changes in the Work consisting of additions, deletions, or other revisions. Any dispute as to the sum of the Unilateral Change Order or timing of payment shall be resolved pursuant to the Payment provisions and the Claims provisions herein. **A Unilateral Change Order is NOT a Construction Change Document (which is defined above as a Change Order that DSA must approve).**

17.4.2. The District may issue a Unilateral Change Order in the absence of agreement on the terms of a Change Order.

17.5. Force Account Directives

17.5.1. When work, for which a definite price has not been agreed upon in advance, is to be paid for on a force account basis, all direct costs necessarily incurred and paid by the Contractor for labor, material, and equipment used in the performance of that Work, shall be subject to the approval of the District and compensation will be determined as set forth herein.

17.5.2. District will issue a Force Account Directive to proceed with the Work on a force account basis, and a not-to-exceed budget will be established by District.

17.5.3. All requirements regarding direct cost for labor, labor burden, material, equipment, and markups on direct costs for overhead and profit described in this section shall apply to Force Account Directives. However, District will only pay for actual costs verified in the field by the District or its authorized representative(s) on a daily basis.

17.5.4. Contractor shall be responsible for all cost related to the administration of Force Account Directive. The markup for overhead and profit for Contractor modifications shall be full compensation to the Contractor to administer Force Account Directive.

17.5.5. Contractor shall notify District or its authorized representative(s) at least twenty-four (24) hours prior to proceeding with any of the force account work. Furthermore, the Contractor shall notify the District when it has consumed eighty percent (80%) of the budget, and shall not exceed the budget unless

specifically authorized in writing by the District. Contractor will not be compensated for force account work in the event that Contractor fails to timely notify the District regarding the commencement of force account work, or exceeding the force account budget.

17.5.6. Contractor shall diligently proceed with the work, and on a daily basis, submit a daily force account report on a form supplied by the District no later than 5:00 p.m. each day. The report shall contain a detailed itemization of the daily labor, material, and equipment used on the force account work only. The names of the individuals performing the force account work shall be included on the daily force account reports. The type and model of equipment shall be identified and listed. District will review the information contained in the reports, and sign the reports no later than the next work day, and return a copy of the report to Contractor for its records. District will not sign, nor will Contractor receive compensation for work District cannot verify. Contractor will provide a weekly force account summary indicating the status of each Force Account Directive in terms of percent complete of the not-to-exceed budget and the estimated percent complete of the work.

17.5.7. In the event Contractor and District reach a written agreement on a set cost for the work while the work is proceeding based on a Force Account Directive, the Contractor's signed daily force account reports shall be discontinued and all previously signed reports shall be invalid.

17.6. Price Request

17.6.1. Definition of Price Request. A Price Request ("PR") is a written request prepared by the Architect or the District, requesting the Contractor to submit to the District and the Architect an estimate of the effect of a proposed change in the Work on the Contract Price and the Contract Time.

17.6.2. Scope of Price Request. A Price Request shall contain adequate information, including any necessary Drawings and Specifications, to enable Contractor to provide the cost breakdowns required herein. Contractor shall not be entitled to any additional compensation for preparing a response to a Price Request, whether ultimately accepted or not.

17.6.3. Contractor shall not consider Price Requests to be instructions either to stop work in progress or to execute the proposed change.

17.6.4. Within the time specified in Price Request after receipt of Price Request, Contractor shall submit a quotation estimating cost adjustments to the Contract Price and the Contract Time necessary to execute the change, with the following documentation and information:

17.6.4.1. Include a list of quantities of products required or eliminated and unit costs, with total amount of purchases and credits to be made. If requested, furnish survey data to substantiate quantities.

17.6.4.2. Indicate applicable taxes, delivery charges, equipment rental, and amounts of trade discounts.

17.6.4.3. Include costs of labor and supervision directly attributable to the change.

17.6.4.4. Include an updated Contractor's Construction Schedule that indicates the effect of the change, including, but not limited to, changes in activity duration, start and finish times, and activity relationship. Use available total float before requesting an extension of the Contract Time.

17.7. Proposed Change Order

17.7.1. Proposed Change Order. The Contractor may issue a Proposed Change Order ("PCO"), only as a

written request prepared by it to the District and the Architect, requesting that the District issue a Change Order based upon a proposed change to the Work.

17.7.2. Changes in Contract Price. A PCO shall include breakdowns pursuant to the provisions herein to validate any change in Contract Price and include all reasonable documentation as required herein.

17.7.3. Changes in Time. A PCO shall also include any changes in time required to complete the Project. Include an updated Contractor's Construction Schedule that indicates the effect of the change, including, but not limited to, changes in activity duration, start and finish times, and activity relationships. Use available total float before requesting an extension of the Contract Time. Any additional time requested shall not be the number of days to make the proposed change, but must be based upon the impact to the Construction Schedule as defined in the Contract Documents. If Contractor fails to request a time extension in a PCO, then the Contractor is thereafter precluded from requesting time and/or claiming a delay. If the Contractor is requesting additional time and believes that time is both Excusable and Compensable, then the Contractor must provide detailed documentation that supports its position and that addresses all the components of the "Excusable and Compensable Delay(s)" section above.

17.7.4. Unknown and/or Unforeseen Conditions. If Contractor submits a PCO requesting an increase in Contract Price and/or Contract Time that is based at least partially on Contractor's assertion that Contractor has encountered unknown and/or unforeseen condition(s) on the Project, then Contractor shall base the PCO on provable information that, beyond a reasonable doubt and to the District's satisfaction, demonstrates that the unknown and/or unforeseen condition(s) were actually unknown and/or unforeseen and that the condition(s) were reasonably unknown and/or unforeseen. If not, the District shall deny the PCO and the Contractor shall complete the Project without any increase in Contract Price and/or Contract Time based on that PCO.

17.7.5. Time to Submit PCO. Contractor shall submit its PCO within five (5) days of the date Contractor discovers, or reasonably should discover, the circumstances giving rise to the proposed change order, unless additional time to submit a proposed change order is granted in writing by the District. Time is of the essence in Contractor's written notice pursuant to the preceding sentence so that the District can promptly investigate and consider alternative measures to address the basis for the PCO. Accordingly, Contractor acknowledges that its failure, for any reason, to give written notice (with Supporting Documentation to permit the District's review and evaluation) within this time frame shall be deemed Contractor's waiver, release, discharge and relinquishment of any right to assert or claim any entitlement to an adjustment of the Contract Time or the Contract Price on account of the circumstances giving rise to the PCO.

17.7.6. COVID-19 and other Infectious Disease(s).

17.7.6.1. Contractor agrees that its bid, the Contract Price and the Contract Time are based on the Contractor's full compliance with all applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with Infectious Disease(s) (as defined herein) including COVID-19, and/or any similar virus or derivative strain at the time of Contract award. Therefore, any cost or delay associated with Infectious Disease(s), or any derivative or similar strain thereof, or any federal, state, or local order relating thereto, shall not be considered compensable unless:

17.7.6.1.1. It occurred after the date of the award of the Contract to Contractor;

17.7.6.1.2. It materially increases the Contract Price or the Contract Time; and

17.7.6.1.3. Contractor notifies the District within 10 days of notice of any a new derivative, strain, or new public health order(s), including the anticipated increase to the Contract Price or Contract Time due to the new derivative, strain, or new public health order(s), and

Contractor substantiates those costs with detailed supporting documentation as required for a PCO.

17.7.6.2. If, during the construction of the Project, the applicable and existing federal, state, and/or local statutes, orders, rules, regulations, ordinances, and/or directives relating to construction site safety in connection with Infectious Disease(s), and/or any similar virus or derivative strain, are changed or rescinded (e.g., by the reduction of potential exposure or risk due to vaccinations), the Parties agree to reduce the Contract Price and the Contract Time due to the removal of the required efforts. If the Parties cannot mutually agree on the appropriate reduction, the District may issue a Unilateral Change Order for an amount of time and money it determines to be both reasonable and appropriate. The Parties agree that any dispute related to this provision will be resolved pursuant to the Claims Resolution Process herein.

17.8. Format for Proposed Change Order

17.8.1. The following “Format For Proposed Change For Subcontractor Performed Work” and “Format For Proposed Change For Contractor Performed Work” shall be used as applicable by the District and the Contractor (e.g. Change Orders, PCO’s) to communicate proposed additions and deductions to the Contract, supported by attached documentation.

FORMAT FOR PROPOSED CHANGE FOR SUBCONTRACTOR PERFORMED WORK

	<u>SUBCONTRACTOR PERFORMED WORK</u>	<u>ADD</u>	<u>DEDUCT</u>
(A)	<u>Labor Charge</u> 1. Hours. Attach total itemized hours, by each Subcontractor at each tier. 2. Rate. This shall be no more than the Straight-Time Total Hourly Rate as determined by the Department of Industrial Relations ("DIR") for the applicable labor category.		
(B)	<u>Labor Burden & Worker's Compensation Charge</u> 1. This shall be no more than <u>twenty percent (20%)</u> of item (A) , the Labor Charge. 2. This shall be the total cumulative charge permitted for all Subcontractors or all labor performed by the Subcontractor or Subcontractor's Subcontractor(s) (i.e., all "lower-tier" Subcontractor(s)).		
(C)	<u>Subtotal (A+B)</u>		
(D)	<u>Material Charge</u> Attach itemized quantity and unit cost plus sales tax and invoice(s) from vendor(s).		
(E)	<u>Equipment Charge</u> Attach invoice(s) from supplier(s).		
(F)	<u>Subtotal (C+D+E)</u>		
(G)	<u>Subcontractor's Overhead and Profit Charge</u> 1. This shall be no more than <u>eight percent (8%)</u> of item (F) . 2. This shall be the total cumulative mark-up permitted for the Subcontractor and Subcontractor's Subcontractor(s) (i.e., all "lower-tier" Subcontractor(s)).		
(H)	<u>Subtotal (F+G)</u>		
(I)	<u>Contractor's Overhead, Profit, Bond and Insurance</u> 1. This shall be no more than <u>six percent (6%)</u> of Item (F) . 2. This shall be the total mark-up permitted for Contractor.		
(J)	<u>TOTAL (H+I)</u>		
(K)	<u>Time</u>	_____ Days	

FORMAT FOR PROPOSED CHANGE FOR CONTRACTOR PERFORMED WORK

	<u>CONTRACTOR PERFORMED WORK</u>	<u>ADD</u>	<u>DEDUCT</u>
(A)	<u>Labor Charge</u> 1. Hours. Attach total itemized hours. 2. Rate. This shall be no more than the Straight-Time Total Hourly Rate as determined by the Department of Industrial Relations ("DIR") for the applicable labor category.		
(B)	<u>Labor Burden & Worker's Compensation Charge</u> 1. This shall be no more than <u>twenty percent (20%)</u> of item (A), the Labor Charge. 2. This shall be the total cumulative charge permitted for all labor performed by Contractor.		
(C)	<u>Subtotal (A+B)</u>		
(D)	<u>Material Charge</u> Attach itemized quantity and unit cost plus sales tax and invoice(s) from vendor(s).		
(E)	<u>Equipment Charge</u> Attach invoice(s) from supplier(s).		
(F)	<u>Subtotal (C+D+E)</u>		
(G)	<u>Contractor's Overhead, Profit, Bond and Insurance</u> 1. This shall be no more than <u>six percent (6%)</u> of Item (F). 2. This shall be the total mark-up permitted for Contractor.		
(H)	<u>TOTAL (F+G)</u>		
(I)	<u>Time</u>	_____ Days	

17.8.2. All Proposed Change Order requests by Contractor for a change shall include a complete itemized breakdown with the following detail:

17.8.2.1. Labor. Labor breakdown by trade classification, wage rates, and estimated hours. Labor costs shall only include fringe benefits indicated by governing trade organizations. Wages shall not exceed current prevailing wages in the locality for performance of the changes.

17.8.2.1.1. The Contractor's or Subcontractors' labor burden and Workers' Compensation premium shall only be charged as indicated herein. In no event shall Contractor include any other charges than as indicated herein without the prior written approval of the District.

17.8.2.2. Material. Material quantities, and types of products, and transportation costs, if applicable.

17.8.2.3. Equipment. Equipment breakdown by make, type, size, rental rates (if not owned), equipment hours and transportation costs, if applicable.

17.8.2.3.1. The equipment costs shall not exceed one hundred percent (100%) of the Association of Equipment Distributors (AED) rental rates and delay factors or Caltrans rates and delay factors, whichever is less. Hourly, daily, weekly, or monthly rates shall be used, whichever is lower. Hourly rates including operator shall not be used.

17.8.2.3.2. The time to be paid for equipment shall be the actual time that the equipment is in (1) productive operation on the Work or (2) idled because of the event or circumstance giving rise to the Proposed Change Order.

17.8.2.3.2.1. To calculate the costs of idle equipment, the Contractor must use the applicable idle equipment rate. For example, and clarification purposes only, if the rate for "X" piece of equipment is \$100 and the applicable delay factor is .20 for that piece of equipment, then the hourly rate for idle equipment shall be \$20 (\$100 x .20), which shall be applied against the number of hours idle. In no event shall Contractor charge an amount greater than 50% of the applicable equipment rate for idle equipment.

17.8.2.3.2.2. In computing the hourly rental of equipment, any time less than thirty (30) minutes shall be considered one-half (1/2) hour.

17.8.2.3.2.3. No payment will be made for time while equipment is inoperative due to breakdown, or for non-workdays.

17.8.2.3.2.4. The rental time shall not include the time required to move the equipment to and from the project site. No mobilization or demobilization will be allowed for equipment already on site. If equipment is not moved by its own power, then loading and transportation costs will be paid in lieu of rental time thereof. However, neither moving time nor loading and transportation costs will be paid if the equipment is used on the Project Site in any other way than upon the work directly related to the event or circumstance giving rise to the Proposed Change Order.

17.8.2.3.3. Individual pieces of equipment having a replacement value of one thousand dollars (\$1,000) or less shall be considered to be small tools or small equipment, and no payment will be made since the costs of these tools and equipment is included as part of the markup for overhead and profit defined herein.

17.8.2.3.4. Payment to the Contractor for the use of equipment as set forth above shall constitute full compensation to the Contractor for the cost of fuel, power, oil, lubricants,

supplies, small equipment, necessary attachments, repairs and maintenance of any kind, depreciation, storage, insurance, labor (except for equipment operators), and any and all costs to the Contractor incidental to the use of the equipment.

17.8.2.3.5. Should Contractor, or any of its owners, officers, directors or agents, hold any ownership interest in any company, organization, association or corporation from whom rental equipment is secured. Contractor shall immediately notify District of such and the price set for any such rental shall be agreed upon in advance by the Contractor and the District.

17.8.2.4. Overhead, Profit, Bond and Insurance Costs. Markup for overhead and profit, which shall be used to compensate Contractor for all costs for all administration, general conditions, and supervision, including, without limitation:

17.8.2.4.1. All home office overhead, field office overhead, field office personnel including, but not limited to, principals, project managers, superintendents, supervisory foremen, estimators, project engineers, detailers, draftsmen, schedulers, consultants, watchmen, payroll clerks, administrative assistants, labor compliance costs and secretaries.

17.8.2.4.2. All field and field office expenses including, but not limited to, field trailers, parking, storage sheds, office equipment and supplies, telephone service and long distance telephone calls, computers, fax machines, temporary utilities, sanitary facilities and services, janitorial services, small tools and equipment with a cost under \$1000 each, portable scaffolding, blocking, shores, appliances, job vehicles, security and fencing, conformance to regulatory requirements including compliance to safety regulations, safety programs and meetings, cartage, warranties, As-Built Drawings, as well as any related maintenance costs.

17.8.2.4.3. Administrative functions such as, but not limited to, reviewing, coordinating, distributing, processing, posting, recording, estimating, negotiating, expediting, engineering, drawing, detailing, revising shop drawings, carting, cleaning, protecting the work, and other incidental Work related to the change.

17.8.2.4.4. All other costs and taxes required to be paid, but not included under direct costs as defined above including, without limitation, payroll taxes, social security, etc.

17.8.2.4.5. All costs for Contractor's bonds and insurance.

17.8.2.4.6. Taxes: Federal excise tax shall not be included. District will issue an exemption on request.

17.8.2.5. Contract Time. Justification for any adjustment in Contract Time including a schedule analysis identifying critical schedule activities delayed by the request. Contract Time shall be extended or reduced by Change Orders, Unilateral Change Orders, or Force Account Directives for a period of time commensurate with the time reasonably necessary to perform a Change. This time must be requested in writing by the Contractor with the Price Request, PCO, or expressly in writing as part of its documentation for Unilateral Change Orders, or Force Account Directives. The Contractor shall justify any Contract Time extension by submittal of a schedule analysis as required in this Changes section of these General Conditions accurately portraying the impact of the change on the critical path of the Construction Schedule. Changes performed within available float shall not justify an extension to the Contract Time. The District shall make the final determination of the amount of Contract Time to allocate to any Change.

17.8.2.6. Supporting Documentation. Contractor shall include with each PCO, along with the itemized breakdown as required herein, reasonable documentation substantiating the

requested change in the Contract Price and Contract Time. If the District deems Contractor's supporting documentation incomplete or inadequate to substantiate the requested change to the Contract Price and Contract Time, the District may request that Contractor supplement the PCO with additional, reasonable supporting documentation.

17.9. Change Order Certification

17.9.1. All Change Orders and PCOs shall include the following certification by the Contractor. The Parties acknowledged that if a Change Order is approved that does not include this language, that Change Order shall be deemed to include this certification language:

The Contractor approves the foregoing as to the changes, if any, and the price specified for each item and the extension of time allowed, if any, for completion of the entire Work as stated herein, and agrees to furnish all labor, materials, and service, and perform all work necessary to complete all additional work specified for the consideration stated herein. Submission of sums that have no basis in fact or which Contractor knows are false are at the sole risk of Contractor and may be a violation of the False Claims Act set forth under Government Code section 12650 et seq. It is understood that the changes herein to the Contract shall only be effective when approved by the governing board of the District. It is expressly understood that the value of the extra Work or changes includes all of the Contractor's costs, expenses, field overhead, home office overhead, profit, both direct and indirect, resulting from additional time required on the Project or resulting from delay to the Project. Any costs, expenses, damages, or time extensions not included are deemed waived.

17.10. Determination of Change Order Cost

17.10.1. The amount of the increase or decrease in the Contract Price from a Change Order, if any, shall be determined in one or more of the following ways as applicable to a specific situation and at the District's discretion:

17.10.1.1. District acceptance of a PCO;

17.10.1.2. By agreement between District and Contractor.

17.10.1.3. By unit prices or alternates contained in Contractor's original bid. If the Bid for the Work included proposal(s) for Alternate Bid Item(s), during Contractor's performance of the Work, the District may elect to add any such Alternate Bid Item(s) if the that item did not form a basis for award of the Contract or delete any such Alternate Bid Item(s) if that item formed a basis for award of the Contract. If the District elects to add or delete an Alternate Bid Item(s) pursuant to the foregoing, the cost or credit for that Alternate Bid Item(s) shall be as set forth in the Contractor's Bid, at the District's discretion. If any Alternate Bid Item is added or deleted from the Work pursuant to the foregoing, the Contract Time shall be adjusted by the number of days allocated for the added or deleted Alternate Bid Item in the Contract Documents; if days are not allocated for any Alternate Bid Item added or deleted pursuant to the foregoing, the Contract Time shall be equitably adjusted.

17.10.1.4. By the District, based upon actual and necessary costs incurred by the Contractor as determined by the District on the basis of the Contractor's records. Promptly upon determining the extent of adjustment to the Contract Price, the District shall notify the Contractor in writing of the same; the Contractor shall be deemed to have accepted the District's determination of the amount of adjustment to the Contract Price on account of a Change to the

Work unless Contractor shall notify the District, in writing, not more than fifteen (15) days from the date of the District's written notice, of any objection to the District's determination. Failure of the Contractor to timely notify the District of Contractor's objections to the District's determination of the extent of adjustment to the Contract Price shall be deemed Contractor's acceptance of the District's determination and a waiver of any right or basis of the Contractor to thereafter protest or otherwise object to the District's determination. Notwithstanding any objection of the Contractor to the District's determination of the extent of any adjustment to the Contract Price pursuant to this provision, Contractor shall diligently proceed to perform and complete any such Change.

17.11. Deductive Change Orders

If Contractor offers a proposed amount for a deductive Change Order(s), Contractor shall include a minimum of five percent (5%) total overhead and profit to be deducted with the amount of the work of the Change Order(s). If Subcontractor work is involved, Subcontractors shall also include a minimum of five percent (5%) overhead and profit to be deducted with the amount of its deducted work, for a total minimum of ten percent (10%) total overhead and profit to be deducted. Any deviation from this provision shall not be allowed.

17.12. Discounts, Rebates and Refunds

For purposes of determining the cost, if any, of any change, addition, or omission to the Work hereunder, all trade discounts, rebates, refunds, and all returns from the sale of surplus materials and equipment shall accrue and be credited to the Contractor, and the Contractor shall make provisions so that such discounts, rebates, refunds, and returns may be secured, and the amount thereof shall be allowed as a reduction of the Contractor's cost in determining the actual cost of construction for purposes of any change, addition, or omission in the Work as provided herein.

17.13. Accounting Records

With respect to portions of the Work performed by Change Orders, Unilateral Change Orders, or Force Account Directives, Contractor shall keep and maintain cost-accounting records satisfactory to the District, which shall be available to the District on the same terms as any other books and records Contractor is required to maintain pursuant to the Contract Documents.

17.14. Notice Required

If Contractor is seeking an adjustment in the Contract Price, or any extension in the Contract Time for Completion, it shall notify District pursuant to the provisions of the Contract Documents. No adjustment in the Contract Price or Contract Time shall be considered unless made in accordance with the Contract Documents. Contractor shall proceed to execute the Work even though the adjustment may not have been agreed upon. Any change in the Contract Price or extension of the Contract Time resulting from such contract adjustment shall only be authorized by a Change Order.

17.15. Applicability to Subcontractors

Any requirements under this Article shall be equally applicable to Change Orders, Unilateral Change Orders, or Force Account Directives issued to Subcontractors by the Contractor to the extent as required by the Contract Documents.

17.16. Alteration to Change Order Language

Contractor shall not alter Change Orders or reserve time in Change Orders. Contractor shall execute finalized Change Orders and proceed under the provisions herein with proper notice.

17.17. Failure of Contractor to Execute Change Order

Contractor shall be in default of the Contract if Contractor fails to execute a Change Order when the Contractor agrees with the addition and/or deletion of the Work in that Change Order.

18. REQUEST FOR INFORMATION

18.1. Any Request for Information ("RFI") shall reference all applicable Contract Document(s), including Specification section(s), detail(s), page number(s), drawing number(s), and sheet number(s), etc. Contractor shall make suggestions and interpretations of the issue raised by each RFI. An RFI cannot modify the Contract Price, Contract Time, or the Contract Documents.

18.2. Contractor shall be liable to the District for all costs incurred by the District associated with the processing, reviewing, evaluating and responding to any RFI, including without limitation, fees of the Architect and any other design consultant to the Architect or the District, that District reasonably determines:

18.2.1. Does not reflect adequate or competent supervision or coordination by the Contractor or any Subcontractor; or

18.2.2. Does not reflect the Contractor's adequate or competent knowledge of the requirements of the Work or the Contract; or

18.2.3. Requests an interpretation or decision of a matter where the information sought is equally available to the Contractor; or

18.2.4. Is not justified for any other reason.

18.3. Prior to submitting the RFI, Contractor shall diligently review the Contract Documents for information responsive to the RFI, including information incorporated by reference. Contractor should not issue an RFI regarding information contained in or inferable from the Contract Documents, including information incorporated by reference. An RFI is invalid if the RFI response is contained in or inferable from the Contract Documents.

18.4. Contractor shall be responsible for preparing and submitting each RFI so as to not cause delay to the progress of the Work nor to cause any impact to the Contractor's labor productivity. An RFI may be considered untimely if not submitted within **Forty Eight (48) hours** of receipt from a Contractor's subcontractor. Untimely submission of any RFI will preclude Contractor from asserting any claims for delay or for labor impact against the District.

18.5. If the Contractor fails to timely notify the Architect in writing of any Conditions encountered and the Contractor proceeds to perform any portion of the Work containing or affected by such Conditions the Contractor shall bear all costs associated with or required to correct, remove, or otherwise remedy any portion of the Work affected thereby without adjustment of the Contract Time or the Contract Price. In requesting information of the District to address and resolve any conditions, the Contractor shall act with promptness in submitting any written request so as to allow the District a reasonable period of time to review, evaluate and respond to any request, taking into account the then current status of the progress and completion of the Work and the actual or potential impact of any conditions upon the completion of the Work within the Contract Time. The Contract Time shall not be subject to adjustment in the event that the Contractor shall fail to timely request information from the District.

19. PAYMENTS

19.1. Contract Price

19.1.1. The Contract Price is stated in the Agreement and, including authorized adjustments, is the total amount payable by the District to the Contractor for performance of the Work pursuant to the Contract Documents. If all or a portion of the Project is being funded by funds requiring approval by the State Allocation Board (SAB), payment may be subject to that approval being received, funding by the SAB, and funds being released by the Office of Public School Construction (OPSC).

19.2. Applications for Progress Payments

19.2.1. Procedure for Applications for Progress Payments

19.2.1.1. Application for Progress Payment

19.2.1.1.1. Not before the fifth (5th) day of each calendar month during the progress of the Work, Contractor shall submit to the District and the Architect an itemized Application for Payment for Work completed in accordance with the Schedule of Values. The Application for Payment shall be notarized, if required, and supported by the following or each portion thereof unless waived by the District in writing:

19.2.1.1.1.1. The amount paid to the date of the Application for Payment to the Contractor, to all its Subcontractors, and all others furnishing labor, material, or equipment for its Contract;

19.2.1.1.1.2. The amount being requested by the Application for Payment by the Contractor on its own behalf and separately stating the amount requested on behalf of each of the Subcontractors and all others furnishing labor, material, and equipment under the Contract;

19.2.1.1.1.3. The balance that will be due to each of the entities after payment is made;

19.2.1.1.1.4. A certification that the As-Built Drawings and annotated Specifications are current;

19.2.1.1.1.5. An Itemized breakdown of Work performed;

19.2.1.1.1.6. An updated and acceptable construction schedule in conformance with the provisions herein;

19.2.1.1.1.7. The additions to and subtractions from the Contract Price and Contract Time;

19.2.1.1.1.8. A total of the retention held;

19.2.1.1.1.9. The material invoices, evidence of equipment purchases, rentals, and other support and details of cost as the District may require from time to time;

19.2.1.1.1.10. The percentage of completion of the Contractor's Work by line item;

19.2.1.1.1.11. The Schedule of Values updated from the preceding Application for Payment;

19.2.1.1.1.12. A duly completed and executed conditional waiver and release upon progress payment compliant with Civil Code section 8132 from each subcontractor of any tier and supplier to be paid from the current progress payment;

19.2.1.1.1.13. A duly completed and executed unconditional waiver and release upon progress payment compliant with Civil Code section 8134 from each subcontractor of any tier and supplier that was paid from the previous progress payment; and

19.2.1.1.1.14. A certification by the Contractor of the following:

The Contractor warrants title to all Work performed as of the date of this payment application. The Contractor further warrants that all Work performed as of the date of this payment application is free and clear of liens, claims, security interests, or encumbrances in favor of the Contractor, Subcontractors, material and equipment suppliers, workers, or other persons or entities making a claim by reason of having provided labor, materials, and equipment relating to the Work, except those of which the District has been informed.

19.2.1.1.1.15. If requested by the District, a third party, or as required by the California Department of Industrial Relations, all requested or required certified payroll record ("CPR(s)") for each journeyman, apprentice, worker, or other employee employed by the Contractor and/or each Subcontractor in connection with the Work for the period of the Application for Payment.

19.2.1.1.2. Except as expressly provided for herein, no payments shall be made by the District on account of any item of the Work, including without limitation, materials or equipment that, at the time of the Contractor's submittal of an Application for Progress Payment, has/have not been incorporated into and made a part of the Work.

19.2.1.1.3. Contractor shall be subject to the False Claims Act set forth under Government Code section 12650 et seq., for information provided with any Application for Progress Payment.

19.2.2. Prerequisites for Progress Payments

19.2.2.1. First Payment Request: The following items, if applicable, must be completed before District will accept and/or process Contractor's first payment request:

19.2.2.1.1. Installation of the Project sign;

19.2.2.1.2. Installation of field office;

19.2.2.1.3. Installation of temporary facilities and fencing;

19.2.2.1.4. Schedule of Values;

19.2.2.1.5. Contractor's Construction Schedule;

19.2.2.1.6. Schedule of unit prices, if applicable;

19.2.2.1.7. Submittal Schedule;

19.2.2.1.8. Receipt by Architect of all submittals due as of the date of the payment application;

19.2.2.1.9. Copies of necessary permits;

- 19.2.2.1.10.** Copies of authorizations and licenses from governing authorities;
- 19.2.2.1.11.** Initial progress report;
- 19.2.2.1.12.** Surveyor qualifications;
- 19.2.2.1.13.** Written acceptance of District's survey of rough grading, if applicable;
- 19.2.2.1.14.** List of all Subcontractors, with names, license numbers, telephone numbers, and Scope of Work;
- 19.2.2.1.15.** All bonds and insurance endorsements; and
- 19.2.2.1.16.** Resumes of Contractor's project manager, and if applicable, job site secretary, record documents recorder, and job site superintendent.

19.2.2.2. Second Payment Request: District will not process the second payment request until and unless all submittals and Shop Drawings have been accepted for review by the Architect.

19.2.2.3. No Waiver of Criteria: Any payment made to Contractor where criteria set forth herein have not been met shall not constitute a waiver of said criteria by District. The approval of any Application for Progress Payment or the disbursement of any Progress Payment to the Contractor shall not be deemed nor constitute acceptance of defective Work or Work not in conformity with the Contract Documents. Instead, such payment shall be construed as a good faith effort by District to resolve differences so Contractor may pay its Subcontractors and suppliers. Contractor agrees that failure to submit such items may constitute a material breach of the Contract by Contractor and may subject Contractor to termination.

19.3. Progress Payments

19.3.1. District's Approval of Application for Payment

19.3.1.1. Upon receipt of an Application for Payment, District shall act in accordance with the following:

19.3.1.1.1. Each Application for Payment shall be reviewed by the District as soon as practicable after receipt for the purpose of determining that the Application for Payment is a proper Application for Payment.

19.3.1.1.2. Any Application for Payment determined not to be a proper Application for Payment suitable for payment shall be returned to the Contractor as soon as practicable, but not later than seven (7) days, after receipt. An Application for Payment returned pursuant to this paragraph shall be accompanied by a document setting forth in writing the reasons why the Application for Payment is not proper. The number of days available to the District to make a payment without being subject to any applicable statute regarding prompt payment or interest accrual, shall be reduced by the number of days by which the District exceeds this seven-day return requirement.

19.3.1.1.3. An approved Application for Payment shall be considered payable if funds are available for payment after the deduction of amounts allowed by law and/or pursuant to the section herein entitled "Decisions to Withhold Payment,"

19.3.1.2. The District's review of the Contractor's Application for Payment will be based

on the District's and the Architect's observations at the Site and the data comprising the Application for Payment that the Work has progressed to the point indicated and that, to the best of the District's and the Architect's knowledge, information, and belief, the quality of the Work is in accordance with the Contract Documents. The foregoing representations are subject to:

19.3.1.2.1. Observation of the Work for general conformance with the Contract Documents,

19.3.1.2.2. Results of subsequent tests and inspections,

19.3.1.2.3. Minor deviations from the Contract Documents correctable prior to Completion, and

19.3.1.2.4. Specific qualifications expressed by the Architect.

19.3.1.3. District's approval of each Application for Payment shall be based on Contractor complying with all requirements for a fully complete and valid Application for Payment.

19.3.2. Payments to Contractor

19.3.2.1. Within thirty (30) days after District's receipt of each undisputed and properly submitted Application for Payment, Contractor shall be paid a sum equal to ninety-five percent (95%) of the value of the Work performed (as verified by Architect and Inspector and certified by Contractor) up to the last day of the previous month, less the aggregate of previous payments and amount to be withheld. The value of the Work completed shall be Contractor's best estimate. No inaccuracy or error in Contractor's estimate shall operate to release the Contractor, or any Surety upon any bond, from damages arising from such Work, or from the District's right to enforce each and every provision of this Contract, and the District shall have the right subsequently to correct any error made in any estimate for payment.

19.3.2.2. District shall withhold five percent (5%) retention from all Progress Payments.

19.3.2.3. District may withhold ten percent (10%) retention from all Progress Payments pursuant to Public Contract Code section 7201, if the Project is determined to be "substantially complex."

19.3.2.4. The Contractor shall not be entitled to have any payment requests processed, or be entitled to have any payment made for Work performed, so long as any lawful or proper direction given by the District concerning the Work, or any portion thereof, remains incomplete.

19.3.2.5. In accordance with Public Contract Code §20104.50, in the event that the District shall fail to make any Progress Payment within thirty (30) days after receipt of an undisputed and properly submitted Application for Progress Payment, the District shall pay the Contractor interest on the undisputed amount of such Application for Progress Payment equal to the legal rate of interest set forth in California Code of Civil Procedure §685.010(a).

19.3.3. No Waiver

No payment by District hereunder shall be interpreted so as to imply that District has inspected, approved, or accepted any part of the Work. Notwithstanding any payment, the District may enforce each and every provision of this Contract. The District may correct or require correction of any error subsequent to any payment.

19.3.4. Warranty of Title

19.3.4.1. If a lien or a claim based on a stop notice or stop payment notice of any nature should at any time be filed against the Work or any District property, by any entity that has supplied material or services at the request of the Contractor, Contractor and Contractor's Surety shall promptly, on demand by District and at Contractor's and Surety's own expense, take any and all action necessary to cause any such lien or a claim based on a stop notice or stop payment notice to be released or discharged immediately therefrom.

19.3.4.2. If the Contractor fails to furnish to the District within ten (10) calendar days after demand by the District, satisfactory evidence that a lien or a claim based on a stop notice or stop payment notice has been so released, discharged, or secured, the District may discharge such indebtedness and deduct the amount required therefore, together with any and all losses, costs, damages, and attorney's fees and expense incurred or suffered by District from any sum payable to Contractor pursuant to the Contract.

19.4. Decisions to Withhold Payment

19.4.1. Reasons to Withhold Payment

District may withhold payment in whole, or in part, to the extent reasonably necessary to protect the District if, in the District's opinion, the representations to the District required herein cannot be made. District may withhold payment, in whole, or in part, to such extent as may be necessary to protect the District from loss because of, but not limited to:

19.4.1.1. Defective Work not remedied within **FORTY-EIGHT (48)** hours of written notice to Contractor;

19.4.1.2. Stop notices, stop payment notices or other liens served upon the District as a result of the Contract;

19.4.1.3. Liquidated damages assessed against the Contractor;

19.4.1.4. The cost to complete the Work if there exists reasonable doubt that the Work can be completed for the unpaid balance of the Contract Price or by the Completion Date;

19.4.1.5. Damage to the District or other contractor(s);

19.4.1.6. Unsatisfactory performance of the Work by Contractor;

19.4.1.7. Failure to store and properly secure materials;

19.4.1.8. Failure of the Contractor to submit, on a timely basis, proper, sufficient, and acceptable documentation required by the Contract Documents, including, without limitation, a Construction Schedule, Schedule of Submittals, Schedule of Values, Monthly Progress Schedules, Shop Drawings, Product Data and samples, Proposed product lists, executed Change Orders, and/or verified reports;

19.4.1.9. Failure of the Contractor to maintain As-Built Drawings;

19.4.1.10. Erroneous estimates by the Contractor of the value of the Work performed, or other false statements in an Application for Payment;

19.4.1.11. Unauthorized deviations from the Contract Documents;

19.4.1.12. Failure of the Contractor to perform the Work in a timely manner in compliance with the Construction Schedule, established progress schedules, and/or completion dates;

19.4.1.13. If requested by the District, or the failure to provide to the DIR, certified payroll records acceptable to the District and the DIR for each journeyman, apprentice, worker, or other employee employed by the Contractor and/or each Subcontractor in connection with the Work for the period of the Application for Payment;

19.4.1.14. Failure to properly pay prevailing wages as defined in Labor Code sections 1720 et seq. and/or failure to comply with any other Labor Code requirements;

19.4.1.15. Failure to properly maintain or clean up the Site;

19.4.1.16. Failure to timely indemnify, defend or hold harmless the District;

19.4.1.17. Any payments due to the District, including but not limited to payments for failed tests, utilities changes, or permits;

19.4.1.18. Failure to pay Subcontractor(s) or supplier(s) as required by law and by the Contract Documents;

19.4.1.19. Failure to pay any royalty, license or similar fees;

19.4.1.20. Failure of the Contractor to submit on a timely basis all Closeout Documentation in a manner and form that is proper, sufficient, and reasonably acceptable to the District, and to not cause a delay in the Completion or approval of the Project; or

19.4.1.21. Failure to perform any implementation and/or monitoring required by any SWPPP for the Project and/or the imposition of any penalties or fines imposed therefore against Contractor or District.

19.4.1.22. Payment is delayed due to an audit inquiry by the State, the County Office of Education, the County, or any entity with jurisdiction related to the Project.

19.4.1.23. Contractor is otherwise in breach, default or in substantial violation of any provision of the Contract;

19.4.2. Reallocation of Withheld Amounts

19.4.2.1. District may, in its discretion, apply any withheld amount to pay outstanding claims or obligations as defined herein. In so doing, District shall make such payments on behalf of Contractor. If any payment is so made by District, then that amount shall be considered a payment made pursuant to the Contract and District shall not be liable to Contractor for any payment made in good faith. These payments may be made without prior judicial determination of claim or obligation. District will render Contractor an accounting of funds disbursed on behalf of Contractor.

19.4.2.2. If Contractor defaults or neglects to perform the Work in accordance with the Contract Documents or fails to perform any provision thereof, District may, after **FORTY-EIGHT (48)** hours written notice to the Contractor and, without prejudice to any other remedy, make good such deficiencies. District shall adjust the total Contract Price by reducing the amount thereof by the cost of making good such deficiencies. If District deems it inexpedient to correct Work that is damaged, defective, or not done in accordance with Contract provisions, an

equitable reduction in the Contract Price (of at least one hundred twenty-five percent (125%) of the estimated reasonable value of the nonconforming Work) shall be made therefor.

19.4.3. Payment After Cure

When Contractor cures the grounds for declining approval, payment shall be made for amounts so withheld. No interest shall be paid on any retention or amounts withheld due to the failure of the Contractor to perform in accordance with the terms and conditions of the Contract Documents.

19.5. Subcontractor Payments

19.5.1. Payments to Subcontractors. No later than seven (7) days after receipt, or pursuant to Business and Professions Code section 7108.5 and Public Contract Code section 7107, the Contractor shall pay to each Subcontractor, out of the amount paid to the Contractor on account of such Subcontractor's portion of the Work, the amount to which said Subcontractor is entitled. Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to its Sub-subcontractors in a similar manner.

19.5.2. No Obligation of District for Subcontractor Payment. District shall have no obligation to pay, or to see to the payment of, money to a Subcontractor except as may otherwise be required by law.

19.5.3. Joint Checks. District shall have the right in its sole discretion, if necessary for the protection of the District, to issue joint checks made payable to the Contractor and Subcontractors and material or equipment suppliers. The joint check payees shall be responsible for the allocation and disbursement of funds included as part of any such joint payment. In no event shall any joint check payment be construed to create any contract between the District and a Subcontractor of any tier, any obligation from the District to such Subcontractor, or rights in such Subcontractor against the District.

20. COMPLETION OF THE WORK

20.1. Completion

20.1.1. The Project may only be accepted by action of the governing board of the District.

20.1.2. District shall accept the Project and may have a Notice of Completion recorded when Project Completion has been achieved in accordance with the Contract Documents and to the satisfaction of District. For purposes of the payment of Retention, Completion is defined in Public Contract Code section 7107. For purposes of the timely filing of Stop Payment Notices, Completion is defined in California Civil Code section 9200, et seq.

20.1.3. There is no "*substantial completion*" for this Project. Even so, the District, at its sole option, may accept the Project and record a Notice of Completion when Project Completion has been completed to the satisfaction of District, except for minor corrective items, as distinguished from incomplete items. If Contractor fails to complete all minor corrective items within thirty-five (35) days after the date of the District's acceptance of the Project, District shall withhold from the final payment one hundred fifty percent (150%) of an estimate of the amount sufficient to complete the corrective items, as determined by District, until the item(s) are completed.

20.1.4. At the end of the thirty-five (35) day period, if there are any items remaining to be corrected, District may elect to proceed as provided herein related to adjustments to Contract Price, and/or District's right to perform the Work of the Contractor.

20.2. Closeout Procedures

20.2.1. Punch List

Contractor shall notify the Architect when Contractor considers the Work complete. Upon notification, Architect will prepare a list of minor items to be completed or corrected ("Punch List"). Contractor and/or its Subcontractors shall proceed promptly to complete and correct items on the Punch List. Failure to include an item on Punch List does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

20.2.2. Closeout Requirements

20.2.2.1. Utility Connections

Buildings shall be connected to water, gas, sewer, and electric services, complete and ready for use. Service connections shall be made and existing services reconnected.

20.2.2.2. As-Built Drawings

20.2.2.2.1. In addition to its requirement to provide monthly As-Built Drawings to the District, the Contractor shall provide a final set of As-Built Drawings, sometimes referred to as "Record Drawings," showing all of the Work as actually constructed upon Completion of the Project as indicated in the Specifications.

20.2.2.2.2. Contractor is liable and responsible for any and all inaccuracies in the As-Built Drawings, even if inaccuracies become evident at a future date.

20.2.2.2.3. Upon Completion of the Work and as a condition precedent to approval of final payment, Contractor shall obtain the Inspector's approval of the final set of As-Built Drawings.

20.2.2.3. Operations & Maintenance Manuals: Contractor shall prepare all operation and maintenance manuals and date as indicated in the Specifications.

20.2.2.4. Closeout Documentation: Contractor shall provide all Closeout Documentation, which shall include the following, without limitation:

20.2.2.4.1. A full set of final As-Built Drawings, as further defined herein.

20.2.2.4.2. All Operations & Maintenance Manuals and information, as further defined herein.

20.2.2.4.3. All Warranties, as further defined herein.

20.2.2.4.4. Verified report(s) for all scope(s) of work (DSA 6-C, Rev 03/22/13, or more recent revision if available).

20.3. Final Inspection

20.3.1. Contractor shall comply with Punch List procedures as provided herein, and maintain the presence of Contractor's superintendent and project manager until the Punch List is complete to ensure proper and timely completion of the Punch List. Under no circumstances shall Contractor demobilize its forces prior to completion of the Punch List. Upon receipt of Contractor's written notice that all of the Punch List items have been fully completed and the Work is ready for final inspection and acceptance, Architect and Project Inspector will inspect the Work and shall submit to Contractor and District a final inspection report noting the Work, if any, required in order to complete in accordance with the Contract

Documents. Absent unusual circumstances, this report shall consist of the Punch List items not yet satisfactorily completed.

20.3.2. Upon Contractor's completion of all items on the Punch List and any other uncompleted portions of the Work, the Contractor shall notify the District and Architect, who shall again inspect such Work. If the Architect finds the Work complete and acceptable under the Contract Documents, the Architect will notify Contractor, who shall then jointly submit to the Architect and the District its final Application for Payment.

20.3.3. Final Inspection Requirements

20.3.3.1. Before calling for final inspection, Contractor shall determine that the following have been performed:

20.3.3.1.1. The Work has been completed.

20.3.3.1.2. All life safety items are completed and in working order.

20.3.3.1.3. Mechanical and electrical Work are complete and tested, fixtures are in place, connected, and ready for tryout.

20.3.3.1.4. Electrical circuits scheduled in panels and disconnect switches labeled.

20.3.3.1.5. Painting and special finishes complete.

20.3.3.1.6. Doors complete with hardware, cleaned of protective film, relieved of sticking or binding, and in working order.

20.3.3.1.7. Tops and bottoms of doors sealed.

20.3.3.1.8. Floors waxed and polished as specified.

20.3.3.1.9. Broken glass replaced and glass cleaned.

20.3.3.1.10. Grounds cleared of Contractor's equipment, raked clean of debris, and trash removed from Site.

20.3.3.1.11. Work cleaned, free of stains, scratches, and other foreign matter, of damaged and broken material replaced.

20.3.3.1.12. Finished and decorative work shall have marks, dirt, and superfluous labels removed.

20.3.3.1.13. Final cleanup, as provided herein.

20.4. Costs of Multiple Inspections

More than two (2) requests of the District to make a final inspection shall be considered an additional service of District, Architect, Construction Manager, and/or Project Inspector, and all subsequent costs will be invoiced to Contractor and if funds are available, withheld from remaining payments.

20.5. Partial Occupancy or Use Prior to Completion

20.5.1. District's Rights to Occupancy. The District may occupy or use any completed or partially completed portion of the Work at any stage. Neither the District's Final Acceptance, the making of Final

Payment, any provision in Contract Documents, nor the use or occupancy of the Work, in whole or in part, by District shall constitute acceptance of Work not in accordance with the Contract Documents nor relieve the Contractor or the Contractor's Performance Bond Surety from liability with respect to any warranties or responsibility for faulty or defective Work or materials, equipment and workmanship incorporated therein. The District and the Contractor shall agree in writing to the responsibilities assigned to each of them for payments, security, maintenance, heat, utilities, damage to the Work, insurance, the period for correction of the Work, and the commencement of warranties required by the Contract Documents. Any dispute as to responsibilities shall be resolved pursuant to the Claims provisions herein, with the added provision that during the dispute process, the District shall have the right to occupy or use any portion of the Work that it needs or desires to use.

20.5.2. Inspection Prior to Occupancy or Use. Immediately prior to partial occupancy or use, the District, the Contractor, and the Architect shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

20.5.3. No Waiver. Unless otherwise agreed upon, partial or entire occupancy or use of a portion or portions of the Work shall not constitute beneficial occupancy or acceptance of the Work not complying with the requirements of the Contract Documents.

21. FINAL PAYMENT AND RETENTION

21.1. Final Payment

21.1.1. Upon receipt and approval of a valid and final Application for Payment, the Architect will issue a final Certificate of Payment or similar document indicating Architect's agreement that the Project has reached Completion. The District shall thereupon jointly inspect the Work and either accept the Work as complete or notify the Architect and the Contractor in writing of reasons why the Work has not reached Completion to the satisfaction of the District.

21.1.2. Upon acceptance of the Work of the Contractor as having reached Completion to the satisfaction of the District (that, absent unusual circumstances, will occur when the Punch List items have been satisfactorily completed), the District may record a Notice of Completion with the County Recorder, and the Contractor shall, upon receipt of final payment from the District, pay all the amount(s) due to its Subcontractors.

21.2. Prerequisites for Final Payment

The following conditions must be fulfilled prior to Final Payment:

21.2.1. A full and final waiver or release of all stop notices and stop payment notices in connection with the Work shall be submitted by Contractor, including a release of stop notice or stop payment notice in recordable form, together with (to the extent permitted by law) a copy of the full and final release of all stop notice or stop payment notice rights.

21.2.2. A duly completed and executed conditional waiver and release upon final payment compliant with Civil Code section 8136 from each subcontractor of any tier and supplier to be paid from the current progress payment.

21.2.3. A duly completed and executed unconditional waiver and release upon final payment compliant with Civil Code section 8138 from each subcontractor of any tier and supplier that was paid from the previous progress payment.

21.2.4. Contractor shall have made all corrections to the Work that are required to remedy any defects therein, to obtain compliance with the Contract Documents or any requirements of applicable codes and

ordinances, or to fulfill any of the orders or directions of District required under the Contract Documents.

21.2.5. Each Subcontractor shall have delivered to the Contractor all written guarantees, warranties, applications, and bonds required by the Contract Documents for its portion of the Work.

21.2.6. Contractor must have completed all requirements set forth under "Closeout Procedures," including, without limitation, submission of an approved set of complete As-Built Drawings.

21.2.7. Architect shall have issued its written approval that final payment can be made.

21.2.8. Contractor shall have delivered to the District all manuals and materials required by the Contract Documents.

21.2.9. Contractor shall have completed final clean up as provided herein.

21.3. Retention

21.3.1. The retention, less any amounts disputed by the District or that the District has the right to withhold pursuant to provisions herein, shall be paid:

21.3.1.1. After approval of the District by the Architect's Certificate of Payment;

21.3.1.2. After the satisfaction of the conditions set forth herein;

21.3.1.3. Within sixty (60) days after Completion;

21.3.1.4. No earlier than thirty-five (35) days of the recording of the Notice of Completion by District, if a Notice of Completion is recorded by the District.

21.4. Substitution of Securities

The District will permit the substitution of securities in accordance with the provisions of Public Contract Code section 22300.

21.5. Claims Asserted After Final Payment

Any lien, stop payment notice or other claim filed or asserted after the Contractor's acceptance of the Final Payment by any Subcontractor, of any tier, laborer, Material Supplier or others in connection with or for Work performed under the Contract Documents shall be the sole and exclusive responsibility of the Contractor pursuant to the indemnification obligations of the Contract Documents. In the event any lien, stop payment notice or other claim of any Subcontractor, Laborer, Material Supplier or others performing Work under the Contract Documents remain unsatisfied after Final Payment is made, Contractor shall refund to District all monies that the District may pay or be compelled to pay in discharging any lien, stop payment notice or other claim, including, without limitation all costs and reasonable attorneys' fees incurred by District in connection therewith.

22. UNCOVERING WORK, CORRECTION OF WORK AND RIGHT TO TAKEOVER WORK

22.1. Uncovering of Work

If a portion of the Work is covered without Project Inspector or Architect approval or not in compliance with the Contract Documents, it must, if required in writing by the District, the Project Inspector, or the Architect, be uncovered for the Project Inspector's or the Architect's observation and be replaced at the Contractor's expense without change in the Contract Price or Contract Time.

22.2. Rejection of Work

Prior to the District's Acceptance of the Work, any Work or materials or equipment forming a part of the Work or incorporated into the Work that is defective or not in conformity with the Contract Documents may be rejected by the District, the Architect or the Project Inspector and the Contractor shall correct all rejected Work without any adjustment to the Contract Price or the Contract Time, even if the Work, materials or equipment have been previously inspected by the Architect or the Project Inspector or even if they failed to observe the defective or non-conforming Work, materials or equipment.

22.3. Nonconforming Work

22.3.1. Contractor shall promptly remove from Premises all Work identified by District as failing to conform to the Contract Documents whether incorporated or not. Contractor shall promptly replace and re-execute its own Work to comply with the Contract Documents without additional expense to the District and shall bear the expense of making good all work of other contractors destroyed or damaged by any removal or replacement pursuant hereto and/or any delays to the District or other Contractors caused thereby.

22.3.2. If Contractor does not remove Work that District has identified as failing to conform to the Contract Documents within a reasonable time, not to exceed **FORTY-EIGHT (48)** hours, District may remove it and may store any material at Contractor's expense. If Contractor does not pay expense(s) of that removal within ten (10) days' time thereafter, District may, upon ten (10) days' written notice, sell any material at auction or at private sale and shall deduct all costs and expenses incurred by the District and/or District may withhold those amounts from payment(s) to Contractor.

22.4. Correction of Work

22.4.1. Correction of Rejected Work. Pursuant to the notice provisions herein, the Contractor shall promptly correct the Work rejected by the District, the Architect, or the Project Inspector as failing to conform to the requirements of the Contract Documents, whether observed before or after Completion and whether or not fabricated, installed, or completed. The Contractor shall bear costs of correcting the rejected Work, including additional testing, inspections, and compensation for the Inspector's or the Architect's services and expenses made necessary thereby.

22.4.2. One-Year Warranty Corrections. If, within one (1) year after the date of Completion of the Work or a designated portion thereof, or after the date for commencement of warranties established hereunder, or by the terms of an applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the District to do so. This period of one (1) year shall be extended with respect to portions of the Work first performed after Completion by the period of time between Completion and the actual performance of the Work. This obligation hereunder shall survive acceptance of the Work under the Contract and termination of the Contract. The District shall give such notice promptly after discovery of the condition.

22.5. District's Right to Takeover Work

22.5.1. If the Contractor should neglect to prosecute the Work properly or fail to perform any provisions of this Contract, the District, after **FORTY-EIGHT (48)** hours written notice to the Contractor, may, without prejudice to any other remedy it may have, make good such deficiencies and may deduct the cost thereof from the payment then or thereafter due the Contractor.

22.5.2. If it is found at any time, before or after Completion of the Work, that Contractor has varied from the Drawings and/or Specifications, including, but not limited to, variation in material, quality, form, or finish, or in the amount or value of the materials and labor used, District may require at its option:

22.5.2.1. That all such improper Work be removed, remade or replaced, and all work disturbed by these changes be made good by Contractor at no additional cost to the District;

22.5.2.2. That the District deduct from any amount due Contractor the sum of money equivalent to the difference in value between the work performed and that called for by the Drawings and Specifications; or

22.5.2.3. That the District exercise any other remedy it may have at law or under the Contract Documents, including but not limited to the District hiring its own forces or another contractor to replace the Contractor's nonconforming Work, in which case the District shall either issue a deductive Change Order, a Unilateral Change Order, or invoice the Contractor for the cost of that work. Contractor shall pay any invoices within thirty (30) days of receipt of same or District may withhold those amounts from payment(s) to Contractor.

22.5.3. Acceptance of Defective or Non-Conforming Work. The District may, in its sole and exclusive discretion, elect to accept Work that is defective or that is not in accordance with the requirements of the Contract Documents, instead of requiring its removal and correction, in which case the Contract Price shall be reduced as appropriate and equitable.

23. TERMINATION AND SUSPENSION

23.1. District's Right to Terminate Contractor for Cause

23.1.1. Grounds for Termination. The District, in its sole discretion, may terminate the Contract and/or terminate the Contractor's right to perform the work of the Contract based upon the following:

23.1.1.1. Contractor refuses or fails to execute the Work or any separable part thereof with sufficient diligence as will ensure its completion within the time specified or any extension thereof, or

23.1.1.2. Contractor fails to complete said Work within the time specified or any extension thereof, or

23.1.1.3. Contractor persistently fails or refused to perform Work or provide material of sufficient quality as to be in compliance with Contract Documents; or

23.1.1.4. Contractor files a petition for relief as a debtor, or a petition is filed against the Contractor without its consent, and the petition not dismissed within sixty (60) days; or

23.1.1.5. Contractor makes a general assignment for the benefit of its creditors, or a receiver is appointed on account of its insolvency; or

23.1.1.6. Contractor persistently or repeatedly refuses fails, except in cases for which extension of time is provided, to supply enough properly skilled workers or proper materials to complete the Work in the time specified; or

23.1.1.7. Contractor fails to make prompt payment to Subcontractors, or for material, or for labor; or

23.1.1.8. Contractor persistently disregards laws, or ordinances, or instructions of District; or

23.1.1.9. Contractor fails to supply labor, including that of Subcontractors, that can work in harmony with all other elements of labor employed or to be employed on the Work; or

23.1.1.10. Contractor or its Subcontractor(s) is/are otherwise in breach, default, or in substantial violation of any provision of this Contract.

23.1.2. Notification of Termination

23.1.2.1. Upon the occurrence at District's sole determination of any of the above conditions, District may, without prejudice to any other right or remedy, serve written notice upon Contractor and its Surety of District's termination of this Contract and/or the Contractor's right to perform the work of the Contract. This notice will contain the reasons for termination. Unless, within three (3) days after the service of the notice, any and all condition(s) shall cease, and any and all violation(s) shall cease, or arrangement satisfactory to District for the correction of the condition(s) and/or violation(s) be made, this Contract and/or the Contractor's right to perform the Work shall cease and terminate. Upon termination, Contractor shall not be entitled to receive any further payment until the entire Work is finished.

23.1.2.2. Upon termination, District may immediately serve written notice of tender upon Surety whereby Surety shall have the right to takeover and perform this Contract only if Surety:

23.1.2.2.1. Within three (3) days after service upon it of the notice of tender, gives District written notice of Surety's intention to takeover and perform this Contract; and

23.1.2.2.2. Commences performance of the Contract within seven (7) days from date of serving of its notice to District.

23.1.2.3. If Surety fails to notify District or begin performance as indicated herein, District may takeover the Work and execute the Work to completion by any method it may deem advisable at the expense of Contractor and/or its Surety. Contractor and/or its Surety shall be liable to District for any excess cost or other damages the District incurs thereby. Time is of the essence in the Contract. If the District takes over the Work as herein provided, District may, without liability for so doing, take possession of and utilize in completing the Work such materials, appliances, plan, and other property belonging to Contractor as may be on the Site of the Work, in bonded storage, or previously paid for.

23.1.2.4. Conversion to Termination for Convenience. In the event the Contract is terminated under this "District's Right to Terminate Contractor for Cause" section and it is finally determined by an arbitrator, court, jury or other tribunal having jurisdiction, for any reason, that the Contractor was not in default under the provisions hereof or that the District's exercise of its rights under this section was defective, deficient, ineffective, invalid or improper for any reason, the termination shall be deemed a termination for convenience of the District under the "Termination of Contractor for Convenience" section herein and thereupon, the rights and obligations of the District and the Contractor shall be determined in accordance with the "Termination of Contractor for Convenience" section herein.

23.1.3. Effect of Termination

23.1.3.1. Contractor shall, only if ordered to do so by the District, immediately remove from the Site all or any materials and personal property belonging to Contractor that have not been incorporated in the construction of the Work, or which are not in place in the Work. District retains the right, but not the obligation, to keep and use any materials and personal property belonging to Contractor that have not been incorporated in the construction of the Work, or which are not in place in the Work. Contractor and its Surety shall be liable upon the performance bond for all damages caused the District by reason of the Contractor's failure to complete the Contract.

23.1.3.2. In the event that the District shall perform any portion of, or the whole of the Work, pursuant to the provisions of the General Conditions, the District shall not be liable nor account to the Contractor in any way for the time within which, or the manner in which, the Work is performed by the District or for any changes the District may make in the Work or for the money expended by the District in satisfying claims and/or suits and/or other obligations in connection with the Work.

23.1.3.3. In the event that the Contract is terminated for any reason, no allowances or compensation will be granted for the loss of any anticipated profit by the Contractor or any impact or impairment of Contractor's bonding capacity.

23.1.3.4. If the expense to the District to finish the Work exceeds the unpaid Contract Price, Contractor and Surety shall pay difference to District within twenty-one (21) days of District's request.

23.1.3.5. Assignment and Assumption of Subcontracts. District shall have the right (but shall have no obligation) to assume and/or assign to a general contractor or construction manager or other third party who is qualified and has sufficient resources to complete the Work, the rights of the Contractor under its subcontracts with any or all Subcontractors. In the event of an assumption or assignment by the District, no Subcontractor shall have any claim against the District or third party for Work performed by Subcontractor or other matters arising prior to termination of the Contract. The District or any third party, as the case may be, shall be liable only for obligations to the Subcontractor arising after assumption or assignment. Should the District so elect, the Contractor shall execute and deliver all documents and take all steps, including the legal assignment of its contractual rights, as the District may require, for the purpose of fully vesting in the District the rights and benefits of it Subcontractor under Subcontracts or other obligations or commitments. All payments due the Contractor hereunder shall be subject to a right of offset by the District for expenses and damages suffered by the District as a result of any default, acts, or omissions of the Contractor. Contractor must include this assignment provision in all of its contracts with its Subcontractors.

23.1.3.6. The foregoing provisions are in addition to and not in limitation of any other rights or remedies available to District.

23.2. Emergency Termination of Public Contracts Act of 1949

23.2.1. The Contract is subject to termination as provided by sections 4410 and 4411 of the Government Code of the State of California, being a portion of the Emergency Termination of Public Contracts Act of 1949.

23.2.1.1. Section 4410 of the Government Code states:

In the event a national emergency occurs, and public work, being performed by contract, is stopped, directly or indirectly, because of the freezing or diversion of materials, equipment or labor, as the result of an order or a proclamation of the President of the United States, or of an order of any federal authority, and the circumstances or conditions are such that it is impracticable within a reasonable time to proceed with a substantial portion of the work, then the public agency and the contractor may, by written agreement, terminate said contract.

23.2.1.2. Section 4411 of the Government Code states:

Such an agreement shall include the terms and conditions of the termination of the contract and provision for the payment of compensation or money, if any, which either party shall

pay to the other or any other person, under the facts and circumstances in the case.

23.2.2. Compensation to the Contractor shall be determined at the sole discretion of District on the basis of the reasonable value of the Work done, including preparatory work. As an exception to the foregoing and at the District's discretion, in the case of any fully completed separate item or portion of the Work for which there is a separate previously submitted unit price or item on the accepted Schedule of Values, that price shall control. District, in its sole discretion, may adopt the Contract Price as the reasonable value of the Work performed or any portion thereof.

23.3. Termination of Contractor for Convenience

23.3.1. District in its sole discretion may terminate the Contract upon three (3) days written notice to the Contractor. Under a termination for convenience, the District retains the right to all the options available to the District if there is a termination for cause. In case of a termination for convenience, Contractor shall have no claims against the District except:

23.3.1.1. The actual cost for labor, materials, and services performed that is unpaid and can be documented through timesheets, invoices, receipts, or otherwise, and

23.3.1.2. Five percent (5%) of the total cost of work performed as of the date of termination, or five percent (5%) of the value of the Work yet to be performed, whichever is less. This five percent (5%) amount shall be full compensation for all Contractor's and its Subcontractor(s)' mobilization and/or demobilization costs and any anticipated loss profits resulting from termination of the Contractor for convenience.

23.4. Suspension of Work

23.4.1. District may, without cause, order Contractor in writing to suspend, delay or interrupt the Project in whole or in part for such period of time as District may determine. When the District resumes the Project, the Parties will attempt to negotiate an adjustment in the Contract Price for increases or decreases in the cost of performance of the Project caused by suspense, delay or interruption. If the Parties cannot agree on an adjusted Contract Price, the District may terminate the Contract as permitted herein.

23.4.2. In the event the District shall order suspension of the Work, an adjustment shall be made to the Contract Price for increases in the direct cost of performance of the Work of the Contract Documents, actually caused by suspension, delay or interruption ordered by the District; provided however that no adjustment of the Contract Price shall be made to the extent: (i) that performance is, was or would have been so suspended, delayed or interrupted by another cause for which the Contractor is responsible under the Contract Documents; or (ii) that an equitable adjustment is made or denied under another provision of the Contract Documents. The foregoing notwithstanding, any adjustment of the Contract Price shall not include any adjustment to increase the Contractor's overhead, general administrative costs or profit, all of which will remain as reflected in the Schedule of Values submitted by the Contractor pursuant to the Contract Documents. In the event of the District's suspension of the Work, the Contract Time shall be equitably adjusted.

23.5. Scope Reduction

In cases of suspension, partial or complete termination, or at the discretion of the District, the District reserves the right to unilaterally approve a deductive Change Order to reduce scope of work or perform work with other forces or its own forces.

24. CLAIMS RESOLUTION

24.1. Exclusive Remedy.

24.1.1. Compliance with the claim resolution process and timelines described in this Claims Resolution section as well as the notice provisions of the Contract are express conditions precedent to Contractor's right to commence litigation or arbitration, file a claim under the California Government Code, or commence any other legal action related to the Project ("Claims Resolution Process").

24.1.2. Contractor acknowledges that its failure, for any reason, to provide written notice and all required supporting documentation to permit the District's review and evaluation within the time frame required by this Claims Resolution Process, shall be deemed Contractor's waiver, release, discharge and relinquishment of any right to assert, request, or demand any entitlement to an adjustment of the Contract Time or the contract Price on account of any instruction, request, drawings, specifications, action, condition, omission, default or other situation.

24.1.3. To the extent any provision(s) of this Claims Resolution Process conflict with or otherwise impair the timeframes and procedures of Public Contract Code section 9204, the provisions of Section 9204 shall control. If provisions of this Claims Resolution Process are supplementary and/or in addition to the requirements of Section 9204, but do not conflict with or otherwise impair the timeframes and procedures of Section 9204, the provisions of this Claims Resolution Process and the Contract shall control.

24.2. Performance during Claim Resolution Process.

The Contractor shall diligently proceed with Work on the Project at the same time that Claims are addressed under the Claims Resolution Process. It is the intent of District to resolve Claims with the Contractor as close to the events giving rise to the Claims as possible, and to avoid stale or late Claims and the late documenting of Claims. Contractor's failure to diligently proceed in accordance with the District's instructions or the Contract terms will be considered a material breach of the Contract and a waiver of Contractor's rights under this Contract.

24.3. Waiver.

If Contractor fails to timely submit any written notices required under the terms of the Contract or in this Claims Resolution section, Contractor waives and releases its rights regarding further review of its Claim, unless Contractor and District mutually agree in writing to other time limits.

24.4. Intention.

The Claims Resolution Process required herein is intended to provide a concise mechanism for resolving Claims as they arise during the Project, while requiring accurate documentation related to contested issues as to those Claims that are not contemporaneously resolved.

24.5. Other Provisions.

If portions of the Contract, other than this Claims Resolution Process, establish a specific process regarding a specific subject, then that process shall govern and control the resolutions of any disagreements thereunder. Otherwise, the provisions in this Claims Resolution Process shall control the resolution of all Claims.

24.6. Claim Presentation

24.6.1. Claim: A claim is a written demand by Contractor (or by Contractor on behalf of a Subcontractor) that the Contractor must submit by **registered mail or certified mail return receipt requested** for:

24.6.1.1. An extension to the Contract Time, including relief from damages or penalties assessed by the District for delay;

24.6.1.2. Payment of money or damages arising from work done by, or on behalf of, the Contractor pursuant to the Contract and payment that is not otherwise expressly provided for in the Contract Documents or the Contractor is not otherwise entitled; or

24.6.1.3. Payment that is disputed by the District.

(“Claim”)

24.6.2. A PCO may be a Claim, but the Parties agree that a PCO shall only be a Claim if:

24.6.2.1. The District states in writing that it disagrees with the terms of a PCO and directs the Contractor to utilize the Claim Resolution Process, or

24.6.2.2. The District rejects in whole or in part a PCO and the Contractor states in writing that it is utilizing the Claim Resolution Process for the portion of the PCO that the District rejected.

24.6.3. Subcontractor Claims.

24.6.3.1. Public Contract Code section 9204(d)(5) states that the Contractor may present to the District a Claim on behalf of a Subcontractor or lower tier Subcontractor. A Subcontractor may request in writing, either on his or her own behalf or on behalf of a lower tier Subcontractor, that the Contractor present a claim for Work which was performed by the Subcontractor or by a lower tier Subcontractor on behalf of the Subcontractor. The Subcontractor requesting that the Claim be presented to the District shall furnish reasonable documentation to support the Claim. Within 45 days of receipt of this written request, the Contractor shall notify the Subcontractor in writing as to whether the Contractor presented the claim to the District and, if the Contractor did not present the Claim, provide the Subcontractor with a statement of the reasons for not having done so.

24.6.3.2. Contractor is responsible for providing this Claims Resolution Process to its Subcontractors and for ensuring that all Subcontractors or others who may assert Claims by and through Subcontractors and/or the Contractor are informed of this Claims Resolution Process. No Claim submitted by any party that fails to follow the provisions of this Claims Resolution Process will be considered. Contractor shall indemnify, keep and hold harmless the District and its consultants, against all suits, claims, damages, losses, and expenses, including but not limited to attorney’s fees, caused by, arising out of, resulting from, or incidental to, the failure to provide this Claims Resolution Process to its Subcontractors or others who may assert Claims by and through Subcontractors and/or the Contractor.

24.6.4. Contractor Must Timely Identify, Present and Document Any Claim

24.6.4.1. Every Claim shall be stated with specificity in writing and signed by Contractor under penalty of perjury and presented to the District within ten (10) calendar days from the date Contractor discovers or reasonably should discover, that an act, error or omission of District, its agents or employees, or action, condition or other situation has occurred that may entitle Contractor to make a Claim. This shall include the Contractor’s actual or constructive knowledge of any instruction, request, drawings, specifications, action, condition, omission, default or other situation for which the contractor believes there should an adjustment of the Contract Price or Contract Time. Contractor shall provide this writing even if Contractor has not yet been damaged, delayed, or incurred extra cost when Contractor discovers, or reasonably should

discover, the act, error, omission, action, condition or situation giving rise to the incidents giving rise to the Claim. The writing shall:

24.6.4.1.1. Identify all of the issues, events, conditions, circumstances and/or causes giving rise to the Claim;

24.6.4.1.2. Identify all pertinent dates and/or durations and all actual and/or anticipated effects on the Contract Price, milestones and/or Contract Time adjustments; and

24.6.4.1.3. Identify in detail line-item costs if the Claim seeks money.

24.6.4.1.4. If the Claim involves extra work, a detailed cost breakdown of the amounts the Contractor is seeking, including actual cost records (including without limitation, payroll records, material and rental invoices and the like) demonstrating that those costs have actually been incurred. To the extent costs have not yet been incurred at the time the Claim is submitted, actual cost records must be submitted on a current basis not less than once a week during any periods costs are incurred. A cost record will be considered current if submitted within seven (7) days of the date the cost reflected in the record is incurred. At the request of District, extra costs may be subject to further verification procedures (such as having an inspector verify the performance of alleged extra work on a daily basis).

24.6.4.1.5. If the Claim involves an error or omission in the Contract Documents:

24.6.4.1.5.1. An affirmative representation under penalty of perjury by Contractor and any affected Subcontractors and suppliers that the error or omission was not discovered prior to submitting a proposal for the Work, and

24.6.4.1.5.2. A detailed statement demonstrating that the error or omission reasonably should not have been discovered, by Contractor, its Subcontractors and suppliers, prior to submitting a proposal for the Work.

24.6.4.1.6. If the Claim involves a request for additional compensation for escalation of materials costs, then this provision exclusively governs those request(s) by Contractor and the following are all conditions precedent to Contractor's submission of a Change Order Request or Claim for additional compensation for escalation of materials costs.

24.6.4.1.6.1. Contractor shall not be entitled to submit a request for compensation for escalation of materials unless the actual increase in the cost of the materials in question exceeds ten percent (10%) of the **total** material costs on the Project at the time of bid.

24.6.4.1.6.2. The cost escalation is the result of unusual and unforeseeable market conditions not reasonably foreseeable at the time of award of the Contract and was not an escalated cost resulting from any action or inaction of the Contractor.

24.6.4.1.6.3. Contractor timely ordered and/or purchased the materials at issue, based on (1) Contractor's constructive knowledge of the supply chain for required materials and (2) Contractor's request to utilize the provisions in the Contract Documents related to the District's payment for materials and equipment purchased and stored on Site or offsite.

24.6.4.1.6.4. Contractor's material costs were reasonable at the time of Contractor's bid for the Project.

24.6.4.1.6.5. Contractor demonstrates an actual increase in the cost of materials in its Contract Price at the time of award of the Contract and/or as reflected in Contractor's escrowed bid documents compared to Contractor's actual material payment cost paid either at time of purchase or delivery, whichever is earlier.

24.6.4.1.6.6. An actual year-to-date price increase has occurred and can be substantiated by the E.N.R. 20-City Average Material Cost Index for the material at issue that demonstrates the claim for an increase in price of the material at the time of delivery of the higher priced material to the Project.

24.6.4.2. The writing shall be accompanied by all documents substantiating Contractor's position regarding the Claim.

24.6.4.3. A Claim that asserts an effect on any schedule milestones and/or Contract Time shall include all pertinent scheduling data demonstrating the impact(s) on the critical path(s), milestone(s) and/or Contract Time.

24.6.4.4. Contractor agrees that it shall not base its damages, its calculations or its Claim on a "total cost" approach, a "modified total cost" approach or a "jury verdict method" approach.

24.6.5. Certification. Each copy of the Claim Documentation shall be certified by a responsible officer of the Contractor in accordance with the requirements of the Contract Documents. This certification shall be under penalty of perjury and must include the following language immediately above or before the Contractor's signature: ***"I declare under penalty of perjury under the laws of the State of California that the information provided and statements made in this Claim are true and correct, substantiated and of merit."*** The Contractor acknowledges that this requirement is not a mere formality but is intended to ensure that the Contractor only submits Claims that it believes are true and correct, substantiated and have merit. Should Contractor fail to submit the foregoing written statement signed under penalty of perjury, Contractor waives and releases its Claim, including all rights and remedies in connection therewith. This certification must include a certification of any portion of the Claim from Subcontractor(s) or others who are asserting Claims by and through Subcontractors and/or the Contractor

24.6.6. District's Written Statement/Decision on Claim. The District shall issue a written statement/decision regarding the Claim to the Contractor within forty-five (45) days of receipt of the written Claim from the Contractor, or three (3) days after the District's first regular governing board meeting after that 45-day period if the District's governing board does not meet within that first 45-day period. If the District fails to timely provide a written statement/decision regarding the Claim, the Claim shall be deemed rejected in its entirety.

24.6.7. Contractor Must Demand an Informal Meet and Confer Conference if Contractor Pursues Any Claim

24.6.7.1. FAILURE OF A CONTRACTOR TO TIMELY DEMAND A MEET AND CONFER CONFERENCE IS A WAIVER OF ITS RIGHT TO PURSUE ALL OR A PORTION OF ITS CLAIM.

24.6.7.2. Where There Is No Agreement: If there is no agreement between Contractor and the District on a Claim, then within ten (10) calendar days of the date of the District's written statement/decision in response to a Claim or PCO, if Contractor pursues that Claim, then Contractor must demand, by **registered mail or certified mail return receipt requested**, a meet and confer conference with District staff. A meet and confer conference with District staff shall be a condition precedent to Contractor seeking any further relief, including a mediation as indicated below.

24.6.7.3. Where There Is Partial Agreement: If Contractor and the District partially agree on a Claim but do not reach complete agreement, then the Parties shall complete a Change Order, if applicable, for the issues and/or amounts agreed to. For those issues not agreed to, if Contractor pursues those issues from that Claim, then Contractor must demand, by **registered mail or certified mail return receipt requested**, a meet and confer conference with District staff regarding those issues. A meet and confer conference with District staff shall be a condition precedent to Contractor seeking any further relief, including a mediation as indicated below, in connection with the District's rejection.

24.6.7.4. Meet and Confer Conference. District and Contractor shall schedule the meet and confer conference as soon as reasonably possible after Contractor's written demand for a meet and confer conference, but in no case later than thirty (30) days after Contractor's demand.

24.6.7.5. District's Written Decision. Within ten (10) **business** days of the meet and confer conference, the District shall issue a written decision. If the District fails to timely provide a written statement/decision after the meet and confer conference, all Claim issues that were part of the meet and confer conference shall be deemed rejected in their entirety.

24.6.7.5.1. If the District's decision completely resolves the Claim, then the Parties shall complete a Change Order, if applicable, for the issues and/or amounts agreed to.

24.6.7.5.2. If the District rejects the Contractor's Claim in whole or in part or does not issue a timely written response, then the parties shall mediate the remaining issues of the Claim.

24.6.7.5.3. Contractor's costs incurred in seeking relief for Claims are not recoverable from District.

24.6.8. Mediation.

24.6.8.1. At the District's sole discretion, this mediation may be a multiple-party mediation with the Architect, the Construction Manager, the Inspector, and/or other District consultants.

24.6.8.2. The District and Contractor shall mutually agree to a mediator within ten (10) **business** days after the disputed portion of the Claim has been identified in writing. If the parties cannot agree upon a mediator, each party shall select a mediator and those mediators shall select a qualified neutral third party to mediate with regard to the disputed portion of the Claim. Each party shall bear the fees and costs charged by its respective mediator in connection with the selection of the neutral mediator.

24.6.9. Contractor's Obligation to File a Government Code Claim. Nothing in this Contract, including this Claims Resolution Process, waives, modifies or tolls the Contractor's obligation to present a timely claim under Government Code section 910, et seq. Therefore, in addition to complying with this Claims Resolution Process, the Contractor is required to present claims to the District pursuant to Government Code section 910, et seq. If after the requirements of this Claims Resolution Process are satisfied, and all or a portion of the Claim remains unresolved, and if the Government Code claim is rejected by the District, the Contractor may proceed under the post-mediation provisions of this Claims Resolution Process.

24.6.10. Post Mediation Provisions

24.6.10.1. Claims of \$375,000 or Less: The provisions of Public Contract Code § 20104.4 shall apply. Pursuant to Public Contract Code § 20104.4(a), within sixty (60) days, but no earlier

than thirty (30) days, following the filing of responsive pleadings, the court shall submit the matter to nonbinding mediation unless waived by mutual stipulation of both parties. Pursuant to Public Contract Code § 9204(d)(2)(D), a mediation conducted pursuant to this Claims Resolution Process shall excuse the obligation under Public Contract Code § 20104.4(a) to mediate after litigation has been commenced unless otherwise agreed to by the parties in writing.

24.6.10.2. Litigation of Claims in Excess of \$375,000. If, after a mediation as indicated above, the Parties have not resolved the Claim, either Party may commence an action in a court of competent jurisdiction to contest that decision within ninety (90) days following the conclusion of that mediation or one (1) year following the accrual of the cause of action, whichever is later. By mutual agreement, the Parties can agree to instead resolve the Claim through arbitration.

24.6.11. The District shall be entitled to remedy any false claims, as defined in California Government Code section 12650 *et seq.*, made to the District by the Contractor or any Subcontractor under the standards set forth in Government Code section 12650 *et seq.* Any Contractor or Subcontractor who submits a false claim shall be liable to the District for three times the amount of damages that the District sustains because of the false claim. A Contractor or Subcontractor who submits a false claim shall also be liable to the District for (a) the costs, including attorney fees, of a civil action brought to recover any of those penalties or damages, and (b) a civil penalty of up to \$11,000 for each false claim. In addition, Contractor may be subject to criminal prosecution under California Penal Code §72 and/or civil liability under False Claims Act. If so, the District may be entitled to recover its costs incurred to investigate any False Claim, including but not limited to attorneys' fees and expert fees incurred in connection with that investigation.

24.7. Documentation of Resolution.

If a Claim is resolved, the District shall determine if that resolution shall be documented in an Agreement and Release of Any and All Claims form or other document, as appropriate.

24.8. Claim Resolution Process – Non-Applicability.

The procedures and provisions in this Claims Resolution section shall **not** apply to:

24.8.1. District's determination of what Work is or will be constructed, or whether the Work complies with the Contract Documents for purposes of accepting the Work;

24.8.2. District's rights and obligations as a public entity, such as, but without limitation, the revocation of prequalified or qualified status, barring a contractor from District contracts, the imposition of penalties or forfeitures prescribed by statute or regulation; provided, however, that penalties imposed against a public entity by statutes such as Public Contract Code section 7107, shall be subject to the mandatory dispute resolution provisions of this Claims Resolution section and the Contract;

24.8.3. Personal injury, wrongful death or property damage claims;

24.8.4. Latent defect or breach of warranty or guarantee to repair;

24.8.5. Stop notices or stop payment notices; or

24.8.6. Any other District rights as set forth herein.

24.9. The District's failure to respond to a Claim from the Contractor within the time periods described herein or to otherwise meet the time requirements of Public Contract Code section 9204 shall

automatically result in the Claim being deemed rejected in its entirety, with no admission by the District as to the merits of the Claim.

- 24.10.** If District fails to timely issue payment for any Claim or portion of a Claim as required pursuant to these Claim Resolution Procedures, the Contractor is permitted to assess interest indicated in Public Contract Code section 9204. Notwithstanding this provision, and in accordance with Public Contract Code section 7107, the District is entitled to withhold up to 150% of disputed amounts and the District shall not be liable for payment of interest on such disputed amounts pending final adjudication of such disputes.

25. LABOR, WAGE & HOUR, APPRENTICE AND RELATED PROVISIONS

25.1. Contractor & Subcontractor Registration

25.1.1. Contractor shall comply with the registration and compliance monitoring provisions of Labor Code section 1771.4, including furnishing its CPRs to the Labor Commissioner of California and complying with any applicable enforcement by the Department of Industrial Relations. Labor Code section 1771.1(a) states the following:

“A contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal, subject to the requirements of Section 4104 of the Public Contract Code, or engage in the performance of any contract for public work, as defined in this chapter, unless currently registered and qualified to perform public work pursuant to Section 1725.5. It is not a violation of this section for an unregistered contractor to submit a bid that is authorized by Section 7029.1 of the Business and Professions Code or by Section 10164 or 20103.5 of the Public Contract Code, provided the contractor is registered to perform public work pursuant to Section 1725.5 at the time the contract is awarded.”

25.1.2. Contractor acknowledges that, for purposes of Labor Code section 1725.5, all or some of the Work is a public work to which Labor Code section 1771 applies. Contractor shall comply with Labor Code section 1725.5, including without limitation the registration requirements. Additionally, all Contractor's Subcontractors shall comply with Labor Code section 1725.5 to be qualified to bid on, be listed in a bid proposal, subject to the requirements of Section 4104 of the Public Contract Code, or engage in the performance of the Contract. Contractor represents that all of its Subcontractors are registered pursuant to Labor Code section 1725.5.

25.1.3. The Project is subject to compliance monitoring and enforcement by the Department of Industrial Relations. Contractor shall post job site notices, as prescribed by regulation. Contractor shall comply with all requirements of Labor Code section 1771.4, except the requirements that are exempted by the Labor Commissioner for the Project.

25.2. Wage Rates, Travel and Subsistence

25.2.1. Pursuant to the provisions of article 2 (commencing at section 1770), chapter 1, part 7, division 2, of the Labor Code of California, the general prevailing rate of per diem wages and the general prevailing rate for holiday and overtime work in the locality in which this public work is to be performed for each craft, classification, or type of worker needed to execute this Contract are on file at the District's principal office and copies will be made available to any interested party on request and are available to any interested party on request or at www.dir.ca.gov/oprl/statistics_and_databases.html. Contractor shall obtain and post a copy of these wage rates at the job site.

25.2.2. Holiday and overtime work, when permitted by law, shall be paid for at a rate of at least one and one-half times the above specified rate of per diem wages, unless otherwise specified. The holidays upon which those rates shall be paid need not be specified by the District, but shall be all holidays recognized in the applicable collective bargaining agreement. If the prevailing rate is not based on a collectively

bargained rate, the holidays upon which the prevailing rate shall be paid shall be as provided in Section 6700 of the Government Code.

25.2.3. Contractor shall pay and shall cause to be paid each worker engaged in Work on the Project not less than the general prevailing rate of per diem wages determined by the Director of the Department of Industrial Relations (“DIR”) (“Director”), regardless of any contractual relationship which may be alleged to exist between Contractor or any Subcontractor and such workers.

25.2.4. If during the period this bid is required to remain open, the Director determines that there has been a change in any prevailing rate of per diem wages in the locality in which the Work under the Contract is to be performed, such change shall not alter the wage rates in the Invitation to Bid or the Contract subsequently awarded.

25.2.5. Pursuant to Labor Code section 1775, Contractor shall, as a penalty to District, forfeit the statutory amount, (currently not to exceed two hundred dollars (\$200) for each calendar day, or portion thereof), for each worker paid less than the prevailing rates, as determined by the District and/or the Director, for the work or craft in which that worker is employed for any public work done under Contract by Contractor or by any Subcontractor under it.

25.2.5.1. The amount of the penalty shall not be less than forty dollars (\$40) for each calendar day, or portion thereof, unless the failure of Contractor was a good faith mistake and, if so, the error was promptly and voluntarily corrected when brought to the attention of Contractor.

25.2.5.2. The amount of the penalty shall not be less than eighty dollars (\$80) for each calendar day or portion thereof, if Contractor has been assessed penalties within the previous three (3) years for failing to meet Contractor’s prevailing wage obligations on a separate contract, unless those penalties were subsequently withdrawn or overturned.

25.2.5.3. The amount of the penalty may not be less than one hundred twenty dollars (\$120) for each calendar day, or portion thereof, if the Labor Commissioner determines the Contractor willfully violated Labor Code section 1775.

25.2.5.4. The difference between such prevailing wage rates and the amount paid to each worker for each calendar day or portion thereof for which each worker was paid less than the prevailing wage rate, shall be paid to each worker by Contractor.

25.2.6. Any worker employed to perform Work on the Project, which Work is not covered by any classification listed in the general prevailing wage rate of per diem wages determined by the Director, shall be paid not less than the minimum rate of wages specified therein for the classification which most nearly corresponds to Work to be performed by him, and such minimum wage rate shall be retroactive to time of initial employment of such person in such classification.

25.2.7. Pursuant to Labor Code section 1773.1, per diem wages are deemed to include employer payments for health and welfare, pension, vacation, travel time, subsistence pay, and apprenticeship or other training programs authorized by section 3093, and similar purposes.

25.2.8. Contractor shall post at appropriate conspicuous points on the Site of Project, a schedule showing all determined minimum wage rates and all authorized deductions, if any, from unpaid wages actually earned. In addition, Contractor shall post a sign-in log for all workers and visitors to the Site, a list of all subcontractors of any tier on the Site, and the required Equal Employment Opportunity poster(s).

25.3. Hours of Work

25.3.1. As provided in article 3 (commencing at section 1810), chapter 1, part 7, division 2, of the Labor Code, eight (8) hours of labor shall constitute a legal days work. The time of service of any worker employed at any time by Contractor or by any Subcontractor on any subcontract under this Contract upon the Work or upon any part of the Work contemplated by this Contract shall be limited and restricted by Contractor to eight (8) hours per day, and forty (40) hours during any one week, except as hereinafter provided. Notwithstanding the provisions hereinabove set forth, Work performed by employees of Contractor in excess of eight (8) hours per day and forty (40) hours during any one week, shall be permitted upon this public work upon compensation for all hours worked in excess of eight (8) hours per day at not less than one and one-half times the basic rate of pay.

25.3.2. Contractor shall keep and shall cause each Subcontractor to keep an accurate record showing the name of and actual hours worked each calendar day and each calendar week by each worker employed by Contractor in connection with the Work or any part of the Work contemplated by this Contract. The record shall be kept open at all reasonable hours to the inspection of District and to the Division of Labor Standards Enforcement of the DIR.

25.3.3. Pursuant to Labor Code section 1813, Contractor shall as a penalty to the District forfeit the statutory amount (believed by the District to be currently twenty five dollars (\$25)) for each worker employed in the execution of this Contract by Contractor or by any Subcontractor for each calendar day during which such worker is required or permitted to work more than eight (8) hours in any one calendar day and forty (40) hours in any one calendar week in violation of the provisions of article 3 (commencing at section 1810), chapter 1, part 7, division 2, of the Labor Code.

25.3.4. Any Work necessary to be performed after regular working hours, or on Sundays or other holidays shall be performed without additional expense to the District.

25.4. Payroll Records

25.4.1. Contractor and all Subcontractors must comply with the compliance monitoring provisions of Labor Code section 1771.4, including furnishing its certified payroll records ("CPR(s)") to the Labor Commissioner of California and complying with any applicable enforcement by DIR. Labor Code section 1771.4 requires Contractor and Subcontractors to provide electronic copies of CPRs to the Labor Commissioner of California at least once every thirty (30) days, and within thirty (30) days of Project Completion. The failure to timely provide the CPRs could result in penalties as determined by Labor Code section 1771.4, applicable laws, and regulations

25.4.2. If requested by the District, Contractor shall provide to the District and shall cause each Subcontractor performing any portion of the Work to provide the District and an accurate CPR(s), showing the name, address, social security number, work classification, straight time, and overtime hours worked each day and week, and the actual per diem wages paid to each journeyman, apprentice, worker, or other employee employed by the Contractor and/or each Subcontractor in connection with the Work.

25.4.3. In addition to any other requirements pursuant to Labor Code sections 1770, et seq., the CPRs enumerated hereunder shall be certified and shall be provided to the District on a weekly basis. The CPRs from the Contractor and each Subcontractor for each week shall be provided on or before Wednesday of the week following the week covered by the CPRs. District shall not make any payment to Contractor until:

25.4.3.1. Contractor and/or its Subcontractor(s) provide CPRs acceptable to the District, and

25.4.3.2. The District is given sufficient time to review and/or audit the CPRs to determine their acceptability. Any delay in Contractor and/or its Subcontractor(s) providing CPRs to the District in a timely manner will directly delay the District's review and/or audit of the CPRs

and Contractor's payment.

25.4.4. All CPRs shall be available for inspection at all reasonable hours at the principal office of Contractor on the following basis:

25.4.4.1. A certified copy of an employee's CPR shall be made available for inspection or furnished to the employee or the employee's authorized representative on request.

25.4.4.2. CPRs shall be made available for inspection or furnished upon request to a representative of District, Division of Labor Standards Enforcement, Division of Apprenticeship Standards, and/or the Department of Industrial Relations.

25.4.4.3. CPRs shall be made available upon request by the public for inspection or copies thereof made; provided, however, that a request by the public shall be made through either the District, Division of Apprenticeship Standards, or the Division of Labor Standards Enforcement. If the requested CPRs have not been provided pursuant to the provisions herein, the requesting party shall, prior to being provided the records reimburse the costs of preparation by Contractor, Subcontractors, and the entity through which the request was made. The public shall not be given access to the records at the principal office of Contractor.

25.4.5. The form of certification for the CPRs shall be as follows:

I, _____ (Name-Print), the undersigned, am the _____
_____ (Position in business) with the authority to act for and on behalf of _____
_____ (Name of business and/or Contractor), certify under penalty of perjury that the
records or copies thereof submitted and consisting of _____
(Description, number of pages) are the originals or true, full, and correct copies of the originals
which depict the payroll record(s) of actual disbursements by way of cash, check, or whatever
form to the individual or individual named, and (b) we have complied with the requirements of
sections 1771, 1811, and 1815 of the Labor Code for any work performed by our employees on
the Project.

Date: _____ Signature: _____
(Section 16401 of Title 8 of the California Code of Regulations)

25.4.6. Each Contractor shall file a certified copy of the CPRs with the entity that requested the records within ten (10) days after receipt of a written request.

25.4.7. Any copy of records made available for inspection as copies and furnished upon request to the public or any public agency by District, Division of Apprenticeship Standards, or Division of Labor Standards Enforcement shall be marked or obliterated in such a manner as to prevent disclosure of an individual's name, address, and social security number. The name and address of Contractor awarded Contract or performing Contract shall not be marked or obliterated.

25.4.8. Contractor shall inform District of the location of the records enumerated hereunder, including the street address, city, and county, and shall, within five (5) Business Days, provide a notice of change of location and address.

25.4.9. In the event of noncompliance with the requirements of this section, Contractor shall have ten (10) days in which to comply subsequent to receipt of written notice specifying in what respects Contractor must comply with this section. Should noncompliance still be evident after the ten (10) day period, Contractor shall, as a penalty to District, forfeit one hundred dollars (\$100) for each calendar day, or portion thereof, for each worker, until strict compliance is effectuated. Upon the request of Division of Apprenticeship Standards or Division of Labor Standards Enforcement, these penalties shall be withheld

from progress payments then due.

25.4.10. It shall be the responsibility of Contractor to ensure compliance with the provisions of Labor Code section 1776.

25.5. Apprentices

25.5.1. Contractor acknowledges and agrees that, if this Contract involves a dollar amount greater than or a number of working days greater than that specified in Labor Code section 1777.5, then this Contract is governed by the provisions of Labor Code Section 1777.5. It shall be the responsibility of Contractor to ensure compliance with this Article and with Labor Code section 1777.5 for all apprenticeship occupations.

25.5.2. Apprentices of any crafts or trades may be employed and, when required by Labor Code section 1777.5, shall be employed provided they are properly registered in full compliance with the provisions of the Labor Code.

25.5.3. Every apprentice shall be paid the standard wage paid to apprentices under the regulations of the craft or trade at which the apprentice is employed, and shall be employed only at the work of the craft or trade to which the apprentice is registered.

25.5.4. Only apprentices, as defined in section 3077 of the Labor Code, who are in training under apprenticeship standards and written apprentice agreements under chapter 4 (commencing at section 3070), division 3, of the Labor Code, are eligible to be employed. The employment and training of each apprentice shall be in accordance with the provisions of the apprenticeship standards and apprentice agreements under which the apprentice is training.

25.5.5. Pursuant to Labor Code section 1777.5, if that section applies to this Contract as indicated above, Contractor and any Subcontractors employing workers in any apprenticeable craft or trade in performing any Work under this Contract shall apply to the applicable joint apprenticeship committee for a certificate approving the Contractor or Subcontractor under the applicable apprenticeship standards and fixing the ratio of apprentices to journeymen employed in performing the Work.

25.5.6. Pursuant to Labor Code section 1777.5, if that section applies to this Contract as indicated above, Contractor and any Subcontractor may be required to make contributions to the apprenticeship program.

25.5.7. If Contractor or Subcontractor willfully fails to comply with Labor Code section 1777.5, then, upon a determination of noncompliance by the Administrator of Apprenticeship, it shall:

25.5.7.1. Be denied the right to bid on any subsequent project for one (1) year from the date of such determination;

25.5.7.2. Forfeit as a penalty to District the full amount as stated in Labor Code section 1777.7. Interpretation and enforcement of these provisions shall be in accordance with the rules and procedures of the California Apprenticeship Council and under the authority of the Chief of the Division of Apprenticeship Standards.

25.5.8. Contractor and all Subcontractors shall comply with Labor Code section 1777.6, which section forbids certain discriminatory practices in the employment of apprentices.

25.5.9. Contractor shall become fully acquainted with the law regarding apprentices prior to commencement of the Work. Special attention is directed to sections 1777.5, 1777.6, and 1777.7 of the Labor Code, and title 8, California Code of Regulations, section 200 et seq. Questions may be directed to the State Division of Apprenticeship Standards, 455 Golden Gate Avenue, San Francisco, California 94102.

25.5.10. Contractor shall ensure compliance with all certification requirements for all workers on the Project including, without limitation, the requirements for electrician certification in Labor Code sections 108, et seq.

25.6. Non-Discrimination

25.6.1. Contractor herein agrees not to discriminate in its recruiting, hiring, promotion, demotion, or termination practices on the basis of race, religious creed, national origin, ancestry, sex, age, or physical handicap in the performance of this Contract and to comply with the provisions of the California Fair Employment and Housing Act as set forth in part 2.8 of division 3 of the California Government Code, commencing at section 12900; the Federal Civil Rights Act of 1964, as set forth in Public Law 88-352, and all amendments thereto; Executive Order 11246, and all administrative rules and regulations found to be applicable to Contractor and Subcontractor.

25.6.2. Special requirements for Federally Assisted Construction Contracts: During the performance of this Contract, Contractor agrees to incorporate in all subcontracts the provisions set forth in Chapter 60-1.4(b) of Title 41 published in Volume 33 No. 104 of the Federal Register dated May 28, 1968.

25.7. Labor First Aid

Contractor shall maintain emergency first aid treatment for Contractor's workers on the Project which complies with the Federal Occupational Safety and Health Act of 1970 (29 U.S.C. § 651 et seq.) the California Occupational Safety and Health Act of 1973, and all related regulations, including without limitation section 330 et seq. of Title 8 of the California Code of Regulations.

26. MISCELLANEOUS

26.1. Assignment of Antitrust Actions

26.1.1. Section 7103.5(b) of the Public Contract Code states:

In entering into a public works contract or subcontract to supply goods, services, or materials pursuant to a public works contract, the Contractor or subcontractor offers and agrees to assign to the awarding body all rights, title, and interest in and to all causes of action it may have under Section 4 of the Clayton Act (15 U.S.C. Sec. 15) or under the Cartwright Act (Chapter 2 (commencing with Section 16700) of Part 2 of Division 7 of the Business and Professions Code), arising from purchases of goods, made and become effective at the time the awarding body tenders final payment to the Contractor, without further acknowledgment by the parties.

26.1.2. Section 4552 of the Government Code states:

In submitting a bid to a public purchasing body, the bidder offers and agrees that if the bid is accepted, it will assign to the purchasing body all rights, title, and interest in and to all causes of action it may have under Section 4 of the Clayton Act (15 U.S.C. Sec. 15) or under the Cartwright Act (Chapter 2 (commencing with Section 16700) of Part 2 of Division 7 of the Business and Professions Code), arising from purchases of goods, materials, or services by the bidder for sale to the purchasing body pursuant to the bid. Such assignment shall be made and become effective at the time the purchasing body tenders final payment to the bidder.

26.1.3. Section 4553 of the Government Code states:

If an awarding body or public purchasing body receives, either through judgment or settlement, a monetary recovery for a cause of action assigned under this chapter, the assignor shall be entitled to receive reimbursement for actual legal costs incurred and may, upon demand, recover from the

public body any portion of the recovery, including treble damages, attributable to overcharges that were paid by the assignor but were not paid by the public body as part of the bid price, less the expenses incurred in obtaining that portion of the recovery.

26.1.4. Section 4554 of the Government Code states:

Upon demand in writing by the assignor, the assignee shall, within one year from such demand, reassign the cause of action assigned under this part if the assignor has been or may have been injured by the violation of law for which the cause of action arose and (a) the assignee has not been injured thereby, or (b) the assignee declines to file a court action for the cause of action.

26.1.5. Under this Article, “public purchasing body” is District and “bidder” is Contractor.

26.2. **Excise Taxes**

If, under Federal Excise Tax Law, any transaction hereunder constitutes a sale on which a Federal Excise Tax is imposed and the sale is exempt from such Federal Excise Tax because it is a sale to a State or Local Government for its exclusive use, District, upon request, will execute documents necessary to show (1) that District is a political subdivision of the State for the purposes of such exemption, and (2) that the sale is for the exclusive use of District. No Federal Excise Tax for such materials shall be included in any Contract Price.

26.3. **Taxes**

Contract Price is to include any and all applicable sales taxes or other taxes that may be due in accordance with section 7051 of the Revenue and Taxation Code; Regulation 1521 of the State Board of Equalization or any other tax code that may be applicable.

26.4. **Shipments**

All shipments must be F.O.B. destination to Site or sites, as indicated in the Contract Documents. There must be no charge for containers, packing, unpacking, drayage, or insurance. The total Contract Price shall be all inclusive (including sales tax) and no additional costs of any type will be considered.

26.5. **Compliance with Government Reporting Requirements**

If this Contract is subject to federal or other governmental reporting requirements because of federal or other governmental financing in whole or in part for the Project which it is part, or for any other reason, Contractor shall comply with those reporting requirements at the request of the District at no additional cost.

END OF DOCUMENT

DOCUMENT 00 71 00

SPECIAL CONDITIONS

1. Project Description

The information provided here is a summary only. All bidders must thoroughly review the Plans and Specifications and the other Contract Documents for a full understanding of the scope of the Work of the Project.

a. Scope.

Furnishing all labor, materials, and equipment, and services as may be needed to remove existing roofs and installing new roof systems on each building and breezeway.

b. Preliminary (Tentative) Schedule. These dates are subject to change, at the District's discretion.

- (1) The District anticipates awarding the Project, if it awards it at all, at its Board meeting in January 17, 2023.
- (2) The District anticipates issuing a Notice to Proceed to the successful Contractor on January 18, 2024.
- (3) Based on this, the District expects Project Completion on August 2, 2024.

2. Mitigation Measures

Contractor shall comply with all applicable mitigation measures, if any, adopted by any public agency with respect to this Project pursuant to the California Environmental Quality Act. (Public Resources Code section 21000 et. seq.) The District's Mitigation Monitoring Plan is not a Contract Document, but is referenced and available as indicated in the Existing Information and Documentation Regarding Project Site (Document 00 31 19).

3. Site Specific Conditions

- a. **Access.** Access to the school buildings and entry to buildings, classrooms, restrooms, mechanical rooms, electrical rooms, or other rooms, for construction purposes, must be coordinated with District and onsite District personnel before Contractor commences Work. Unless agreed to otherwise in writing, only a school custodian will be allowed to unlock and lock doors in existing building(s). The custodian will be available only while school is in session. If a custodian is required to arrive before 7:00 a.m. or leave after 3:30 p.m. to accommodate Contractor's Work, the overtime wages for the custodian will be paid by Contractor, unless, at the discretion of District, other arrangements are made in advance.
- b. **Master Key.** Upon request, District may, at its own discretion, provide a master key to the school site for the convenience of Contractor. Contractor agrees to pay all expenses to re-key the entire school site and all other affected District buildings if the master key is lost or stolen or if any unauthorized party obtains a copy of the key or access to the school.
- c. **Maintaining Services.** Contractor is advised that Work is to be performed in spaces regularly scheduled for instruction. Interruption and/or periods of shutdown of public access, electrical service, water service, lighting, or other utilities shall be only as arranged in advance with District. Contractor shall provide temporary services to all facilities interrupted by Contractor's Work.
- d. **Maintaining Utilities.** Contractor shall maintain in operation during term of Contract, drainage lines, storm drains, sewers, water, gas, electrical, steam, and other utility service lines within working area.

- e. **Work During Instructional Time.** By submitting its bid, Contractor affirms that Work may be performed during ongoing instruction in existing facilities. If so, Contractor agrees to cooperate to the best of its ability to minimize any disruption to the school up to, and including, rescheduling specific work activities, at no additional cost to District.
- f. **No Work During Student Testing.** Contractor shall, at no additional cost to District and at District's request, coordinate its Work to not disturb District students including, without limitation, not performing any Work when students at the Site are taking State-required tests.
- g. **Badge and Vest Policy for Contractors.** Contractor shall provide their workers and all of Subcontractors' workers, and delivery personnel or others entering the Site, with identification badges and a brightly colored construction vest. These badges and vests shall be worn by all persons who are working on the Project Site.

(1) Badges must be filled out in full and contain the following information:

- a) Name of Contractor
- b) Name of Employee
- c) Contractor's address and phone number

(2) Badges must be worn by all these persons when on Site and must be visible at all times. Contractors must inform these persons that they are required to allow District employees, the Architect, the Construction Manager, the Program Manager, or the Project Inspector to review the information on the badges upon request to, without limitation, confirm a person's identity and a person's right to be on Site, and in any particular area on the Site, at any time.

(3) Failure to display an identification badge and/or to wear a vest as required by this policy may result in the assessment of fines against the Contractor.

4. **Fingerprinting**

The Contractor must comply with the Criminal Background Investigation / Fingerprinting Certification (Doc. 00 45 85) by utilizing only the following method indicated (checked) and not any other method.



All Workers Fingerprinted. The Contractor has complied with the fingerprinting requirements of Education Code section 45125.1 with respect to all Contractor's employees and all of its subcontractors' employees who interact with pupils, outside of the immediate supervision and control of the pupil's parent or guardian or a school employee, has a valid criminal records summary as described in Education Code Section 44237 (Contractor shall "require each applicant for employment in a position requiring contact with minor pupils to submit two sets of fingerprints prepared for submittal by the employer to the Department of Justice for the purpose of obtaining criminal record summary information from the Department of Justice and the Federal Bureau of Investigation."). A complete and accurate list of Contractor's employees and of all of its subcontractors' employees who may interact with District pupils during the course and scope of the Contract is attached hereto; and/or



Physical Barrier. Pursuant to Education Code section 45125.2, Contractor has installed or will install, prior to commencement of work, a physical barrier at the Project site, that will limit contact between Contractor's employees and District pupils at all times; and/or



Continual Supervision by Fingerprinted Employee. Pursuant to Education Code section 45125.2, Contractor certifies that all employees will be under the continual supervision of, and monitored by, an employee of the Contractor who the California Department of Justice has ascertained has not been convicted of a violent or serious felony. The name and title of the employee who will be supervising

Contractor's employees and its subcontractors' employees is:

Name: _____ Title: _____



Unoccupied Site. The Work on the Contract is at an unoccupied school site and no employee and/or subcontractor or supplier of any tier of Contract shall come in contact with the District pupils.

5. **Substitutions for Specified Items**

Requests for substitutions after award of the Contract shall be submitted within **THIRTY-FIVE (35)** days of the date of the Notice of Award. This time period may be extended by the District only, in its sole discretion.

6. **Weather Days**

Delays due to Adverse Weather conditions will only be permitted in compliance with the provisions in the General Conditions and only if the number of days of Adverse Weather exceeds the following parameters:

SOUTHERN CALIFORNIA: 16 Days

7. **Insurance Policy Limits.** Contractor's insurance shall be with insurance companies with an A.M. Best rating of no less than A-VII. The limits of insurance shall not be less than:

Commercial General Liability	Includes: Bodily Injury, Property Damage, Personal & Advertising Injury, Product Liability and Completed Operations	\$2,000,000 each occurrence; \$4,000,000 general aggregate
Automobile Liability – <u>Any</u> Auto	Combined Single Limit	\$1,000,000 per occurrence
Excess Liability (Umbrella)		\$1,000,000 per occurrence; \$6,000,000 aggregate
Workers Compensation		Statutory limits pursuant to State law
Employers' Liability		\$2,000,000 each incident, each disease; \$2,000,000 policy limit
Sexual Abuse / Molestation		\$1,000,000 each incident; \$2,000,000 policy limit
Builder's Risk (Course of Construction)		Issued for the value and scope of Work indicated herein.
Property of Others	Combined Single Limit General Aggregate	Issued for the value and scope of Work stored off-site.

- a. **Contractor's Pollution Liability Coverage:** The Contractor will procure and maintain contractor's pollution liability insurance, providing limits of \$1,000,000 per occurrence and \$5,000,000 the aggregate, on an occurrence form. The policy shall cover all activities and operations during construction at the Project Site. The policy must cover mold during the period of construction and throughout the statute of repose.

8. **Permits, Certificates, Licenses, Fees, Approval**

a. **Approvals, Certificates, Fees, Inspections, Licenses, Permits, Etc.**

- (1) **Permits in Bid Price.** Contractor shall include in its Bid the cost of any approvals, certificates, fees, excavations, licenses, permits or similar requirements necessary for the performance of the Work ("Permits").
 - a) "Permits" includes, without limitation, any of the following if required: temporary or permanent building, mechanical, electrical or plumbing permits; certificates of occupancy; curb-breaking permits, highway entrance permits; water permits; etc.
 - b) "Permits" does not include Project Inspector fees (which will be paid by the District unless otherwise indicated herein), professional licensing, or contractors' licensing.
 - c) The Contractor shall be required to obtain all Permits. The Contractor shall ensure sufficient time in its Construction Schedule to secure and obtain all permits and shall not be permitted to claim a delay in the Project due to a delay in obtaining a Permit.

b. **Storm Water Permits**

- (1) Contractor shall perform the Work of the Project related to being District's Qualified SWPPP (Storm Water Pollution Prevention Plan) Practitioner ("QSP").
- (2) As District's QSP, Contractor shall be responsible for storm water and non-storm water visual observations, sampling, and analysis per the District's SWPPP.
- (3) Contractor shall strictly follow the requirements to implement all the provisions of the SWPPP including, without limitation, preparation of monitoring and recording reports and providing those to District.
- (4) Contractor's indemnity obligations are applicable to any damages, penalties, fees, charges, or related expenses assessed or charged to the District by any water boards or agencies with jurisdiction related to compliance with the Storm Water Permits.

9. **Project Inspection**

In addition to the requirements in the Contract Documents related to cooperation with and authority of the DSA Project Inspector(s) for the Project, Contractor must comply with the requirements of the most recent versions of DSA document PR 13-01. Below are provisions of this document from PR 13-01 (rev 08/21/17).

- (1) The contractor shall carefully study the DSA-approved documents and shall plan a schedule of operations well ahead of time.
- (2) If at any time it is discovered that work is being done which is not in accordance with the DSA-approved construction documents, the contractor shall correct the work immediately.
- (3) Verify that DSA 152 and, when applicable, DSA 152-IPi forms were issued for the project prior to the commencement of construction.
- (4) Meet with the design team, the Laboratory of Record and the project inspector to mutually communicate and understand the structural/material and fire/life safety testing and inspection program, and the methods of communication appropriate for the project.

- (5) Notify the project inspector and, when applicable, in-plant inspector, in writing, of the commencement of construction of each and every aspect of the work at least 48 hours in advance by submitting Commencement/Completion of Work Notification (form DSA 156), or other agreed-upon written documents, to the project inspector.
 - (6) Notify the project inspector and, when applicable, the in-plant inspector, of the completion of construction of each and every aspect of the work by submitting form DSA 156 (or other agreed-upon written documents) to the project inspector.
 - (7) Consider the relationship of the signed-off blocks and sections of the form DSA 152 and the commencement of subsequent work. Until the project inspector has signed off applicable blocks and sections of the form DSA 152, the contractor may be prohibited from proceeding with subsequent construction activities that cover up the unapproved work. Any subsequent construction activities that cover up the unapproved work will be subject to a "Stop Work Order" from DSA or the school district (see IR A-13 for additional information), and are subject to removal and remediation if found to be in noncompliance with the DSA-approved construction documents.
 - (8) Submit the final verified report. All prime contractors are required to submit final Contractor Verified Reports (form DSA 6-C).
10. **Health & Safety.** This provision includes additional requirements related to the Contractor's responsibility related to the health of its workers and to the procedures it must follow related to COVID-19, and is in addition to the requirements already indicated in the Contract Documents including, without limitation, in the Agreement and the General Conditions.

END OF DOCUMENT

SUMMARY OF WORK

PART 1 - GENERAL

1.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Site Access Conditions and Requirements;
- B. Special Conditions.

1.02 SUMMARY OF WORK COVERED BY CONTRACT DOCUMENTS

- A. Provide and install District Standard CAT6 cabling listed below:
 - (1) Superior Essex – Model # 66-240-5A, Category 6 Cable DataGain Category 6+ CMR, Green
 - (2) Leviton – Model # 61110-RV6 eXtreme Cat 6 Quickport Connector, Green
- B. Run CAT 6 cable from IDF rooms on sites to the classrooms. Sites listed below.
 - (1) Alameda Elementary School, 8613 Alameda St., Downey, CA 90242
 - (2) Carpenter Elementary School, 9439 Foster Rd., Downey, CA 90242
 - (3) Gallatin Elementary School, 9513 Brookshire Ave., Downey, CA 90240
 - (4) Gauldin Elementary School, 9724 Spry St., Downey, CA 90242
 - (5) Imperial Elementary School, 8133 Imperial Hwy., Downey, CA 90242
 - (6) Lewis Elementary School, 13220 Bellflower Blvd., Downey, CA 90242
 - (7) Old River Elementary School, 11994 Old River School Rd., Downey, CA 90241
 - (8) Pace Education Center, 9625 Van Ruiten St., Bellflower, CA 90706
 - (9) Price Elementary School, 9525 Tweedy Ln., Downey, CA 90240
 - (10) Rio Hondo Elementary School, 7731 Muller St., Downey, CA 90241
 - (11) Rio San Gabriel Elementary School, 9338 Gotham St., Downey, CA 90241

- (12) Unsworth Elementary School, 9001 Lindsay St., Downey, CA 90240
- (13) Ward Elementary School, 8851 Adoree St., Downey, CA 90242
- (14) Williams Elementary School, 7530 Arnett St., Downey, CA 90241
- (15) Doty Middle School, 10301 Woodruff Ave., Downey, CA 90241
- (16) Sussman Middle School, 12500 Birchdale Ave., Downey, CA 90242
- (17) Columbus High School, 12330 Woodruff Ave., Downey, CA 90241
- (18) Downey High School, 11040 Brookshire Ave., Downey, CA 90241
- (19) Warren High School, 8141 De Palma St., Downey, CA 90241I

1.03 CODES, REGULATIONS, AND STANDARDS

- A. The codes, regulations, and standards adopted by the state and federal agencies having jurisdiction shall govern minimum requirements for this Project. Where codes, regulations, and standards conflict with the Contract Documents, these conflicts shall be brought to the immediate attention of the District and the Architect.
- B. Codes, regulations, and standards shall be as published effective as of date of bid opening, unless otherwise specified or indicated.

1.04 PROJECT RECORD DOCUMENTS

- A. Contractor shall maintain on Site one set of the following record documents; Contractor shall record actual revisions to the Work:
 - (1) Contract Drawings.
 - (2) Specifications.
 - (3) Addenda.
 - (4) Change Orders and other modifications to the Contract.
 - (5) Reviewed shop drawings, product data, and samples.
 - (6) Field test records.
 - (7) Inspection certificates.
 - (8) Manufacturer's certificates.
- B. Contractor shall store Record Documents separate from documents used for construction. Provide files, racks, and secure storage for Record Documents and samples.
- C. Contractor shall record information concurrent with construction progress.

- D. Specifications: Contractor shall legibly mark and record at each product section of the Specifications the description of the actual product(s) installed, including the following:
 - (1) Manufacturer's name and product model and number.
 - (2) Product substitutions or alternates utilized.
 - (3) Changes made by Addenda and Change Orders and written directives.

1.05 EXAMINATION OF EXISTING CONDITIONS

- A. Contractor shall be held to have examined the Project Site and acquainted itself with the conditions of the Site and of the streets or roads approaching the Site.
- B. Prior to commencement of Work, Contractor shall survey the Site and existing buildings and improvements to observe existing damage and defects such as cracks, sags, broken, missing or damaged glazing, other building elements and Site improvements, and other damage.
- C. Should Contractor observe cracks, sags, and other damage to and defects of the Site and adjacent buildings, paving, and other items not indicated in the Contract Documents, Contractor shall immediately report same to the District and the Architect.

1.06 CONTRACTOR'S USE OF PREMISES

- A. If unoccupied and only with District's prior written approval, Contractor may use the building(s) at the Project Site without limitation for its operations, storage, and office facilities for the performance of the Work. If the District chooses to beneficially occupy any building(s), Contractor must obtain the District's written approval for Contractor's use of spaces and types of operations to be performed within the building(s) while so occupied. Contractor's access to the building(s) shall be limited to the areas indicated.
- B. If the space at the Project Site is not sufficient for Contractor's operations, storage, office facilities and/or parking, Contractor shall arrange and pay for any additional facilities needed by Contractor.
- C. Contractor shall not interfere with use of or access to occupied portions of the building(s) or adjacent property.
- D. Contractor shall maintain corridors, stairs, halls, and other exit-ways of building clear and free of debris and obstructions at all times.
- E. No one other than those directly involved in the demolition and construction, or specifically designated by the District or the Architect shall be permitted in the areas of work during demolition and construction activities.
- F. The Contractor shall install the construction fence and maintain that it will be locked when not in use. Keys to this fencing will be provided to the District.

1.07 PROTECTION OF EXISTING STRUCTURES AND UTILITIES

- A. The Drawings show above-grade and below-grade structures, utility lines, and other installations that are known or believed to exist in the area of the Work. Contractor shall locate these existing installations before proceeding with excavation and other operations that could damage same; maintain them in service, where appropriate; and repair damage to them caused by the performance of the Work. Should damage occur to these existing installations, the costs of repair shall be at the Contractor's expense and made to the District's satisfaction.
- B. Contractor shall be alert to the possibility of the existence of additional structures and utilities. If Contractor encounters additional structures and utilities, Contractor will immediately report to the District for disposition of same as indicated in the General Conditions.

1.08 UTILITY SHUTDOWNS AND INTERRUPTIONS

- A. Contractor shall give the District a minimum of three (3) days written notice in advance of any need to shut off existing utility services or to effect equipment interruptions. The District will set exact time and duration for shutdown, and will assist Contractor with shutdown. Work required to re-establish utility services shall be performed by the Contractor.
- B. Contractor shall obtain District's written approval as indicated in the General Conditions in advance of deliveries of material or equipment or other activities that may conflict with District's use of the building(s) or adjacent facilities.

1.09 STRUCTURAL INTEGRITY

- A. Contractor shall be responsible for and supervise each operation and work that could affect structural integrity of various building elements, both permanent and temporary.
- B. Contractor shall include structural connections and fastenings as indicated or required for complete performance of the Work.

PART 2 – PRODUCTS Not Used.

PART 3 – EXECUTION Not Used.

END OF DOCUMENT

DOCUMENT 01 22 00
ALTERNATES AND UNIT PRICING

PART 4 – ALTERNATES

4.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions;
- C. Bid Form and Proposal;
- D. Instruction to Bidders.

4.02 DESCRIPTION

The items of work indicated below propose modifications to, substitutions for, additions to and/or deletions from the various parts of the Work specified in other Sections of the Specifications. The acceptance or rejection of any of the alternates is strictly at the option of the District subject to District's acceptance of Contractor's stated prices contained in this Proposal.

4.03 GENERAL

Where an item is omitted, or scope of Work is decreased, all Work pertaining to the item whether specifically stated or not, shall be omitted and where an item is added or modified or where scope of Work is increased, all Work pertaining to that required to render same ready for use on the Project in accordance with intention of Drawings and Specifications shall be included in an agreed upon price amount.

4.04 BASE BID

The Base Bid includes all work required to construct the Project completely and in accordance with the Contract Documents.

END OF DOCUMENT

PRODUCT OPTIONS AND SUBSTITUTIONS

PART 5 - GENERAL

5.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. Instructions to Bidders;
- B. General Conditions, including, without limitation, Substitutions For Specified Items; and
- C. Special Conditions.

5.02 SUBSTITUTIONS OF MATERIALS AND EQUIPMENT

- A. Catalog numbers and specific brands or trade names followed by the designation "or equal" are used in conjunction with material and equipment required by the Specifications to establish the standards of quality, utility, and appearance required. Substitutions which are equal in quality, utility, and appearance to those specified may be reviewed subject to the provisions of the General Conditions.
- B. Wherever more than one manufacturer's product is specified, the first-named product is the basis for the design used in the work and the use of alternative-named manufacturers' products or substitutes may require modifications in that design. If such alternatives are proposed by Contractor and are approved by the District and/or the Architect, Contractor shall assume all costs required to make necessary revisions and modifications of the design resulting from the substitutions requested by the Contractor.
- C. When materials and equipment are specified by first manufacturer's name and product number, second manufacturer's name and "or approved equal," supporting data for the second product, if proposed by Contractor, shall be submitted in accordance with the requirements for substitutions. The District's Board has found and determined that certain item(s) shall be used on this Project based on the purpose(s) indicated pursuant to Public Contract Code section 3400(c). These findings, as well as the products and brand or trade names, have been identified in the Notice to Bidders.
- D. The Contractor will not be allowed to substitute specified items unless the request for substitution is submitted as follows:
 - (1) District must receive any notice of request for substitution of a specified item a minimum of ten (10) calendar days prior to bid opening.

- (2) Within 35 days after the date of the Notice of Award, the Contractor shall submit data substantiating the request(s) for all substitution(s) containing sufficient information to assess acceptability of product or system and impact on Project, including, without limitation, the requirements specified in the Special Conditions and the technical Specifications. Insufficient information shall be grounds for rejection of substitution.
- E. If the District and/or Architect, in reviewing proposed substitute materials and equipment, require revisions or corrections to be made to previously accepted Shop Drawings and supplemental supporting data to be resubmitted, Contractor shall promptly do so. If any proposed substitution is judged by the District and/or Architect to be unacceptable, the specified material or equipment shall be provided.
- F. Samples may be required. Tests required by the District and/or Architect for the determination of quality and utility shall be made at the expense of Contractor, with acceptance of the test procedure first given by the District.
- G. In reviewing the supporting data submitted for substitutions, the District and/or Architect will use for purposes of comparison all the characteristics of the specified material or equipment as they appear in the manufacturer's published data even though all the characteristics may not have been particularly mentioned in the Contract Documents. If more than two (2) submissions of supporting data are required, the cost of reviewing the additional supporting data shall be borne by Contractor, and the District will deduct the costs from the Contract Price. The Contractor shall be responsible for any re-design costs occasioned by District's acceptance and/or approval of any substitute.
- H. The Contractor shall, in the event that a substitute is less costly than that specified, credit the District with one hundred percent (100%) of the net difference between the substitute and the originally specified material. In this event, the Contractor agrees to execute a deductive Change Order to reflect that credit. In the event Contractor furnishes a material, process, or article more expensive than that specified, the difference in the cost of that material, process, or article so furnished shall be borne by Contractor.
- I. In no event shall the District be liable for any increase in Contract Price or Contract Time due to any claimed delay in the evaluation of any proposed substitute or in the acceptance or rejection of any proposed substitute.

PART 6 – PRODUCTS Not Used.

PART 7 – EXECUTION Not Used.

END OF DOCUMENT

DOCUMENT 01 26 00

CHANGES IN THE WORK

CONTRACTOR SHALL COMPLY WITH ALL APPLICABLE PROVISIONS IN THE AGREEMENT, GENERAL CONDITIONS, AND SPECIAL CONDITIONS, IF USED, RELATED TO CHANGES AND/OR REQUESTS FOR CHANGES.

END OF DOCUMENT

DOCUMENT 01 29 00

**APPLICATION FOR PAYMENT AND
CONDITIONAL AND UNCONDITIONAL WAIVER AND RELEASE FORMS**

**CONTRACTOR SHALL COMPLY WITH ALL PROVISIONS IN THE GENERAL
CONDITIONS RELATED TO APPLICATIONS FOR PAYMENT AND/OR PAYMENTS.**

DOWNEY UNIFIED SCHOOL DISTRICT

CAT 6 CABLING

**APPLICATION FOR PAYMENT AND
CONDITIONAL AND UNCONDITIONAL
WAIVER AND RELEASE FORMS
DOCUMENT 01 29 00-9**

**CONDITIONAL WAIVER AND RELEASE
ON PROGRESS PAYMENT
(CIVIL CODE SECTION 8132)**

NOTICE: THIS DOCUMENT WAIVES THE CLAIMANT'S LIEN, STOP PAYMENT NOTICE, AND PAYMENT BOND RIGHTS EFFECTIVE ON RECEIPT OF PAYMENT. A PERSON SHOULD NOT RELY ON THIS DOCUMENT UNLESS SATISFIED THAT THE CLAIMANT HAS RECEIVED PAYMENT.

Name of Claimant: _____

Name of Customer: _____

Job Location: _____

Owner: _____

Through Date: _____

Conditional Waiver and Release

This document waives and releases lien, stop payment notice, and payment bond rights the claimant has for labor and service provided, and equipment and material delivered, to the customer on this job through the Through Date of this document. Rights based upon labor or service provided, or equipment or material delivered, pursuant to a written change order that has been fully executed by the parties prior to the date that this document is signed by the claimant, are waived and released by this document, unless listed as an Exception below. This document is effective only on the claimant's receipt of payment from the financial institution on which the following check is drawn:

Maker of Check: _____

Amount of Check: \$_____

Check Payable to: _____

Exceptions

This document does not affect any of the following:

- (1) Retentions.
- (2) Extras for which the claimant has not received payment.
- (3) The following progress payments for which the claimant has previously given a conditional waiver and release but has not received payment:

Date(s) of waiver and release: _____

Amount(s) of unpaid progress payment(s): \$_____

DOWNEY UNIFIED SCHOOL DISTRICT

CAT 6 CABLING

**APPLICATION FOR PAYMENT AND
CONDITIONAL AND UNCONDITIONAL
WAIVER AND RELEASE FORMS
DOCUMENT 01 29 00-10**

- (4) Contract rights, including (A) a right based on rescission, abandonment, or breach of contract, and (B) the right to recover compensation for work not compensated by the payment.

Claimant's Signature: _____

Claimant's Title: _____

Date of Signature: _____

**UNCONDITIONAL WAIVER AND RELEASE
ON PROGRESS PAYMENT
(CIVIL CODE SECTION 8134)**

NOTICE TO CLAIMANT: THIS DOCUMENT WAIVES AND RELEASES LIEN, STOP PAYMENT NOTICE, AND PAYMENT BOND RIGHTS UNCONDITIONALLY AND STATES THAT YOU HAVE BEEN PAID FOR GIVING UP THOSE RIGHTS. THIS DOCUMENT IS ENFORCEABLE AGAINST YOU IF YOU SIGN IT, EVEN IF YOU HAVE NOT BEEN PAID. IF YOU HAVE NOT BEEN PAID, USE A CONDITIONAL WAIVER AND RELEASE FORM.

Name of Claimant: _____

Name of Customer: _____

Job Location: _____

Owner: _____

Through Date: _____

Unconditional Waiver and Release

This document waives and releases lien, stop payment notice, and payment bond rights the claimant has for labor and service provided, and equipment and material delivered, to the customer on this job through the Through Date of this document. Rights based upon labor or service provided, or equipment or material delivered, pursuant to a written change order that has been fully executed by the parties prior to the date that this document is signed by the claimant, are waived and released by this document, unless listed as an Exception below. The claimant has received the following progress payment: \$_____

Exceptions

This document does not affect any of the following:

1. Retentions.
- (5) Extras for which the claimant has not received payment.
- (6) Contract rights, including (A) a right based on rescission, abandonment, or breach of contract, and (B) the right to recover compensation for work not compensated by the payment.

Claimant's Signature: _____

Claimant's Title: _____

Date of Signature: _____

DOWNEY UNIFIED SCHOOL DISTRICT

CAT 6 CABLING

**APPLICATION FOR PAYMENT AND
CONDITIONAL AND UNCONDITIONAL
WAIVER AND RELEASE FORMS
DOCUMENT 01 29 00-12**

**CONDITIONAL WAIVER AND RELEASE
ON FINAL PAYMENT
(CIVIL CODE SECTION 8136)**

NOTICE: THIS DOCUMENT WAIVES THE CLAIMANT'S LIEN, STOP PAYMENT NOTICE, AND PAYMENT BOND RIGHTS EFFECTIVE ON RECEIPT OF PAYMENT. A PERSON SHOULD NOT RELY ON THIS DOCUMENT UNLESS SATISFIED THAT THE CLAIMANT HAS RECEIVED PAYMENT.

Name of Claimant: _____

Name of Customer: _____

Job Location: _____

Owner: _____

Conditional Waiver and Release

This document waives and releases lien, stop payment notice, and payment bond rights the claimant has for labor and service provided, and equipment and material delivered, to the customer on this job. Rights based upon labor or service provided, or equipment or material delivered, pursuant to a written change order that has been fully executed by the parties prior to the date that this document is signed by the claimant, are waived and released by this document, unless listed as an Exception below. This document is effective only on the claimant's receipt of payment from the financial institution on which the following check is drawn:

Maker of Check: _____

Amount of Check: \$_____

Check Payable to: _____

Exceptions

This document does not affect any of the following: _____

Disputed claims for extras in the amount of: \$_____

Claimant's Signature: _____

Claimant's Title: _____

Date of Signature: _____

DOWNEY UNIFIED SCHOOL DISTRICT

CAT 6 CABLING

**APPLICATION FOR PAYMENT AND
CONDITIONAL AND UNCONDITIONAL
WAIVER AND RELEASE FORMS
DOCUMENT 01 29 00-13**

**UNCONDITIONAL WAIVER AND RELEASE
ON FINAL PAYMENT
(CIVIL CODE SECTION 8138)**

NOTICE TO CLAIMANT: THIS DOCUMENT WAIVES AND RELEASES LIEN, STOP PAYMENT NOTICE, AND PAYMENT BOND RIGHTS UNCONDITIONALLY AND STATES THAT YOU HAVE BEEN PAID FOR GIVING UP THOSE RIGHTS. THIS DOCUMENT IS ENFORCEABLE AGAINST YOU IF YOU SIGN IT, EVEN IF YOU HAVE NOT BEEN PAID. IF YOU HAVE NOT BEEN PAID, USE A CONDITIONAL WAIVER AND RELEASE FORM.

Name of Claimant: _____

Name of Customer: _____

Job Location: _____

Owner: _____

Unconditional Waiver and Release

This document waives and releases lien, stop payment notice, and payment bond rights the claimant has for all labor and service provided, and equipment and material delivered, to the customer on this job. Rights based upon labor or service provided, or equipment or material delivered, pursuant to a written change order that has been fully executed by the parties prior to the date that this document is signed by the claimant, are waived and released by this document, unless listed as an Exception below. The claimant has been paid in full.

Exceptions

This document does not affect any of the following: _____

Disputed claims for extras in the amount of: \$_____

Claimant's Signature: _____

Claimant's Title: _____

Date of Signature: _____

PROJECT MEETINGS

PART 8 – GENERAL

8.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions; and
- B. Special Conditions.

8.02 PROGRESS MEETINGS:

- A. Contractor shall schedule and hold regular weekly progress meetings after a minimum of one week's prior written notice of the meeting date and time to all Invitees as indicated below.
- B. Location: Contractor's field office.
- C. The Contractor shall notify and invite the following entities ("Invitees"):
 - (1) District Representative.
 - (2) Contractor.
 - (3) Contractor's Project Manager.
 - (4) Contractor's Superintendent.
 - (5) Subcontractors, as appropriate to the agenda of the meeting.
 - (6) Suppliers, as appropriate to the agenda of the meeting.
 - (7) Construction Manager, if any.
 - (8) Architect
 - (9) Engineer(s), if any and as appropriate to the agenda of the meeting.
 - (10) Others, as appropriate to the agenda of the meeting.
- D. The District's and/or the Architect's Consultants will attend at their discretion, in response to the agenda.
- E. The District representative, the Construction Manager, and/or another District Agent shall take and distribute meeting notes to attendees and other concerned parties. If exceptions are taken to anything in the meeting notes,

those exceptions shall be stated in writing to the District within five (5) working days following District's distribution of the meeting notes.

8.03 PRE-INSTALLATION/PERFORMANCE MEETING:

- A. Contractor shall schedule a meeting prior to the start of each of the following portions of the Work: cutting and patching of plaster and roofing, and other weather-exposed and moisture-resistant products. Contractor shall invite all Invitees to this meeting, and others whose work may affect or be affected by the quality of the cutting and patching work.
- B. Contractor shall review in detail prior to this meeting, the manufacturer's requirements and specifications, applicable portions of the Contract Documents, Shop Drawings, and other submittals, and other related work. At this meeting, invitees shall review and resolve conflicts, incompatibilities, or inadequacies discovered or anticipated.
- C. Contractor shall review in detail Project conditions, schedule, requirements for performance, application, installation, and quality of completed Work, and protection of adjacent Work and property.
- D. Contractor shall review in detail means of protecting the completed Work during the remainder of the construction period.

PART 9 - PRODUCTS Not Used.

PART 10 - EXECUTION Not Used.

END OF DOCUMENT

SCHEDULING OF WORK

PART 11 – GENERAL

11.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions;
- C. Summary of Work; and
- D. Submittals.

11.02 SECTION INCLUDES

- A. Scheduling of Work under this Contract shall be performed by Contractor in accordance with requirements of this Section.
 - (1) Development of schedule, cost and resource loading of the schedule, monthly payment requests, and project status reporting requirements of the Contract shall employ computerized Critical Path Method ("CPM") scheduling ("CPM Schedule").
 - (2) CPM Schedule shall be cost loaded based on Schedule of Values as approved by District.
 - (3) Submit schedules and reports as specified in the General Conditions.
- B. Upon Award of Contract, Contractor shall immediately commence development of Initial and Original CPM Schedules to ensure compliance with CPM Schedule submittal requirements.

11.03 CONSTRUCTION SCHEDULE

- A. Within ten (10) days of being awarded the Contract and before request for first progress payment, the Contractor shall prepare and submit to the Project Manager a construction progress schedule conforming to the Milestone Schedule below.
- B. The Construction Schedule shall be continuously updated, and an updated schedule shall be submitted with each application for progress payment. Each revised schedule shall indicate the work actually accomplished during the previous period and the schedule for completion of the remaining work.

C. Milestone Schedule:

CONSTRUCTION STARTS

Warren HS Softball and Baseball
Downey/Warren HS Sports' Stadium*

FINAL PROJECT COMPLETION

*Pending football playoffs

September 7, 2022

December 2022

January 2023

11.04 QUALIFICATIONS

- A. Contractor shall employ experienced scheduling personnel qualified to use the latest version of [i.e., Primavera Project Planner]. Experience level required is set forth below. Contractor may employ such personnel directly or may employ a consultant for this purpose.
- (1) The written statement shall identify the individual who will perform CPM scheduling.
 - (2) Capability and experience shall be verified by description of construction projects on which individual has successfully applied computerized CPM.
 - (3) Required level of experience shall include at least two (2) projects of similar nature and scope with value not less than three fourths ($\frac{3}{4}$) of the Total Bid Price of this Project. The written statement shall provide contact persons for referenced projects with current telephone and address information.
- B. District reserves the right to approve or reject Contractor's scheduler or consultant at any time. District reserves the right to refuse replacing of Contractor's scheduler or consultant, if District believes replacement will negatively affect the scheduling of Work under this Contract.

11.05 GENERAL

- A. Progress Schedule shall be based on and incorporate milestone and completion dates specified in Contract Documents.
- B. Overall time of completion and time of completion for each milestone shown on Progress Schedule shall adhere to times in the Contract, unless an earlier (advanced) time of completion is requested by Contractor and agreed to by District. Any such agreement shall be formalized by a Change Order.
- (1) District is not required to accept an early completion schedule, i.e., one that shows an earlier completion date than the Contract Time.
 - (2) Contractor shall not be entitled to extra compensation in event agreement is reached on an earlier completion schedule and Contractor completes its Work, for whatever reason, beyond completion date shown in its early completion schedule but within the Contract Time.

- (3) A schedule showing the work completed in less than the Contract Time, and that has been accepted by District, shall be considered to have Project Float. The Project Float is the time between the scheduled completion of the work and the Completion Date. Project Float is a resource available to both District and the Contractor.
- C. Ownership Project Float: Neither the District nor Contractor owns Project Float. The Project owns the Project Float. As such, liability for delay of the Completion Date rests with the party whose actions, last in time, actually cause delay to the Completion Date.
 - (1) For example, if Party A uses some, but not all of the Project Float and Party B later uses remainder of the Project Float as well as additional time beyond the Project Float, Party B shall be liable for the time that represents a delay to the Completion Date.
 - (2) Party A would not be responsible for the time since it did not consume the entire Project Float and additional Project Float remained; therefore, the Completion Date was unaffected by Party A.
- D. Progress Schedule shall be the basis for evaluating job progress, payment requests, and time extension requests. Responsibility for developing Contract CPM Schedule and monitoring actual progress as compared to Progress Schedule rests with Contractor.
- E. Failure of Progress Schedule to include any element of the Work, or any inaccuracy in Progress Schedule, will not relieve Contractor from responsibility for accomplishing the Work in accordance with the Contract. District's acceptance of schedule shall be for its use in monitoring and evaluating job progress, payment requests, and time extension requests and shall not, in any manner, impose a duty of care upon District, or act to relieve Contractor of its responsibility for means and methods of construction.
- F. Software: Use **[i.e., District Project Planner for Windows, latest version]**. Such software shall be compatible with Windows operating system. Contractor shall transmit contract file to District on compact disk at times requested by District.
- G. Transmit each item under the form approved by District.
 - (1) Identify Project with District Contract number and name of Contractor.
 - (2) Provide space for Contractor's approval stamp and District's review stamps.
 - (3) Submittals received from sources other than Contractor will be returned to the Contractor without District's review.

11.06 INITIAL CPM SCHEDULE

- A. Initial CPM Schedule submitted for review at the pre-construction conference shall serve as Contractor's schedule for up to ninety (90) calendar days after the Notice to Proceed.

- B. Indicate detailed plan for the Work to be completed in first ninety (90) days of the Contract; details of planned mobilization of plant and equipment; sequence of early operations; procurement of materials and equipment. Show Work beyond ninety (90) calendar days in summary form.
- C. Initial CPM Schedule shall be time scaled.
- D. Initial CPM Schedule shall be cost and resource loaded. Accepted cost and resource loaded schedule will be used as basis for monthly progress payments until acceptance of the Original CPM Schedule. Use of Initial CPM Schedule for progress payments shall not exceed ninety (90) calendar days.
- E. District and Contractor shall meet to review and discuss the Initial CPM Schedule within seven (7) calendar days after it has been submitted to District.
 - (1) District's review and comment on the schedule shall be limited to Contract conformance (with sequencing, coordination, and milestone requirements).
 - (2) Contractor shall make corrections to schedule necessary to comply with Contract requirements and shall adjust schedule to incorporate any missing information requested by District. Contractor shall resubmit Initial CPM Schedule if requested by District.
- F. If, during the first ninety (90) days after Notice to Proceed, the Contractor is of the opinion that any of the Work included on its Initial CPM Schedule has been impacted, the Contractor shall submit to District a written Time Impact Evaluation ("TIE") in accordance with Article 1.12 of this Section. The TIE shall be based on the most current update of the Initial CPM Schedule.

11.07 ORIGINAL CPM SCHEDULE

- A. Submit a detailed proposed Original CPM Schedule presenting an orderly and realistic plan for completion of the Work in conformance with requirements as specified herein.
- B. Progress Schedule shall include or comply with following requirements:
 - (1) Time scaled, cost and resource (labor and major equipment) loaded CPM schedule.
 - (2) No activity on schedule shall have duration longer than fifteen (15) work days, with exception of submittal, approval, fabrication and procurement activities, unless otherwise approved by District.
 - (a) Activity durations shall be total number of actual work days required to perform that activity.
 - (3) The start and completion dates of all items of Work, their major components, and milestone completion dates, if any.

- (4) District furnished materials and equipment, if any, identified as separate activities.
- (5) Activities for maintaining Project Record Documents.
- (6) Dependencies (or relationships) between activities.
- (7) Processing/approval of submittals and shop drawings for all material and equipment required per the Contract. Activities that are dependent on submittal acceptance or material delivery shall not be scheduled to start earlier than expected acceptance or delivery dates.
 - (a) Include time for submittals, re-submittals and reviews by District. Coordinate with accepted schedule for submission of Shop Drawings, samples, and other submittals.
 - (b) Contractor shall be responsible for all impacts resulting from re-submittal of Shop Drawings and submittals.
- (8) Procurement of major equipment, through receipt and inspection at jobsite, identified as separate activity.
 - (a) Include time for fabrication and delivery of manufactured products for the Work.
 - (b) Show dependencies between procurement and construction.
- (9) Activity description; what Work is to be accomplished and where.
- (10) The total cost of performing each activity shall be total of labor, material, and equipment, excluding overhead and profit of Contractor. Overhead and profit of the General Contractor shall be shown as a separate activity in the schedule. Sum of cost for all activities shall equal total Contract value.
- (11) Resources required (labor and major equipment) to perform each activity.
- (12) Responsibility code for each activity corresponding to Contractor or Subcontractor responsible for performing the Work.
- (13) Identify the activities which constitute the controlling operations or critical path. No more than twenty-five (25%) of the activities shall be critical or near critical. Near critical is defined as float in the range of one (1) to (10) days.
- (14) Twenty (20) workdays for developing punch list(s), completion of punch-list items, and final clean up for the Work or any designated portion thereof. No other activities shall be scheduled during this period.
- (15) Interface with the work of other contractors, District, and agencies such as, but not limited to, utility companies.

- (16) Show detailed Subcontractor Work activities. In addition, furnish copies of Subcontractor schedules upon which CPM was built.
 - (a) Also furnish for each Subcontractor, as determined by District, submitted on Subcontractor letterhead, a statement certifying that Subcontractor concurs with Contractor's Original CPM Schedule and that Subcontractor's related schedules have been incorporated, including activity duration, cost and resource loading.
 - (b) Subcontractor schedules shall be independently derived and not a copy of Contractor's schedule.
 - (c) In addition to Contractor's schedule and resource loading, obtain from electrical, mechanical, and plumbing Subcontractors, and other Subcontractors as required by District, productivity calculations common to their trades, such as units per person day, feet of pipe per day per person, feet of wiring per day per person, and similar information.
 - (d) Furnish schedule for Contractor/Subcontractor CPM schedule meetings which shall be held prior to submission of Original CPM schedule to District. District shall be permitted to attend scheduled meetings as an observer.
- (17) Activity durations shall be in Work days.
- (18) Submit with the schedule a list of anticipated non-Work days, such as weekends and holidays. The Progress Schedule shall exclude in its Work day calendar all non-Work days on which Contractor anticipates critical Work will not be performed.
- C. Original CPM Schedule Review Meeting: Contractor shall, within sixty (60) days from the Notice to Proceed date, meet with District to review the Original CPM Schedule submittal.
 - (1) Contractor shall have its Project Manager, Project Superintendent, Project Scheduler, and key Subcontractor representatives, as required by District, in attendance. The meeting will take place over a continuous one (1) day period.
 - (2) District's review will be limited to submittal's conformance to Contract requirements including, but not limited to, coordination requirements. However, review may also include:
 - (a) Clarifications of Contract Requirements.
 - (b) Directions to include activities and information missing from submittal.
 - (c) Requests to Contractor to clarify its schedule.

- (3) Within five (5) days of the Schedule Review Meeting, Contractor shall respond in writing to all questions and comments expressed by District at the Meeting.

11.08 ADJUSTMENTS TO CPM SCHEDULE

- A. Adjustments to Original CPM Schedule: Contractor shall have adjusted the Original CPM Schedule submittal to address all review comments from original CPM Schedule review meeting and resubmit network diagrams and reports for District's review.
 - (1) District, within ten (10) days from date that Contractor submitted the revised schedule, will either:
 - (a) Accept schedule and cost and resource loaded activities as submitted, or
 - (b) Advise Contractor in writing to review any part or parts of schedule which either do not meet Contract requirements or are unsatisfactory for District to monitor Project's progress, resources, and status or evaluate monthly payment request by Contractor.
 - (2) District may accept schedule with conditions that the first monthly CPM Schedule update be revised to correct deficiencies identified.
 - (3) When schedule is accepted, it shall be considered the "Original CPM Schedule" which will then be immediately updated to reflect the current status of the work.
 - (4) District reserves right to require Contractor to adjust, add to, or clarify any portion of schedule which may later be discovered to be insufficient for monitoring of Work or approval of partial payment requests. No additional compensation will be provided for such adjustments, additions, or clarifications.
- B. Acceptance of Contractor's schedule by District will be based solely upon schedule's compliance with Contract requirements.
 - (1) By way of Contractor assigning activity durations and proposing sequence of Work, Contractor agrees to utilize sufficient and necessary management and other resources to perform work in accordance with the schedule.
 - (2) Upon submittal of schedule update, updated schedule shall be considered "current" CPM Schedule.
 - (3) Submission of Contractor's schedule to District shall not relieve Contractor of total responsibility for scheduling, sequencing, and pursuing Work to comply with requirements of Contract Documents, including adverse effects such as delays resulting from ill-timed Work.

- C. Submittal of Original CPM Schedule, and subsequent schedule updates, shall be understood to be Contractor's representation that the Schedule meets requirements of Contract Documents and that Work shall be executed in sequence indicated on the schedule.
- D. Contractor shall distribute Original CPM Schedule to Subcontractors for review and written acceptance, which shall be noted on Subcontractors' letterheads to Contractor and transmitted to District for the record.

11.09 MONTHLY CPM SCHEDULE UPDATE SUBMITTALS

- A. Following acceptance of Contractor's Original CPM Schedule, Contractor shall monitor progress of Work and adjust schedule each month to reflect actual progress and any anticipated changes to planned activities.
 - (1) Each schedule update submitted shall be complete, including all information requested for the Original CPM Schedule submittal.
 - (2) Each update shall continue to show all Work activities including those already completed. These completed activities shall accurately reflect "as built" information by indicating when activities were actually started and completed.
- B. A meeting will be held on approximately the twenty-fifth (25th) of each month to review the schedule update submittal and progress payment application.
 - (1) At this meeting, at a minimum, the following items will be reviewed: Percent (%) complete of each activity; Time Impact Evaluations for Change Orders and Time Extension Request; actual and anticipated activity sequence changes; actual and anticipated duration changes; and actual and anticipated Contractor delays.
 - (2) These meetings are considered a critical component of overall monthly schedule update submittal and Contractor shall have appropriate personnel attend. At a minimum, these meetings shall be attended by Contractor's General Superintendent and Scheduler.
 - (3) Contractor shall plan on the meeting taking no less than four (4) hours.
- C. Within five (5) working days after monthly schedule update meeting, Contractor shall submit the updated CPM Schedule update.
- D. Within five (5) work days of receipt of above noted revised submittals, District will either accept or reject monthly schedule update submittal.
 - (1) If accepted, percent (%) complete shown in monthly update will be basis for Application for Payment by the Contractor. The schedule update shall be submitted as part of the Contractor's Application for Payment.

- (2) If rejected, update shall be corrected and resubmitted by Contractor before the Application for Payment is submitted.
- E. Neither updating, changing or revising of any report, curve, schedule, or narrative submitted to District by Contractor under this Contract, nor District's review or acceptance of any such report, curve, schedule or narrative shall have the effect of amending or modifying in any way the Completion Date or milestone dates or of modifying or limiting in any way Contractor's obligations under this Contract.

11.10 SCHEDULE REVISIONS

- A. Updating the Schedule to reflect actual progress shall not be considered revisions to the Schedule. Since scheduling is a dynamic process, revisions to activity durations and sequences are expected on a monthly basis.
- B. To reflect revisions to the Schedule, the Contractor shall provide District with a written narrative with a full description and reasons for each Work activity revised. For revisions affecting the sequence of work, the Contractor shall provide a schedule diagram which compares the original sequence to the revised sequence of work. The Contractor shall provide the written narrative and schedule diagram for revisions two (2) working days in advance of the monthly schedule update meeting.
- C. Schedule revisions shall not be incorporated into any schedule update until the revisions have been reviewed by District. District may request further information and justification for schedule revisions and Contractor shall, within three (3) days, provide District with a complete written narrative response to District's request.
- D. If the Contractor's revision is still not accepted by District, and the Contractor disagrees with District's position, the Contractor has seven (7) calendar days from receipt of District's letter rejecting the revision to provide a written narrative providing full justification and explanation for the revision. The Contractor's failure to respond in writing within seven (7) calendar days of District's written rejection of a schedule revision shall be contractually interpreted as acceptance of District's position, and the Contractor waives its rights to subsequently dispute or file a claim regarding District's position.
- E. At District's discretion, the Contractor can be required to provide Subcontractor certifications of performance regarding proposed schedule revisions affecting said Subcontractors.

11.11 RECOVERY SCHEDULE

- A. If the Schedule Update shows a completion date twenty-one (21) calendar days beyond the Contract Completion Date, or individual milestone completion dates, the Contractor shall submit to District the proposed revisions to recover the lost time within seven (7) calendar days. As part of this submittal, the Contractor shall provide a written narrative for each revision made to recapture the lost time. If the revisions include sequence changes, the Contractor shall provide a schedule diagram comparing the original sequence to the revised sequence of work.

- B. The revisions shall not be incorporated into any schedule update until the revisions have been reviewed by District.
- C. If the Contractor's revisions are not accepted by District, District and the Contractor shall follow the procedures in paragraph 1.09.C, 1.09.D and 1.09.E above.
- D. At District's discretion, the Contractor can be required to provide Subcontractor certifications for revisions affecting said Subcontractors.

11.12 TIME IMPACT EVALUATION ("TIE") FOR CHANGE ORDERS, AND OTHER DELAYS

- A. When Contractor is directed to proceed with changed Work, the Contractor shall prepare and submit within fourteen (14) calendar days from the Notice to Proceed a TIE which includes both a written narrative and a schedule diagram depicting how the changed Work affects other schedule activities. The schedule diagram shall show how the Contractor proposes to incorporate the changed Work in the schedule and how it impacts the current schedule-update critical path. The Contractor is also responsible for requesting time extensions based on the TIE's impact on the critical path. The diagram must be tied to the main sequence of schedule activities to enable District to evaluate the impact of changed Work to the scheduled critical path.
- B. Contractor shall be required to comply with the requirements of Paragraph 1.09.A for all types of delays such as, but not limited to, Contractor/Subcontractor delays, adverse weather delays, strikes, procurement delays, fabrication delays, etc.
- C. Contractor shall be responsible for all costs associated with the preparation of TIEs, and the process of incorporating them into the current schedule update. The Contractor shall provide District with four (4) copies of each TIE.
- D. Once agreement has been reached on a TIE, the Contract Time will be adjusted accordingly. If agreement is not reached on a TIE, the Contract Time may be extended in an amount District allows, and the Contractor may submit a claim for additional time claimed by contractor.

11.13 TIME EXTENSIONS

- A. The Contractor is responsible for requesting time extensions for time impacts that, in the opinion of the Contractor, impact the critical path of the current schedule update. Notice of time impacts shall be given in accord with the General Conditions.
- B. Where an event for which District is responsible impacts the projected Completion Date, the Contractor shall provide a written mitigation plan, including a schedule diagram, which explains how (e.g., increase crew size, overtime, etc.) the impact can be mitigated. The Contractor shall also include a detailed cost breakdown of the labor, equipment, and material the Contractor would expend to mitigate District-caused time impact. The Contractor shall submit its mitigation plan to District within fourteen (14)

calendar days from the date of discovery of the impact. The Contractor is responsible for the cost to prepare the mitigation plan.

- C. Failure to request time, provide TIE, or provide the required mitigation plan will result in Contractor waiving its right to a time extension and cost to mitigate the delay.
- D. No time will be granted under this Contract for cumulative effect of changes.
- E. District will not be obligated to consider any time extension request unless the Contractor complies with the requirements of Contract Documents.
- F. Failure of the Contractor to perform in accordance with the current schedule update shall not be excused by submittal of time extension requests.
- G. If the Contractor does not submit a TIE within the required fourteen (14) calendar days for any issue, it is mutually agreed that the Contractor does not require a time extension for said issue.

11.14 SCHEDULE REPORTS

- A. Submit four (4) copies of the following reports with the Initial CPM Schedule, the Original CPM Schedule, and each monthly update.
- B. Required Reports:
 - (1) Two activity listing reports: one sorted by activity number and one by total Project Float. These reports shall also include each activity's early/late and actual start and finish dates, original and remaining duration, Project Float, responsibility code, and the logic relationship of activities.
 - (2) Cost report sorted by activity number including each activity's associated cost, percentage of Work accomplished, earned value- to date, previous payments, and amount earned for current update period.
 - (3) Schedule plots presenting time-scaled network diagram showing activities and their relationships with the controlling operations or critical path clearly highlighted.
 - (4) Cash flow report calculated by early start, late start, and indicating actual progress. Provide an exhibit depicting this information in graphic form.
 - (5) Planned versus actual resource (i.e., labor) histogram calculated by early start and late start.
- C. Other Reports:

In addition to above reports, District may request, from month to month, any two of the following reports. Submit four (4) copies of all reports.

- (1) Activities by early start.
 - (2) Activities by late start.
 - (3) Activities grouped by Subcontractors or selected trades.
 - (4) Activities with scheduled early start dates in a given time frame, such as fifteen (15) or thirty (30) day outlook.
- D. Furnish District with report files on compact disks containing all schedule files for each report generated.

11.15 PROJECT STATUS REPORTING

- A. In addition to submittal requirements for CPM scheduling identified in this Section, Contractor shall provide a monthly project status report (i.e., written narrative report) to be submitted in conjunction with each CPM Schedule as specified herein. Status reporting shall be in form specified below.
- B. Contractor shall prepare monthly written narrative reports of status of Project for submission to District. Written status reports shall include:
- (1) Status of major Project components (percent (%) complete, amount of time ahead or behind schedule) and an explanation of how Project will be brought back on schedule if delays have occurred.
 - (2) Progress made on critical activities indicated on CPM Schedule.
 - (3) Explanations for any lack of work on critical path activities planned to be performed during last month.
 - (4) Explanations for any schedule changes, including changes to logic or to activity durations.
 - (5) List of critical activities scheduled to be performed next month.
 - (6) Status of major material and equipment procurement.
 - (7) Any delays encountered during reporting period.
 - (8) Contractor shall provide printed report indicating actual versus planned resource loading for each trade and each activity. This report shall be provided on weekly and monthly basis.
 - (a) Actual resource shall be accumulated in field by Contractor, and shall be as noted on Contractor's daily reports. These reports will be basis for information provided in computer-generated monthly and weekly printed reports.
 - (b) Contractor shall explain all variances and mitigation measures.

- (9) Contractor may include any other information pertinent to status of Project. Contractor shall include additional status information requested by District at no additional cost.
- (10) Status reports, and the information contained therein, shall not be construed as claims, notice of claims, notice of delay, or requests for changes or compensation.

11.16 WEEKLY SCHEDULE REPORT

At the Weekly Progress Meeting, the Contractor shall provide and present a time-scaled three (3) week look-ahead schedule that is based and correlated by activity number to the current schedule (i.e., Initial, Original CPM, or Schedule Update).

11.17 DAILY CONSTRUCTION REPORTS

On a daily basis, Contractor shall submit a daily activity report to District for each workday, including weekends and holidays when worked. Contractor shall develop the daily construction reports on a computer-generated database capable of sorting daily Work, manpower, and man-hours by Contractor, Subcontractor, area, sub-area, and Change Order Work. Upon request of District, furnish computer disk of this data base. Obtain District's written approval of daily construction report data base format prior to implementation. Include in report:

- A. Project name and Project number.
- B. Contractor's name and address.
- C. Weather, temperature, and any unusual site conditions.
- D. Brief description and location of the day's scheduled activities and any special problems and accidents, including Work of Subcontractors. Descriptions shall be referenced to CPM scheduled activities.
- E. Worker quantities for its own Work force and for Subcontractors of any tier.
- F. Equipment, other than hand tools, utilized by Contractor and Subcontractors.

11.18 PERIODIC VERIFIED REPORTS

Contractor shall complete and verify construction reports on a form prescribed by the Division of the State Architect and file reports on the first day of February, May, August, and November during the preceding quarter year; at the completion of the Contract; at the completion of the Work; at the suspension of Work for a period of more than one (1) month; whenever the services of Contractor or any of Contractor's Subcontractors are terminated for any reason; and at any time a special verified report is required by the Division of the State Architect. Refer to section 4-336 and section 4-343 of Part 1, Title 24 of the California Code of Regulations.

PART 12 – PRODUCTS Not Used.

PART 13 - EXECUTION Not Used.

END OF DOCUMENT

SUBMITTALS

PART 14 - GENERAL

14.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Contractor's Submittals and Schedules, Drawings and Specifications;
- B. Special Conditions.

14.02 SECTION INCLUDES:

- A. Definitions:
 - (1) Shop Drawings and Product Data are as indicated in the General Conditions and include, but are not limited to, fabrication, erection, layout and setting drawings, formwork and falsework drawings, manufacturers' standard drawings, descriptive literature, catalogues, brochures, performance and test data, wiring and control diagrams. In addition, there are other drawings and descriptive data pertaining to materials, equipment, piping, duct and conduit systems, and methods of construction as may be required to show that the materials, equipment or systems and all positions conform to the requirement of the Contract Documents, including, without limitation, the Drawings.
 - (2) "Manufactured" applies to standard units usually mass-produced; "fabricated" means specifically assembled or made out of selected materials to meet design requirements. Shop Drawings shall establish the actual detail of manufactured or fabricated items, indicated proper relation to adjoining work and amplify design details of mechanical and electrical equipment in proper relation to physical spaces in the structure.
 - (3) Manufacturer's Instructions: Where any item of Work is required by the Contract Documents to be furnished, installed, or performed, at a minimum, in accordance with a specified product manufacturer's instructions, the Contractor shall procure and distribute copies of these to the District, the Architect, and all other concerned parties and shall furnish, install, or perform the work, at a minimum, in accordance with those instructions.

- B. Samples, Shop Drawings, Product Data, and other items as specified, in accordance with the following requirements:
- (1) Contractor shall submit all Shop Drawings, Product Data, and Samples to the District, the Architect, the Project Inspector, and the Construction Manager.
 - (2) Contractor shall comply with all time frames herein and in the General Conditions and, in any case, shall submit required information in sufficient time to permit proper consideration and action before ordering any materials or items represented by such Shop Drawings, Product Data, and/or Samples.
 - (3) Contractor shall allow sufficient time so that no delay occurs due to required lead time in ordering or delivery of any item to the Site. Contractor shall be responsible for any delay in progress of Work due to its failure to observe these requirements.
 - (4) Time for completion of Work shall not be extended on account of Contractor's failure to promptly submit Shop Drawings, Product Data, and/or Samples.
 - (5) Reference numbers on Shop Drawings shall have Architectural and/or Engineering Contract Drawings reference numbers for details, sections, and "cuts" shown on Shop Drawings. These reference numbers shall be in addition to any numbering system that Contractor chooses to use or has adopted as standard.
 - (6) When the magnitude or complexity of submittal material prevents a complete review within the stated time frame, Contractor shall make this submittal in increments to avoid extended delays.
 - (7) Contractor shall certify on submittals for review that submittals conform to Contract requirements. Also certify that Contractor-furnished equipment can be installed in allocated space. In event of any variance, Contractor shall specifically state in transmittal and on Shop Drawings, portions vary and require approval of a substitute. Submittals shall not be used as a means of requesting a substitution.
 - (8) Unless specified otherwise, sampling, preparation of samples, and tests shall be in accordance with the latest standard of the American Society for Testing and Materials.
 - (9) Upon demand by Architect or District, Contractor shall submit samples of materials and/or articles for tests or examinations and consideration before Contractor incorporates same in Work. Contractor shall be solely responsible for delays due to sample(s) not being submitted in time to allow for tests. Acceptance or rejection will be expressed in writing. Work shall be equal to approved samples in every respect. Samples that are of value after testing will remain the property of Contractor.

C. Submittal Schedule:

- (1) Contractor shall prepare its proposed submittal schedule that is coordinated with the proposed construction schedule and submit both to the District within ten (10) days after the date of the Notice to Proceed. Contractor's proposed schedules shall become the Project Construction Schedule and the Project Submittal Schedule after each is approved by the District.
- (2) Contractor is responsible for all lost time should the initial submittal be rejected, marked "revise and resubmit", etc.
- (3) All Submittals shall be forwarded to the District by the date indicated on the approved Submittal Schedule, unless an earlier date is necessary to maintain the Construction Schedule, in which case those Submittals shall be forwarded to the District so as not to delay the Construction Schedule.
- (4) Contractor may be assessed \$100 a day for each day it is late in submitting a shop drawing or sample. No extensions of time will be granted to Trade Contractor or any Subcontractor because of its failure to have shop drawings and samples submitted in accordance with the Schedule.

14.03 SHOP DRAWINGS:

- A. Contractor shall submit one reproducible transparency and six (6) opaque reproductions. The District will review and return the reproducible copy and one (1) opaque reproduction to Contractor.
- B. Before commencing installation of any Work, the Contractor shall submit and receive approval of all drawings, descriptive data, and material list(s) as required to accomplish Work.
- C. Review of Shop Drawings is regarded as a service to assist Contractor and in all cases original Contract Documents shall take precedence as outlined under General Conditions.
- D. No claim for extra time or payment shall be based on work shown on Shop Drawings unless the claim is (1) noted on Contractor's transmittal letter accompanying Shop Drawings and (2) Contractor has complied with all applicable provisions of the General Conditions, including, without limitation, provisions regarding changes and payment, and all required written approvals.
- E. District shall not review Shop Drawings for quantities of materials or number of items supplied.
- F. District's and/or Architect's review of Shop Drawing will be general. District and/or Architect review does not relieve Contractor of responsibility for dimensions, accuracy, proper fitting, construction of Work, furnishing of materials, or Work required by Contract Documents and not indicated on

Shop Drawings. The District's and/or Architect's review of Shop Drawings is not to be construed as approving departures from Contract Documents.

- G. Review of Shop Drawings and Schedules does not relieve Contractor from responsibility for any aspect of those Drawings or Schedules that is a violation of local, County, State, or Federal laws, rules, ordinances, or rules and regulations of commissions, boards, or other authorities or utilities having jurisdiction.
- H. Before submitting Shop Drawings for review, Contractor shall check Shop Drawings of its subcontractors for accuracy, and confirm that all Work contiguous with and having bearing on other work shown on Shop Drawings is accurately drawn and in conformance with Contract Documents.
- I. Submitted drawings and details must bear stamp of approval of Contractor:
 - (1) Stamp and signature shall clearly certify that Contractor has checked Shop Drawings for compliance with Drawings.
 - (2) If Contractor submits a Shop Drawing without an executed stamp of approval, or whenever it is evident (despite stamp) that Drawings have not been checked, the District and/or Architect will not consider them and will return them to the Contractor for revision and resubmission. In that event, it will be deemed that Contractor has not complied with this provision and Contractor shall bear risk of all delays to same extent as if it had not submitted any Shop Drawings or details.
- J. Submission of Shop Drawings (in either original submission or when resubmitted with correction) constitutes evidence that Contractor has checked all information thereon and that it accepts and is willing to perform Work as shown.
- K. Contractor shall pay for cost of any changes in construction due to improper checking and coordination. Contractor shall be responsible for all additional costs, including coordination. Contractor shall be responsible for costs incurred by itself, the District, the Architect, the Project Inspector, the Construction Manager, any other Subcontractor or contractor, etc., due to improperly checked and/or coordination of submittals.
- L. Shop Drawings must clearly delineate the following information:
 - (1) Project name and address.
 - (2) Specification number and description.
 - (3) Architect's name and project number.
 - (4) Shop Drawing title, number, date, and scale.
 - (5) Names of Contractor, Subcontractor(s) and fabricator.
 - (6) Working and erection dimensions.

- (7) Arrangements and sectional views.
 - (8) Necessary details, including complete information for making connections with other Work.
 - (9) Kinds of materials and finishes.
 - (10) Descriptive names of materials and equipment, classified item numbers, and locations at which materials or equipment are to be installed in the Work. Contractor shall use same reference identification(s) as shown on Contract Drawings.
- M. Contractor shall prepare composite drawings and installation layouts when required to solve tight field conditions.
- (1) Shop Drawings shall consist of dimensioned plans and elevations and must give complete information, particularly as to size and location of sleeves, inserts, attachments, openings, conduits, ducts, boxes, structural interferences, etc.
 - (2) Contractor shall coordinate these composite Shop Drawings and installation layouts in the field between itself and its Subcontractor(s) for proper relationship to the Work, the work of other trades, and the field conditions. The Contractor shall check and approve all submittal(s) before submitting them for final review.

14.04 PRODUCT DATA OR NON REPRODUCIBLE SUBMITTALS:

- A. Contractor shall submit manufacturer's printed literature in original form. Any fading type of reproduction will not be accepted. Contract must submit a minimum of six (6) each, to the District. District shall return one (1) to the Contractor, who shall reproduce whatever additional copies it requires for distribution.
- B. Contractor shall submit six (6) copies of a complete list of all major items of mechanical, plumbing, and electrical equipment and materials in accordance with the approved Submittal Schedule, except as required earlier to comply with the approved Construction Schedule. Other items specified are to be submitted prior to commencing Work. Contractor shall submit items of like kind at one time in a neat and orderly manner. Partial lists will not be acceptable.
- C. Submittals shall include manufacturer's specifications, physical dimensions, and ratings of all equipment. Contractor shall furnish performance curves for all pumps and fans. Where printed literature describes items in addition to that item being submitted, submitted item shall be clearly marked on sheet and superfluous information shall be crossed out. If highlighting is used, Contractor shall mark all copies.
- D. Equipment submittals shall be complete and include space requirements, weight, electrical and mechanical requirements, performance data, and supplemental information that may be requested.

- E. Imported Materials Certification must be submitted at least ten (10) days before material is delivered.

14.05 SAMPLES:

- A. Contractor shall submit for approval Samples as required and within the time frame in the Contract Documents. Materials such as concrete, mortar, etc., which require on-site testing will be obtained from Project Site.
- B. Contractor shall submit four (4) samples except where greater or lesser number is specifically required by Contract Documents including, without limitation, the Specifications.
 - (1) Samples must be of sufficient size and quality to clearly illustrate functional characteristics, with integrally related parts and attachment devices.
 - (2) Samples must show full range of texture, color, and pattern.
- C. Contractor shall make all Submittals, unless it has authorized Subcontractor(s) to submit and Contractor has notified the District in writing to this effect.
- D. Samples to be shipped prepaid or hand-delivered to the District.
- E. Contractor shall mark samples to show name of Project, name of Contractor submitting, Contract number and segment of Work where representative Sample will be used, all applicable Specifications Sections and documents, Contract Drawing Number and detail, and ASTM or FS reference, if applicable.
- F. Contractor shall not deliver any material to Site prior to receipt of District's and/or Architect's completed written review and approval. Contractor shall furnish materials equal in every respect to approved Samples and execute Work in conformance therewith.
- G. District's and/or Architect's review, acceptance, and/or approval of Sample(s) will not preclude rejections of any material upon discovery of defects in same prior to final acceptance of completed Work.
- H. After a material has been approved, no change in brand or make will be permitted.
- I. Contractor shall prepare its Submittal Schedule and submit Samples of materials requiring laboratory tests to specified laboratory for testing not less than ninety (90) days before such materials are required to be used in Work.
- J. Samples which are rejected must be resubmitted promptly after notification of rejection and be marked "Resubmitted Sample" in addition to other information required.
- K. Field Samples and Mock-Ups are to be removed by Contractor at District's direction:

- (1) Size: As Specified.
- (2) Furnish catalog numbers and similar data, as requested.

14.06 REVIEW AND RESUBMISSION REQUIREMENTS:

- A. The District will arrange for review of Sample(s), Shop Drawing(s), Product Data, and other submittal(s) by appropriate reviewer and return to Contractor as provided below within twenty-one (21) days after receipt or within twenty-one (21) days after receipt of all related information necessary for such review, whichever is later.
- B. One (1) copy of product or materials data will be returned to Contractor with the review status.
- C. Samples to be incorporated into the Work will be returned to Contractor, together with a written notice designating the Sample with the appropriate review status and indicating errors discovered on review, if any. Other Samples will not be returned, but the same notice will be given with respect thereto, and that notice shall be considered a return of the Sample.
- D. Contractor shall revise and resubmit any Sample(s), Shop Drawing(s), Product Data, and other submittal(s) as required by the reviewer. Such resubmittals will be reviewed and returned in the same manner as original Sample(s), Shop Drawing(s), Product Data, and other submittal(s), within fourteen (14) days after receipt thereof or within fourteen (14) days after receipt of all related information necessary for such review. Such resubmittal shall not delay the Work.
- E. Contractor may proceed with any of the Work covered by Sample(s), Shop Drawing(s), Product Data, and other submittal(s) upon its return if designated as no exception taken, or revise as noted, provided the Contractor proceeds in accordance with the District and/or the Architect's notes and comments.
- F. Contractor shall not begin any of the work covered by a Sample(s), Shop Drawing(s), Product Data, and other submittal(s), designated as revise and resubmit or rejected, until a revision or correction thereof has been reviewed and returned to Contractor.
- G. Sample(s), Shop Drawing(s), Product Data, and other submittal(s) designated as revise and resubmit or rejected and requiring resubmittal, shall be revised or corrected and resubmitted to the District no later than fourteen (14) days or a shorter period as required to comply with the approved Construction Schedule, after its return to Contractor.
- H. Neither the review nor the lack of review of any Sample(s), Shop Drawing(s), Product Data, and other submittal(s) shall waive any of the requirements of the Contract Documents, or relieve Contractor of any obligation thereunder.
- I. District's and/or Architect's review of Shop Drawings does not relieve the Contractor of responsibility for any errors that may exist. Contractor is responsible for the dimensions and design of adequate connections and details and for satisfactory construction of all the Work.

PART 15 – PRODUCTS Not Used.

PART 16 - EXECUTION Not Used.

END OF DOCUMENT

SITE STANDARDS

PART 17 – GENERAL

17.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including without limitation, Site Access, Conditions, and Regulations;
- B. Special Conditions;
- C. Drug-Free Workplace Certification;
- D. Tobacco-Free Environment Certification;
- E. Criminal Background Investigation/Fingerprinting Certification;
- F. Temporary Facilities and Controls.

17.02 REQUIREMENTS OF THE DISTRICT:

- A. Drug-Free Schools and Safety Requirements:
 - (1) All school sites and other District Facilities have been declared "Drug-Free Zones." No drugs, alcohol and/or smoking are allowed at any time in any buildings and/or grounds on District property. No students, staff, visitors, or contractors are to use drugs on these sites.
 - (2) Smoking and the use of tobacco products by all persons is prohibited on or in District property. District property includes school buildings, school grounds, school-owned vehicles and vehicles owned by others while on District property. Contractor shall post: "Non-Smoking Area" in a highly visible location in each work area, staging area, and parking area. Contractor may designate a smoking area outside of District property within the public right-of-way, provided that this area remains quiet and unobtrusive to adjacent neighbors. This smoking area is to be kept clean at all times.
 - (3) Contractor shall ensure that no alcohol, firearms, weapons, or controlled substances enter or are used at the Site. Contractor shall immediately remove from the Site and terminate the employment of any employee(s) found in violation of this provision.
- B. Language: Profanity or other unacceptable and/or loud language will not be tolerated, "Cat calls" or other derogatory language toward students, staff, volunteers, parents or public will not be allowed.

C. Disturbing the Peace (Noise and Lighting):

- (1) Contractor shall observe the noise ordinance of the Site at all times including, without limitation, all applicable local, city, and/or state laws, ordinances, and/or regulations regarding noise and allowable noise levels.
- (2) The use of radios, etc., shall be controlled to keep all sound at a level that cannot be heard beyond the immediate area of use. District reserves the right to prohibit the use of radios at the Site, except for mobile phones or other handheld communication radios.
- (3) If portable lights are used after dark, all light must be located so as not to direct light into neighboring property.

D. Traffic:

- (1) Driving on the Premises shall be limited to periods when students and public are not present. If driving or deliveries must be made during the school hours, two (2) or more ground guides shall lead the vehicle across the area of travel. In no case shall driving take place across playgrounds or other pedestrian paths during recess, lunch, and/or class period changes. The speed limit on-the Premises shall be five (5) miles per hour (maximum) or less if conditions require.
- (2) All paths of travel for deliveries, including without limitation, material, equipment, and supply deliveries, shall be reviewed and approved by District in advance. Any damage will be repaired to the pre-damaged condition by the Contractor.
- (3) District shall designate a construction entry to the Site. If Contractor requests, District determines it is required, and to the extent possible, District shall designate a staging area so as not to interfere with the normal functioning of school facilities. Location of gates and fencing shall be approved in advance with District and at Contractor's expense.
- (4) Parking areas shall be reviewed and approved by District in advance. No parking is to occur under the drip line of trees or in softscape areas that could otherwise be damaged.

- E. All of the above shall be observed and complied with by the Contractor and all workers on the Site. Failure to follow these directives could result in individual(s) being suspended or removed from the work force at the discretion of the District. The same rules and regulations shall apply equally to delivery personnel, inspectors, consultants, and other visitors to the Site.

PART 18 - PRODUCTS Not Used.

PART 19 - EXECUTION Not Used.

END OF DOCUMENT

REGULATORY REQUIREMENTS

PART 20 - GENERAL

20.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Obtaining of Permits, Licenses and Registrations and Work to Comply with All Applicable Laws and Regulations;
- B. Special Conditions; and
- C. Quality Control.

20.02 DESCRIPTION:

This section covers the general requirements for regulatory requirements pertaining to the Work and is supplementary to all other regulatory requirements mentioned or referenced elsewhere in the Contract Documents.

20.03 REQUIREMENTS OF REGULATORY AGENCIES:

- A. All statutes, ordinances, laws, rules, codes, regulations, standards, and the lawful orders of all public authorities having jurisdiction over the Work, are hereby incorporated into these Contract Documents as if repeated in full herein and are intended to be included in any reference to Code or Building Code, unless otherwise specified, including, without limitation, the references in the list below. Contractor shall make available at the Site copies of all the listed documents applicable to the Work as the District and/or Architect may request, including, without limitation, applicable portions of the California Code of Regulations ("CCR").
 - (1) California Building Standards Administrative Code, Part 1, Title 24, CCR.
 - (2) California Building Code (CBC), Part 2, Title 24, CCR; (International Building Code volumes 1-2 and California Amendments).
 - (3) California Electrical Code (CEC), Part 3, Title 24, CCR; (National Electrical Code and California Amendments).
 - (4) California Mechanical Code (CMC), Part 4, Title 24, CCR; (Uniform Mechanical Code and California Amendments).
 - (5) California Plumbing Code (CPC), Part 5, Title 24, CCR; (Uniform Plumbing Code and California Amendments).

- (6) California Fire Code (CFC), Part 9, Title 24, CCR; (International Fire Code and California Amendments).
- (7) California Referenced Standards Code, Part 12, Title 24, CCR.
- (8) State Fire Marshal Regulations, Public Safety, Title 19, CCR.
- (9) Partial List of Applicable National Fire Protection Association (NFPA) Standards:
 - (a) NFPA 13 - Automatic Sprinkler System.
 - (b) NFPA 14 - Standpipes Systems.
 - (c) NFPA 17A - Wet Chemical System
 - (d) NFPA 24 - Private Fire Mains.
 - (e) (California Amended) NFPA 72 - National Fire Alarm Codes.
 - (f) NFPA 253 - Critical Radiant Flux of Floor Covering System.
 - (g) NFPA 2001 - Clean Agent Fire Extinguishing Systems.
- (10) California Division of the State Architect interpretation of Regulations ("DSA IR"), including, without limitation:
 - (a) DSA IR A-6 — Construction Change Document Submittal and Approval Processes.
 - (b) DSA IR A-7 — Project Inspector Certification and Approval.
 - (c) DSA IR A-8 — Project Inspector and Assistant Inspector Duties and Performance.
 - (d) DSA IR A-12 — Assistant Inspector Approval.
- (11) DSA Procedures ("DSA PR")
 - (a) DSA PR 13-01 – Construction Oversight Process
 - (b) DSA PR 13-02 – Project Certification Process

B. This Project shall be governed by applicable regulations, including, without limitation, the State of California's Administrative Regulations for the Division of the State Architect-Structural Safety (DSA/SS), Chapter 4, Part 1, Title 24, CCR, and the most current version on the date the bids are opened and as it pertains to school construction including, without limitation:

- (1) Test and testing laboratory per Section 4-335. District shall pay for the testing laboratory.
- (2) Special inspections per Section 4-333(c).

- (3) Deferred Approvals per section 4-317(g).
- (4) Verified reports per Sections 4-336 & 4-343(c).
- (5) Duties of the Architect & Engineers shall be per Sections 4-333(a) and 4-341.
- (6) Duties of the Contractor shall be per Section 4-343.
- (7) Duties of Project Inspector shall be per Section 4-334.
- (8) Addenda and Construction Change Documents per Section 4-338.

Contractor shall keep and make available all applicable parts of the most current version of Title 24 referred to in the plans and specifications at the Site during construction.

C. Items of deferred approval shall be clearly marked on the first sheet of the Architect's and/or Engineer's approved Drawings. All items later submitted for approval shall be per Title 24 requirements to the DSA.

- (1) Contractor shall submit the following to Architect for review and endorsement:
 - (a) Product information on proposed material/system supplier.
 - (b) Drawings, specifications, and calculations prepared, signed, and stamped by an architect or engineer licensed in the State of California for that portion of the Work.
 - (c) All other requirements as may be required by DSA.
- (2) Cost of preparing and submitting documentation per DSA Deferred Approval requirements including required modifications to Drawings and Specifications, whether or not indicated in the Contract Documents, shall be borne by Contractor.
- (3) Contractor shall not begin fabrication and installation of deferred approval items without first obtaining DSA approval of Drawings and Specifications.
- (4) Schedule of Work Subject to DSA Deferred Approval: Window wall systems exceeding 10 feet in span.

PART 21 – PRODUCTS Not Used.

PART 22 – EXECUTION Not Used.

END OF DOCUMENT

ABBREVIATIONS AND ACRONYMS

PART 23 – GENERAL

23.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions including without limitation, Definitions;
- B. Special Conditions.

23.02 DOCUMENT INCLUDES:

- A. Abbreviations used throughout the Contract Documents.
- B. Reference to a technical society, organization, or body is by abbreviation, as follows:

1.	AA	The Aluminum Association
2.	AAMA	American Architectural Manufacturers Association
3.	AASHTO	American Association of State Highway and Transportation Officials
4.	ABPA	Acoustical and Board Products Association
5.	ACI	American Concrete Institute
6.	AGA	American Gas Association
7.	AGC	Associated General Contractors of America
8.	AHC	Architectural Hardware Consultant
9.	AI	Asphalt Institute
10.	AIA	American Institute of Architects
11.	AIEE	American Institute of Electrical Engineers
12.	AISC	American Institute of Steel Construction
13.	AISI	American Iron and Steel Institute
14.	AMCA	Air Moving and Conditioning Association
15.	ANSI	American National Standards Institute
16.	APA	American Plywood Association
17.	ARI	Air Conditioning and Refrigeration Institute
18.	ASHRAE	American Society of Heating, Refrigeration and Air Conditioning Engineers
19.	ASME	American Society of Mechanical Engineers
20.	ASSE	American Society of Structural Engineers
21.	ASTM	American Society of Testing and Materials
22.	AWPB	American Wood Preservers Bureau
23.	AWPI	American Wood preservers Institute
24.	AWS	American Welding Society

25.	AWSC	American Welding Society Code
26.	AWI	Architectural Woodwork Institute
27.	AWWA	American Water Works Association
28.	BIA	Brick Institute of America
29.	CCR	California Code of Regulations
30.	CLFMI	Chain Link Fence Manufacturers Institute
31.	CMG	California Masonry Guild
32.	CRA	California Redwood Association
33.	CRSI	Concrete Reinforcing Steel Institute
34.	CS	Commercial Standards
35.	CSI	Construction Specifications Institute
36.	CTI	Cooling Tower Institute
37.	FGMA	Flat Glass Manufacturer's Association
38.	FIA	Factory Insurance Association
39.	FM	Factory Mutual
40.	FS	Federal Specification
41.	FTI	Facing Title Institute
42.	GA	Gypsum Association
43.	ICC	International Code Council
44.	IEEE	Institute of Electrical and Electronic Engineers
45.	IES	Illumination Engineering Society
46.	LIA	Lead Industries Association
47.	MIA	Marble Institute of America
48.	MLMA	Metal Lath Manufacturers Association
49.	MS	Military Specifications
50.	NAAMM	National Association of Architectural Metal Manufacturers
51.	NBHA	National Builders Hardware Association
52.	NBFU	National Board of Fire Underwriters
53.	NBS	National Bureau of Standards
54.	NCMA	National Concrete Masonry Association
55.	NEC	National Electrical Code
56.	NEMA	National Electrical Manufacturers Association
57.	NFPA	National Fire Protection Association/National Forest Products Association
58.	NMWIA	National Mineral Wool Insulation Association
59.	NTMA	National Terrazzo and Mosaic Association
60.	NWMA	National Woodwork Manufacturer's Association
61.	ORS	Office of Regulatory Services (California)
62.	OSHA	Occupational Safety and Health Act
63.	PCI	Precast Concrete Institute
64.	PCA	Portland Cement Association
65.	PDCA	Painting and Decorating Contractors of America
66.	PDI	Plumbing Drainage Institute
67.	PEI	Porcelain Enamel Institute
68.	PG&E	Pacific Gas & Electric Company
69.	PS	Product Standards
70.	SDI	Steel Door Institute; Steel Deck Institute
71.	SJI	Steel Joist Institute
72.	SSPC	Steel Structures Painting Council
73.	TCA	Tile Council of America
74.	TPI	Truss Plate Institute
75.	UBC	Uniform Building Code

76.	UL	Underwriters Laboratories Code
77.	UMC	Uniform Mechanical Code
78.	USDA	United States Department of Agriculture
79.	VI	Vermiculite Institute
80.	WCLA	West Coast Lumberman's Association
81.	WCLB	West Coast Lumber Bureau
82.	WEUSER	Western Electric Utilities Service Engineering Requirements
83.	WIC	Woodwork Institute of California
84.	WPOA	Western Plumbing Officials Association

PART 24 - PRODUCTS Not Used.

PART 25 - EXECUTION Not Used.

END OF DOCUMENT

DEFINITIONS

PART 26 - GENERAL

26.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions including without limitation, Definitions;
- B. Special Conditions.

26.02 QUALITY ASSURANCE

- A. For products or workmanship specified by association, trade, or Federal Standards, Contractor shall comply with requirements of the standard, except when more rigid requirements are specified in the Contract Documents, or are required by applicable codes.
- B. Contractor shall conform to current reference standard publication date in effect on the date of bid opening.
- C. Contractor shall obtain copies of standards unless specifically required not to by the Contract Documents.
- D. Contractor shall maintain a copy of all standards at jobsite during submittals, planning, and progress of the specific Work, until final completion, unless specifically required not to by the Contract Documents.
- E. Should specified reference standards conflict with Contract Documents, Contractor shall request clarification from the District and/or the Architect before proceeding.
- F. The contractual relationship of the parties to the Contract shall not be altered from the contractual relationship as indicated in the Contract Documents by mention or inference otherwise in any referenced document.
- G. Governing Codes shall be as shown in the Contract Documents including, without limitation, the Specifications.

END OF DOCUMENT

REFERENCES**PART 27 - GENERAL****27.01 SCHEDULE OF REFERENCES:**

The following information is intended only for the general assistance of the Contractor, and the District does not represent that all of the information is current. It is the Contractor's responsibility to verify the correct information for each of the entities listed.

AA	The Aluminum Association 1400 Crystal Drive, Suite 430 Arlington, VA 22202 www.aluminum.org	703/358-2960
AABC	Associated Air Balance Council 1518 K Street, NW, Suite 503 Washington, DC 20005 www.aabc.com	202/737-0202
AAMA	American Architectural Manufacturers Association 1827 Walden Office Sq., Suite 550 Schaumburg, IL 60173-4268 www.aamanet.org	847/303-5664
AASHTO	American Association of State Highway and Transportation Officials 444 N Capitol St. NW - Suite 249 Washington, DC 20001 www.transportation.org	202/624-5800
AATCC	American Association of Textile Chemists and Colorists P.O. Box 12215 One Davis Drive Research Triangle Park, NC 27709 2215 www.aatcc.org	919/549-8141
ACA	American Coatings Association 1500 Rhode Island Ave., NW Washington DC, 20005 www.paint.org	202/462-6272

ACI	American Concrete Institute 38800 Country Club Dr. Farmington Hills, MI 48331-3439 www.concrete.org	248/848-3700
ACPA	American Concrete Pipe Association 8445 Freeport Parkway, Suite 350 Irving, TX 75063-2595 www.concrete-pipe.org	972/506-7216
ADC	Air Duct Council 1901 N. Roselle Road, Suite 800 Schaumburg, Illinois 60195 www.flexibleduct.org	847/706-6750
AF&PA	American Forest and Paper Association 1101 K Street, NW, Suite 700 Washington, DC 20005 www.afandpa.org	202/463-2700
AGA	American Gas Association 400 North Capitol Street, NW Washington, DC 20001 www.aga.org	202/824-7000
AGC	Associate General Contractors of America 2300 Wilson Blvd., Suite 300 Arlington, VA 22201 www.agc.org	703/548-3118
AHA	American Hardboard Association 1210 West Northwest Highway Palatine, IL 60067 domensino.com/AHA/default.htm	847/934-8800
AI	Asphalt Institute 2696 Research Park Drive Lexington, KY 40511-8480 www.asphaltinstitute.org	859/288-4960
AIA	The American Institute of Architects 1735 New York Ave., NW Washington, DC 20006-5292 www.aia.org	202/626-7300
AISC	American Institute of Steel Construction 130 East Randolph Street Suite 2000 Chicago, IL 60601 www.aisc.org	312.670.2400

AIA	American Insurance Association (formerly the National Board of Fire Underwriters) 555 12th St, NW, Suite 550 Washington DC 20004 www.aiadc.org	202/828-7100
AISI	American Iron and Steel Institute 25 Massachusetts Ave., NW, Suite 800 Washington, DC 20001 www.steel.org	202/452.7100
AITC	American Institute of Timber Construction 7012 S. Revere Parkway Suite 140 Centennial, CO 80112 www.aitc-glulam.org	503/639.0651
ALI	Associated Laboratories, Inc. P.O. Box 152837 Dallas, TX 75315 www.assoc-labs.com	214/565-0593
ALSC	American Lumber Standards Committee, Inc. 7470 New Technology Way, Suite F Frederick, MD 21703 www.alsc.org	301/972-1700
AMCA	Air Movement and Control Association International, Inc. 30 W. University Drive Arlington Heights, IL 60004 www.amca.org	847/394-0150
ANLA	American Nursery & Landscape Association (now AmericanHort) 525 9 th St NW, Suite 80 Washington, DC 20004 www.americanhort.org	202/789-2900
ANSI	American National Standards Institute 1899 L Street, NW, 11th Floor Washington, DC, 20036 www.ansi.org	202/293.8020
APA	APA-The Engineered Wood Association 7011 S. 19th Street Tacoma, WA 98466-5333 www.apawood.org	253/565-6600

APA	Architectural Precast Association 325 John Know Rd, Ste L103 Tallahassee, FL 32303 www.archprecast.org	850/205.5637
ARI	Air Conditioning and Refrigeration Institute (now Air-Conditioning, Heating, & Refrigeration Institute) 2111 Wilson Blvd, Suite 500 Arlington, VA 22201 www.ahrinet.org	703/524-8800
ARMA	Asphalt Roofing Manufacturers Association Public Information Department 750 National Press Building 529 14th Street, NW Washington, DC 20045 www.asphaltroofing.org	202/591-2450
ASA	The Acoustical Society of America ASA Office Manager Suite 1N01 2 Huntington Quadrangle Melville, NY 11747-4502 http://asa.aip.org	516/576-2360
ASCE	American Society of Civil Engineers 1801 Alexander Bell Drive Reston, VA 20191 www.asce.org	800/548-2723 703/295-6300
ASHRAE	American Society of Heating, Refrigerating and Air Conditioning Engineers 1791 Tullie Circle, NE Atlanta, GA 30329-2305 www.ashrae.org	800/527-4723 404/636-8400
ASLA	American Society of Landscape Architects 636 Eye Street, NW Washington, DC 20001-3736 www.asla.org	202/898-2444
ASME	American Society of Mechanical Engineers Three Park Avenue New York, NY 10016-5990 www.asme.org	800/434-2763
ASPE	American Society of Plumbing Engineers 2980 S River Rd. Des Plaines, IL 60018 http://aspe.org	847/296-0002

ASQ	American Society for Quality P.O. Box 3005 Milwaukee, WI 53201-3005 or 600 North Plankinton Avenue Milwaukee, WI 53203 http://asq.org	800/248-1946 414/272-8575
ASSE	American Society of Sanitary Engineering 901 Canterbury, Suite A Westlake, Ohio 44145 www.asse-plumbing.org	440/835-3040
ASTM	ASTM International 100 Barr Harbor Drive PO Box C700 West Conshohocken, PA, 19428-2959 www.astm.org	610/832-9500
AWCI	Association of the Wall and Ceiling Industry 513 West Broad Street, Suite 210 Falls Church, VA 22046 www.awci.org	703/538-1600
AWPA	American Wood Protection Association P.O. Box 361784 Birmingham, AL 35236-1784 www.awpa.com	205/733-4077
AWPI	American Wood Preservers Institute 2750 Prosperity Ave. Suite 550 Fairfax, VA 22031-4312 www.arcat.com	800/356-AWPI 703/204-0500
AWS	American Welding Society 8669 Doral Boulevard, Suite 130 Doral, Florida 33166 www.aws.org	800/443-9353 305/443-9353
AWI	Architectural Woodwork Institute 46179 Westlake Drive, Suite 120 Potomac Falls, VA 20165-5874 www.awinet.org	571/323-3636
AWWA	American Water Works Association 6666 West Quincy Avenue Denver, CO 80235 www.awwa.org	800/926-7337 303/794 7711

BHMA	Builders Hardware Manufacturers Association 355 Lexington Avenue, 15th floor New York, NY 10017 www.buildershardware.com	212/297-2122
BIA	The Brick Industry Association 1850 Centennial Park Drive, Suite 301 Reston, VA 20191 www.gobrick.com	703/620-0010
CGA	Compressed Gas Association 14501 George Carter Way, Suite 103 Chantilly VA 20151-2923 www.cganet.com	703/788-2700
CISCA	Ceilings & Interior Systems Construction Association 1010 Jorie Blvd, Suite 30 Oak Brook, IL 60523 www.cisca.org	630/584-1919
CISPI	Cast Iron Soil Pipe Institute 1064 Delaware Avenue SE Atlanta, GA 30316 www.cispi.org	404/622-0073
CLFMI	Chain Link Fence Manufacturers Institute 10015 Old Columbia Road, Suite B-215 Columbia, MD 21046 www.associationsites.com/main-pub.cfm?usr=clfma	410/290-6267
CPA	Composite Panel Association 19465 Deerfield Avenue, Suite 306 Leesburg, VA 20176 www.compositepanel.org	703/724-1128
CPSC	Consumer Product Safety Commission 4330 East West Highway Bethesda, MD 20814 www.cpsc.gov	301/504-7923 800/638-2772
CRA	California Redwood Association 405 Enfrente Drive, Suite 200 Novato, CA 94949 www.calredwood.org	415/382-0662

CRI	Carpet and Rug Institute P.O. Box 2048 Dalton, Georgia 30722-2048 www.carpet-rug.org	706/278-3176
CRSI	Concrete Reinforcing Steel Institute 933 N. Plum Grove Road Schaumburg, IL 60173 4758 www.crsi.org	847/517-1200
CSI	The Construction Specifications Institute 110 South Union Street, Suite 100 Alexandria VA 22314 www.csinet.org	800/689-2900
CTIOA	Ceramic Tile Institute of America 12061 Jefferson Blvd. Culver City, CA 90230-6219 www.ctioa.org	310/574-7800
DHI	Door and Hardware Institute (formerly National Builders Hardware Association) 14150 Newbrook Dr. Chantilly, VA 20151 www.dhi.org	703/222-2010
DIPRA	Ductile Iron Pipe Research Association 2000 2nd Avenue, South Suite 429 Birmingham, AL 35233 www.dipra.org	205/402-8700
DOC	U.S. Department of Commerce 1401 Constitution Ave., NW Washington, D.C. 20230 www.commerce.gov	202/482-2000
DOT	U.S. Department of Transportation 1200 New Jersey Avenue, SE Washington, DC 20590 www.dot.gov	855/368-4200
EJMA	Expansion Joint Manufacturers Association, Inc. 25 North Broadway Tarrytown, NY 10591 www.ejma.org	914/332-0040

EPA	Environmental Protection Agency Ariel Rios Building 1200 Pennsylvania Avenue, N.W. Washington, DC 20460 www.epa.gov	202/272-0167
FCICA	Floor Covering Installation Contractors Association 7439 Millwood Drive West Bloomfield, MI 48322 www.fcica.com	248/661-5015 877/TO-FCICA
FM Global	Factory Mutual Insurance Company Amy Daley Global Practice Leader – Education, Public Entities, Health Care FM Global 270 Central Avenue Johnston, RI 02919-4949 www.fmglobal.com	401/275-3000 401/275-3029
FS	General Services Administration (GSA) Index of Federal Specifications, Standards and Commercial Item Descriptions 470 East L'Enfant Plaza, SW, Suite 8100 Washington, DC 20407 www.gsa.gov	202/619-8925
GA	The Gypsum Association 6525 Belcrest Road, Suite 480 Hyattsville, MD 20782 www.gypsum.org	301/277-8686
GANA	Glass Association of North America 800 SW Jackson St., Suite 1500 Topeka, KS 66612-1200 www.glasswebsite.com	785/271-0208
HMA	Hardwood Manufacturers Association 665 Rodi Road, Suite 305 Pittsburgh, PA 15235 http://hmamembers.org	412/244-0440
HPVA	Hardwood Plywood & Veneer Association 1825 Michael Faraday Drive Reston, Virginia 20190 www.hpva.org	703/435-2900

IAPMO	International Association of Plumbing and Mechanical Officials (formerly the Western Plumbing Officials Association) 4755 E. Philadelphia St. Ontario, CA 91761 www.iapmo.org	909/472-4100
ICC	International Code Council 500 New Jersey Avenue, NW, 6th Floor Washington, DC 20001 www.iccsafe.org	888/422-7233
IEEE	Institute of Electrical and Electronics Engineers 3 Park Avenue, 17th Floor New York, NY 10016-5997 www.ieee.org	212/419-7900
IES	Illuminating Engineering Society 120 Wall Street, Floor 17 New York, NY 10005-4001 www.ies.org	212/248-5000
ITRK	Intertek Testing Services 3933 US Route 11 Cortland, NY 13045 www.intertek.com	607/753-6711
MCAA	Mechanical Contractors Association of America 1385 Piccard Drive Rockville, MD 20850 www.mcaa.org	301/869-5800
MIA	Marble Institute of America 28901 Clemens Rd, Ste 100 Cleveland, OH 44145 www.marble-institute.com	440/250-9222
MMPA (formerly WMMPA)	Moulding & Millwork Producers Association (formerly Wood Moulding & Millwork Producers Association) 507 First Street Woodland, CA 95695 www.wmmpa.com	530/661-9591 800/550-7889

MSS	Manufacturers Standardization Society (MSS) of the Valve and Fittings Industry 127 Park Street, NE Vienna, VA 22180-4602 http://mss-hq.org	703/281-6613
NAAMM	National Association of Architectural Metal Manufacturers 800 Roosevelt Rd. Bldg. C, Suite 312 Glen Ellyn, IL 60137 www.naamm.org	630/942-6591
NAIMA	North American Insulation Manufacturers Association 44 Canal Center Plaza, Suite 310 Alexandria, VA 22314 www.naima.org	703/684-0084
NAPA	National Asphalt Pavement Association 5100 Forbes Blvd. Lanham, MD USA 20706-4407 www.asphaltpavement.org	888/468-6499 301/731-4748
NCSPA	National Corrugated Steel Pipe Association 14070 Proton Road, Suite 100 LB9 Dallas, TX 75244 www.ncspa.org	972/850-1907
NCMA	National Concrete Masonry Association 13750 Sunrise Valley Drive Herndon, VA 20171-4662 www.ncma.org	703/713-1900
NEBB	National Environmental Balancing Bureau 8575 Grovemont Circle Gaithersburg, MD 20877 www.nebb.org	301/977-3698
NECA	National Electrical Contractors Association 3 Bethesda Metro Center, Suite 1100 Bethesda, MD 20814 www.necanet.org	301/657-3110
NEMA	National Electrical Manufacturers Association 1300 North 17th Street, Suite 1752 Rosslyn, Virginia 22209 www.nema.org	703/841-3200

NEII	National Elevator Industry, Inc. 1677 County Route 64 P.O. Box 838 Salem, New York 12865-0838 www.neii.org	518/854-3100
NFPA	National Fire Protection Association 1 Batterymarch Park Quincy, Massachusetts USA 02169-7471 www.nfpa.org	617/770-3000
NHLA	National Hardwood Lumber Association PO Box 34518 Memphis, TN 38184 www.nhla.com	901/377-1818
NIA	National Insulation Association 12100 Sunset Hills Road, Suite 330 Reston, VA 20190 www.insulation.org	703/464-6422
NRCA	National Roofing Contractors Association 10255 W. Higgins Road, Suite 600 Rosemont, IL 60018-5607 www.nrca.net	847/299-9070
NSF	NSF International P.O. Box 130140 789 N. Dixboro Road Ann Arbor, MI 48113-0140, USA www.nsf.org	800/673-6275 734/769-8010
NTMA	National Terrazzo and Mosaic Association PO Box 2605 Fredericksburg, TX 78624 www.ntma.com	800/323-9736
OSHA	Occupational Safety and Health Act U.S. Department of Labor Occupational Safety & Health Administration 200 Constitution Ave., NW Washington, D.C. 20210 www.osha.gov	800/321-OSHA (6742)

PCA	Portland Cement Association 5420 Old Orchard Road Skokie, IL 60077 or 500 New Jersey Ave., N.W. 7 th Floor Washington, D.C. 20001 www.cement.org	847/966-6200 202/408-9494
PCI	Precast/Prestressed Concrete Institute 200 W. Adams St. #2100 Chicago, IL 60606 www.pci.org	312/786-0300
PDCA	Painting and Decorating Contractors of America 2316 Millpark Drive, Ste 220 Maryland Heights, MO 63043 www.pdca.com	800/332-PDCA (7322) 314/514-7322
PDI	Plumbing & Drainage Institute 800 Turnpike Street, Suite 300 North Andover, MA 01845 http://pdionline.org	978/557-0720 800/589-8956
PEI	Porcelain Enamel Institute, Inc. P.O. Box 920220 Norcross, GA 30010 www.porcelainenamel.com	770/676-9366
PG&E	Pacific Gas & Electric Company www.pge.com	800/743-5000
PLANET	Professional Landcare Network 950 Herndon Parkway, Suite 450 Herndon, Virginia 20170 www.landcarenetwork.org	703/736-9666 800/395-2522 703/736-9668
RFCI	Resilient Floor Covering Institute 115 Broad Street, Suite 201 La Grange GA 30240 www.rfci.com	706/882-3833
RIS	Redwood Inspection Service 818 Grayson Road, Suite 201 Pleasant Hill, CA 94523 www.redwoodinspection.com	925/935-1499
SDI	Steel Deck Institute P.O. Box 25 Fox River Grove, IL 60021 www.sdi.org	847/458-4647

SDI	Steel Door Institute 30200 Detroit Road Westlake, Ohio 44145 www.steeldoor.org	440/899-0010
SJI	Steel Joist Institute 234 W. Cheves Street Florence, SC 29501 http://steeljoist.org	843/407-4091
SMA	Stucco Manufacturers Association 500 East Yale Loop Irvine, CA 92614 www.stuccomfgassoc.com	949/387.7611
SMACNA	Sheet Metal and Air Conditioning Contractors' National Association 4201 Lafayette Center Drive Chantilly, Virginia 20151-1219 www.smacna.org	703/803-2980
SPI	SPI: The Plastics Industry Trade Association, Inc. 1667 K St., NW, Suite 1000 Washington, DC 20006 www.plasticsindustry.org	202/974-5200
SSPC	Society for Protective Coatings (formerly the Steel Structures Painting Council) 40 24th St 6th Fl Pittsburgh, PA 15222 www.sspc.org	412/281-2331 877/281-7772
TCA	The Tile Council of North America 100 Clemson Research Blvd. Anderson, SC 29625 www.tcnatile.com	864/646-8453
TPI	Truss Plate Institute 218 North Lee Street, Suite 312 Alexandria, VA 22314 www.tpinst.org	703/683-1010
TPI	Turfgrass Producers International 2 East Main Street East Dundee, IL 60118 www.turfgrasssod.org	800/405-8873 847/649-5555

TCIA	Tree Care Industry Association (formerly the National Arborist Association) 136 Harvey Road, Suite 101 Londonderry, NH 03053 www.tcia.org	800/733-2622
TVI	The Vermiculite Institute c/o The Schundler Company 150 Whitman Avenue Edison, NJ. 08817 www.vermiculiteinstitute.org	732/287-2244
UL	Underwriters Laboratories Inc. 333 Pfingsten Road Northbrook, IL 60062-2096 www.ul.com	847/272-8800 877/854-3577
UNI	Uni-Bell PVC Pipe Association 2711 LBJ Freeway, Suite 1000 Dallas, TX 75234 www.uni-bell.org	972/243-3902
USDA	U.S. Department of Agriculture 1400 Independence Ave., S.W. Washington, DC 20250 www.usda.gov	202/720-2791
WA	Wallcoverings Association 401 North Michigan Avenue Suite 2200 Chicago, IL 60611 www.wallcoverings.org	312/321-5166

WCLIB	West Coast Lumber Inspection Bureau P.O. Box 23145 Portland, OR 97281 or 6980 S.W. Varns Tigard, OR 97223 www.wclib.org	503/639-0651
WCMA	Window Covering Manufacturers Association 355 Lexington Avenue 15th Floor New York, New York 10017 www.wcmanet.org	212/297-2122
WDMA	Window & Door Manufacturers Association 401 N. Michigan Avenue, Suite 2200 Chicago, IL 60611 or 2025 M Street, NW, Ste. 800 Washington, D.C. 20036-3309 www.wdma.com	312/321-6802 202/367-1157
WI	Woodwork Institute P.O. Box 980247 West Sacramento, CA 95798 www.wicnet.org	916/372-9943
WRI	Wire Reinforcement Institute 942 Main Street Hartford, CT 06103 www.wirereinforcementinstitute.org	860/240-9545
WWCA	Western Wall & Ceiling Contractors Association 1910 N. Lime St. Orange, California 92865 www.wwcca.org	714/221-5520
WWPA	Western Wood Products Association 522 SW Fifth Ave., Suite 500 Portland, OR 97204-2122 www2.wwpa.org	503/224-3930

PART 28 - PRODUCTS Not Used.

PART 29 - EXECUTION Not Used.

END OF DOCUMENT

MATERIALS AND EQUIPMENT

PART 30 - GENERAL

30.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Purchase of Materials and Equipment;
- B. Special Conditions;
- C. Imported Materials Certification.

30.02 MATERIAL AND EQUIPMENT

- A. Only items approved by the District and/or Design Professional shall be used.
- B. Contractor shall submit lists of products and other product information in accordance with the Contract Documents, including, without limitation, the provisions regarding the submittals.

30.03 MATERIAL AND EQUIPMENT COLORS

- A. The District and/or Architect will provide a schedule of colors.
- B. No individual color selections will be made until after approval of all pertinent materials and equipment and after receipt of appropriate samples in accordance with the Contract Documents, including, without limitation, the provisions regarding the submittals.
- C. Contractor shall request priority in writing for any item requiring advance ordering to maintain the approved Construction Schedule.

30.04 DELIVERY, STORAGE, AND HANDLING

- A. Contractor shall deliver manufactured materials in original packages, containers, or bundles (with seals unbroken), bearing name or identification mark of manufacturer.
- B. Contractor shall deliver fabrications in as large assemblies as practicable; where specified as shop-primed or shop-finished, package or crate as required to preserve such priming or finish intact and free from abrasion.
- C. Contractor shall store materials in such a manner as necessary to properly protect them from damage. Materials or equipment damaged by handling, weather, dirt, or from any other cause will not be accepted.

- D. Materials are not acceptable that have been warehoused for long periods of time, stored or transported in improper environment, improperly packaged, inadequately labeled, poorly protected, excessively shipped, deviated from normal distribution pattern, or reassembled.
- E. Contractor shall store material so as to cause no obstructions of sidewalks, roadways, access to the Site or buildings, and underground services. Contractor shall protect material and equipment furnished under Contract.
- F. Contractor may store materials on Site with prior written approval by the District, all material shall remain under Contractor's control and Contractor shall remain liable for any damage to the materials. Should the Project Site not have storage area available, the Contractor shall provide for off-site storage at a bonded warehouse and with appropriate insurance coverage at no cost to District.
- G. When any room in Project is used as a shop or storeroom, the Contractor shall be responsible for any repairs, patching, or cleaning necessary due to that use. Location of storage space shall be subject to prior written approval by District.

PART 31 - PRODUCTS

31.01 MANUFACTURERS

- A. Manufacturers listed in various sections of Contract Documents are names of those manufacturers that are believed to be capable of supplying one or more of items specified therein.
- B. The listing of a manufacturer does not imply that every product of that manufacturer is acceptable as meeting the requirements of the Contract Documents.

31.02 FACILITIES AND EQUIPMENT

Contractor shall provide, install, maintain, and operate a complete and adequate facility for handling, the execution, disposal, and distribution of material and equipment as required for proper and timely performance of Work connected with Contract.

31.03 MATERIAL REFERENCE STANDARDS

Where material is specified solely by reference to "standard specifications" and if requested by District, Contractor shall submit for review data on actual material proposed to be incorporated into Work of Contract listing name and address of vendor, manufacturer, or producer, and trade or brand names of those materials, and data substantiating compliance with standard specifications.

PART 32 - EXECUTION

32.01 WORKMANSHIP

- A. Where not more specifically described in any other Contract Documents, workmanship shall conform to methods and operations of best standards and accepted practices of trade or trades involved and shall include items of fabrication, construction, or installation regularly furnished or required for completion (including finish and for successful operation, as intended).
- B. Work shall be executed by tradespersons skilled in their respective lines of Work. When completed, parts shall have been durably and substantially built and present a neat appearance.

32.02 COORDINATION

- A. Contractor shall coordinate installation of Work so as to not interfere with installation of others. Adjustment or rework because of Contractor's failure to coordinate will be at no additional cost to District.
- B. Contractor shall examine in-place work for readiness, completeness, fitness to be concealed or to receive other work, and in compliance with Contract Documents. Concealing or covering Work constitutes acceptance of additional cost which will result should in-place Work be found unsuitable for receiving other Work or otherwise deviating from the requirements of the Contract Documents.

32.03 COMPLETENESS

Contractor shall provide all portions of the Work, unless clearly stated otherwise, installed complete and operational with all elements, accessories, anchorages, utility connections, etc., in manner to assure well-balanced performance, in accordance with manufacturer's recommendations and by Contract Documents. For example, electric water coolers require water, electricity, and drain services; roof drains require drain system; sinks fit within countertop, etc. Terms such as "installed complete," "operable condition," "for use intended," "connected to all utilities," "terminate with proper cap," "adequately anchored," "patch and refinish," "to match similar," should be assumed to apply in all cases, except where completeness of functional or operable condition is specifically stated as not required.

32.04 APPROVED INSTALLER OR APPLICATOR

Installation by a manufacturer's approved installer or applicator is an understood part of Specifications and only approved installer or applicator is to provide on-site Work where specified manufacturer has on-going program of approving (i.e. certifying, bonding, re-warranting) installers or applicators. Newly established relationships between a manufacturer and an installer or applicator who does not have other approved applicator work in progress or completed is not approved for this Project.

32.05 MANUFACTURER'S RECOMMENDATIONS

All installations shall be in accordance with manufacturer's published recommendations and specific written directions of manufacturer's representative. Should Contract Documents differ from recommendations of manufacturer or directions of his representative, Contractor shall analyze differences, make recommendations to the District and the Architect in writing, and shall not proceed until interpretation or clarification has been issued by the District and/or the Architect.

END OF DOCUMENT

QUALITY CONTROL

PART 33 - GENERAL

33.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Inspector, Inspections and Tests, Uncovering of Work and Non-conforming of Work and Correction of Work;
- B. Special Conditions.

33.02 RELATED CODES:

- A. The Work is governed by requirements of Title 24, California Code of Regulations ("CCR"), and the Contractor shall keep a copy of these available at the job Site for ready reference during construction.
- B. The Division of the State Architect ("DSA") shall be notified at or before the start of construction.

33.03 OBSERVATION AND SUPERVISION:

- A. The District and Architect or their appointed representatives will review the Work and the Contractor shall provide facilities and access to the Work at all times as required to facilitate this review. Administration by the Architect and any consulting Structural Engineer will be in accordance with applicable regulations, including, without limitation, CCR, Part 1, Title 24, Section 4-341.
- B. One or more Project Inspector(s) approved by DSA and employed by or in contract with the District, referred to hereinafter as the "Project Inspector", will observe the work in accordance with CCR, Part 1, Title 24, Sections 4-333(b) and 4-342:
 - (1) The Project Inspector and Special Inspector(s) shall have access to the Work wherever it is in preparation or progress for ascertaining that the Work is in accordance with the Contract Documents and all applicable code sections. The Contractor shall provide facilities and operation of equipment as needed, and access as required and shall provide assistance for sampling or measuring materials.
 - (2) The Project Inspector will notify the District and Architect and call the attention of the Contractor to any observed failure of Work or material to conform to Contract Documents.
 - (3) The Project Inspector shall observe and monitor all testing and inspection activities required.

The Contractor shall conform with all applicable laws as indicated in the Contract Documents, including, without limitation, to CCR, Part 1, Title 24, Section 4-343. The Contractor shall supervise and direct the Work and maintain a competent superintendent on the job who is authorized to act in all matters pertaining to the Work. The Contractor's superintendent shall also inspect all materials, as they arrive, for compliance with the Contract Documents. Contractor shall reject defective Work or materials immediately upon delivery or failure of the Work or material to comply with the Contract Documents. The Contractor shall submit verified reports as indicated in the Contract Documents, including, without limitation, the Specifications and as required by Part 1, Title 24, Section 4-336.

33.04 TESTING AGENCIES:

- A. Testing agencies and tests shall be in conformance with the General Documents and the requirements of Part 1, Title 24, Section 4- 335.
- B. Testing and inspection in connection with earthwork shall be under the direction of the District's consulting soils engineer, if any, referred to hereinafter as the "Soils Engineer."
- C. Testing and inspection of construction materials and workmanship shall be performed by a qualified laboratory, referred to hereinafter as the "Testing Laboratory." The Testing Laboratory shall be under direction of an engineer registered in the State of California, shall conform to requirements of ASTM E329, and shall be employed by or in contract with the District.

33.05 TESTS AND INSPECTIONS:

- A. The Contractor shall be responsible for notifying the District and Project Inspector of all required tests and inspections. Contractor shall notify the District and Project Inspector at least seventy-two hours (72) hours in advance of performing any Work requiring testing or inspection.
- B. The Contractor shall provide access to Work to be tested and furnish incidental labor, equipment, and facilities to facilitate all inspections and tests.
- C. The District will pay for first inspections and tests required by the "CCR", and other inspections or tests that the District and/or the Architect may direct to have made, including the following principal items:
 - (1) Tests and observations for earthwork and paving.
 - (2) Tests for concrete mix designs, including tests of trial batches.
 - (3) Tests and inspections for structural steel work.
 - (4) Field tests for framing lumber moisture content.
 - (5) Additional tests directed by the District that establish that materials and installation comply with the Contract Documents.
 - (6) Tests and observations of welding and expansion anchors.

- D. The District may at its discretion, pay and then back charge the Contractor for:
 - (1) Retests or reinspections, if required, and tests or inspections required due to Contractor error or lack of required identifications of material.
 - (2) Uncovering of work in accordance with Contract Documents.
 - (3) Testing done on weekends, holidays, and overtime will be chargeable to the Contractor for the overtime portion.
 - (4) Testing done off Site.
- E. Testing and inspection reports and certifications:
 - (1) If initially received by Contractor, Contractor shall provide to each of the following a copy of the agency or laboratory report of each test or inspection or certification.
 - (a) The District;
 - (b) The Construction Manager, if any;
 - (c) The Architect;
 - (d) The Consulting Engineer, if any;
 - (e) Other engineers on the Project, as appropriate;
 - (f) The Project Inspector; and
 - (g) The Contractor.
 - (2) When the test or inspection is one required by the CCR, a copy of the report shall also be provided to the DSA.

PART 34 - PRODUCTS

34.01 TYPE OF TESTS AND INSPECTIONS

- A. Testing and inspection shall be in accordance with DSA Form 103 (or current version)
 - B. Slump Test
ASTM C 143
 - C. Concrete Tests
- Testing agency shall test concrete used in the work per the following paragraphs:
- (1) Compressive Strength:

- (a) Minimum number of tests required: One (1) set of three (3) cylinders for each 100 cubic yards (Sec. 2604(h) 01) of concrete or major fraction thereof, placed in one (1) day. See Title 24, Section 2605(g).
- (b) Two cylinders of each set shall be tested at twenty-eight (28) days. One (1) cylinder shall be held in reserve and tested only when directed by the Architect or District.
- (c) Concrete shall test the minimum ultimate compressive strength in twenty-eight 28 days, as specified on the structural drawings.
- (d) In the event that the twenty-eight (28) day test falls below the minimum specified strength, the effective concrete in place shall be tested by taking cores in accordance with UBC Standard No. 26-13 and tested as required for cylinders.
- (e) In the event that the test on core specimens falls below the minimum specified strength, the concrete will be deemed defective and shall be removed and replaced upon such direction of the Architect, and in a manner acceptable to the Division of the State Architect.

D. Reinforcing, Steel

E. Structural Steel Per Title 24 and as noted:

- (1) Material: Steel per Table in Title 24, Section 2712.
- (2) Qualification of Welders (UBC Std. 27-6).
- (3) Shop fabrication (Section 2712(d). Structural steel only).
- (4) Shop and field welding (Section 2712(e)).

PART 35 - EXECUTION Not Used.

END OF DOCUMENT

TEMPORARY FACILITIES AND CONTROLS

PART 36 – GENERAL

36.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions;
- C. Site Standards; and
- D. Construction Waste Management and Disposal.

36.02 TEMPORARY UTILITIES:

- A. Electric Power and Lighting:
 - (1) Contractor will pay for power during the course of the Work. To the extent power is available in the building(s) or on the Site, Contractor may use the District's existing utilities by making prearranged payments to the District for the utilities used by Contractor and all Subcontractors. Contractor shall be responsible for providing temporary facilities required to deliver that power service from its existing location in the building(s) or on the Site to point of intended use.
 - (2) Contractor shall verify characteristics of power available in building(s) or on the Site. Contractor shall take all actions required to make modifications where power of higher voltage or different phases of current are required. Contractor shall be fully responsible for providing that service and shall pay all costs required therefor.
 - (3) Contractor shall furnish, wire for, install, and maintain temporary electrical lights wherever it is necessary to provide illumination for the proper performance and/or observation of the Work: a minimum of 20 foot-candles for rough work and 50 foot-candles for finish work.
 - (4) Contractor shall be responsible for maintaining existing lighting levels in the project vicinity should temporary outages or service interruptions occur.
- B. Heat and Ventilation:
 - (1) Contractor shall provide temporary heat to maintain environmental conditions to facilitate progress of the Work, to meet specified minimum conditions for the installation and curing of materials, and to

protect materials and finishes from damage due to improper temperature and humidity conditions. Portable heaters shall be standard units complete with controls.

- (2) Contractor shall provide forced ventilation and dehumidification, as required, of enclosed areas for proper installation and curing of materials, to disperse humidity, and to prevent hazardous accumulations of dust, fumes, vapors, and gases.
- (3) Contractor shall pay the costs of installation, maintenance, operation, and removal of temporary heat and ventilation, including costs for fuel consumed, required for the performance of the Work.

C. Water:

- (1) Contractor shall pay for water used during the course of the Work. Contractor shall coordinate and pay for installation or use of water meter in compliance with local water agency requirements. To the extent water is then available in the building(s) or on the Site, Contractor may use the District's existing utilities by making prearranged payments to the District for the utilities used by Contractor and all Subcontractors. Contractor shall be responsible for providing temporary facilities required to deliver such utility service from its existing location in the building(s), on the Site, or other location approved by the local water agency, to point of intended use.
- (2) Contractor shall use backflow preventers on water lines at point of connection to District's water supply. Backflow preventers shall comply with requirements of Uniform Plumbing Code.
- (3) Contractor shall make potable water available for human consumption.

D. Sanitary Facilities:

- (1) Contractor shall provide sanitary temporary facilities in no fewer numbers than required by law and such additional facilities as may be directed by the Inspector for the use of all workers. The facilities shall be maintained in a sanitary condition at all times and shall be left at the Site until removal is directed by the Inspector or Contractor completes all other work at the Site.
- (2) Use of toilet facilities in the Work under construction shall not be permitted except by consent of the Inspector and the District.

E. Telephone Service:

- (1) Contractor shall arrange with local telephone service company for telephone service as required for the performance of the Work. Contractor shall, at a minimum, provide in its field office one line for telephone and one line for fax machine.
- (2) Contractor shall pay the costs for telephone and fax lines installation, maintenance, service, and removal.

F. Fire Protection:

- (1) Contractor shall provide and maintain fire extinguishers and other equipment for fire protection. Such equipment shall be designated for use for fire protection only and shall comply with all requirements of the California Fire, State Fire Marshall and/or its designee.
- (2) Where on-site welding and burning of steel is unavoidable, Contractor shall provide protection for adjacent surfaces.

G. Trash Removal:

- (1) Contractor shall provide trash removal on a timely basis. Under no circumstance shall Contractor use District trash service.

H. Temporary Facilities/Laydown Area:

- (1) District will work with contractor on establishing laydown and parking area during time of work.

36.03 CONSTRUCTION AIDS:

A. Plant and Equipment:

- (1) Contractor shall furnish, operate, and maintain a complete plant for fabricating, handling, conveying, installing, and erecting materials and equipment; and for conveyances for transporting workers. Include elevators, hoists, debris chutes, and other equipment, tools, and appliances necessary for performance of the Work.
- (2) Contractor shall maintain plant and equipment in safe and efficient operating condition. Damages due to defective plant and equipment, and uses made thereof, shall be repaired by Contractor at no expense to the District.

B. None of the District's tools and equipment shall be used by Contractor for the performance of the Work.

36.04 BARRIERS AND ENCLOSURES:

- A. Contractor shall obtain the District's written permission for locations and types of temporary barriers and enclosures, including fire-rated materials proposed for use, prior to their installation.
- B. Contractor shall provide and maintain temporary enclosures to prevent public entry and to protect persons using other buildings and portions of the Site and/or Premises, the public, and workers. Contractor shall also protect the Work and existing facilities from the elements, and adjacent construction and improvements, persons, and trees and plants from damage and injury from demolition and construction operations.

- C. Contractor shall provide site access to existing facilities for persons using other buildings and portions of the Site, the public, and for deliveries and other services and activities.
- D. Tree and Plant Protection:
 - (1) Contractor shall preserve and protect existing trees and plants on the Premises that are not designated or required to be removed, and those adjacent to the Premises.
 - (2) Contractor shall provide barriers to a minimum height of 4'-0" around drip line of each tree and plant, around each group of trees and plants, as applicable, in the proximity of demolition and construction operations, or as denoted on the Plans.
 - (3) Contractor shall not park trucks, store materials, perform Work or cross over landscaped areas. Contractor shall not dispose of paint thinners, water from cleaning, plastering or concrete operations, or other deleterious materials in landscaped areas, storm drain systems, or sewers. Plant materials damaged as a result of the performance of the Work shall, at the option of the District and at Contractor's expense, either be replaced with new plant materials equal in size to those damaged or by payment of an amount representing the value of the damaged materials as determined by the District.
 - (4) Contractor shall remove soil that has been contaminated during the performance of the Work by oil, solvents, and other materials which could be harmful to trees and plants, and replace with good soil, at Contractor's expense.
 - (5) Excavation around Trees:
 - (a) Excavation within drip lines of trees shall be done only where absolutely necessary and with written permission from the District.
 - (b) Where trenching for utilities is required within drip lines, tunneling under and around roots shall be by hand digging and shall be approved by the District. Main lateral roots and taproots shall not be cut. All roots 2 inches in diameter and larger shall be tunneled under and heavily wrapped with wet burlap so as to prevent scarring or excessive drying. Smaller roots that interfere with installation of new work may be cut with prior approval by the District. Roots must first be cut with a Vermeer, or equivalent, root cutter prior to any trenching.
 - (c) Where excavation for new construction is required within drip line of trees, hand excavation shall be employed to minimize damage to root system. Roots shall be relocated in backfill areas wherever possible. If encountered immediately adjacent to location of new construction, roots shall be cut approximately 6 inches back from new construction.

- (d) Approved excavations shall be carefully backfilled with the excavated materials approved for backfilling. Backfill shall conform to adjacent grades without dips, sunken areas, humps, or other surface irregularities. Do not use mechanical equipment to compact backfill. Tamp carefully using hand tools, refilling and tamping until Final Acceptance as necessary to offset settlement.
- (e) Exposed roots shall not be allowed to dry out before permanent backfill is placed. Temporary earth cover shall be provided, or roots shall be wrapped with four layers of wet, untreated burlap and temporarily supported and protected from damage until permanently relocated and covered with backfill.
- (f) Accidentally broken roots should be sawed cleanly 3 inches behind ragged end.

36.05 SECURITY:

The Contractor shall be responsible for project security for materials, tools, equipment, supplies, and completed and partially completed Work.

36.06 TEMPORARY CONTROLS:

A. Noise Control:

- (1) Contractor acknowledges that adjacent facilities may remain in operation during all or a portion of the Work period, and it shall take all reasonable precautions to minimize noise as required by applicable laws and the Contract Documents.
- (2) Notice of proposed noisy operations, including without limitation, operation of pneumatic demolition tools, concrete saws, and other equipment, shall be submitted to the District a minimum of forty-eight (48) hours in advance of their performance.

B. Noise and Vibration:

- (1) Equipment and impact tools shall have intake and exhaust mufflers.
- (2) Contractor shall cooperate with District to minimize and/or cease the use of noisy and vibratory equipment if that equipment becomes objectionable by its longevity.

C. Dust and Dirt:

- (1) Contractor shall conduct demolition and construction operations to minimize the generation of dust and dirt, and prevent dust and dirt from interfering with the progress of the Work and from accumulating in the Work and adjacent areas including, without limitation, occupied facilities.

- (2) Contractor shall periodically water exterior demolition and construction areas to minimize the generation of dust and dirt.
- (3) Contractor shall ensure that all hauling equipment and trucks carrying loads of soil and debris shall have their loads sprayed with water or covered with tarpaulins, and as otherwise required by local and state ordinance.
- (4) Contractor shall prevent dust and dirt from accumulating on walks, roadways, parking areas, and planting, and from washing into sewer and storm drain lines.

D. Water:

- (1) Contractor shall not permit surface and subsurface water, and other liquids, to accumulate in or about the vicinity of the Premises. Should accumulation develop, Contractor shall control the water or other liquid, and suitably dispose of it by means of temporary pumps, piping, drainage lines, troughs, ditches, dams, or other methods.

E. Pollution:

- (1) No burning of refuse, debris, or other materials shall be permitted on or in the vicinity of the Premises.
- (2) Contractor shall comply with applicable regulatory requirements and anti-pollution ordinances during the conduct of the Work including, without limitation, demolition, construction, and disposal operations.

F. Lighting:

- (1) If portable lights are used after dark, all light must be located so as not to direct light into neighboring property.

36.07 JOB SIGN(S):

A. General:

- (1) Contractor shall provide and maintain a Project identification sign with the design, text, and colors designated by the District and/or the Design Professional; locate sign as approved by the District.
- (2) Signs other than the specified Project sign and or signs required by law, for safety, or for egress, shall not be permitted, unless otherwise approved in advance by the District.

B. Materials:

- (1) Structure and Framing: Structurally sound, new or used wood or metal; wood shall be nominal 3/4-inch exterior grade plywood.
- (2) Sign Surface: Minimum 3/4-inch exterior grade plywood.

- (3) Rough Hardware: Galvanized.
 - (4) Paint: Exterior quality, of type and colors selected by the District and/or the Design Professional.
- C. Fabrication:
 - (1) Contractor shall fabricate to provide smooth, even surface for painting.
 - (2) Size: 4'-0" x 8'-0", unless otherwise indicated.
 - (3) Contractor shall paint exposed surfaces of supports, framing, and surface material with exterior grade paint: one coat of primer and one coat of finish paint.
 - (4) Text and Graphics: As indicated.

36.08 PUBLICITY RELEASES:

- A. Contractor shall not release any information, story, photograph, plan, or drawing relating information about the Project to anyone, including press and other public communications medium, including, without limitation, on website(s) without the written permission of the District.

PART 37 – PRODUCTS Not used.

PART 38 – EXECUTION Not used.

END OF DOCUMENT

CONSTRUCTION WASTE MANAGEMENT AND DISPOSAL

PART 39 - GENERAL

39.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions; and
- C. Temporary Facilities and Controls.

39.02 SECTION INCLUDES:

- A. Administrative and procedural requirements for the following:
 - (1) Salvaging non-hazardous construction waste.
 - (2) Recycling non-hazardous construction waste.
 - (3) Disposing of non-hazardous construction waste.

39.03 DEFINITIONS:

- A. Construction Waste: Building and site improvement materials and other solid waste resulting from construction, remodeling, renovation, or repair operations. Construction waste includes packaging.
- B. Demolition Waste: Building and site improvement materials resulting from demolition or selective demolition operations.
- C. Disposal: Removal off-site of demolition and construction waste and subsequent sale, recycling, reuse, or deposit in landfill or incinerator acceptable to authorities having jurisdiction.
- D. Recycle: Recovery of demolition or construction waste for subsequent processing in preparation for reuse.
- E. Salvage: Recovery of demolition or construction waste and subsequent sale or reuse in another facility.
- F. Salvage and Reuse: Recovery of demolition or construction waste and subsequent incorporation into the Work.

39.04 PERFORMANCE REQUIREMENTS:

- A. General: Develop waste management plan that results in end-of Project rates for salvage/recycling of sixty-five percent (65%) by weight (or by volume, but not a combination) of total waste generated by the Work.

39.05 SUBMITTALS:

- A. Waste Management Plan: Submit waste management plan within 30 days of date established for commencement of the Work.
- B. Waste Reduction Progress Reports: Concurrent with each Application for Payment, submit copies of report. Include the following information:
 - (1) Material category.
 - (2) Generation point of waste.
 - (3) Total quantity of waste in tons or cubic yards.
 - (4) Quantity of waste salvaged, both estimated and actual in tons or cubic yards.
 - (5) Quantity of waste recycled, both estimated and actual in tons or cubic yards.
 - (6) Total quantity of waste recovered (salvaged plus recycled) in tons or cubic yards.
 - (7) Total quantity of waste recovered (salvaged plus recycled) as a percentage of total waste.
- C. Waste Reduction Calculations: Before request for final payment, submit copies of calculated end-of-Project rates for salvage, recycling, and disposal as a percentage of total waste generated by the Work.
- D. Records of Donations: Indicate receipt and acceptance of salvageable waste donated to individuals and organizations. Indicate whether organization is tax exempt.
- E. Records of Sales: Indicate receipt and acceptance of salvageable waste sold to individuals and organizations. Indicate whether organization is tax exempt.
- F. Recycling and Processing Facility Records: Indicate receipt and acceptance of recyclable waste by recycling and processing facilities licensed to accept them. Include manifests, weight tickets, receipts, and invoices.
- G. Landfill and Incinerator Disposal Records: Indicate receipt and acceptance of waste by landfills and incinerator facilities licensed to accept them. Include manifests, weight tickets, receipts, and invoices.

- H. CHPS Submittal: CHPS letter template for Credit ME2.0 and ME2.1, signed by Contractor, tabulating total waste material, quantities diverted and means by which it is diverted, and statement that requirements for the credit have been met.
- I. Qualification Data: For Waste Management Coordinator.
- J. Statement of Refrigerant Recovery: Signed by refrigerant recovery technician responsible for recovering refrigerant, stating that all refrigerant that was present was recovered and that recovery was performed according to EPA regulations. Include name and address of technician and date refrigerant was recovered.
- K. Submittal procedures and quantities are specified in Document 01 33 00.

39.06 QUALITY ASSURANCE:

- A. Waste Management Coordinator Qualifications: LEED Accredited Professional by U.S. Green Building Council.
- B. Regulatory Requirements: Comply with hauling and disposal regulations of authorities having jurisdiction.
- C. Waste Management Conference: Conduct conference at Project site to comply with requirements. Review methods and procedures related to waste management including, but not limited to, the following:
 - (1) Review and discuss waste management plan including responsibilities of Waste Management Coordinator.
 - (2) Review requirements for documenting quantities of each type of waste and its disposition.
 - (3) Review and finalize procedures for materials separation and verify availability of containers and bins needed to avoid delays.
 - (4) Review procedures for periodic waste collection and transportation to recycling and disposal facilities.
 - (5) Review waste management requirements for each trade.

39.07 WASTE MANAGEMENT PLAN:

- A. General: Develop plan consisting of waste identification, waste reduction work plan, and cost/revenue analysis. Indicate quantities by weight or volume, but use same units of measurement throughout waste management plan.
- B. Waste Identification: Indicate anticipated types and quantities of site-clearing and construction waste generated by the Work. Include estimated quantities and assumptions for estimates.

- C. Waste Reduction Work Plan: List each type of waste and whether it will be salvaged, recycled, or disposed of in landfill or incinerator. Include points of waste generation, total quantity of each type of waste, quantity for each means of recovery, and handling and transportation procedures.
- (1) Salvaged Materials for Reuse: For materials that will be salvaged and reused in this Project, describe methods for preparing salvaged materials before incorporation into the Work.
 - (2) Salvaged Materials for Sale: For materials that will be sold to individuals and organizations, include list of their names, addresses, and telephone numbers.
 - (3) Salvaged Materials for Donation: For materials that will be donated to individuals and organizations, include list of their names, addresses, and telephone numbers.
 - (4) Recycled Materials: Include list of local receivers and processors and type of recycled materials each will accept. Include names, addresses, and telephone numbers.
 - (5) Disposed Materials: Indicate how and where materials will be disposed of. Include name, address, and telephone number of each landfill and incinerator facility.
 - (6) Handling and Transportation Procedures: Include method that will be used for separating recyclable waste including sizes of containers, container labeling, and designated location on Project site where materials separation will be located.

PART 40 - PRODUCTS Not Used.

PART 41 - EXECUTION

41.01 PLAN IMPLEMENTATION:

- A. General: Implement approved waste management plan. Provide handling, containers, storage, signage, transportation, and other items as required to implement waste management plan during the entire duration of the Contract.
- (1) Comply with Document 01 50 00 for operation, termination, and removal requirements.
- B. [Waste Management Coordinator: Engage a waste management coordinator to be responsible for implementing, monitoring, and reporting status of waste management work plan. Coordinator shall be present at Project site full time for duration of Project.]
- C. Training: Train workers, subcontractors, and suppliers on proper waste management procedures, as appropriate for the Work occurring at Project site.

- (1) Distribute waste management plan to everyone concerned within 3 days of submittal return.
 - (2) Distribute waste management plan to entities when they first begin work on site. Review plan procedures and locations established for salvage, recycling, and disposal.
- D. Site Access and Temporary Controls: Conduct waste management operations to ensure minimum interference with roads, streets, walks, walkways, and other adjacent occupied and used facilities.
- (1) Designate and label specific areas of Project site necessary for separating materials that are to be salvaged, recycled, reused, donated, and sold.
 - (2) Comply with Document 01 50 00 for controlling dust and dirt, environmental protection, and noise control.

41.02 RECYCLING CONSTRUCTION WASTE:

- A. General: Recycle paper and beverage containers used by on-site workers.
- B. Recycling Incentives: Revenues, savings, rebates, tax credits, and other incentives received for recycling waste materials shall accrue to the Contractor.
- C. Procedures: Separate recyclable waste from other waste materials, trash, and debris. Separate recyclable waste by type at Project site to the maximum extent practical.
- (1) Provide appropriately marked containers or bins for controlling recyclable waste until they are removed from Project Site. Include list of acceptable and unacceptable materials at each container and bin.
 - (a) Inspect containers and bins for contamination and remove contaminated materials if found.
 - (2) Stockpile processed materials on site without intermixing with other materials. Place, grade, and shape stockpiles to drain surface water. Cover to prevent windblown dust.
 - (3) Stockpile materials away from construction area. Do not store within drip line of remaining trees.
 - (4) Store components off the ground and protect from the weather.
 - (5) Remove recyclable waste off District property and transport to recycling receiver or processor.

- D. Packaging:
 - (1) Cardboard and Boxes: Break down packaging into flat sheets. Bundle and store in a dry location.
 - (2) Polystyrene Packaging: Separate and bag material.
 - (3) Pallets: As much as possible, require deliveries using pallets to remove pallets from Project Site. For pallets that remain on Site, break down pallets into component wood pieces and comply with requirements for recycling wood.
 - (4) Crates: Break down crates into component wood pieces and comply with requirements for recycling wood.
- E. Site-Clearing Wastes: Chip brush, branches, and trees on site.
- F. Wood Materials:
 - (1) Clean Cut-Offs of Lumber: Grind or chip into small pieces.
 - (2) Clean Sawdust: Bag sawdust that does not contain painted or treated wood.
- G. Gypsum Board: Stack large clean pieces on wood pallets and store in a dry location.
 - (1) Clean Gypsum Board: Grind scraps of clean gypsum board using small mobile chipper or hammer mill. Screen out paper after grinding.

41.03 DISPOSAL OF WASTE:

- A. General: Except for items or materials to be salvaged, recycled, or otherwise reused, remove waste materials from Project Site and legally dispose of them in a landfill or incinerator acceptable to authorities having jurisdiction.
 - (1) Except as otherwise specified, do not allow waste materials that are to be disposed of accumulate on site.
 - (2) Remove and transport debris in a manner that will prevent spillage on adjacent surfaces and areas.
- B. Burning: Do not burn waste materials.
- C. Disposal: Transport waste materials off District property and legally dispose of them.

END OF DOCUMENT

FIELD OFFICES

PART 42 – GENERAL

42.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions; and
- C. Temporary Facilities and Controls.

42.02 SECTION INCLUDES:

- A. Requirements for Field Offices and Field Office Trailers.

42.03 SUMMARY:

- A. General: Contractor shall provide District's Field Office Trailer and contents, for District's use exclusively, during the term of the Contract.
- B. Property: Trailer, furniture, furnishings, equipment, and the like, supplied by the Contractor with the Office Trailer shall remain the property of the Contractor; District property items installed, delivered, and the like by District within the Office Trailer will remain District's property.
- C. Modifications: District reserves the right to modify the trailer or contents, or both, as may be deemed proper by District.
- D. Condition: Trailer and contents shall be clean, neat, substantially finished, in good, proper, and safe condition for use, operation, and the like; the trailer and contents shall not be required to be new.
- E. Installation Timing: Provide safe, fully furnished, functional, proper, complete, and finished trailer properly ready for entire use, within fourteen (14) calendar days of District's notification of the issuance of Notice to Proceed.

42.04 SUBMITTALS:

- A. General: Submit submittals to District in quantity, format, type, and the like, as specified herein.
- B. Office Trailer Data: One (1) copy of manufacturer's descriptive data, technical descriptions, regulatory compliance, industry standards, installation, removal, and maintenance instructions.

- C. Equipment Data: Two (2) copies of manufacturer data for each type of equipment, if directed by District.
- D. Furniture and Furnishings Data: Two (2) copies of manufacturer data for each type of equipment, if directed by District.
- E. Plans: One (1) reproducible copy of appropriately scaled plans of trailer layout. Plans shall include, but not be limited to: lighting; furniture; equipment; telephone and electrical outlets; and the like.
- F. Product Samples: One (1) complete and entire unit of each type, if directed by District.

42.05 QUALITY ASSURANCE

- A. Standards: In the event that provisions of codes, regulations, safety orders, Contract Documents, referenced manufacturer's specifications, manufacturer's instructions, industry standards, and the like, are in conflict, the more restrictive and higher quality shall govern.
- B. Installer: Installer or Installers engaged by Contractor must have a minimum of five (5) years of documented and properly authenticated successful experience of specialization in the installation of the items or systems, or both, specified herein.
- C. Manufacturer: Contractor shall obtain products from nationally and industry recognized Manufacturer with five (5) years minimum, of immediately recent, continuous, documented and properly authenticated successful experience of specialization in the manufacture of the product specified herein.
- D. State Personnel Training: Provide proper training for maintenance and operations, including emergency procedures, and the like, as directed by District.
- E. Units: Shall be sound and free of defects, and shall not include any damage or defect that will impair the safety, installation, performance, or the durability of the entire Office Trailer and appurtenant systems.

42.06 REGULATORY REQUIREMENTS

- A. General: Work shall be executed in accordance with applicable Codes, Regulations, Statutes, Enactments, Rulings, Laws, each authority having jurisdiction, and including, but not limited to, Regulatory Requirements specified herein.
- B. California Building Standards Code ("CBSC").
- C. California Code of Regulations, Title 25, Chapter 3, Sub Chapter 2, Article 3 ("CCR").
- D. Coach Insignia: Trailer shall display California Commercial Coach Insignia; such insignia shall be deemed to show that the trailer is in accordance with the Construction and Fire Safety requirements of CCR.

42.07 UTILITY AND SERVICES

- A. Telephone Service: Contractor shall provide and interface the entire telephone service, and shall properly and timely pay for telephone service for District's non-long-distance use.
- B. Electrical Service: Provide all proper connections and continuously pay for service for the duration of the Work.

42.08 FINISHES

- A. General: Manufacturer standard finish system over surfaces properly cleaned, pretreated, and prepared to obtain proper bond; all visible surfaces shall be coated.
- B. Finish: Color as selected by District from manufacturer standard palette.

PART 43 – EXECUTION

43.01 INSTALLATION

- A. General: Properly prepare area and affected items to receive the Work. Set Work accurately in location, alignment, and elevation; rigidly, securely, and firmly anchor to appropriate structure; install plumb, straight, square, level, true, without racking, rigidly anchored to proper solid blocking, substrate, and the like; provide appropriate type and quantity of reinforcements, fasteners, adhesives, self-adhesive and other tapes; lubricants, coatings, accessories, and the like, as required for a complete, structurally rigid, stable, sound, and appropriately finished installation, in accordance with manufacturer's published instructions, and as indicated. The more restrictive and higher quality requirement shall govern. Moving parts shall be properly secured, without binding, looseness, noise, and the like.
- B. Installation: Install in accordance with 25 CCR 3.2.3 and as directed by District; jack up trailer and level both ways; mount on proper concrete piers with all load off wheels; provide required tie down and accessories per Section 4368 of referenced CCR, and as directed by District.
- C. Rejected Work: Work, materials, unit, items, systems, and the like, not accepted by District shall be deemed rejected, and shall forthwith be removed and replaced with proper and new Work, materials, unit, items, systems, and the like at no cost to District.
- D. Standard: Comply with manufacturer's published instructions, or with instructions as shown or indicated; the more restrictive and higher quality requirement shall govern.
- E. Location: As directed by District.
- F. Fire Resistance: Construct and install in accordance with UL requirements.
- G. Maintenance: Contractor shall maintain trailer and adjacent areas in a safe, clean and hygienic condition throughout the duration of the Work, and as

directed by District. Properly repair or replace furniture or other items, as directed by District. Properly remove unsafe, damaged, or broken furniture, or similar items, and replace with safe and proper items. Contractor shall pay cost of all services, repair, and maintenance, or replacement of each item.

- H. Janitorial Service: Provide professional janitorial services, including, but not limited to, trash, waste paper baskets, fill paper dispensers; clean and dust all furniture, files, and the like; sweep and mop resilient and similar flooring; and vacuum carpeting and similar flooring.

- (1) Frequency: Two (2) times per week, minimum.

- I. Removal: Properly remove the Office Trailer and contents from the Site upon completion of the Contract, or as directed by District in writing. Forthwith properly patch and repair affected areas; replace damaged items with new items. Carefully and properly inventory, clean, pack, store, and protect District property; submit District property to District at a date, time and location as directed by District.

END OF DOCUMENT

OWNER-FURNISHED PRODUCTS

PART 44 – GENERAL

44.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions;
- B. Special Conditions; and
- C. Materials and Equipment.

44.02 SECTION INCLUDES

- A. Requirements for the following:
 - (1) Installing Owner-furnished materials and equipment.
 - (2) Providing necessary utilities, connections and rough-ins.

44.03 DEFINITIONS

- A. Owner: District, who is providing/furnishing materials and equipment.
- B. Installing Contactor: Contractor, who is installing the materials and equipment furnished by the Owner.

44.04 PRODUCT DELIVERY, STORAGE, AND HANDLING

- A. Receive, store and handle products in accordance with the manufacturer's instructions.
- B. Protect equipment items as required to prevent damage during storage and construction.

PART 45 – PRODUCTS

45.01 GENERAL PRODUCT REQUIREMENTS

- A. Installing Contractor's Responsibilities:
 - (1) Verify mounting and utility requirements for Owner-furnished materials and equipment items.
 - (2) Provide mounting and utility rough in for all items where required.

- (a) Rough in locations, sizes, capacities, and similar type items shall be as indicated and required by product manufacturer.

B. Owner and Installing Contractor(s) Responsibilities:

- (1) Owner-Furnished/Contractor Installed ("OFCI"): Furnished by the Owner; installed by the Installing Contractor.
 - (a) General: Owner and Installing Contractor(s) will coordinate deliveries of materials and equipment to coincide with the construction schedule.
 - (b) Owner will furnish specified materials and equipment delivered to the site. Owner/vendor's representative shall be present on Site at the time of delivery to comply with the contract requirements and Specifications Section 01 43 00, Materials and Equipment, Article 1.04.
 - (c) The Owner furnishing specified materials and equipment is responsible to provide manufacturer guarantees as required by the Contract to the Installing Contractor.
 - (d) The Installing Contractor shall:
 - 1) Review, verify and accept the approved manufacturer's submittal/Shop Drawings for all materials and equipment required to be installed by the Installer Contractor and furnished by the Owner. Any discrepancies, including but not limited to possible space conflicts, should be brought to the attention of the Project Manager and/or Program Manager, if applicable.
 - 2) Coordinate timely delivery. Installing Contractor shall receive materials and equipment at Site when delivered and give written receipt at time of delivery, noting visible defects or omissions; if such declaration is not given, the Installing Contractor shall assume responsibility for such defects and omissions.
 - 3) Store materials and equipment until ready for installation and protect from loss and damage. Installing Contractor is responsible for providing adequate storage space.
 - 4) Coordinate with other bid package contractors and field measurement to ensure complete installation.
 - 5) Uncrate, assemble, and set in place.
 - 6) Provide adequate supports.
 - 7) Install materials and equipment in accordance with manufacturer's recommendations, instructions, and

Shop Drawings, supply labor and material required, and make mechanical, plumbing, and electrical connections required to operate equipment.

- 8) Be certified by equipment manufacturer for installation of the specific equipment supplied by the Owner.
- 9) Provide anchorage and/or bracing as required for seismic restraint per Title 24, UBC Standard 27-11 and all other applicable codes.
- 10) Provide the contract-required warranty and guarantee for all work, materials and equipment, and installation upon its completion and acceptance by the District. Guarantee includes all costs associated with the removal, shipping to and from the Site, and re-installation of any equipment found to be defective.

C. Compatibility with Space and Service Requirements:

- (1) Equipment items shall be compatible with space limitations indicated and as shown on the Contract Documents and specified in other sections of the Specifications.
- (2) Modifications to equipment items required to conform to space limitations specified for rough in shall not cause additional cost to the District.

D. Manufacturer's printed descriptions, specifications, and instructions shall govern the Work unless specifically indicated or specified otherwise.

45.02 FURNISHED MATERIALS AND EQUIPMENT

- A. All furnished materials and equipment are indicated or scheduled on the Contract Documents.

PART 46 – EXECUTION

46.01 INSTALLATION

- A. Install equipment items in accordance with the manufacturer's instructions.
- B. Set equipment items securely in place, rigidly or flexibly mounted in accordance with manufacturers' directions.
- C. Make electrical and mechanical connections as indicated and required.
- D. Touch-up and restore damaged or defaced finishes to the Owner's satisfaction.

46.02 CLEANING AND PROTECTION

- A. Repair or replace items not acceptable to the Architect or Owner.

- B. Upon completion of installation, clean equipment items in accordance with manufacturer's recommendations, and protect from damage until final acceptance of the Work by the Owner.

END OF DOCUMENT

PRODUCT DELIVERY, STORAGE AND HANDLING

PART 47 - GENERAL

47.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Site Access, Conditions and Requirements;
- B. Special Conditions.

47.02 PRODUCTS

- A. Products are as defined in the General Conditions.
- B. Contractor shall not use and/or reuse materials and/or equipment removed from existing Premises, except as specifically permitted by the Contract Documents.
- C. Contractor shall provide interchangeable components of the same manufacturer, for similar components.

47.03 TRANSPORTATION AND HANDLING

- A. Contractor shall transport and handle Products in accordance with manufacturer's instructions.
- B. Contractor shall promptly inspect shipments to confirm that Products comply with requirements, quantities are correct, and products are undamaged.
- C. Contractor shall provide equipment and personnel to handle Products by methods to prevent soiling, disfigurement, or damage.

47.04 STORAGE AND PROTECTION

- A. Contractor shall store and protect Products in accordance with manufacturer's instructions, with seals and labels intact and legible. Contractor shall store sensitive products in weather-tight, climate controlled enclosures.
- B. For exterior storage of fabricated Products, Contractor shall place on sloped supports, above ground.
- C. Contractor shall provide off-site storage and protection when Site does not permit on-site storage or protection.

- D. Contractor shall cover products subject to deterioration with impervious sheet covering and provide ventilation to avoid condensation.
- E. Contractor shall store loose granular materials on solid flat surfaces in a well-drained area and prevent mixing with foreign matter.
- F. Contractor shall provide equipment and personnel to store Products by methods to prevent soiling, disfigurement, or damage.
- G. Contractor shall arrange storage of Products to permit access for inspection and periodically inspect to assure Products are undamaged and are maintained under specified conditions.

PART 48 – PRODUCTS Not Used.

PART 49 - EXECUTION Not Used.

END OF DOCUMENT

FIELD ENGINEERING

PART 50 - GENERAL

50.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Site Investigation, and Soils Investigation Report;
- B. Special Conditions;
- C. Site-Visit Certification.

50.02 REQUIREMENTS INCLUDED:

- A. Contractor shall provide and pay for field engineering services by a California-registered engineer, required for the project, including, without limitations:
 - (1) Survey work required in execution of the Project.
 - (2) Civil or other professional engineering services specified, or required to execute Contractor's construction methods.

50.03 QUALIFICATIONS OF SURVEYOR OR ENGINEERS:

Contractor shall only use a qualified licensed engineer or registered land surveyor, to whom District makes no objection.

50.04 SURVEY REFERENCE POINTS:

- A. Existing basic horizontal and vertical control points for the Project are those designated on the Drawings.
- B. Contractor shall locate and protect control points prior to starting Site Work and preserve all permanent reference points during construction. In addition Contractor shall:
 - (1) Make no changes or relocation without prior written notice to District and Architect.
 - (2) Report to District and Architect when any reference point is lost or destroyed, or requires relocation because of necessary changes in grades or locations.

- (3) Require surveyor to replace Project control points based on original survey control that may be lost or destroyed.

50.05 RECORDS:

Contractor shall maintain a complete, accurate log of all control and survey work as it progresses.

50.06 SUBMITTALS:

- A. Contractor shall submit name and address of Surveyor and Professional Engineer to District and Architect prior to its/their work on the Project.
- B. On request of District and Architect, Contractor shall submit documentation to verify accuracy of field engineering work, at no additional cost to the District.
- C. Contractor shall submit a certificate signed by registered engineer or surveyor certifying that elevations and locations of improvements are in conformance or nonconformance with Contract Documents.

PART 51 – PRODUCTS Not Used.

PART 52 - EXECUTION

52.01 COMPLIANCE WITH LAWS:

Contractor is responsible for meeting all applicable codes, OSHA, safety and shoring requirements.

52.02 NONCONFORMING WORK:

Contractor is responsible for any re-surveying required by correction of nonconforming work.

END OF DOCUMENT

FIELD ENGINEERING

PART 53 - GENERAL

53.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Site Investigation, and Soils Investigation Report;
- B. Special Conditions;
- C. Site-Visit Certification.

53.02 REQUIREMENTS INCLUDED:

- A. Contractor shall provide and pay for field engineering services by a California-registered engineer, required for the project, including, without limitations:
 - (1) Survey work required in execution of the Project.
 - (2) Civil or other professional engineering services specified, or required to execute Contractor's construction methods.

53.03 QUALIFICATIONS OF SURVEYOR OR ENGINEERS:

Contractor shall only use a qualified licensed engineer or registered land surveyor, to whom District makes no objection.

53.04 SURVEY REFERENCE POINTS:

- A. Existing basic horizontal and vertical control points for the Project are those designated on the Drawings.
- B. Contractor shall locate and protect control points prior to starting Site Work and preserve all permanent reference points during construction. In addition Contractor shall:
 - (1) Make no changes or relocation without prior written notice to District and Architect.
 - (2) Report to District and Architect when any reference point is lost or destroyed, or requires relocation because of necessary changes in grades or locations.

- (3) Require surveyor to replace Project control points based on original survey control that may be lost or destroyed.

53.05 RECORDS:

Contractor shall maintain a complete, accurate log of all control and survey work as it progresses.

53.06 SUBMITTALS:

- A. Contractor shall submit name and address of Surveyor and Professional Engineer to District and Architect prior to its/their work on the Project.
- B. On request of District and Architect, Contractor shall submit documentation to verify accuracy of field engineering work, at no additional cost to the District.
- C. Contractor shall submit a certificate signed by registered engineer or surveyor certifying that elevations and locations of improvements are in conformance or nonconformance with Contract Documents.

PART 54 – PRODUCTS Not Used.

PART 55 - EXECUTION

55.01 COMPLIANCE WITH LAWS:

Contractor is responsible for meeting all applicable codes, OSHA, safety and shoring requirements.

55.02 NONCONFORMING WORK:

Contractor is responsible for any re-surveying required by correction of nonconforming work.

END OF DOCUMENT

CUTTING AND PATCHING

PART 56 – GENERAL

56.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Inspector, Inspections, and Tests, Integration of Work, Nonconforming Work, and Correction of Work, and Uncovering Work;
- B. Special Conditions;
- C. Hazardous Materials Procedures and Requirements;
- D. Hazardous Materials Certification;
- E. Lead-Based Paint Certification;
- F. Imported Materials Certification.

56.02 CUTTING AND PATCHING:

- A. Contractor shall be responsible for all cutting, fitting, and patching, including associated excavation and backfill, required to complete the Work or to:
 - (1) Make several parts fit together properly.
 - (2) Uncover portions of Work to provide for installation of ill-timed Work.
 - (3) Remove and replace defective Work.
 - (4) Remove and replace Work not conforming to requirements of Contract Documents.
 - (5) Remove Samples of installed Work as specified for testing.
 - (6) Provide routine penetrations of non-structural surfaces for installation of piping and electrical conduit.
 - (7) Attaching new materials to existing remodeling areas – including painting (or other finishes) to match existing conditions.
- B. In addition to Contract requirements, upon written instructions from the District, Contractor shall uncover Work to provide for observations of covered Work in accordance with the Contract Documents; remove samples of installed materials for testing as directed by District; and remove Work to provide for alteration of existing Work.

- C. Contractor shall not cut or alter Work, or any part of it, in such a way that endangers or compromises the integrity of the Work, the Project, or work of others.

56.03 SUBMITTALS:

- A. Prior to any cutting or alterations that may affect the structural safety of Project, or work of others, and well in advance of executing such cutting or alterations, Contractor shall submit written notice to District pursuant to the applicable notice provisions of the Contract Documents, requesting consent to proceed with the cutting or alteration, including the following:
 - (1) The work of the District or other trades.
 - (2) Structural value or integrity of any element of Project.
 - (3) Integrity or effectiveness of weather-exposed or weather-resistant elements or systems.
 - (4) Efficiency, operational life, maintenance or safety of operational elements.
 - (5) Visual qualities of sight-exposed elements.
- B. Contractor's Request shall also include:
 - (1) Identification of Project.
 - (2) Description of affected Work.
 - (3) Necessity for cutting, alteration, or excavations.
 - (4) Effects of Work on District, other trades, or structural or weatherproof integrity of Project.
 - (5) Description of proposed Work:
 - (a) Scope of cutting, patching, alteration, or excavation.
 - (b) Trades that will execute Work.
 - (c) Products proposed to be used.
 - (d) Extent of refinishing to be done.
 - (6) Alternates to cutting and patching.
 - (7) Cost proposal, when applicable.
 - (8) The scheduled date the Contractor intends to perform the Work and the duration of time to complete the Work.

- (9) Written permission of District or other District contractor(s) whose work will be affected.

56.04 QUALITY ASSURANCE:

- A. Contractor shall ensure that cutting, fitting, and patching shall achieve security, strength, weather protection, appearance for aesthetic match, efficiency, operational life, maintenance, safety of operational elements, and the continuity of existing fire ratings.
- B. Contractor shall ensure that cutting, fitting, and patching shall successfully duplicate undisturbed adjacent profiles, materials, textures, finishes, colors, and that materials shall match existing construction. Where there is dispute as to whether duplication is successful or has been achieved to a reasonable degree, the District's decision shall be final.

56.05 PAYMENT FOR COSTS:

- A. Cost caused by ill-timed or defective Work or Work not conforming to Contract Documents, including costs for additional services of the District, its consultants, including but not limited to the Construction Manager, the Architect, the Project Inspector(s), Engineers, and Agents, will be paid by Contractor and/or deducted from the Contract by the District.
- B. District shall only pay for cost of Work if it is part of the original Contract Price or if a change has been made to the contract in compliance with the provisions of the General Conditions. Cost of Work performed upon instructions from the District, other than defective or nonconforming Work, will be paid by District on approval of written Change Order. Contractor shall provide written cost proposals prior to proceeding with cutting and patching.

PART 57 - PRODUCTS

57.01 MATERIALS:

- A. Contractor shall provide for replacement and restoration of Work removed. Contractor shall comply with the Contract Documents and with the Industry Standard(s), for the type of Work, and the Specification requirements for each specific product involved. If not specified, Contractor shall first recommend a product of a manufacturer or appropriate trade association for approval by the District.
- B. Materials to be cut and patched include those damaged by the performance of the Work.

PART 58 – EXECUTION

58.01 INSPECTION:

- A. Contractor shall inspect existing conditions of the Site and the Work, including elements subject to movement or damage during cutting and patching, excavating and backfilling. After uncovering Work, Contractor shall inspect conditions affecting installation of new products.

- B. Contractor shall report unsatisfactory or questionable conditions in writing to District as indicated in the General Conditions and shall proceed with Work as indicated in the General Conditions by District.

58.02 PREPARATION:

- A. Contractor shall provide shoring, bracing and supports as required to maintain structural integrity for all portions of the Project, including all requirements of the Project.
- B. Contractor shall provide devices and methods to protect other portions of Project from damage.
- C. Contractor shall, provide all necessary protection from weather and extremes of temperature and humidity for the Project, including without limitation, any work that may be exposed by cutting and patching Work. Contractor shall keep excavations free from water.

58.03 ERECTION, INSTALLATION AND APPLICATION:

- A. With respect to performance, Contractor shall:
 - (1) Execute fitting and adjustment of products to provide finished installation to comply with and match specified tolerances and finishes.
 - (2) Execute cutting and demolition by methods that will prevent damage to other Work, and provide proper surfaces to receive installation of repairs and new Work.
 - (3) Execute cutting, demolition excavating, and backfilling by methods that will prevent damage to other Work and damage from settlement.
- B. Contractor shall employ original installer or fabricator to perform cutting and patching for:
 - (1) Weather-exposed surfaces and moisture-resistant elements such as roofing, sheet metal, sealants, waterproofing, and other trades.
 - (2) Sight-exposed finished surfaces.
- C. Contractor shall execute fitting and adjustment of products to provide a finished installation to comply with specified products, functions, tolerances, and finishes as shown or specified in the Contract Documents including, without limitation, the Drawings and Specifications.
- D. Contractor shall fit Work airtight to pipes, sleeves, ducts, conduit, and other penetrations through surfaces. Contractor shall conform to all Code requirements for penetrations or the Drawings and Specifications, whichever calls for a higher quality or more thorough requirement. Contractor shall maintain integrity of both rated and non-rated fire walls, ceilings, floors, etc.
- E. Contractor shall restore Work which has been cut or removed. Contractor shall install new products to provide completed Work in accordance with

requirements of the Contract Documents and as required to match surrounding areas and surfaces.

- F. Contractor shall refinish all continuous surfaces to nearest intersection as necessary to match the existing finish to any new finish.

END OF DOCUMENT

CUTTING AND PATCHING

PART 59 – GENERAL

59.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Inspector, Inspections, and Tests, Integration of Work, Nonconforming Work, and Correction of Work, and Uncovering Work;
- B. Special Conditions;
- C. Hazardous Materials Procedures and Requirements;
- D. Hazardous Materials Certification;
- E. Lead-Based Paint Certification;
- F. Imported Materials Certification.

59.02 CUTTING AND PATCHING:

- A. Contractor shall be responsible for all cutting, fitting, and patching, including associated excavation and backfill, required to complete the Work or to:
 - (1) Make several parts fit together properly.
 - (2) Uncover portions of Work to provide for installation of ill-timed Work.
 - (3) Remove and replace defective Work.
 - (4) Remove and replace Work not conforming to requirements of Contract Documents.
 - (5) Remove Samples of installed Work as specified for testing.
 - (6) Provide routine penetrations of non-structural surfaces for installation of piping and electrical conduit.
 - (7) Attaching new materials to existing remodeling areas – including painting (or other finishes) to match existing conditions.
- B. In addition to Contract requirements, upon written instructions from the District, Contractor shall uncover Work to provide for observations of covered Work in accordance with the Contract Documents; remove samples of

installed materials for testing as directed by District; and remove Work to provide for alteration of existing Work.

- C. Contractor shall not cut or alter Work, or any part of it, in such a way that endangers or compromises the integrity of the Work, the Project, or work of others.

59.03 SUBMITTALS:

- A. Prior to any cutting or alterations that may affect the structural safety of Project, or work of others, and well in advance of executing such cutting or alterations, Contractor shall submit written notice to District pursuant to the applicable notice provisions of the Contract Documents, requesting consent to proceed with the cutting or alteration, including the following:
 - (1) The work of the District or other trades.
 - (2) Structural value or integrity of any element of Project.
 - (3) Integrity or effectiveness of weather-exposed or weather-resistant elements or systems.
 - (4) Efficiency, operational life, maintenance or safety of operational elements.
 - (5) Visual qualities of sight-exposed elements.
- B. Contractor's Request shall also include:
 - (1) Identification of Project.
 - (2) Description of affected Work.
 - (3) Necessity for cutting, alteration, or excavations.
 - (4) Effects of Work on District, other trades, or structural or weatherproof integrity of Project.
 - (5) Description of proposed Work:
 - (a) Scope of cutting, patching, alteration, or excavation.
 - (b) Trades that will execute Work.
 - (c) Products proposed to be used.
 - (d) Extent of refinishing to be done.
 - (6) Alternates to cutting and patching.
 - (7) Cost proposal, when applicable.

- (8) The scheduled date the Contractor intends to perform the Work and the duration of time to complete the Work.
- (9) Written permission of District or other District contractor(s) whose work will be affected.

59.04 QUALITY ASSURANCE:

- A. Contractor shall ensure that cutting, fitting, and patching shall achieve security, strength, weather protection, appearance for aesthetic match, efficiency, operational life, maintenance, safety of operational elements, and the continuity of existing fire ratings.
- B. Contractor shall ensure that cutting, fitting, and patching shall successfully duplicate undisturbed adjacent profiles, materials, textures, finishes, colors, and that materials shall match existing construction. Where there is dispute as to whether duplication is successful or has been achieved to a reasonable degree, the District's decision shall be final.

59.05 PAYMENT FOR COSTS:

- A. Cost caused by ill-timed or defective Work or Work not conforming to Contract Documents, including costs for additional services of the District, its consultants, including but not limited to the Construction Manager, the Architect, the Project Inspector(s), Engineers, and Agents, will be paid by Contractor and/or deducted from the Contract by the District.
- B. District shall only pay for cost of Work if it is part of the original Contract Price or if a change has been made to the contract in compliance with the provisions of the General Conditions. Cost of Work performed upon instructions from the District, other than defective or nonconforming Work, will be paid by District on approval of written Change Order. Contractor shall provide written cost proposals prior to proceeding with cutting and patching.

PART 60 - PRODUCTS

60.01 MATERIALS:

- A. Contractor shall provide for replacement and restoration of Work removed. Contractor shall comply with the Contract Documents and with the Industry Standard(s), for the type of Work, and the Specification requirements for each specific product involved. If not specified, Contractor shall first recommend a product of a manufacturer or appropriate trade association for approval by the District.
- B. Materials to be cut and patched include those damaged by the performance of the Work.

PART 61 – EXECUTION

61.01 INSPECTION:

- A. Contractor shall inspect existing conditions of the Site and the Work, including elements subject to movement or damage during cutting and patching, excavating and backfilling. After uncovering Work, Contractor shall inspect conditions affecting installation of new products.
- B. Contractor shall report unsatisfactory or questionable conditions in writing to District as indicated in the General Conditions and shall proceed with Work as indicated in the General Conditions by District.

61.02 PREPARATION:

- A. Contractor shall provide shoring, bracing and supports as required to maintain structural integrity for all portions of the Project, including all requirements of the Project.
- B. Contractor shall provide devices and methods to protect other portions of Project from damage.
- C. Contractor shall, provide all necessary protection from weather and extremes of temperature and humidity for the Project, including without limitation, any work that may be exposed by cutting and patching Work. Contractor shall keep excavations free from water.

61.03 ERECTION, INSTALLATION AND APPLICATION:

- A. With respect to performance, Contractor shall:
 - (1) Execute fitting and adjustment of products to provide finished installation to comply with and match specified tolerances and finishes.
 - (2) Execute cutting and demolition by methods that will prevent damage to other Work, and provide proper surfaces to receive installation of repairs and new Work.
 - (3) Execute cutting, demolition excavating, and backfilling by methods that will prevent damage to other Work and damage from settlement.
- B. Contractor shall employ original installer or fabricator to perform cutting and patching for:
 - (1) Weather-exposed surfaces and moisture-resistant elements such as roofing, sheet metal, sealants, waterproofing, and other trades.
 - (2) Sight-exposed finished surfaces.
- C. Contractor shall execute fitting and adjustment of products to provide a finished installation to comply with specified products, functions, tolerances, and finishes as shown or specified in the Contract Documents including, without limitation, the Drawings and Specifications.

- D. Contractor shall fit Work airtight to pipes, sleeves, ducts, conduit, and other penetrations through surfaces. Contractor shall conform to all Code requirements for penetrations or the Drawings and Specifications, whichever calls for a higher quality or more thorough requirement. Contractor shall maintain integrity of both rated and non-rated fire walls, ceilings, floors, etc.
- E. Contractor shall restore Work which has been cut or removed. Contractor shall install new products to provide completed Work in accordance with requirements of the Contract Documents and as required to match surrounding areas and surfaces.
- F. Contractor shall refinish all continuous surfaces to nearest intersection as necessary to match the existing finish to any new finish.

END OF DOCUMENT

ALTERATION PROJECT PROCEDURES

PART 62 – GENERAL

62.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Integration of Work, Purchase of Materials and Equipment, Uncovering of Work and Non-conforming Work and Correction of Work and Trenches;
- B. Special Conditions.

PART 63 - PRODUCTS

63.01 PRODUCTS FOR PATCHING AND EXTENDING WORK:

- A. New Materials: As specified in the Contract Documents including, without limitation, in the Specifications, Contractor shall match existing products, conditions, and work for patching and extending work.
- B. Type and Quality of Existing Products: Contractor shall determine by inspection, by testing products where necessary, by referring to existing conditions and to the Work as a standard.

PART 64 - EXECUTION

64.01 EXAMINATION:

- A. Contractor shall verify that demolition is complete and that areas are ready for installation of new Work.
- B. By beginning restoration Work, Contractor acknowledges and accepts the existing conditions.

64.02 PREPARATION:

- A. Contractor shall cut, move, or remove items as necessary for access to alterations and renovation Work. Contractor shall replace and restore these at completion.
- B. Contractor shall remove unsuitable material not as salvage unless otherwise indicated in the Contract Documents. Unsuitable material may include, without limitation, rotted wood, corroded metals, and deteriorated masonry and concrete. Contractor shall replace materials as specified for finished Work.

- C. Contractor shall remove debris and abandoned items from all areas of the Site and from concealed spaces.
- D. Contractor shall prepare surface and remove surface finishes to provide for proper installation of new Work and finishes.
- E. Contractor shall close openings in exterior surfaces to protect existing work from weather and extremes of temperature and humidity. Contractor shall insulate ductwork and piping to prevent condensation in exposed areas. Contractor shall insulate building cavities for thermal and/or acoustical protection, as detailed.

64.03 INSTALLATION:

- A. Contractor shall coordinate Work of all alternations and renovations to expedite completion and to accommodate District occupancy.
- B. Designated Areas and Finishes: Contractor shall complete all installations in all respects, including operational, mechanical work and electrical work.
- C. Contractor shall remove, cut, and patch Work in a manner to minimize damage and to provide a means of restoring Products and finishes to original or specified condition.
- D. Contractor shall refinish visible existing surfaces to remain in renovated rooms and spaces, to specified condition for each material, with a neat and square or straight transition to adjacent finishes.
- E. Contractor shall install products as specified in the Contract Documents, including without limitation, the Specifications.

64.04 TRANSITIONS:

- A. Where new Work abuts or aligns with existing, Contractor shall perform a smooth and even transition. Patched Work must match existing adjacent work in texture and appearance.
- B. When finished surfaces are cut so that a smooth transition with new Work is not possible, Contractor shall terminate existing surface along a straight line at a natural line of division and make a recommendation for resolution to the District and the Architect for review and approval.

64.05 ADJUSTMENTS:

- A. Where removal of partitions or walls results in adjacent spaces becoming one, Contractor shall rework floors, walls, and ceilings to a smooth plane without breaks, steps, or bulkheads.
- B. Where a change of plane of 1/4 inch or more occurs, Contractor shall submit a recommendation for providing a smooth transition to the District and the Architect for review and approval.

- C. Contractor shall trim and seal existing wood doors and shall trim and paint metal doors as necessary to clear new floor finish and refinish trim as required.
- D. Contractor shall fit Work at penetrations of surfaces.

64.06 REPAIR OF DAMAGED SURFACES:

- A. Contractor shall patch or replace portions of existing surfaces, which are damaged, lifted, discolored, or showing other imperfections, in the area where the Work is performed.
- B. Contractor shall repair substrate prior to patching finish.

64.07 CULTIVATED AREAS AND OTHER SURFACE IMPROVEMENTS:

- A. Cultivated or planted areas and other surface improvements which are damaged by actions of the Contractor shall be restored by Contractor to their original condition or better, where indicated.
- B. Contractor shall protect and replace, if damaged, all existing guard posts, barricades, and fences.
- C. Contractor shall give special attention to avoid damaging or killing trees, bushes and/or shrubs on the Premises and/or identified in the Contract Documents, including without limitation, the Drawings.

64.08 FINISHES:

- A. Contractor shall finish surfaces as specified in the Contract Documents, including without limitations, the provisions of all Divisions of the Specifications.
- B. Contractor shall finish patches to produce uniform finish and texture over entire area. When finish cannot be matched, Contractor shall refinish entire surface to nearest intersections.

64.09 CLEANING:

- A. Contractor shall continually clean the Site and the Premises as indicated in the Contract Documents, including without limitation, the provisions in the General Conditions and the Specifications regarding cleaning.

END OF DOCUMENT

CONTRACT CLOSEOUT AND FINAL CLEANING

PART 65 - GENERAL

65.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Completion of Work;
- B. Special Conditions;
- C. Temporary Facilities and Controls.

65.02 CLOSEOUT PROCEDURES

Contractor shall comply with all closeout provisions as indicated in the General Conditions.

65.03 FINAL CLEANING

- A. Contractor shall execute final cleaning prior to final inspection.
- B. Contractor shall clean interior and exterior glass and all surfaces exposed to view; remove temporary labels, tape, stains, and foreign substances, polish transparent and glossy surfaces, wax and polish new vinyl floor surfaces, vacuum carpeted and soft surfaces.
- C. Contractor shall clean equipment and fixtures to a sanitary condition.
- D. Contractor shall replace filters of operating equipment.
- E. Contractor shall clean debris from roofs, gutters, down spouts, and drainage systems.
- F. Contractor shall clean Site, sweep paved areas, and rake clean landscaped surfaces.
- G. Contractor shall remove waste and surplus materials, rubbish, and construction facilities from the Site and surrounding areas.

65.04 ADJUSTING

Contractor shall adjust operating products and equipment to ensure smooth and unhindered operation.

65.05 RECORD DOCUMENTS AND SHOP DRAWINGS

- A. Contractor shall legibly mark each item to record actual construction, including:
 - (1) Measured depths of foundation in relation to finish floor datum.
 - (2) Measured horizontal and vertical locations of underground utilities and appurtenances, referenced to permit surface improvements.
 - (3) Measured locations of internal utilities and appurtenances concealed in construction, referenced to visible and accessible features of the Work.
 - (4) Field changes of dimension and detail.
 - (5) Details not on original Contract Drawings
 - (6) Changes made by modification(s).
 - (7) References to related Shop Drawings and modifications.
- B. Contractor will provide one set of Record Drawings to District.
- C. Contractor shall submit all required documents to District and/or Architect prior to or with its final Application for Payment.

65.06 INSTRUCTION OF DISTRICT PERSONNEL

- A. Before final inspection, at agreed upon times, Contractor shall instruct District's designated personnel in operation, adjustment, and maintenance of products, equipment, and systems.
- B. For equipment requiring seasonal operation, Contractor shall perform instructions for other seasons within six months or by the change of season.
- C. Contractor shall use operation and maintenance manuals as basis for instruction. Contractor shall review contents of manual with personnel in detail to explain all aspects of operation and maintenance.
- D. Contractor shall prepare and insert additional data in Operation and Maintenance Manual when the need for such data becomes apparent during instruction.
- E. Contractor shall review contents of manual with personnel in detail to explain all aspects of operation and maintenance.

65.07 SPARE PARTS AND MAINTENANCE MATERIALS

- A. Contractor shall provide products, spare parts, maintenance, and extra materials in quantities specified in the Specifications and in Manufacturer's recommendations.

- B. Contractor shall provide District with all required Operation and Maintenance Data at one time. Partial or piecemeal submissions of Operation and Maintenance Data will not be accepted.

PART 66 – PRODUCTS Not Used.

PART 67 – EXECUTION Not Used.

END OF DOCUMENT

OPERATION AND MAINTENANCE DATA

PART 68 – GENERAL

68.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Completion of the Work;
- B. Special Conditions.

68.02 QUALITY ASSURANCE:

Contractor shall prepare instructions and data by personnel experienced in maintenance and operation of described products.

68.03 FORMAT:

- A. Contractor shall prepare data in the form of an instructional manual entitled "OPERATIONS AND MAINTENANCE MANUAL & INSTRUCTIONS" ("Manual").
- B. Binders: Contractor shall use commercial quality, 8-1/2 by 11 inch, three-side rings, with durable plastic covers; two inch maximum ring size. When multiple binders are used, Contractor shall correlate data into related consistent groupings.
- C. Cover: Contractor shall identify each binder with typed or printed title "OPERATION AND MAINTENANCE MANUAL & INSTRUCTIONS"; and shall list title of Project and identify subject matter of contents.
- D. Contractor shall arrange content by systems process flow under section numbers and sequence of Table of Contents of the Contract Documents.
- E. Contractor shall provide tabbed fly leaf for each separate product and system, with typed description of product and major component parts of equipment.
- F. Text: The content shall include Manufacturer's printed data, or typewritten data on 24 pound paper.
- G. Drawings: Contractor shall provide with reinforced punched binder tab and shall bind in with text; folding larger drawings to size of text pages.

68.04 CONTENTS, EACH VOLUME:

- A. Table of Contents: Contractor shall provide title of Project; names, addresses, and telephone numbers of the Architect, any engineers, subconsultants, Subcontractor(s), and Contractor with name of responsible parties; and schedule of products and systems, indexed to content of the volume.

- B. For Each Product or System: Contractor shall list names, addresses, and telephone numbers of Subcontractor(s) and suppliers, including local source of supplies and replacement parts.
- C. Product Data: Contractor shall mark each sheet to clearly identify specific products and component parts, and data applicable to installation. Delete inapplicable information.
- D. Drawings: Contractor shall supplement product data to illustrate relations of component parts of equipment and systems, to show control and flow diagrams. Contractor shall not use Project Record Documents as maintenance drawings.
- E. Text: Contractor shall include any and all information as required to supplement product data. Contractor shall provide logical sequence of instructions for each procedure, incorporating manufacturer's instructions.
- F. Warranties and Bonds: Contractor shall bind in one copy of each.

68.05 MANUAL FOR MATERIALS AND FINISHES:

- A. Building Products, Applied Materials, and Finishes: Contractor shall include product data, with catalog number, size, composition, and color and texture designations. Contractor shall provide information for re-ordering custom manufactured products.
- B. Instructions for Care and Maintenance: Contractor shall include Manufacturer's recommendations for cleaning agents and methods, precautions against detrimental agents and methods, and recommended schedule for cleaning and maintenance.
- C. Moisture Protection and Weather Exposed Products: Contractor shall include product data listing applicable reference standards, chemical composition, and details of installation. Contractor shall provide recommendations for inspections, maintenance, and repair.
- D. Additional Requirements: Contractor shall include all additional requirements as specified in the Specifications.
- E. Contractor shall provide a listing in Table of Contents for design data, with tabbed fly sheet and space for insertion of data.

68.06 MANUAL FOR EQUIPMENT AND SYSTEMS:

- A. Each Item of Equipment and Each System: Contractor shall include description of unit or system, and component parts and identify function, normal operating characteristics, and limiting conditions. Contractor shall include performance curves, with engineering data and tests, and complete nomenclature, and commercial number of replaceable parts.
- B. Panelboard Circuit Directories: Contractor shall provide electrical service characteristics, controls, and communications.

- C. Contractor shall include color coded wiring diagrams as installed.
- D. Operating Procedures: Contractor shall include start-up, break-in, and routine normal operating instructions and sequences. Contractor shall include regulation, control, stopping, shut-down, and emergency instructions. Contractor shall include summer, winter, and any special operating instructions.
- E. Maintenance Requirements: Contractor shall include routine procedures and guide for trouble-shooting; disassembly, repair, and reassembly instructions; and alignment, adjusting, balancing, and checking instructions.
- F. Contractor shall provide servicing and lubrication schedule, and list of lubricants required.
- G. Contractor shall include manufacturer's printed operation and maintenance instructions.
- H. Contractor shall include sequence of operation by controls manufacturer.
- I. Contractor shall provide original manufacturer's parts list, illustrations, assembly drawings, and diagrams required for maintenance.
- J. Contractor shall provide control diagrams by controls manufacturer as installed.
- K. Contractor shall provide Contractor's coordination drawings, with color coded piping diagrams as installed.
- L. Contractor shall provide charts of valve tag numbers, with location and function of each valve, keyed to flow and control diagrams.
- M. Contractor shall provide list of original manufacturer's spare parts, current prices, and recommended quantities to be maintained in storage.
- N. Additional Requirements: Contractor shall include all additional requirements as specified in Specification(s).
- O. Contractor shall provide a listing in Table of Contents for design data, with tabbed fly sheet and space for insertion of data.

68.07 SUBMITTAL:

- A. Contractor shall submit to the District for review two (2) copies of preliminary draft or proposed formats and outlines of the contents of the Manual within thirty (30) days of Contractor's start of Work.
- B. For equipment, or component parts of equipment put into service during construction and to be operated by District, Contractor shall submit draft content for that portion of the Manual within ten (10) days after acceptance of that equipment or component.

- C. Contractor shall submit two (2) copies of a complete Manual in final form prior to final Application for Payment. Copy will be returned with Architect/Engineer comments. Contractor must revise the content of the Manual as required by District prior to District's approval of Contractor's final Application for Payment.
- D. Contractor must submit two (2) copies of revised Manual in final form within ten (10) days after final inspection.

PART 69 – PRODUCTS Not Used.

PART 70 – EXECUTION Not Used.

END OF DOCUMENT

WARRANTIES

PART 71 - GENERAL

71.01 RELATED DOCUMENTS AND PROVISIONS

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Warranty/Guarantee Information;
- B. Special Conditions.

71.02 FORMAT

- A. Binders: Contractor shall use commercial quality, 8-1/2 by 11 inch, three-side rings, with durable plastic covers; two inch maximum ring size.
- B. Cover: Contractor shall identify each binder with typed or printed title "WARRANTIES" and shall list title of Project.
- C. Table of Contents: Contractor shall provide title of Project; name, address, and telephone number of Contractor and equipment supplier; and name of responsible principal. Contractor shall identify each item with the number and title of the specific Specification, document, provision, or section in which the name of the product or work item is specified.
- D. Contractor shall separate each warranty with index tab sheets keyed to the Table of Contents listing, providing full information and using separate typed sheets as necessary. Contractor shall list each applicable and/or responsible Subcontractor(s), supplier(s), and/or manufacturer(s), with name, address, and telephone number of each responsible principal(s).

71.03 PREPARATION:

- A. Contractor shall obtain warranties, executed in duplicate by each applicable and/or responsible subcontractor(s), supplier(s), and manufacturer(s), within ten (10) days after completion of the applicable item or work. Except for items put into use with District's permission, Contractor shall leave date of beginning of time of warranty blank until the date of completion is determined.
- B. Contractor shall verify that documents are in proper form, contain full information, and are notarized, when required.
- C. Contractor shall co-execute submittals when required.
- D. Contractor shall retain warranties until time specified for submittal.

71.04 TIME OF SUBMITTALS:

- A. For equipment or component parts of equipment put into service during construction with District's permission, Contractor shall submit a draft warranty for that equipment or component within ten (10) days after acceptance of that equipment or component.
- B. Contractor shall submit for District approval all warranties and related documents within ten (10) days after date of completion. Contractor must revise the warranties as required by the District prior to District's approval of Contractor's final Application for Payment.
- C. For items of work delayed beyond date of completion, Contractor shall provide an updated submittal within ten (10) days after acceptance, listing the date of acceptance as start of warranty period.

PART 72 - PRODUCTS Not Used.**PART 73 – EXECUTION Not Used.**

END OF DOCUMENT

RECORD DOCUMENTS

PART 74 - GENERAL

74.01 RELATED DOCUMENTS AND PROVISIONS:

All Contract Documents should be reviewed for applicable provisions related to the provisions in this document, including without limitation:

- A. General Conditions, including, without limitation, Documents on Work;
- B. Special Conditions.

PART 75 - RECORD DRAWINGS

75.01 GENERAL:

- A. As indicated in the Contract Documents, the District will provide Contractor with one set of reproducible, full size original Contract Drawings (mylars).
- B. Contractor shall maintain at each Project Site one set of marked-up plans and shall transfer all changes and information to those marked-up plans, as often as required in the Contract Documents, but in no case less than once each month. Contractor shall submit to the Project Inspector one set of reproducible vellums of the Project Record Drawings ("As-Built") showing all changes incorporated into the Work since the preceding monthly submittal. The As-Built shall be available at the Project Site. The Contractor shall submit reproducible vellums at the conclusion of the Project following review of the blue line prints.
- C. Label and date each Record Drawing "RECORD DOCUMENT" in legibly printed letters.
- D. All deviations in construction, including but not limited to pipe and conduit locations and deviations caused by without limitation Change Orders, Construction Claim Directives, RFI's, and Addenda, shall be accurately and legibly recorded by Contractor.
- E. Locations and changes shall be done by Contractor in a neat and legible manner and, where applicable, indicated by drawing a "cloud" around the changed or additional information.

75.02 RECORD DRAWING INFORMATION:

- A. Contractor shall record the following information:
 - (1) Locations of Work buried under or outside each building, including, without limitation, all utilities, plumbing and electrical lines, and conduits.

- (2) Actual numbering of each electrical circuit to match panel schedule.
- (3) Locations of significant Work concealed inside each building whose general locations are changed from those shown on the Contract Drawings.
- (4) Locations of all items, not necessarily concealed, which vary from the Contract Documents.
- (5) Installed location of all cathodic protection anodes.
- (6) Deviations from the sizes, locations, and other features of installations shown in the Contract Documents.
- (7) Locations of underground work, points of connection with existing utilities, changes in direction, valves, manholes, catch basins, capped stubouts, invert elevations, etc.
- (8) Sufficient information to locate Work concealed in each building with reasonable ease and accuracy.

In some instances, this information may be recorded by dimension. In other instances, it may be recorded in relation to the spaces in the building near which it was installed.

- B. Contractor shall provide additional drawings as necessary for clarification.
- C. Contractor shall provide reproducible record drawings, made from final Shop Drawings marked "No Exceptions Taken" or "Approved as Noted."
- D. After review and approval of the marked-up specifications by the Project Inspector, Contractor shall provide electronic copies of the drawings (in PDF format) with one file with all of the sheets and one set of individual sheet files at the conclusion of the Project.

PART 76 - RECORD SPECIFICATIONS

76.01 GENERAL:

- A. Contractor shall mark each section legibly to record manufacturer, trade name, catalog number, and supplier of each Product and item of equipment actually installed.
- B. After review and approval of the marked-up specifications by the Project Inspector, Contractor shall provide one electronic copy of the specifications (in PDF format) at the conclusion of the Project.

PART 77 - MAINTENANCE OF RECORD DOCUMENTS

77.01 GENERAL


- A. Contractor shall store Record Documents apart from documents used for construction as follows:

- (1) Provide files and racks for storage of Record Documents.
- (2) Maintain Record Documents in a clean, dry, legible condition and in good order.










B. Contractor shall not use Record Documents for construction purposes.

PART 78 – PRODUCTS Not Used.

END OF DOCUMENT

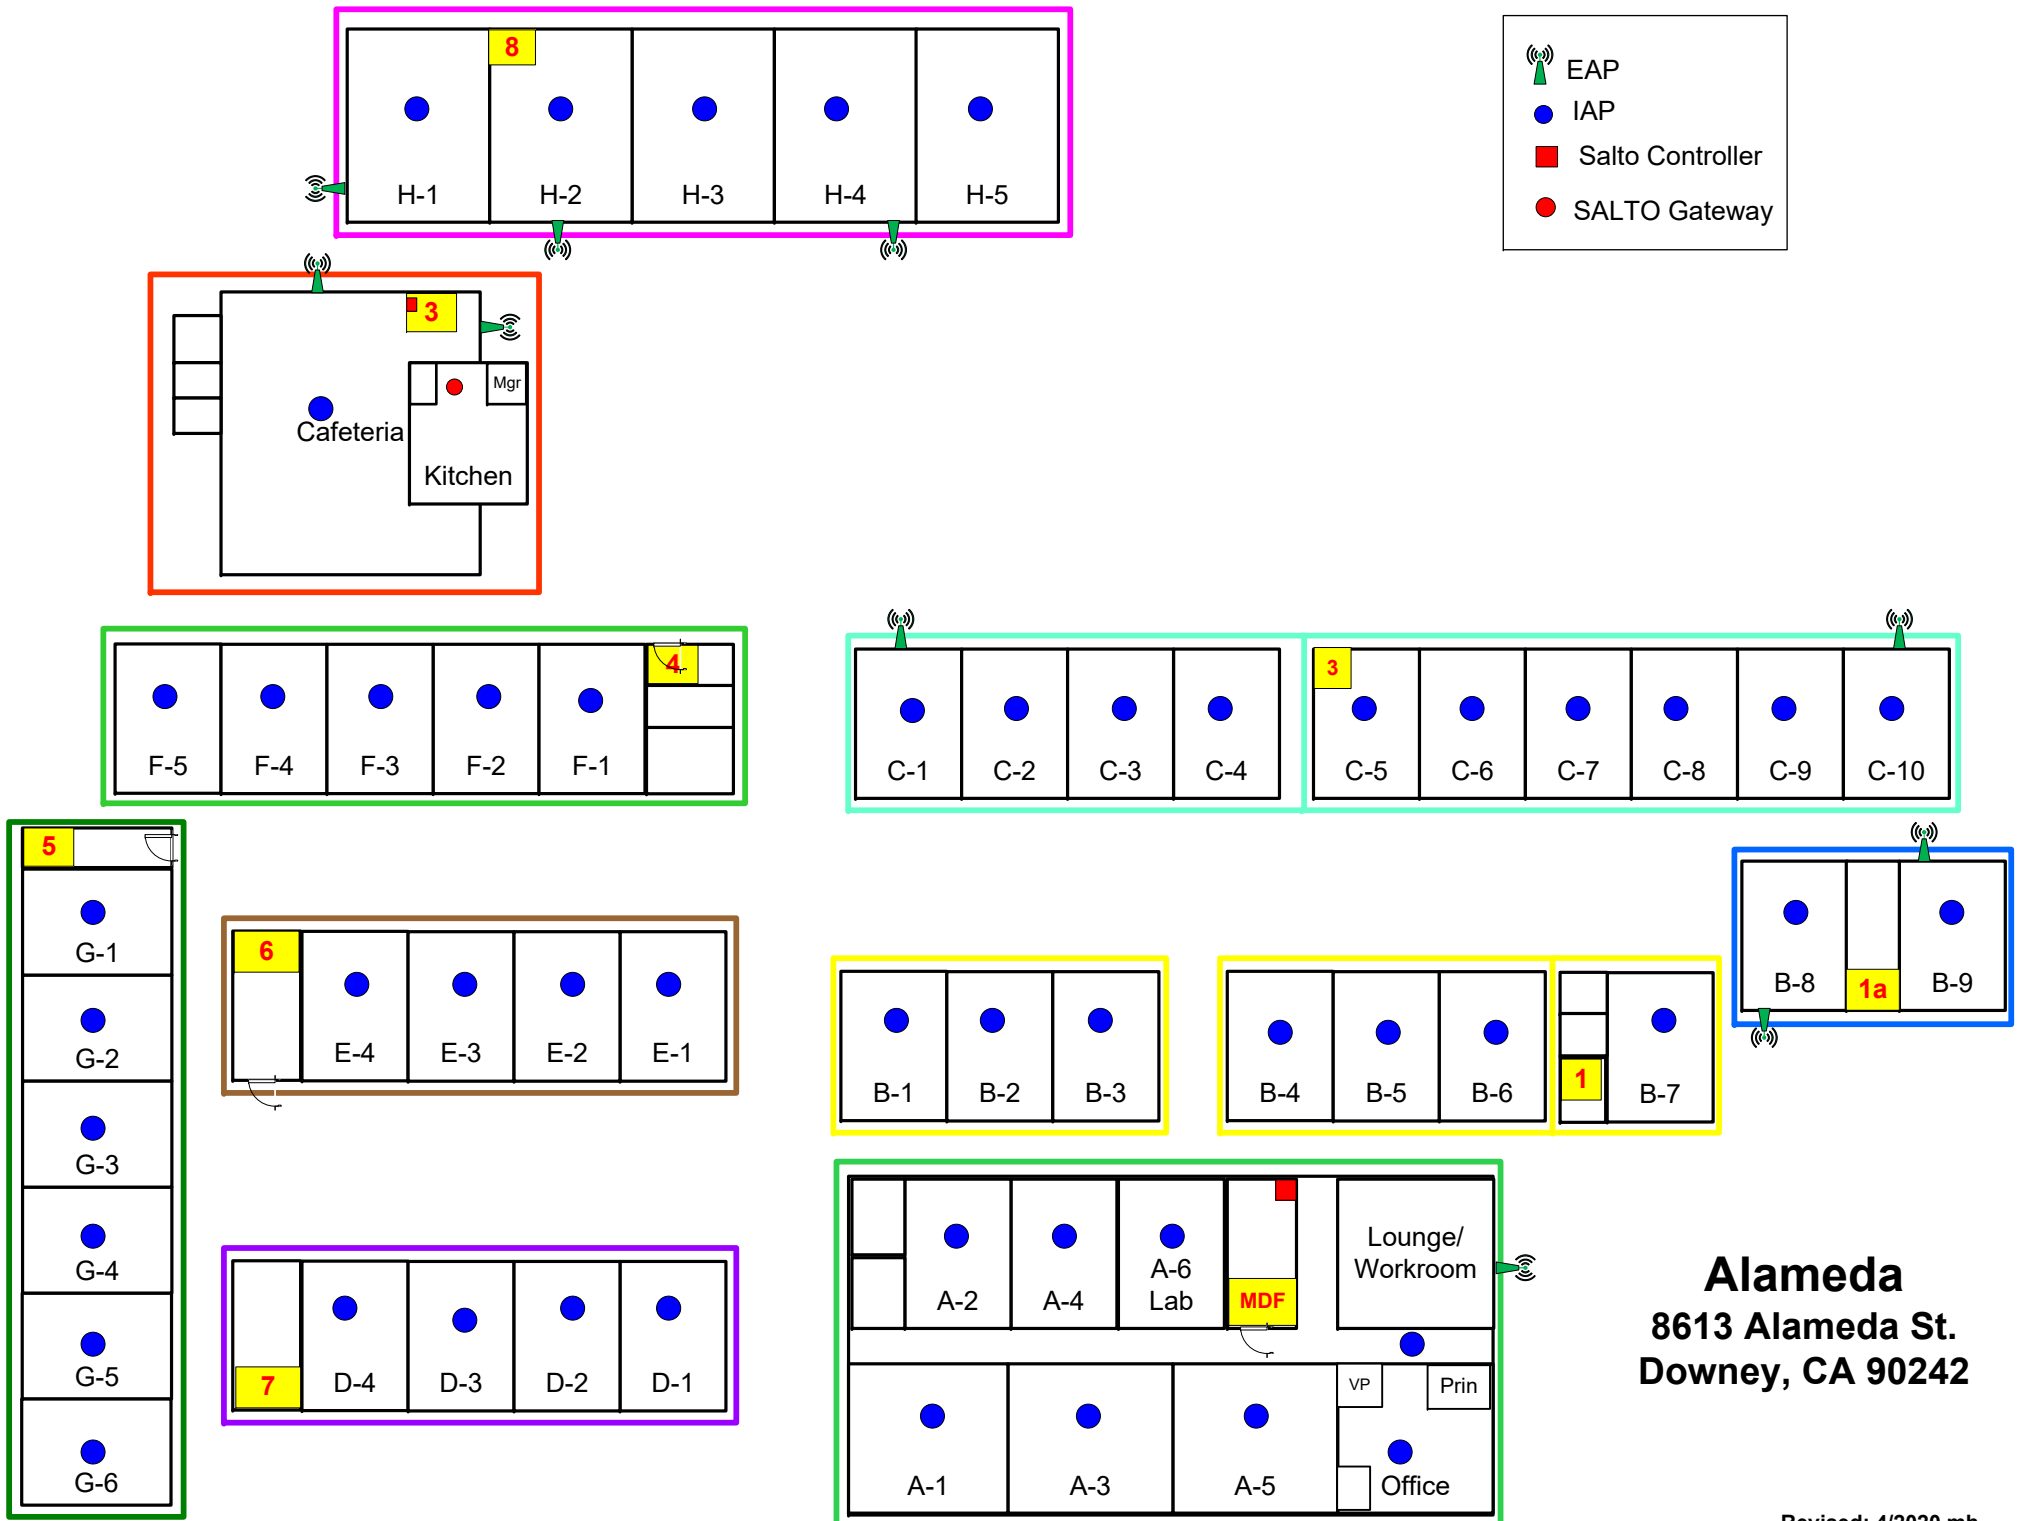

Alameda
 8613 Alameda St.
 Downey, CA 90242

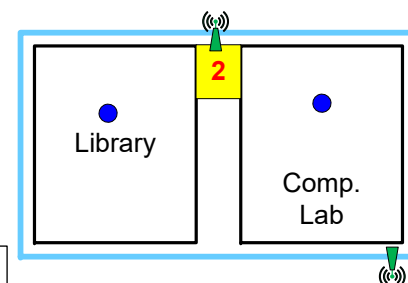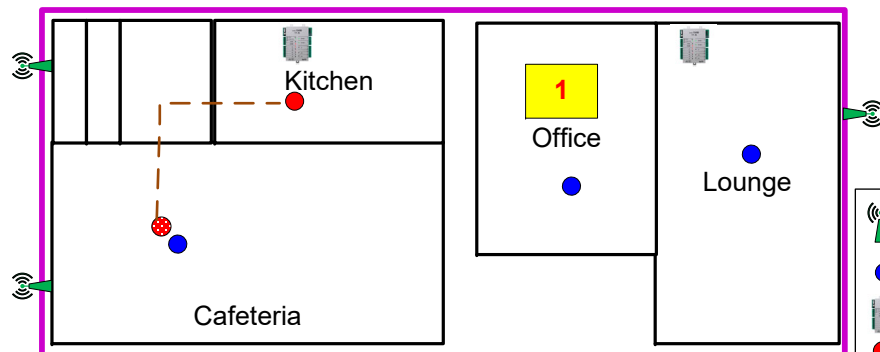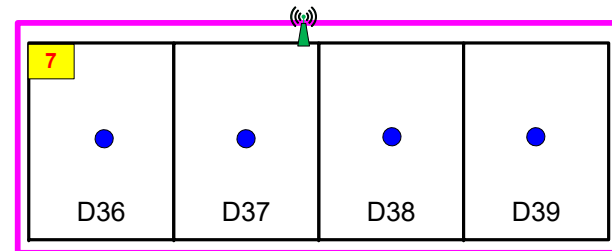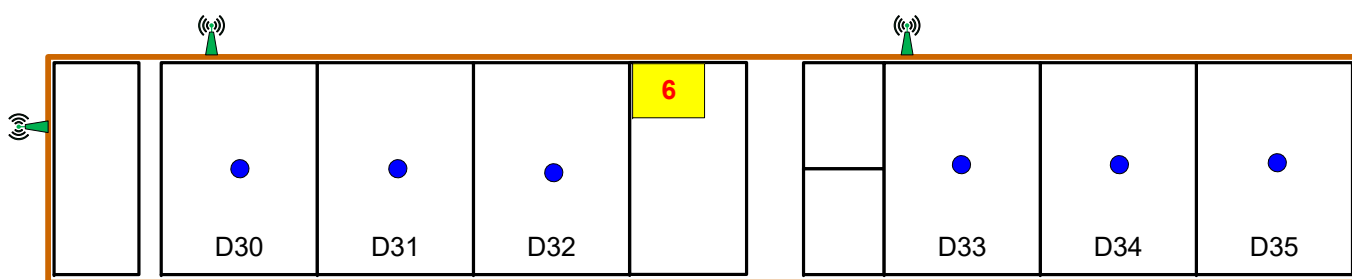


Carpenter
9439 Foster Rd
Downey, CA 90242
 Revised: 5/2020 mh cr

Carpenter Kitchen



Rooms 70-75
Demolished July 2020

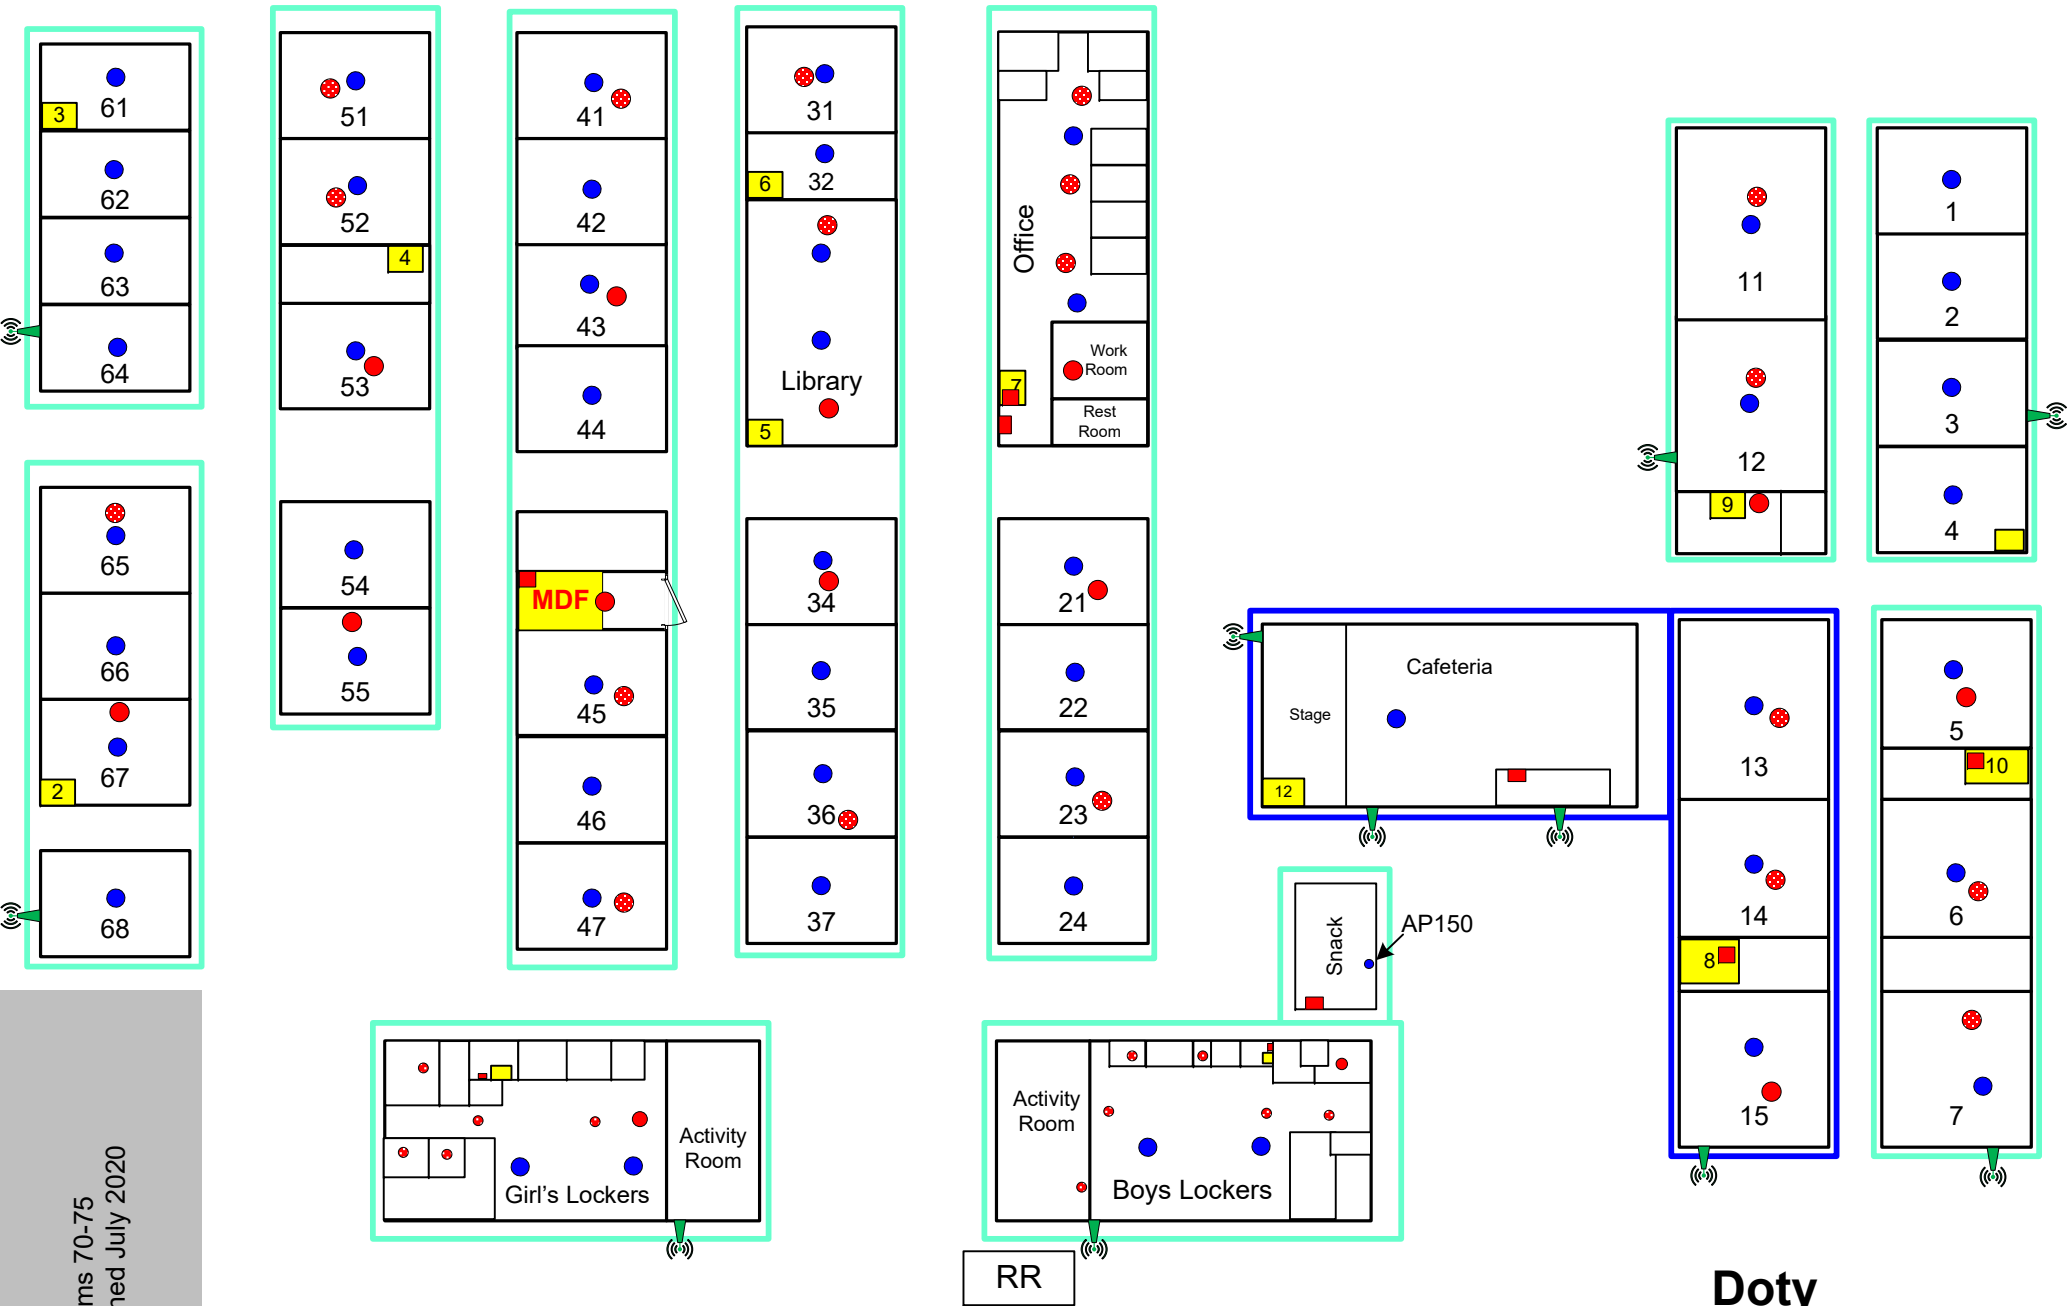



Doty
10301 S Woodruff Ave
Downey, CA 90241
 Revised: 4/2021

 IH-E
 IH-F
 IH-G
 IH-H



 IH-A
 IH-B
 IH-C
 IH-D




Girl's Locker Room

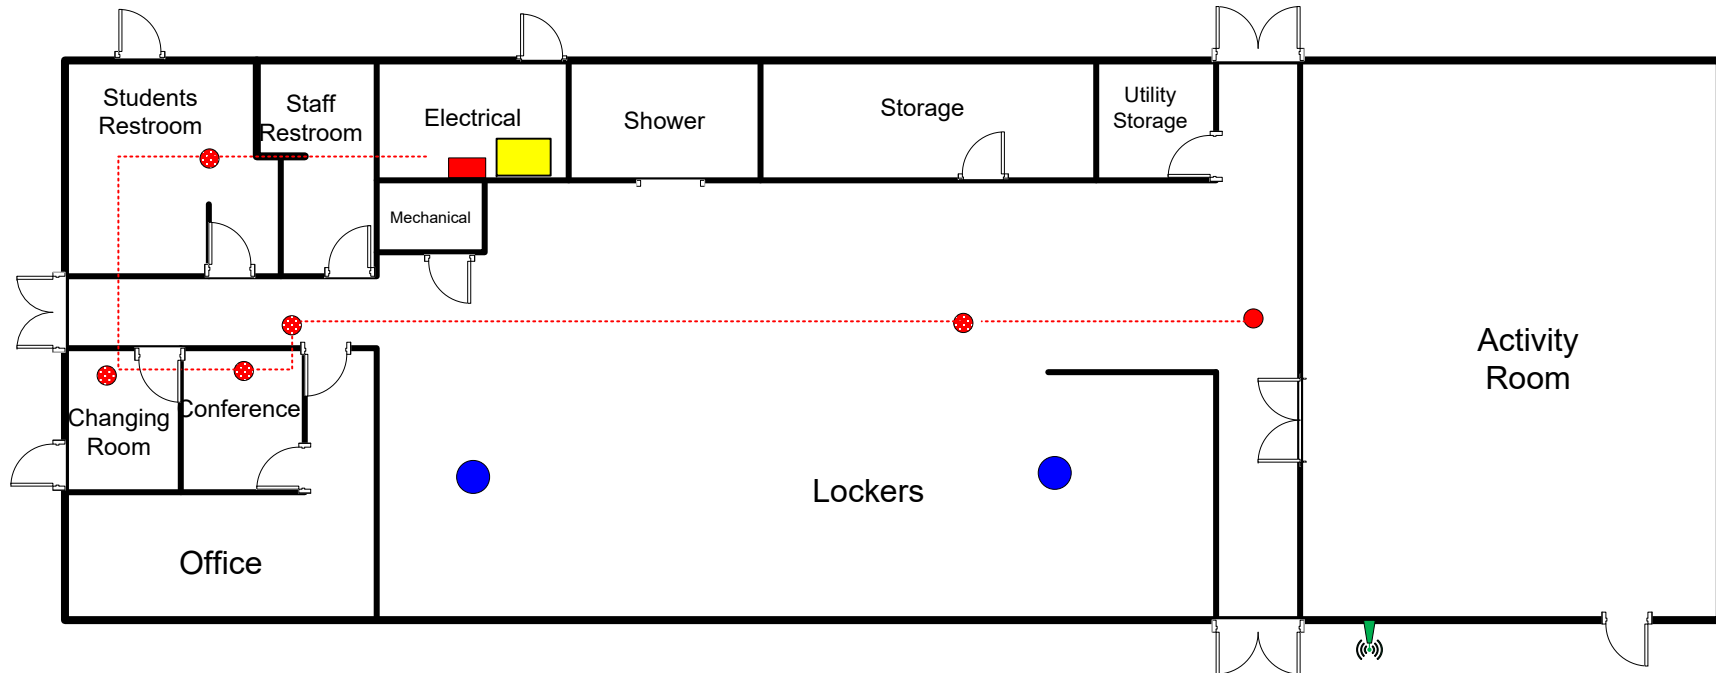


Boy's Locker Room

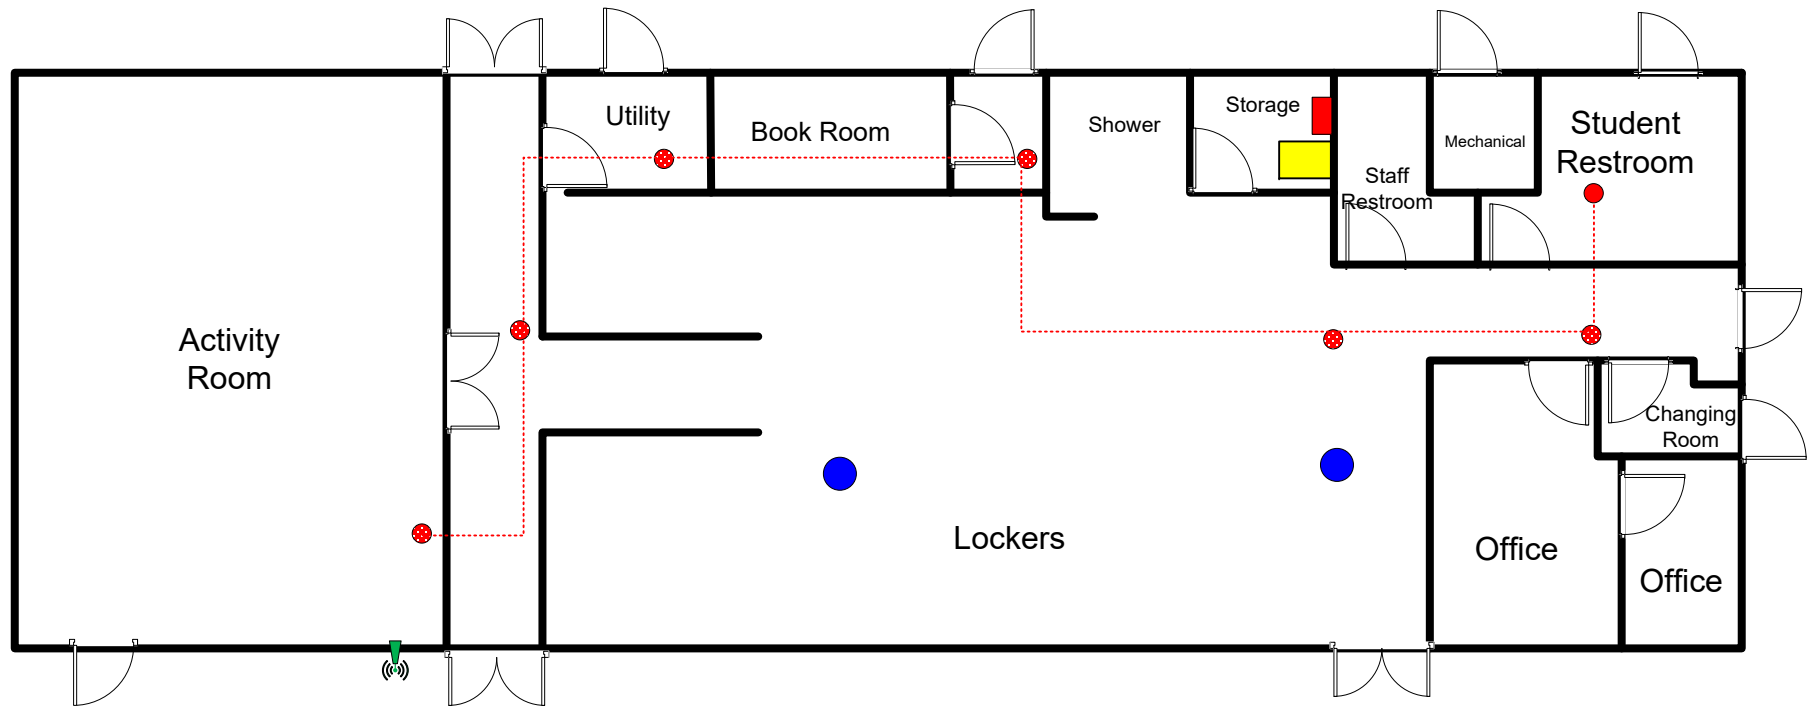

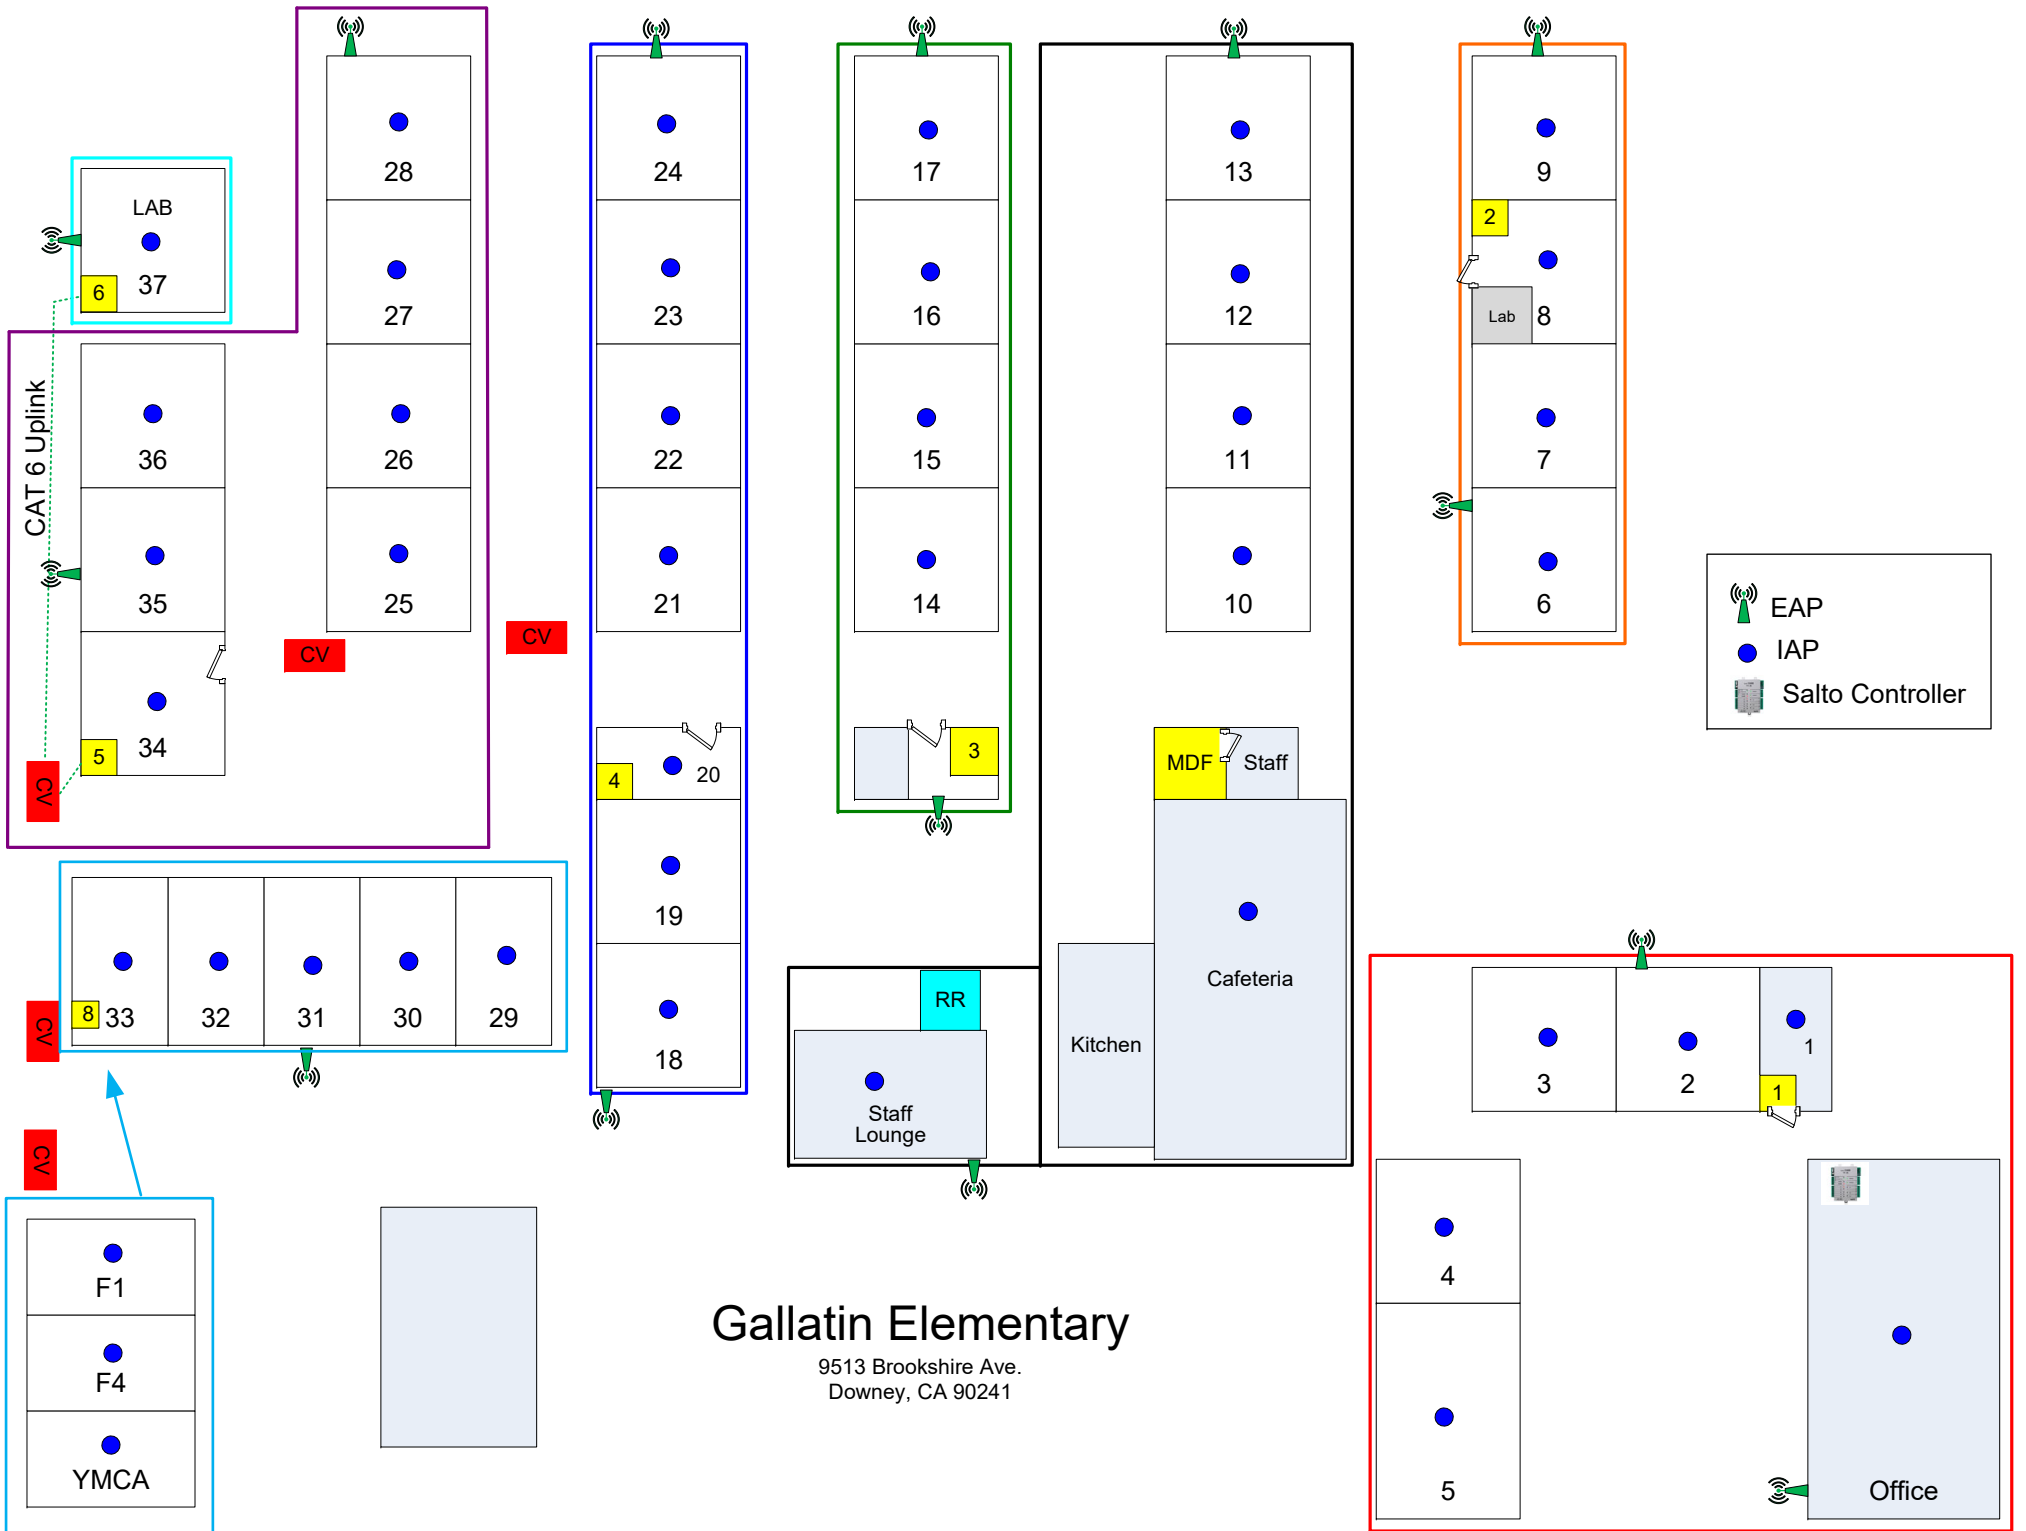



Gallatin Elementary


9513 Brookshire Ave.
Downey, CA 90241

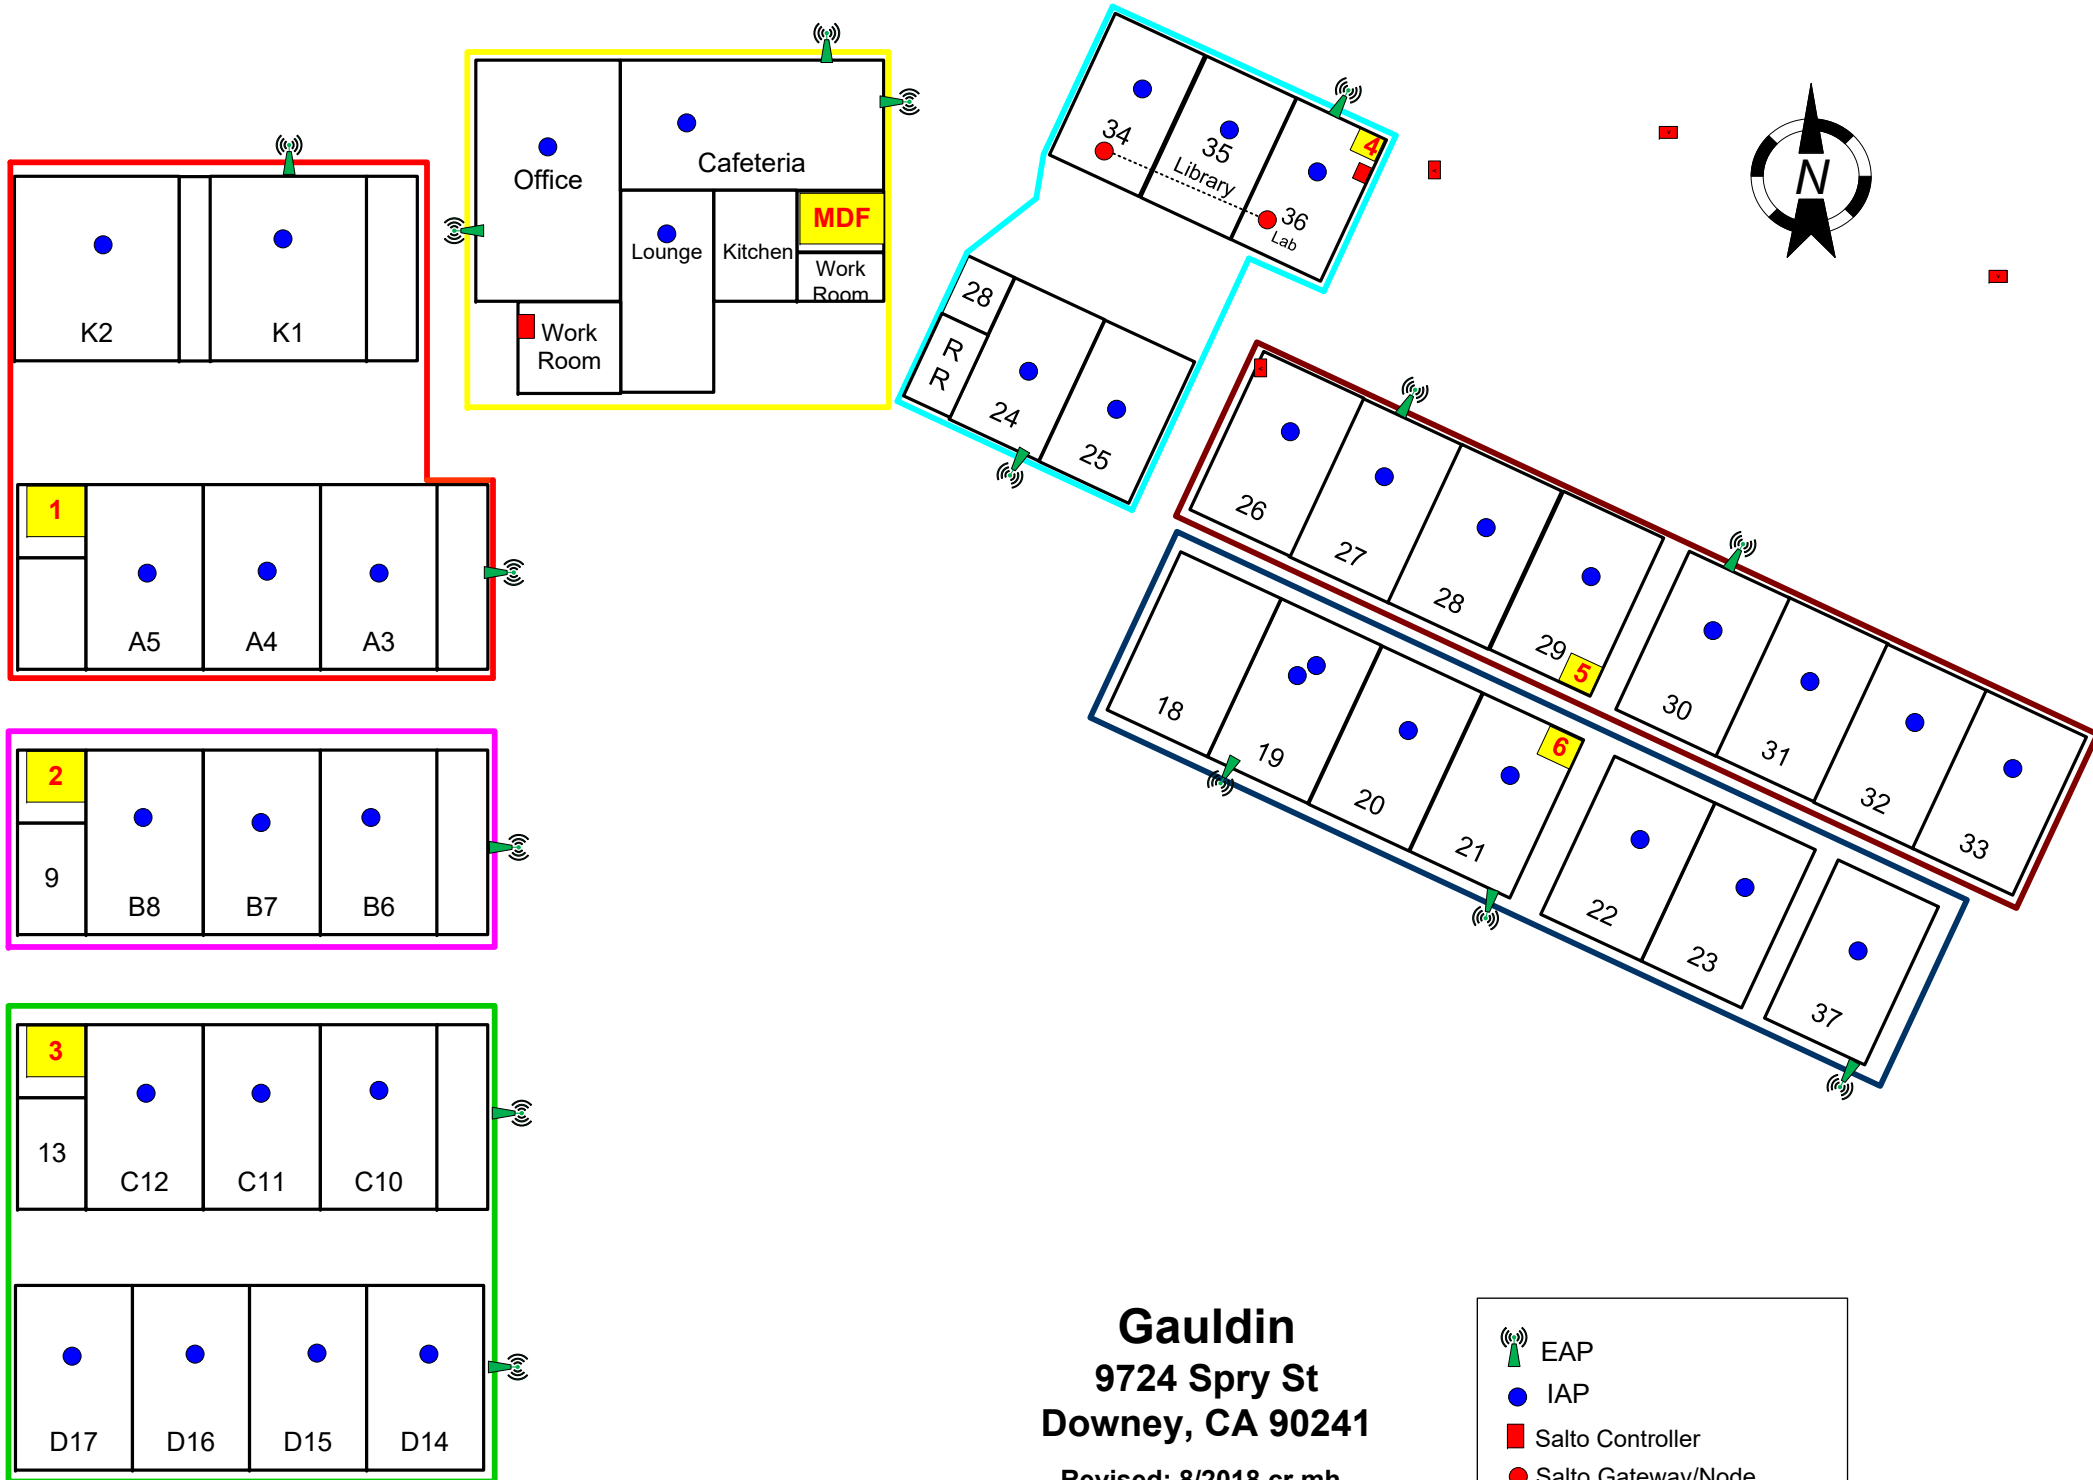

Gauldin
9724 Spry St
Downey, CA 90241
Revised: 8/2018 cr mh





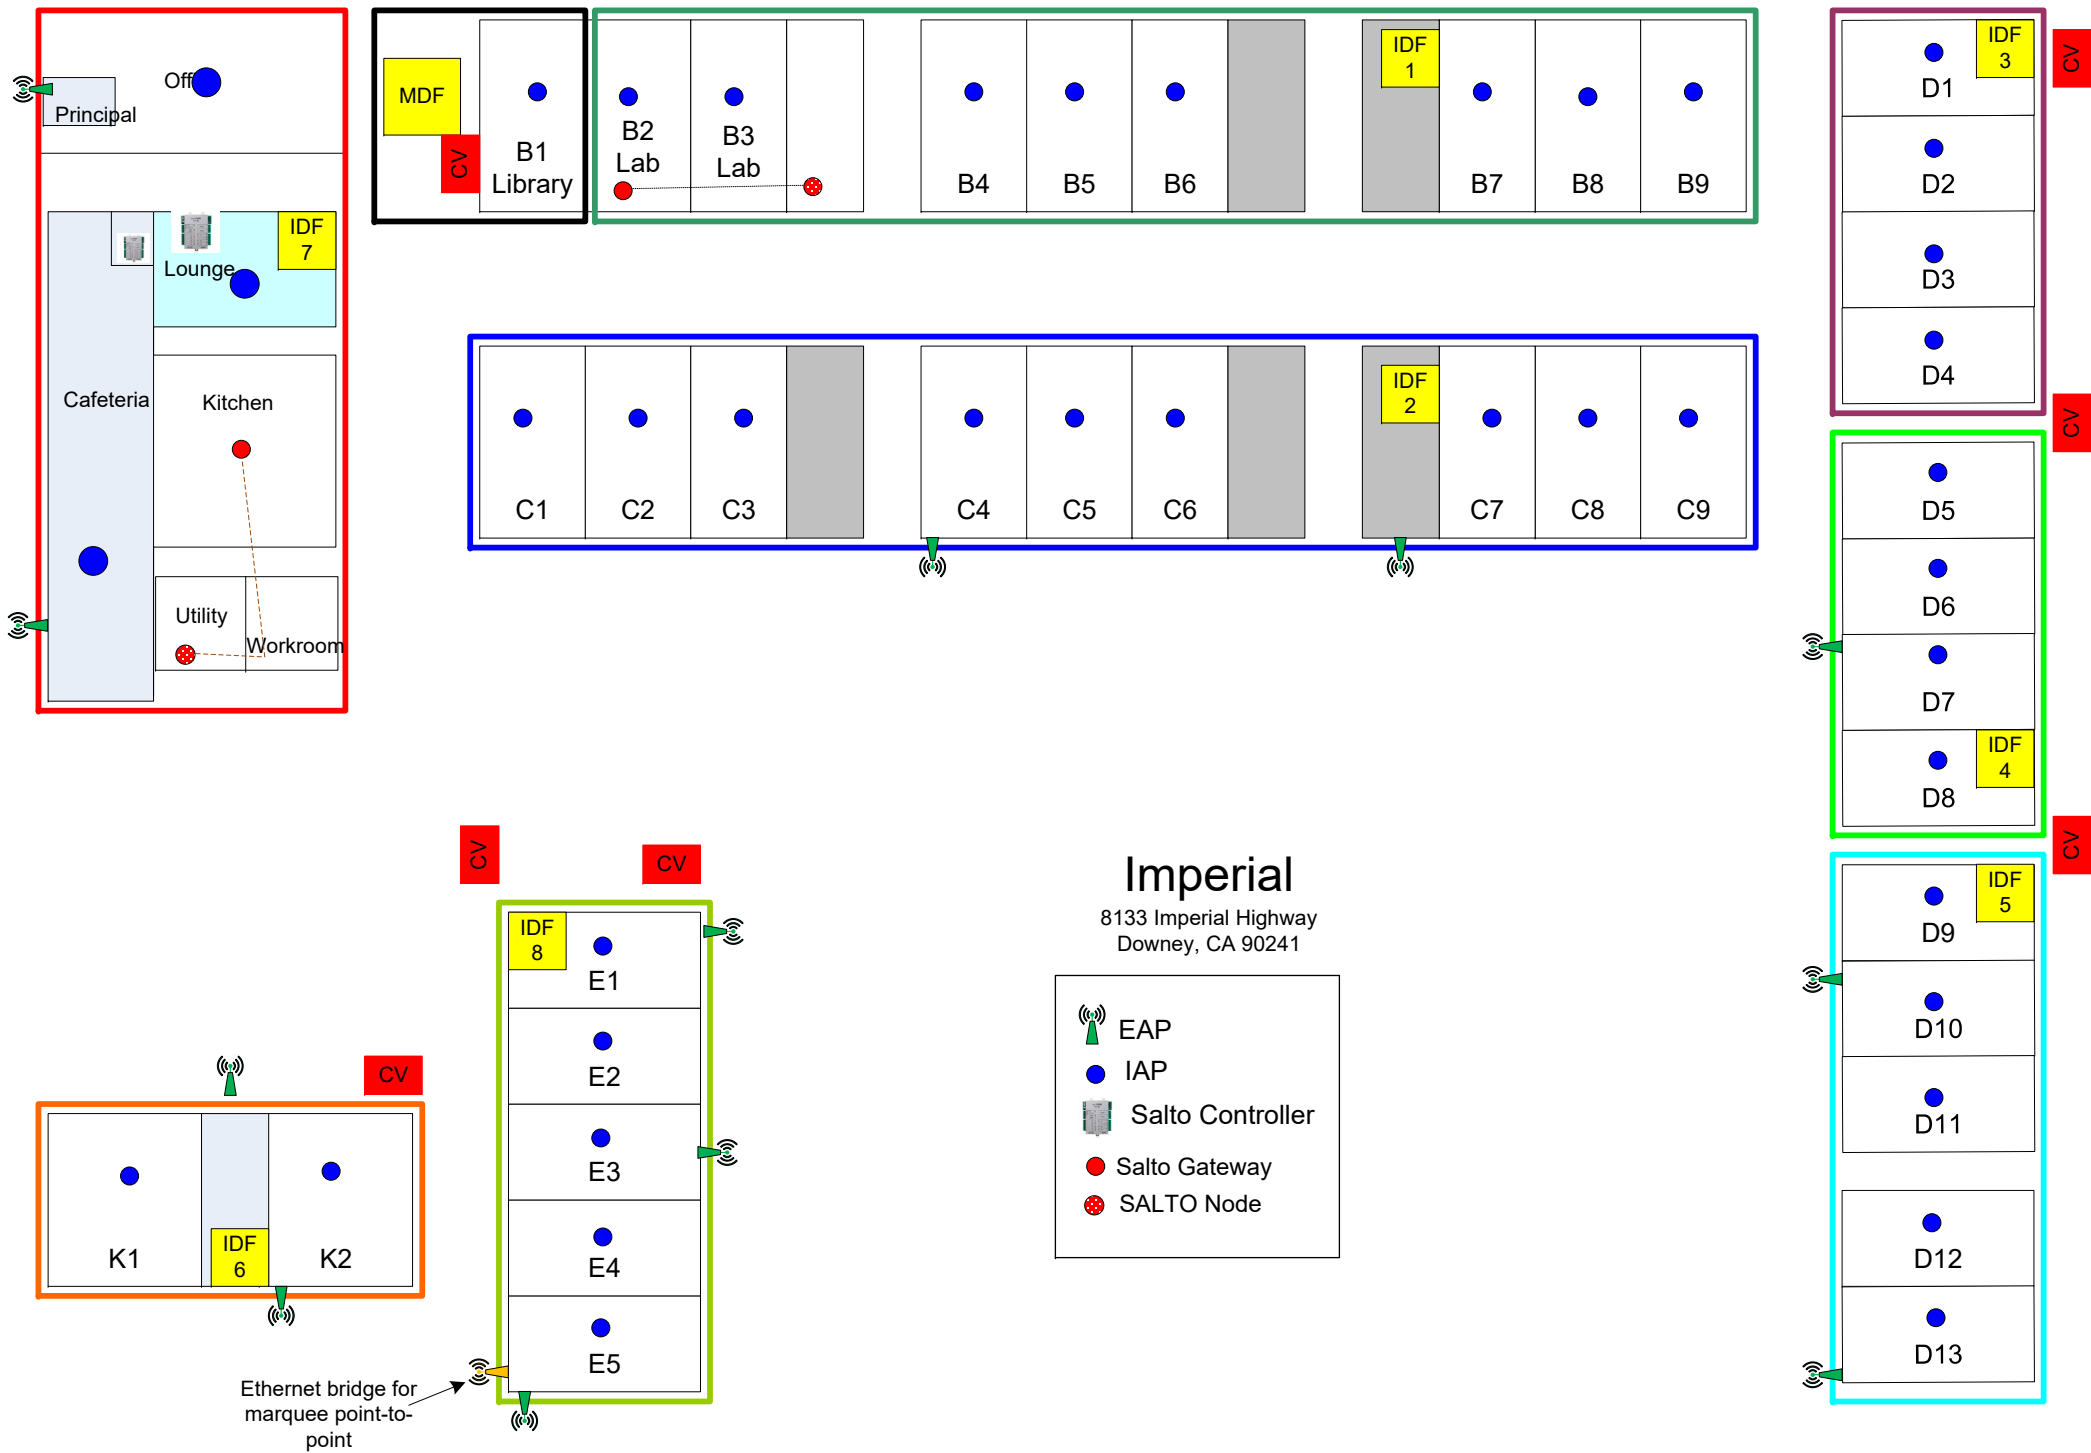


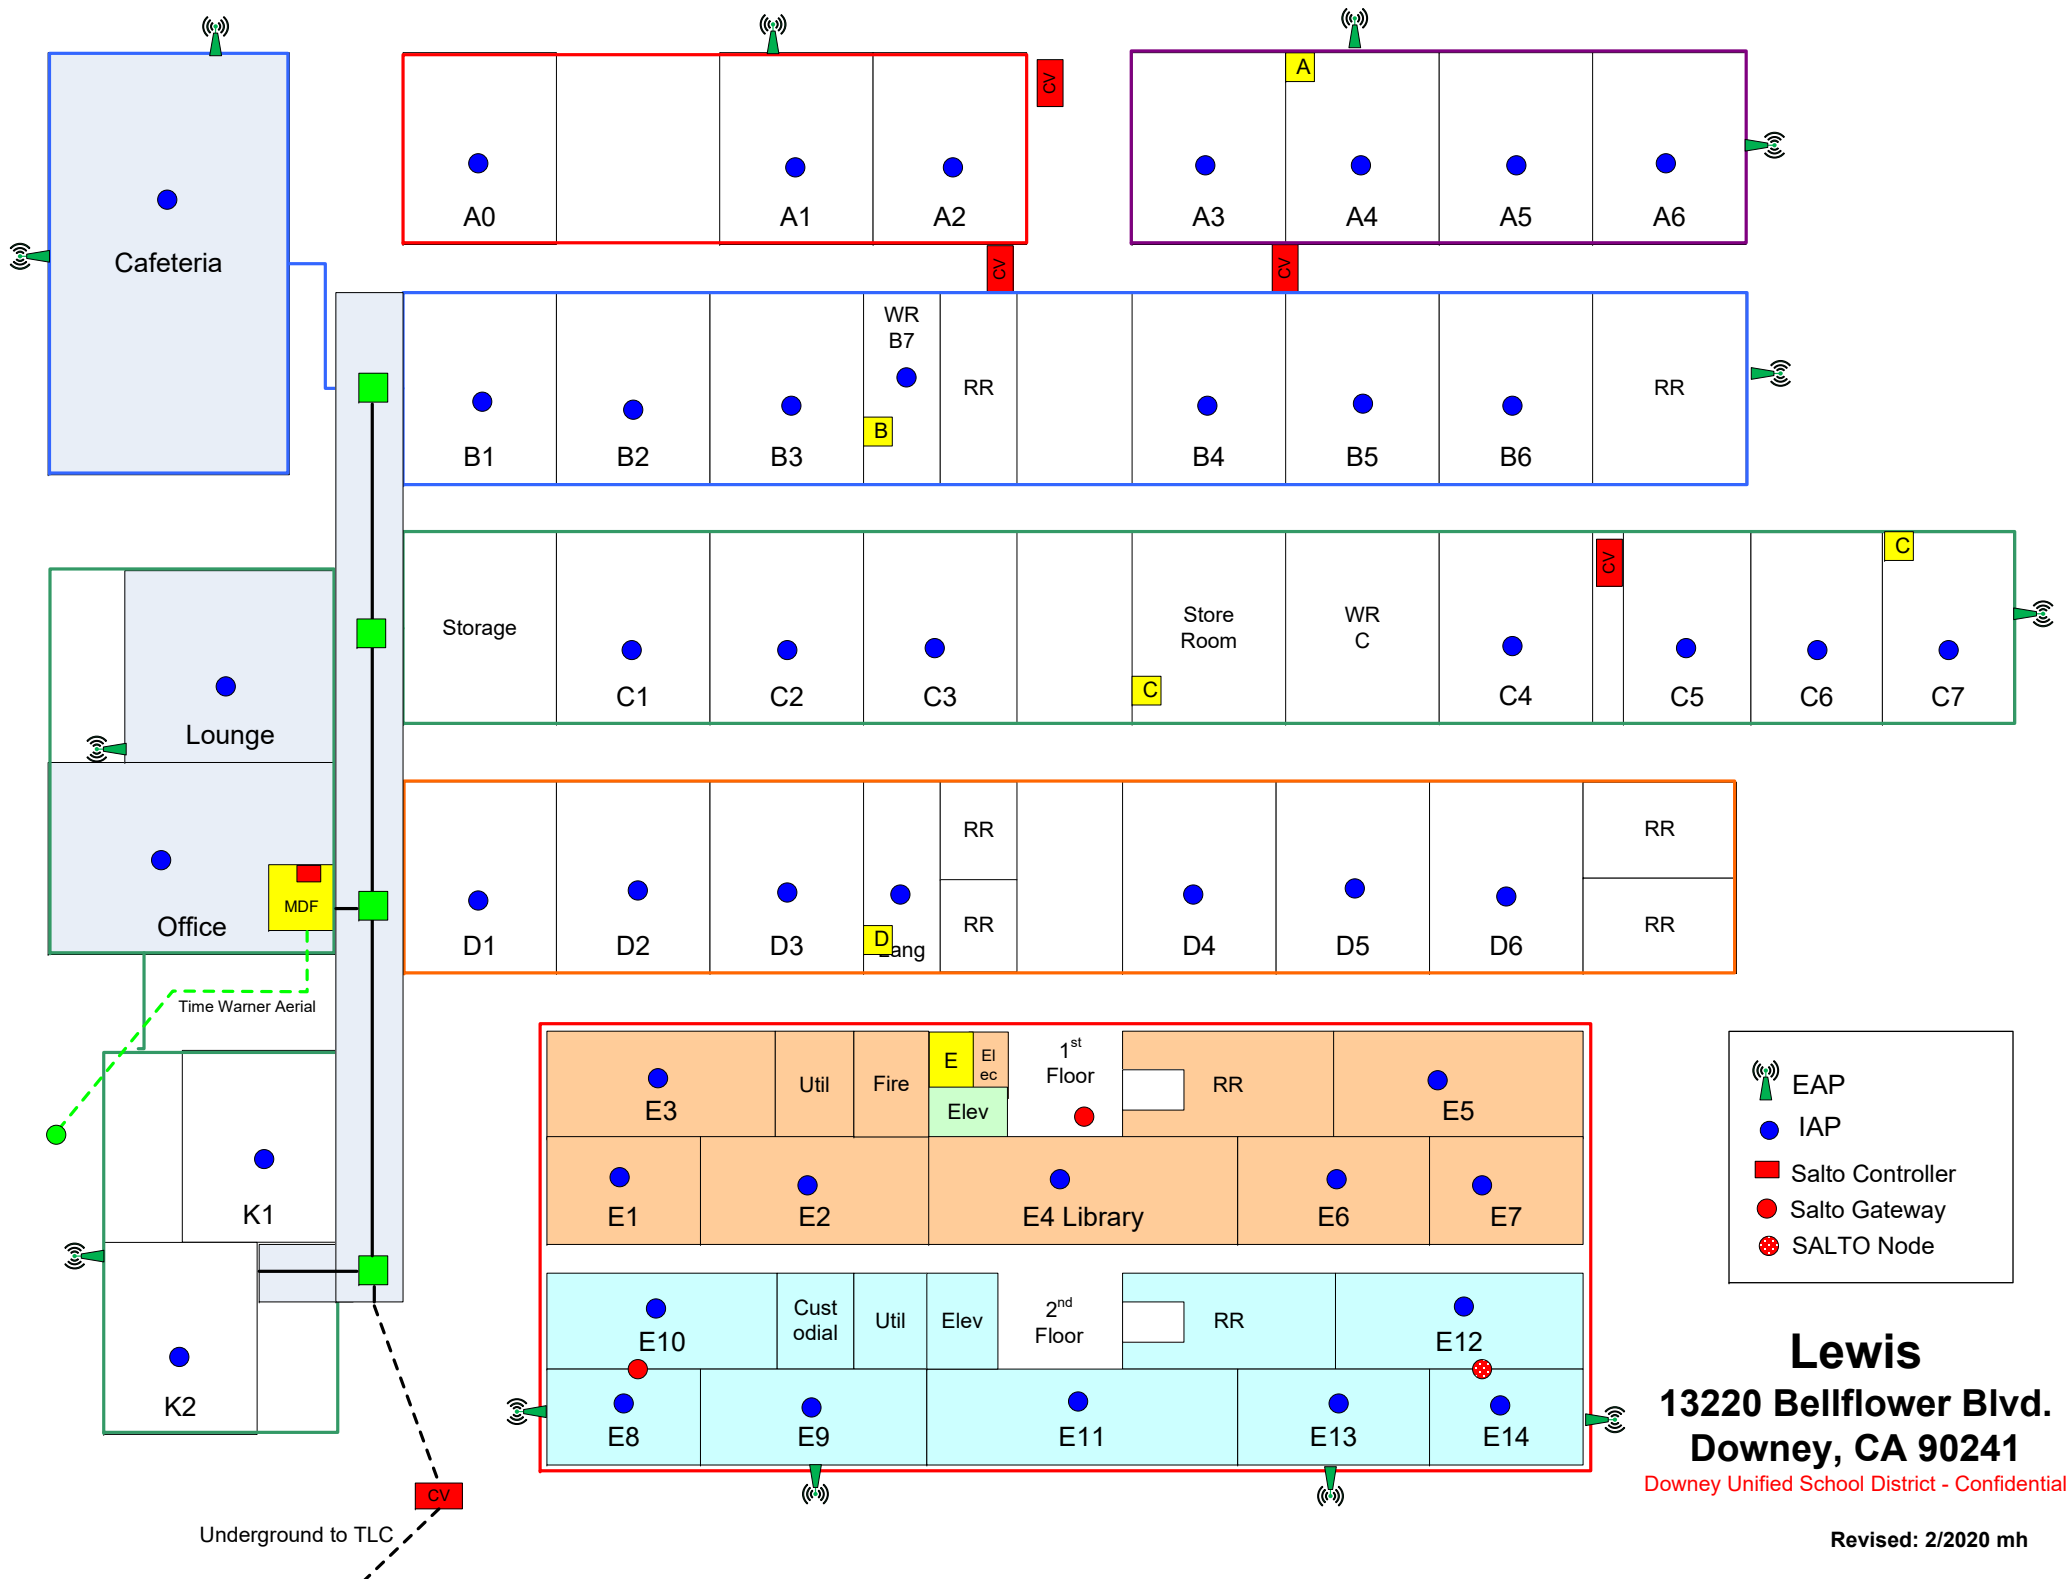






Lewis
13220 Bellflower Blvd.
Downey, CA 90241
 Downey Unified School District - Confidential

Revised: 2/2020 mh

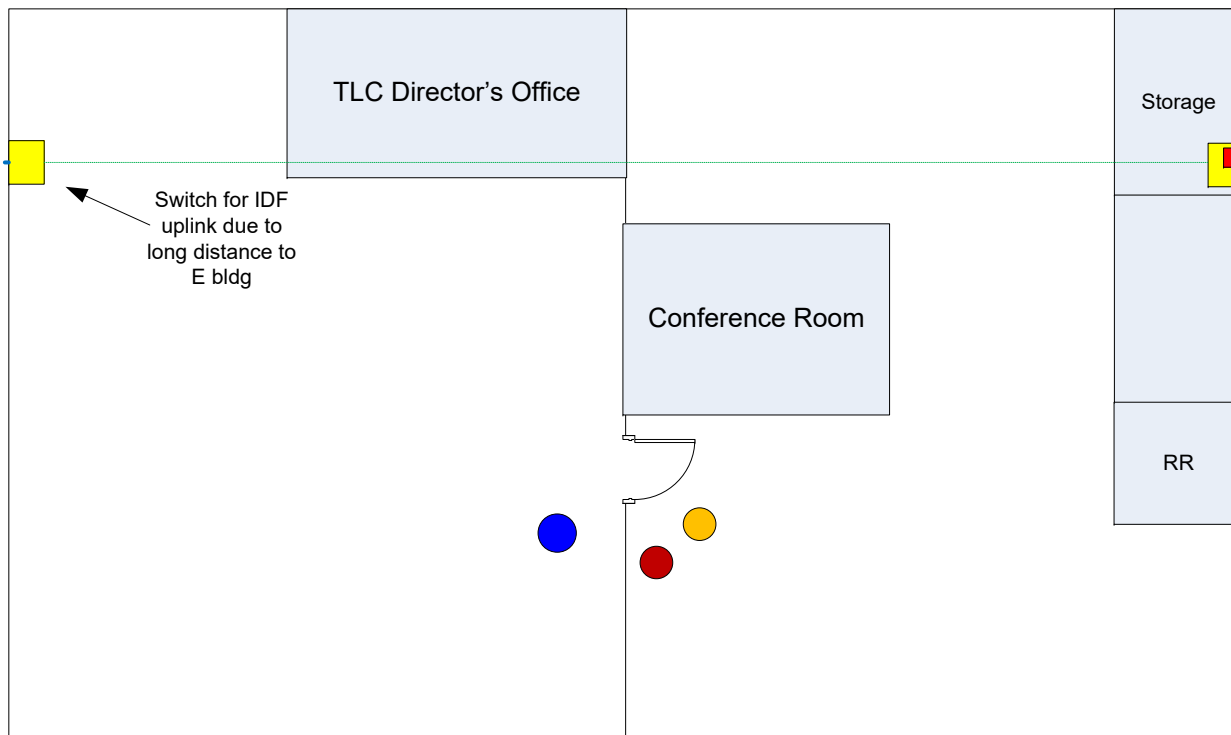

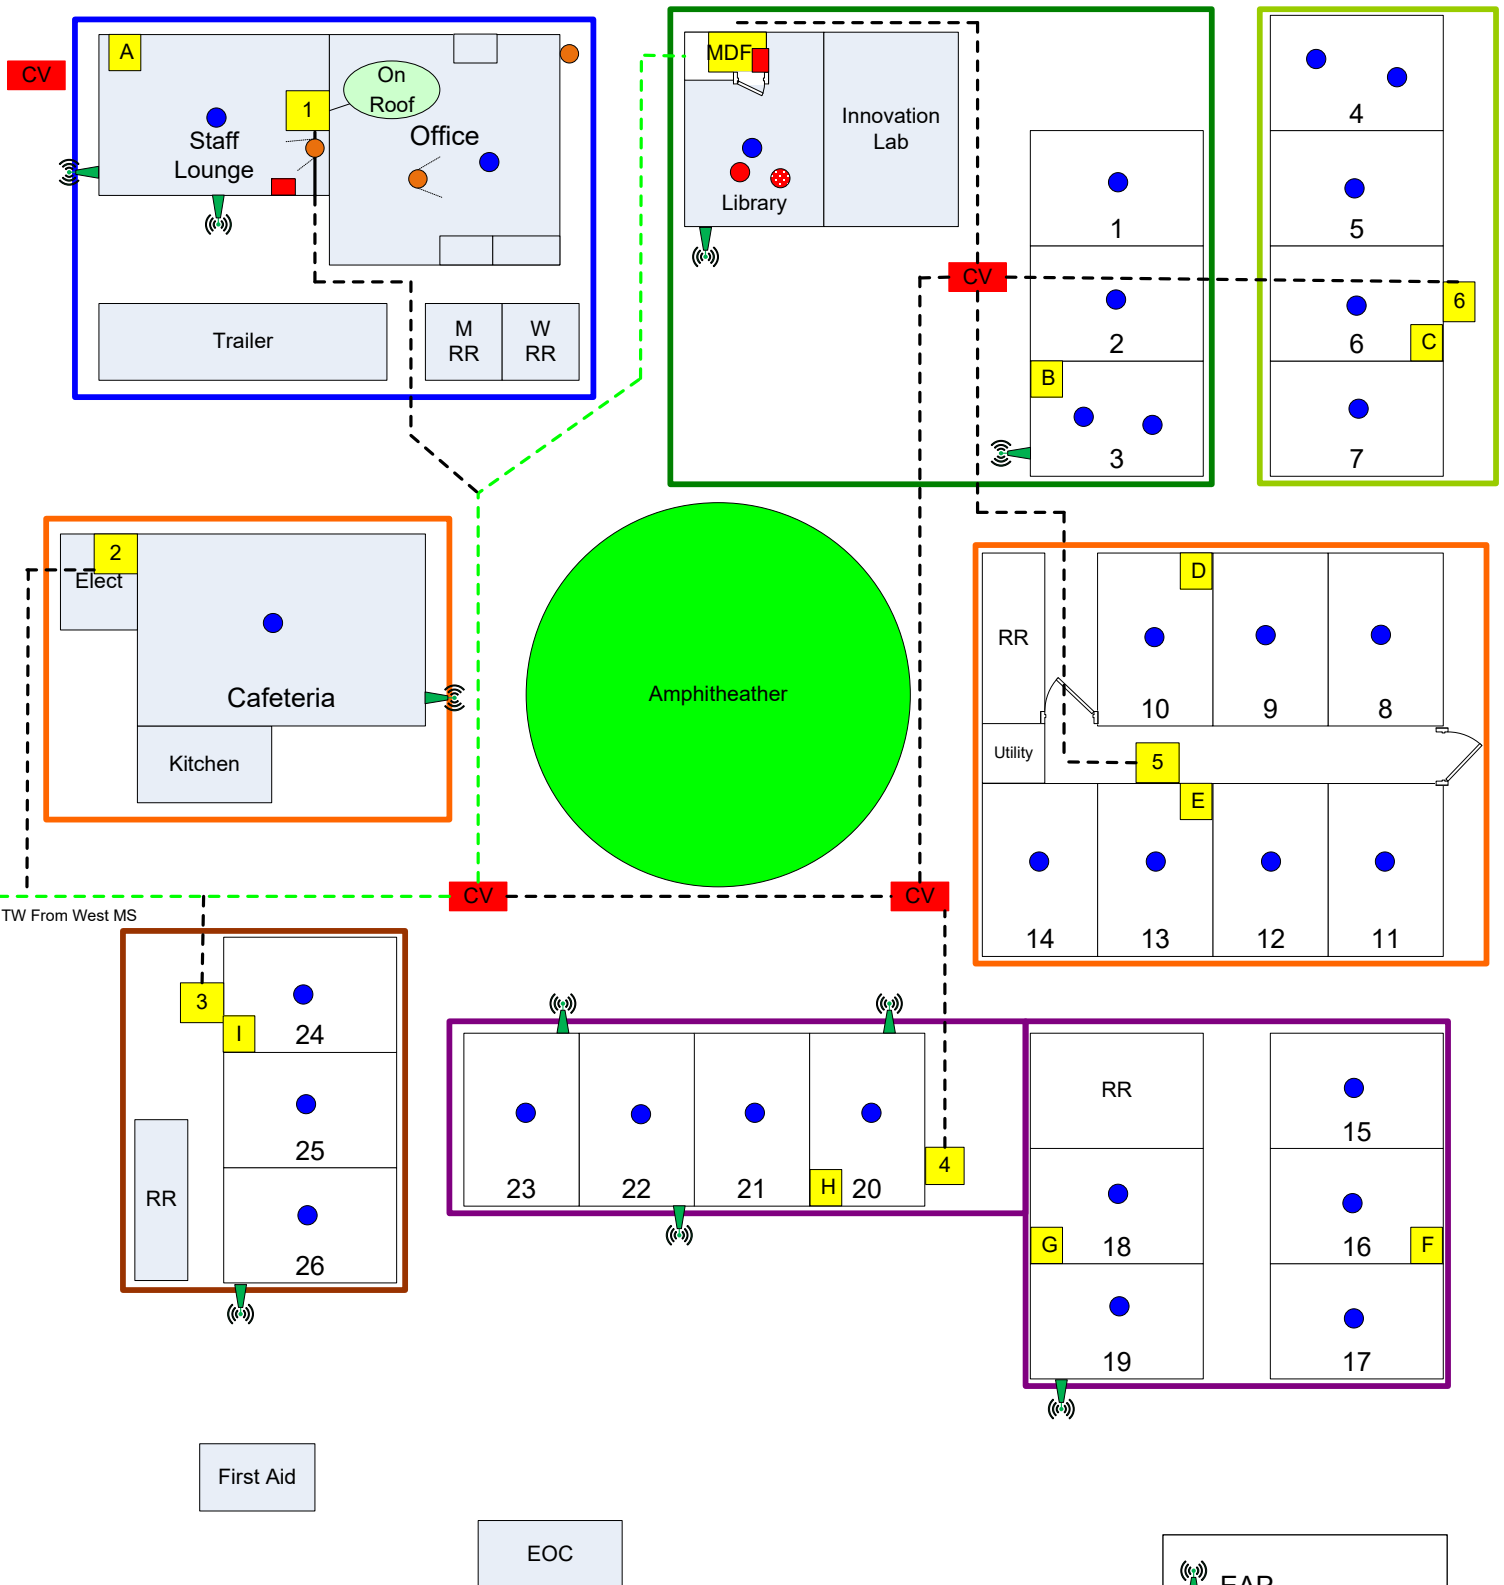


Old River School
 11995 Old River School Road
 Downey, CA 90241
 Downey Unified School District - Confidential

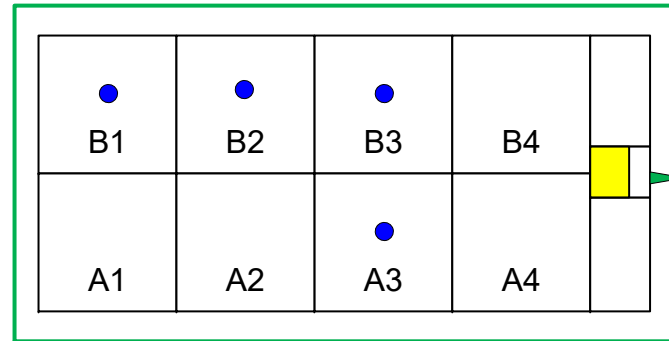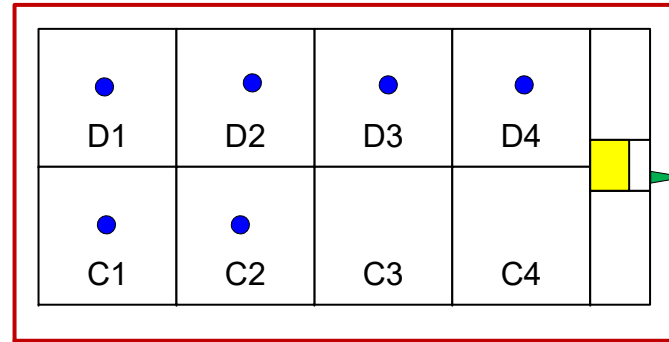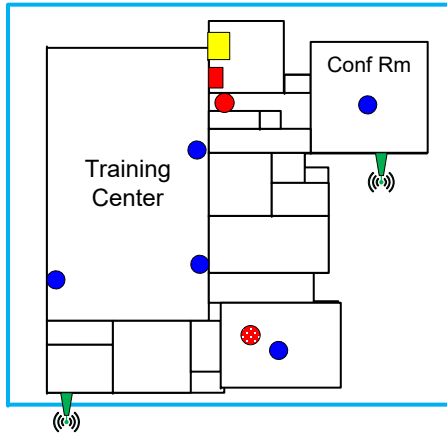


Pace Education Center









9625 Van Ruiten St

Bellflower, CA 90706


















Maude Price

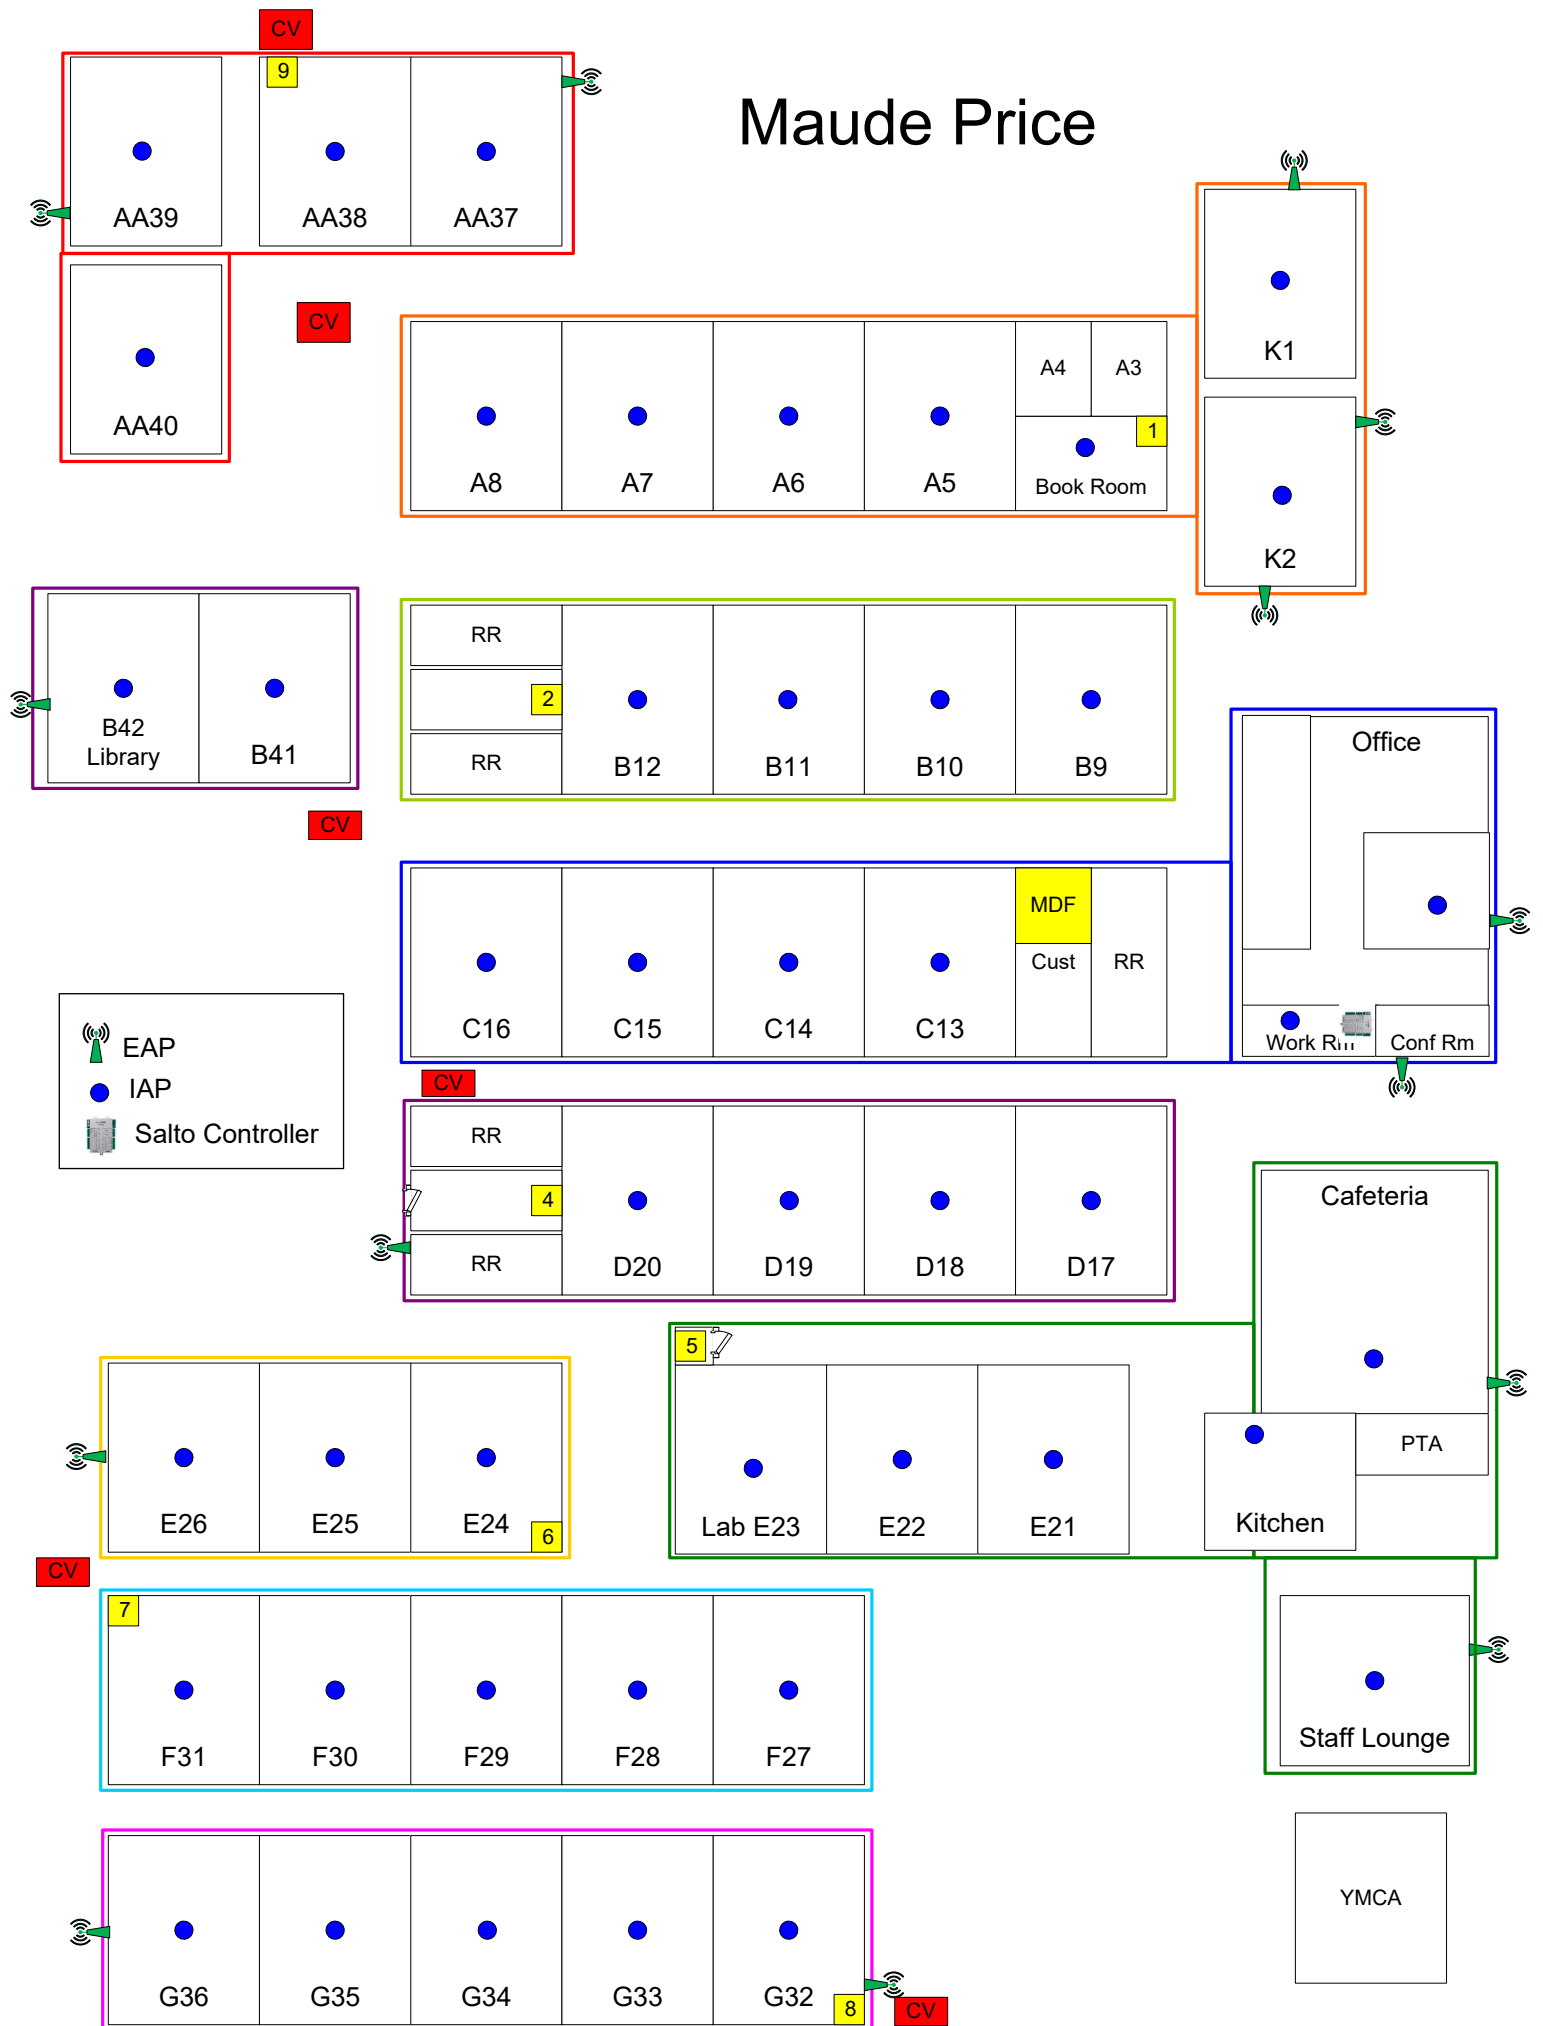

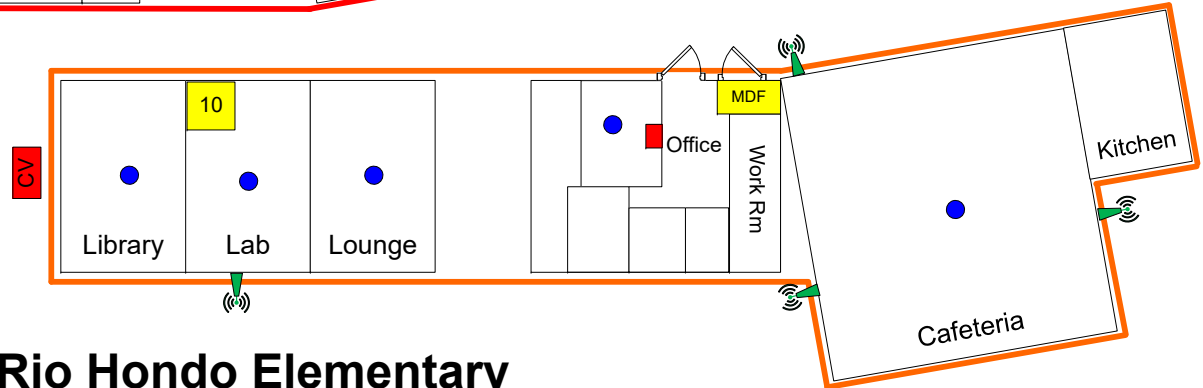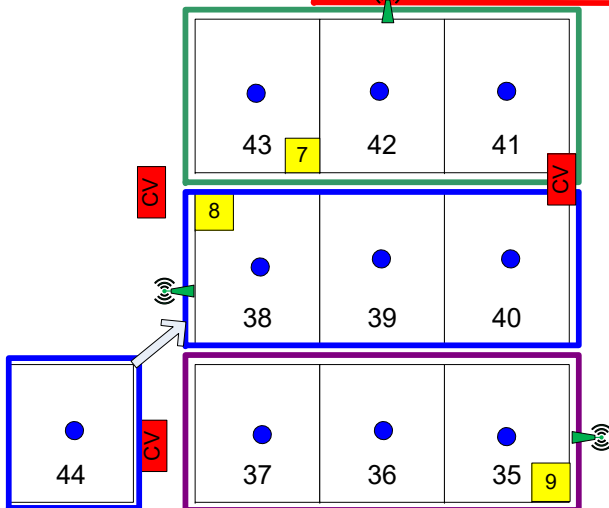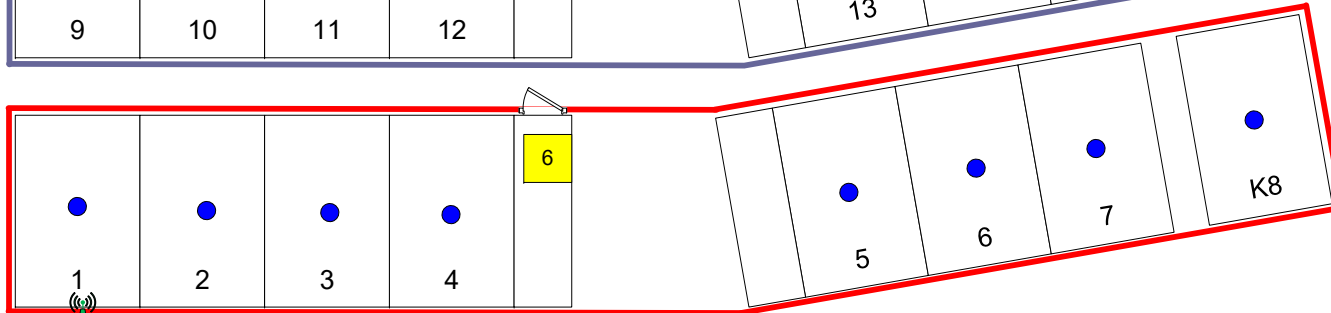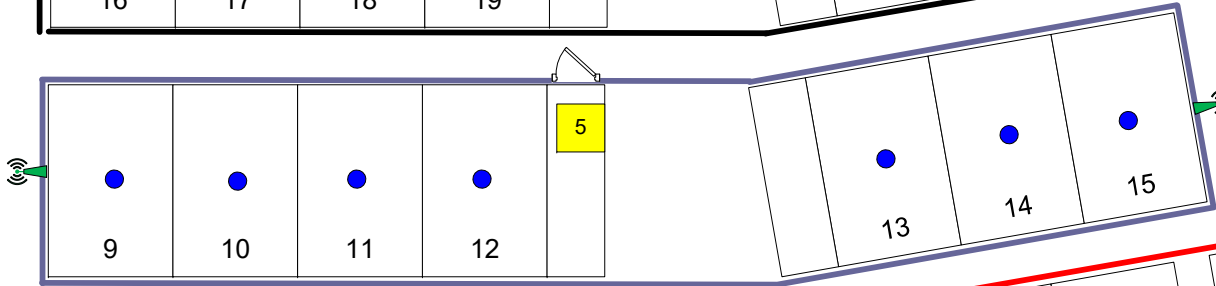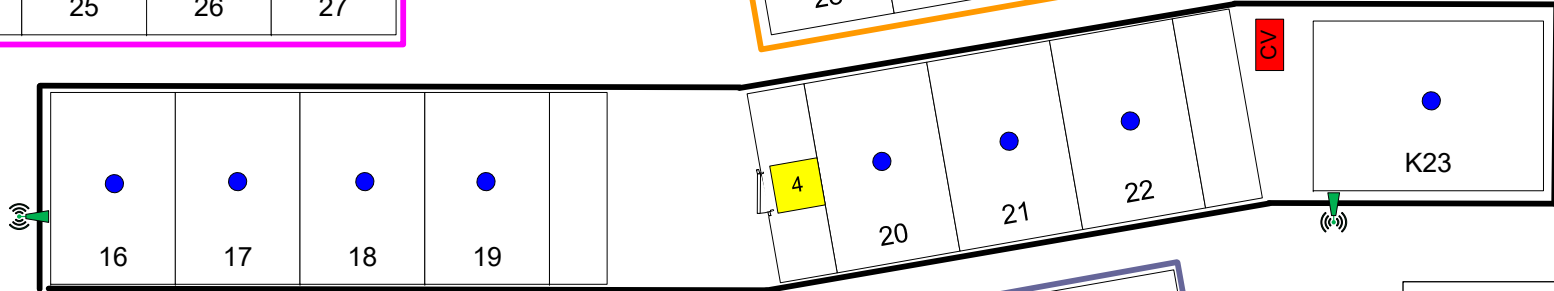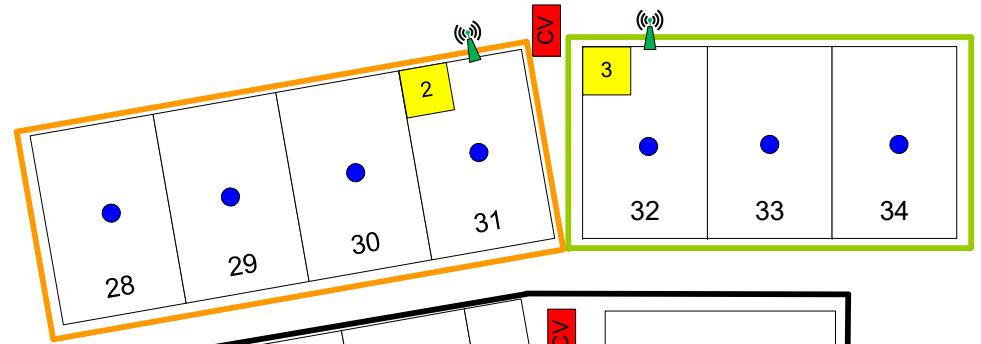



Rio Hondo Elementary
7731 Muller St.
Downey, CA 90241

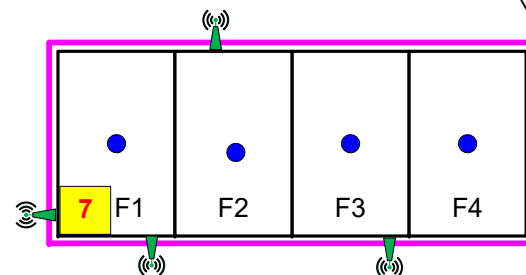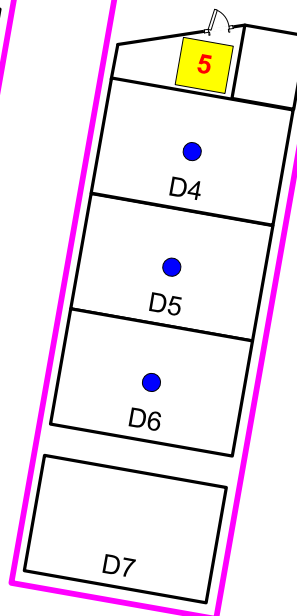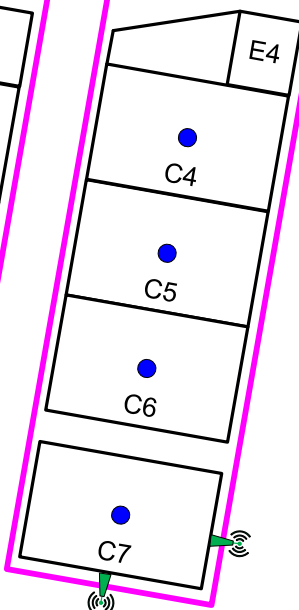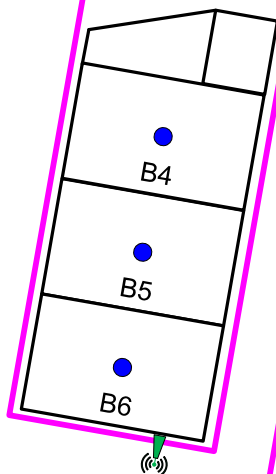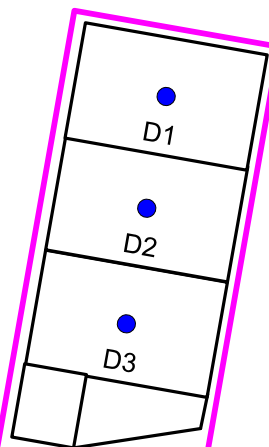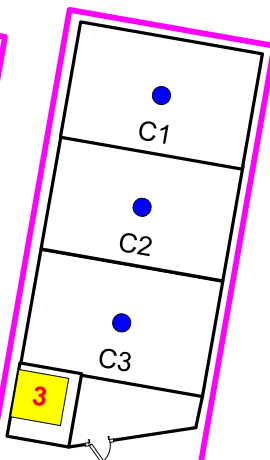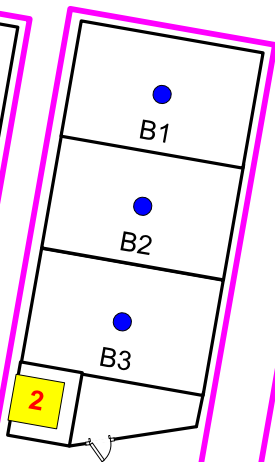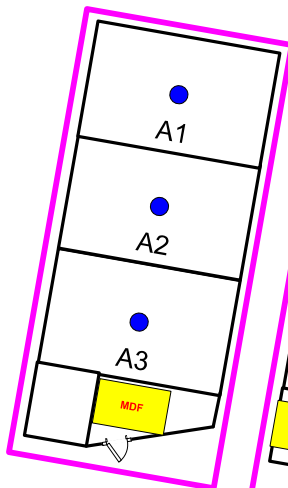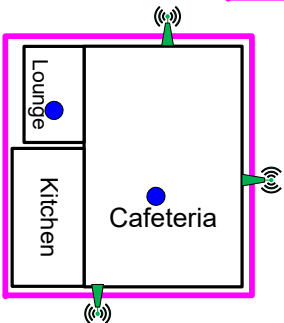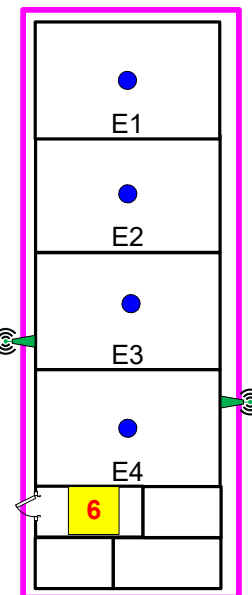


Rio San Gabriel
9338 Gotham St
Downey, CA 90241

Revised: 2/2020 mh





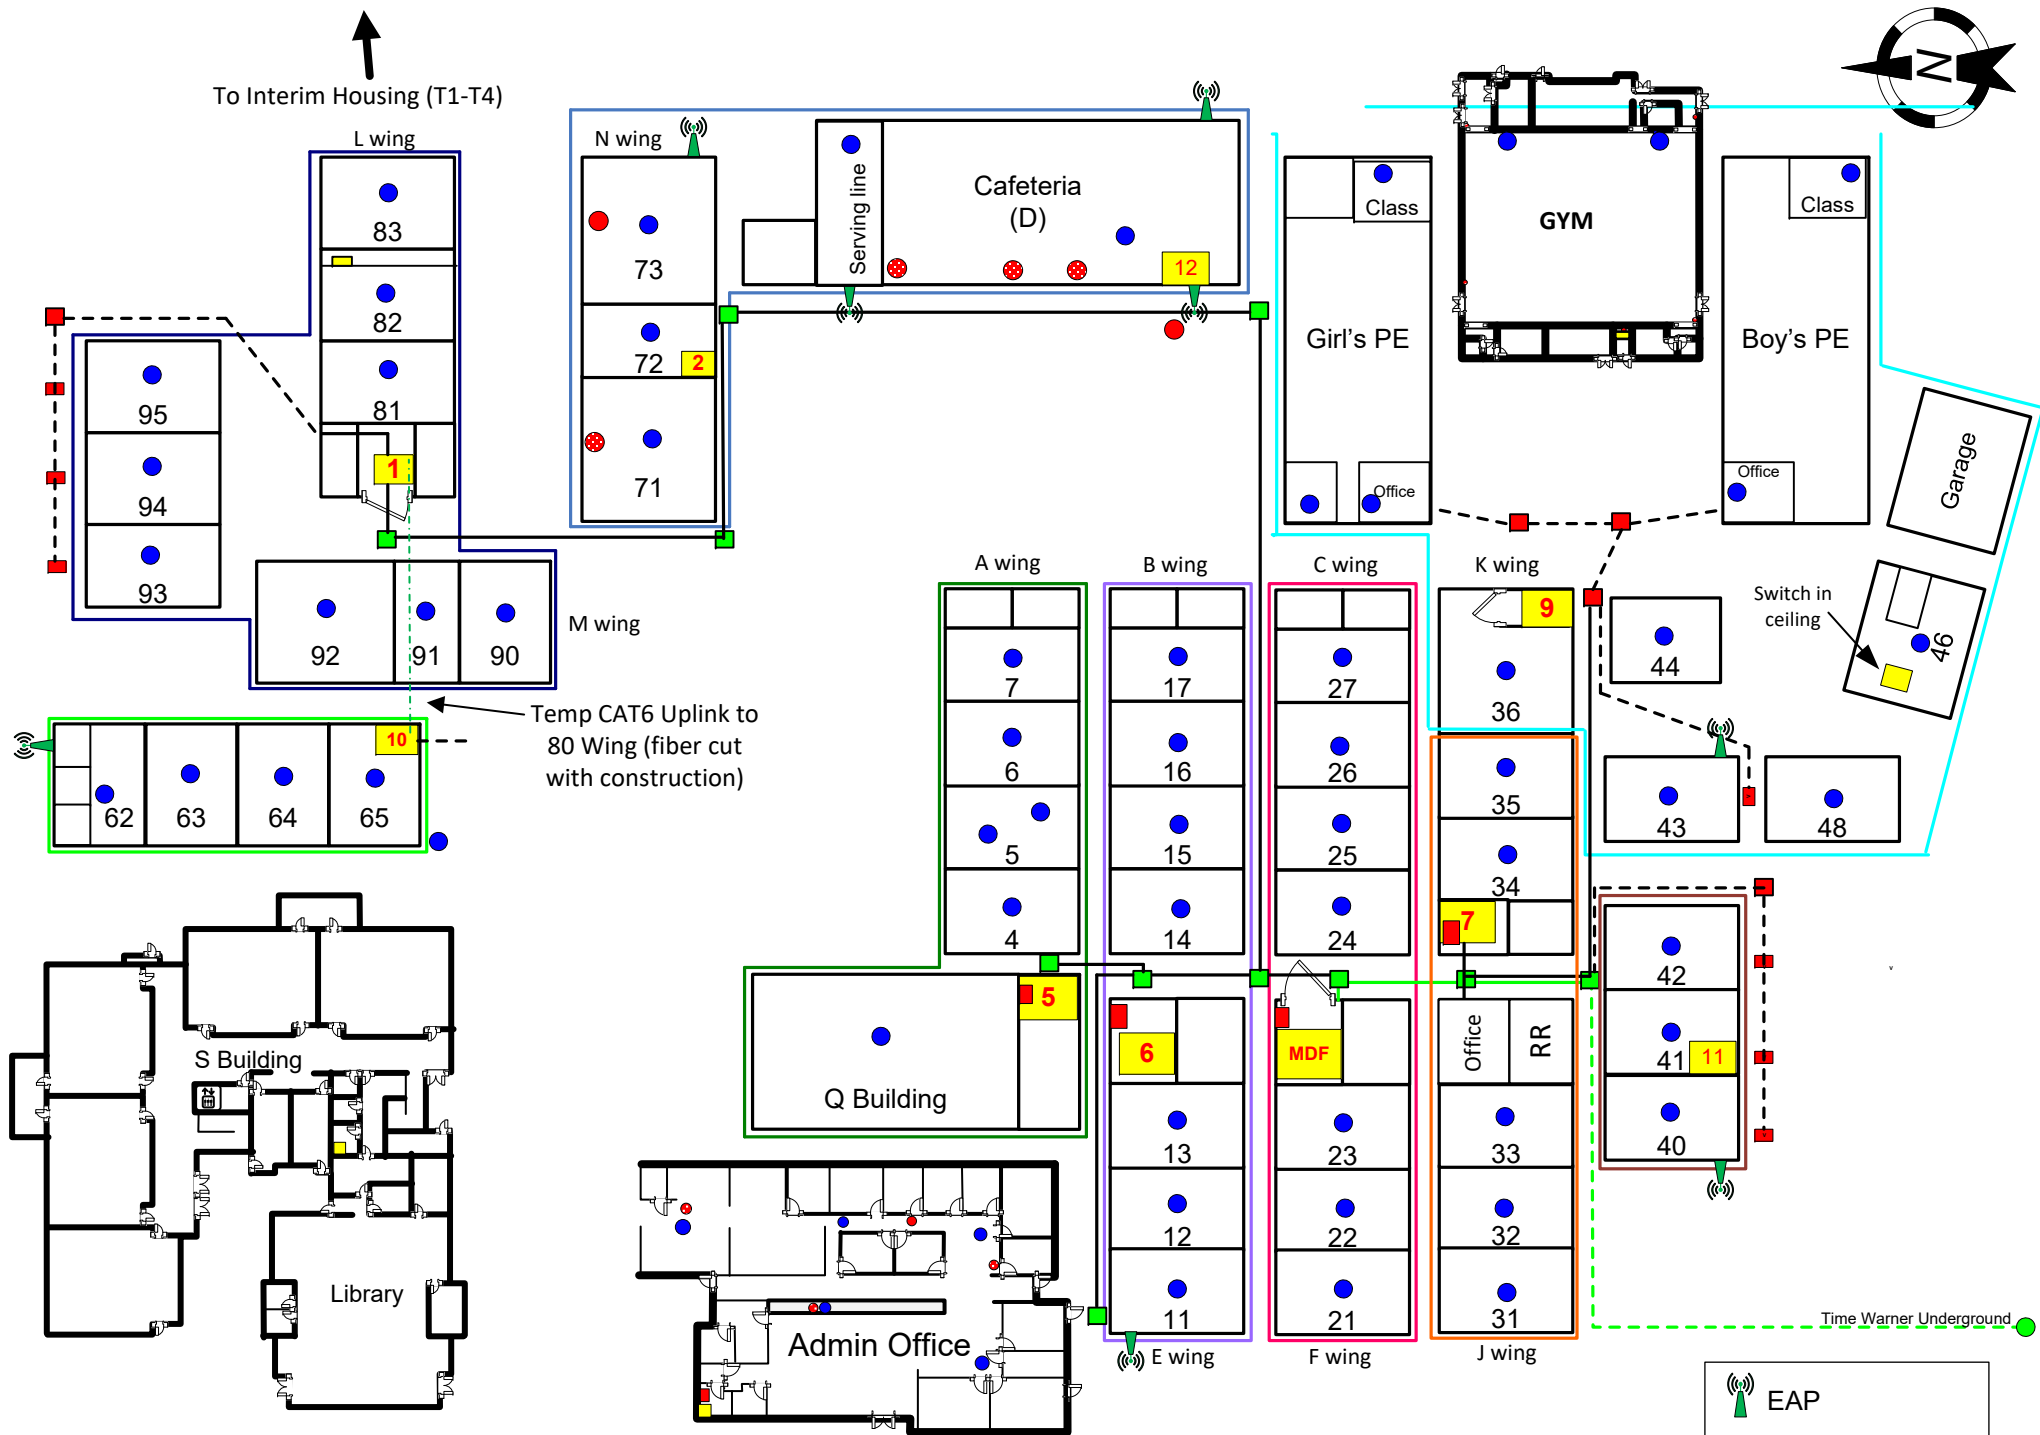


Sussman
12500 Birchdale
Downey, CA 90241
 Downey Unified School District - Confidential

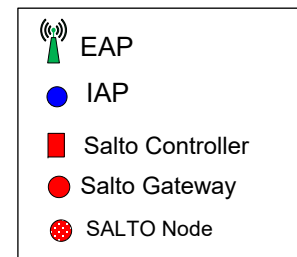


Sussman Admin Office

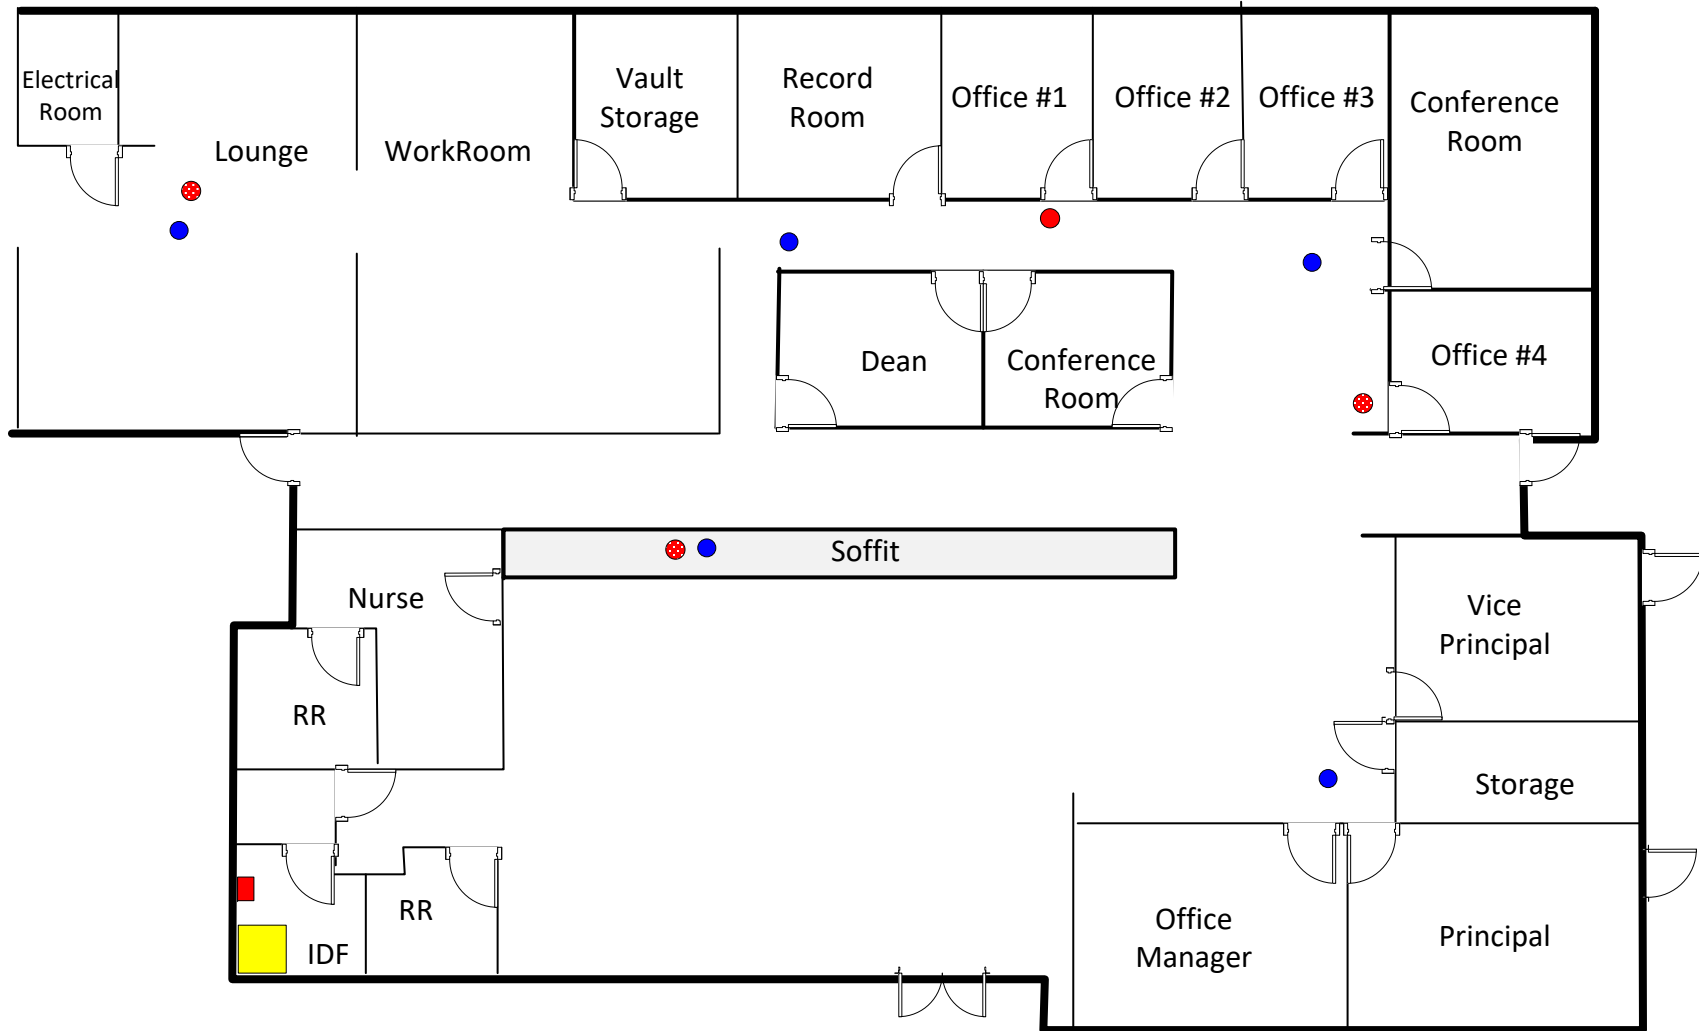



Sussman Gym

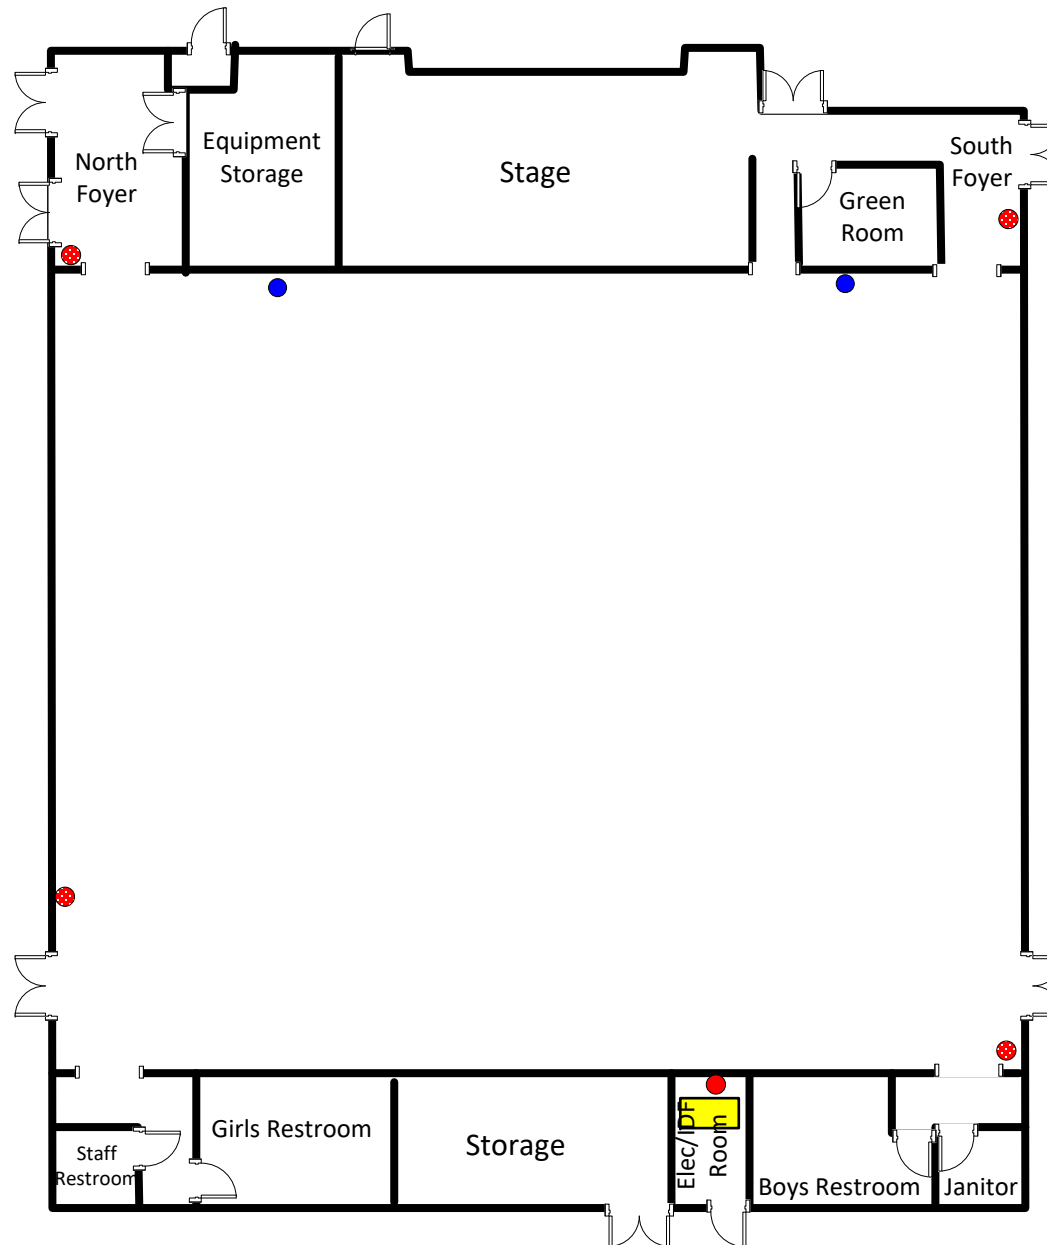



Sussman Girls Locker

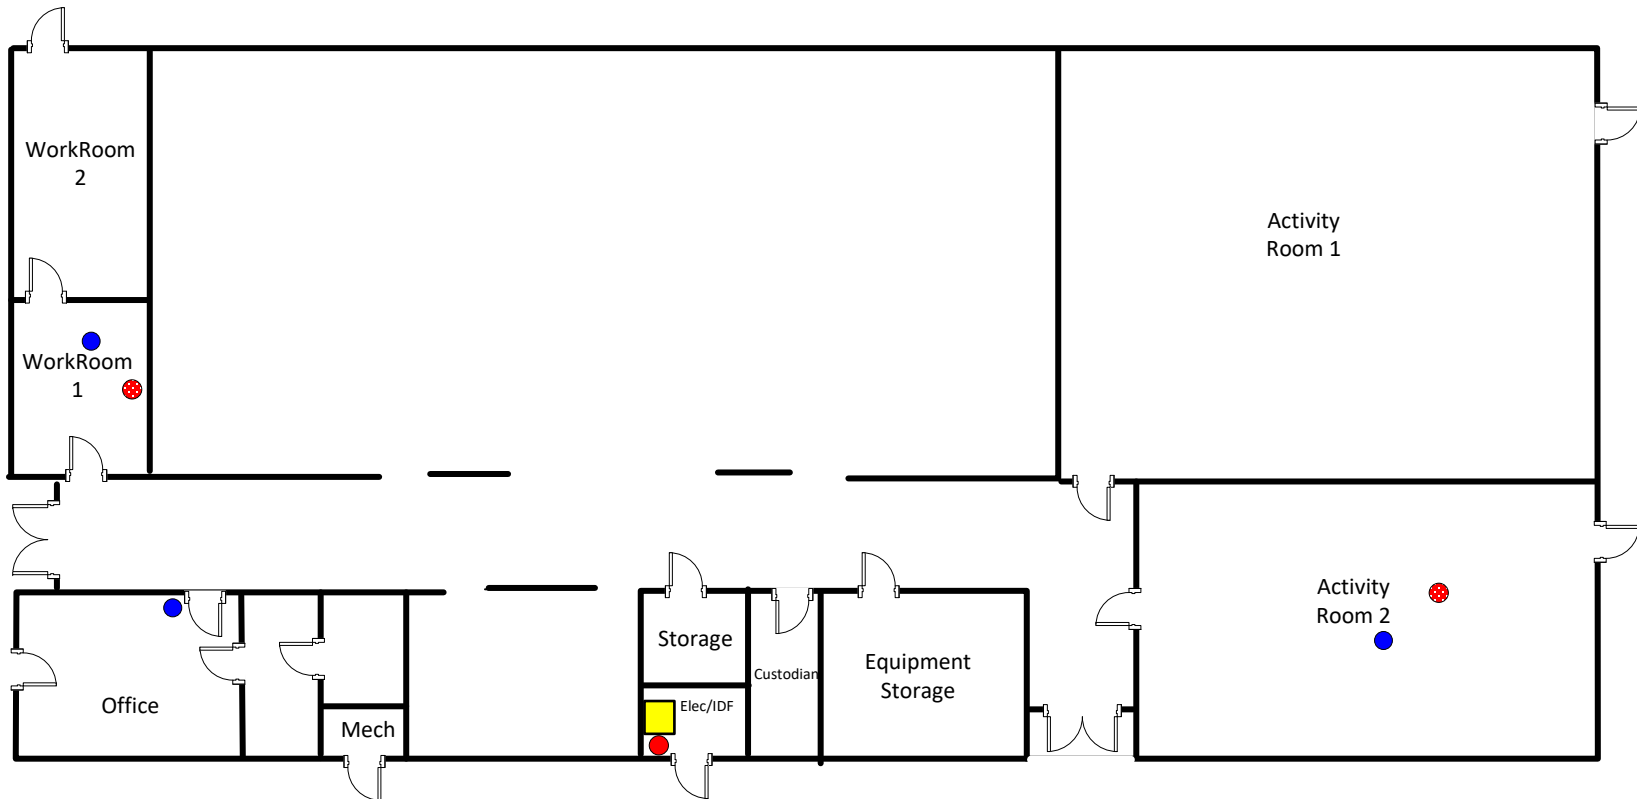



Sussman Boys Locker

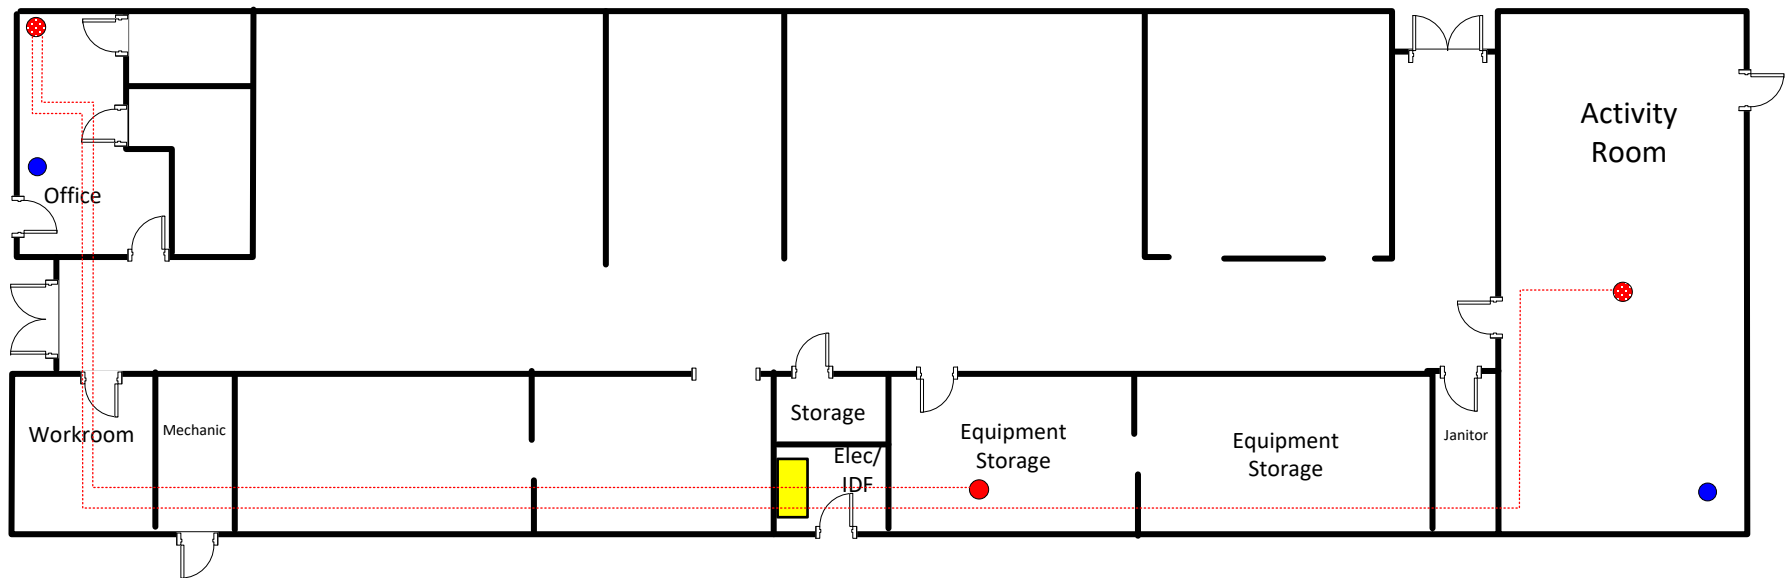


S Building First Floor

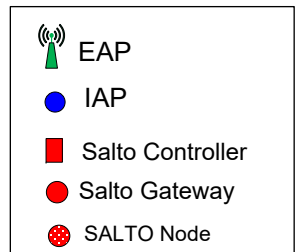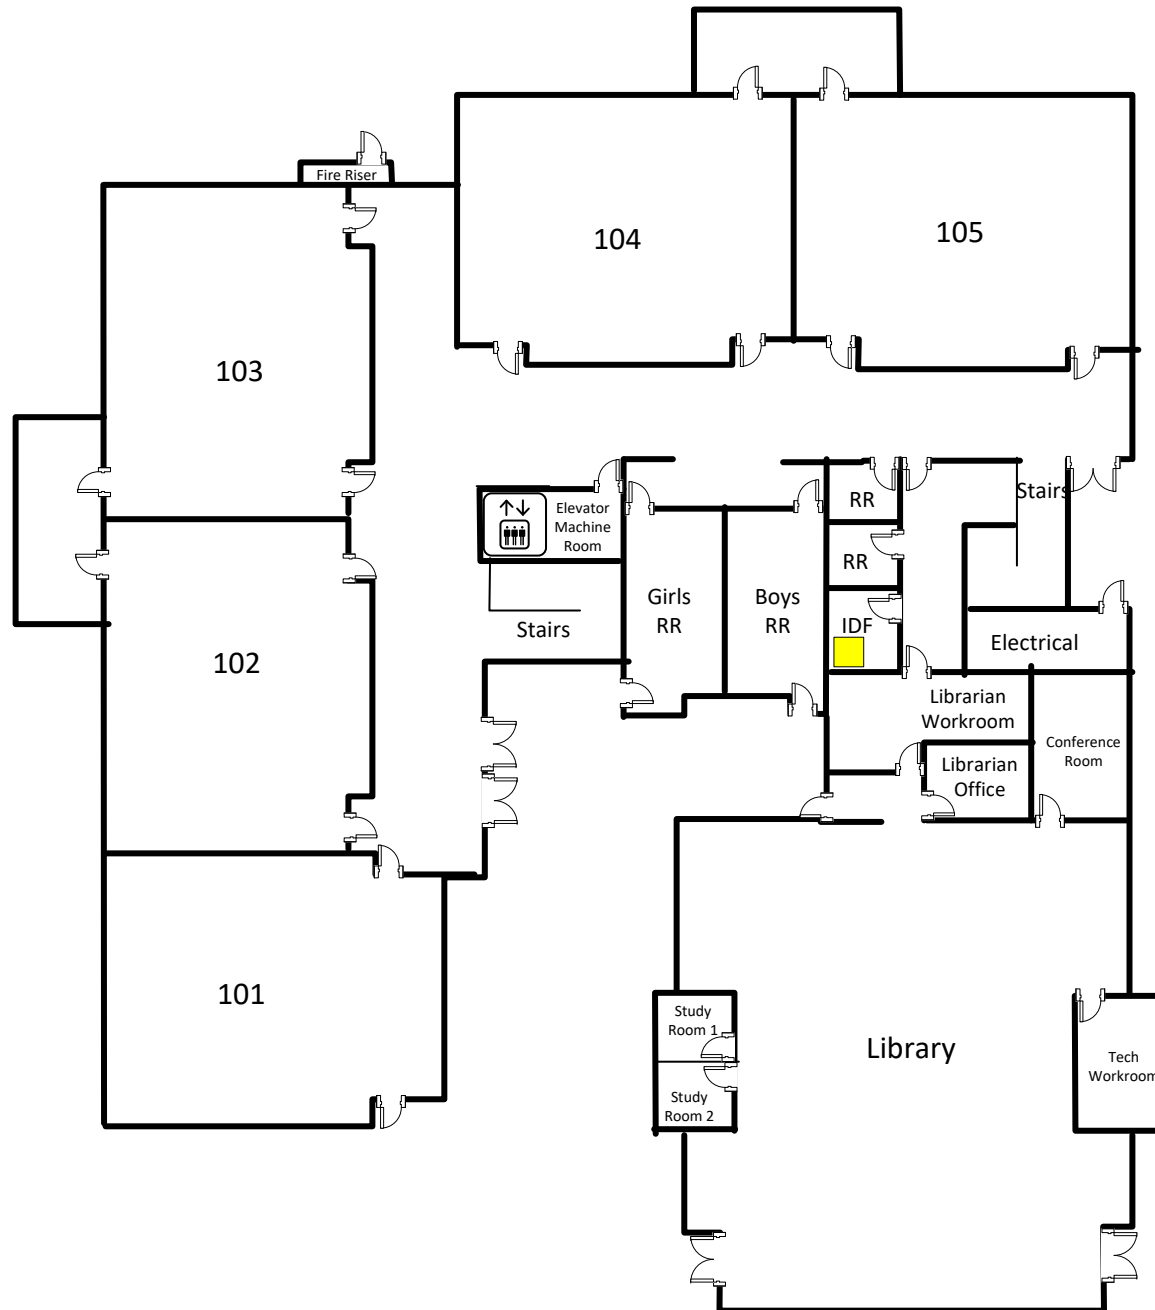















S Building 2nd Floor

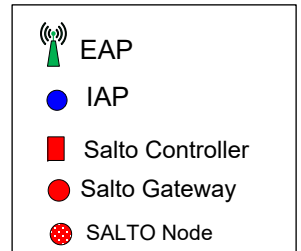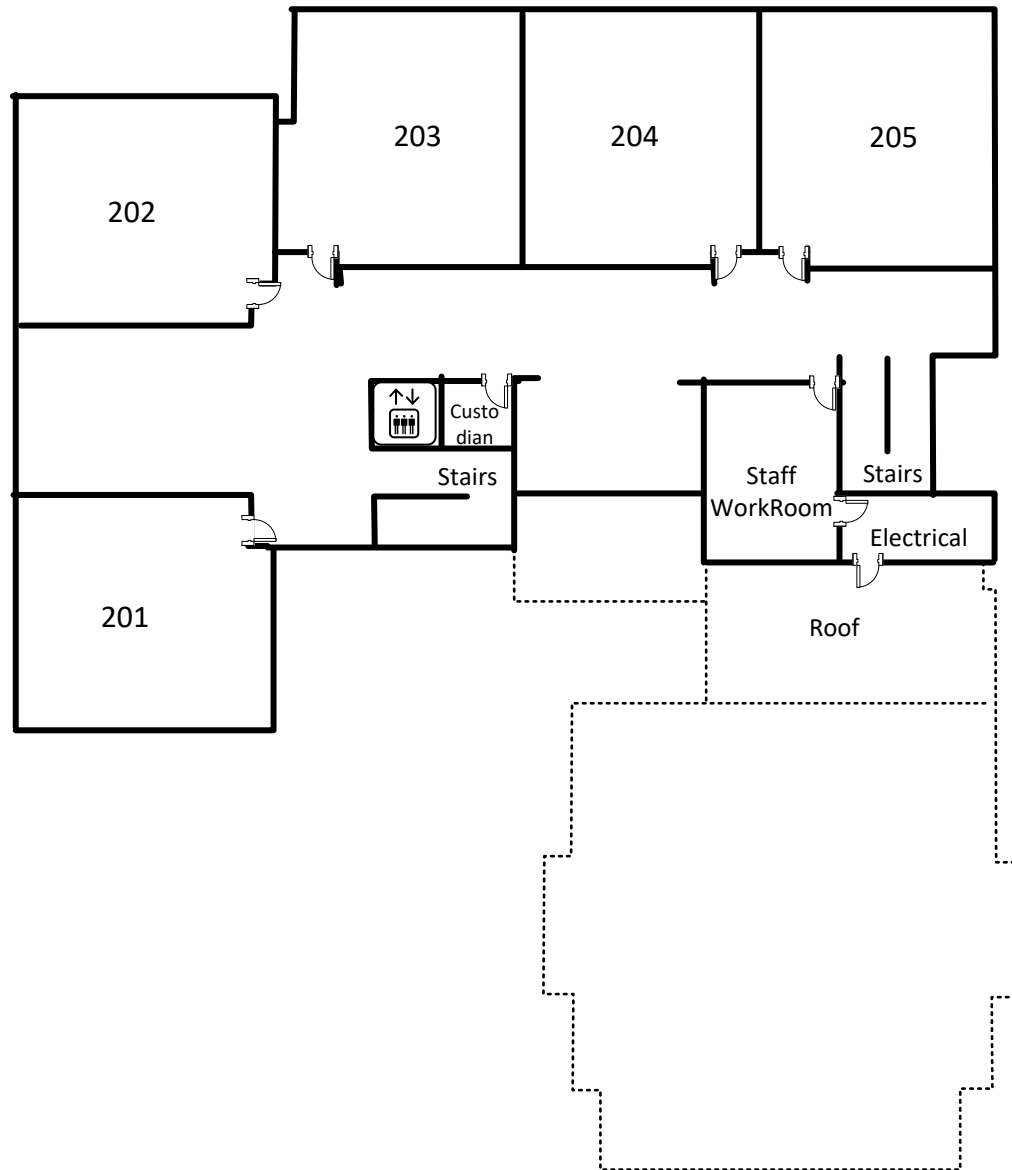







Interim Housing Classrooms

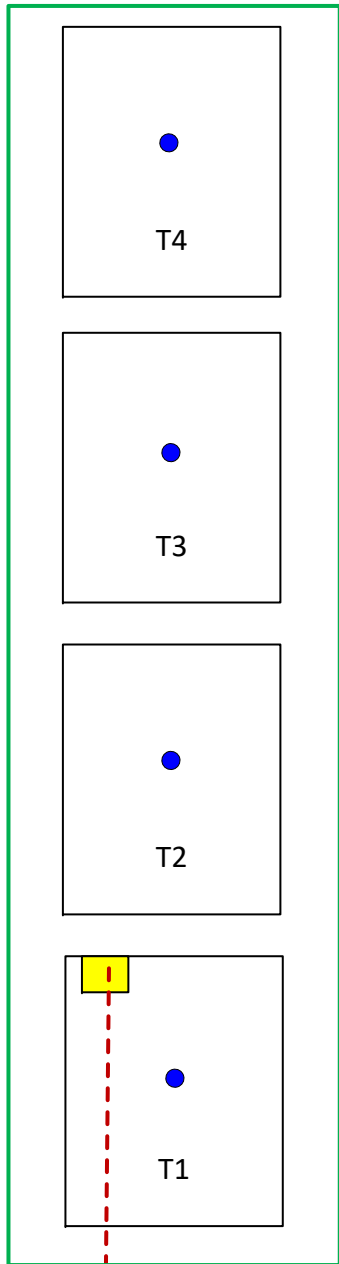

← Aerial fiber to 80 wing
IDF

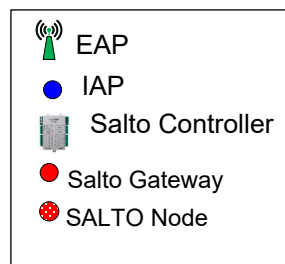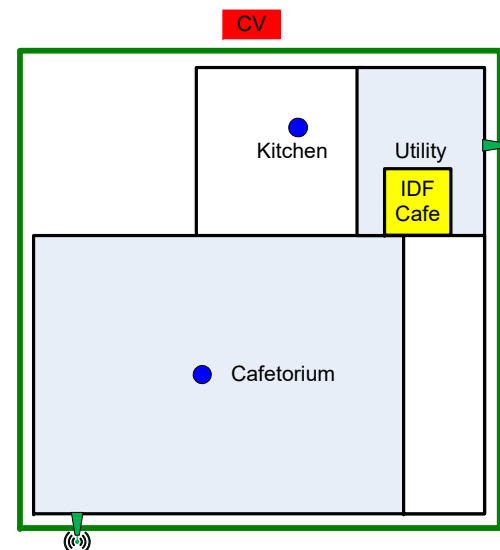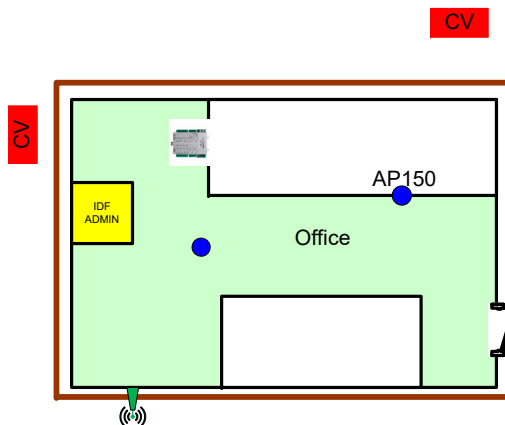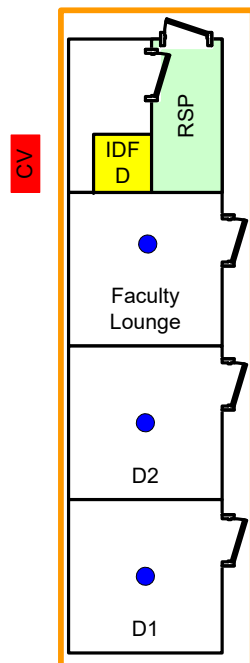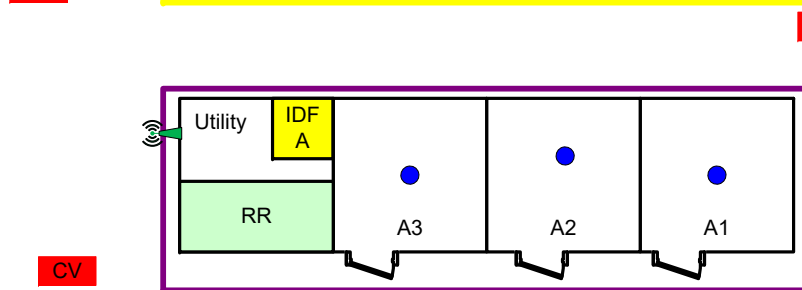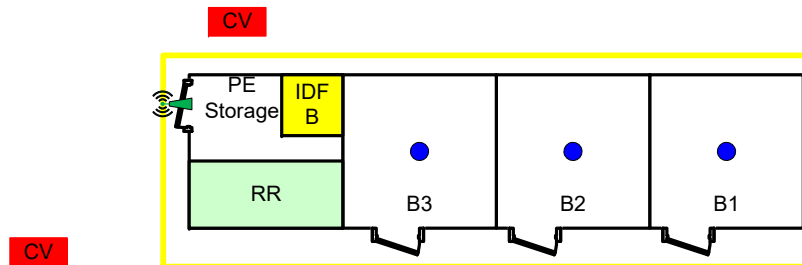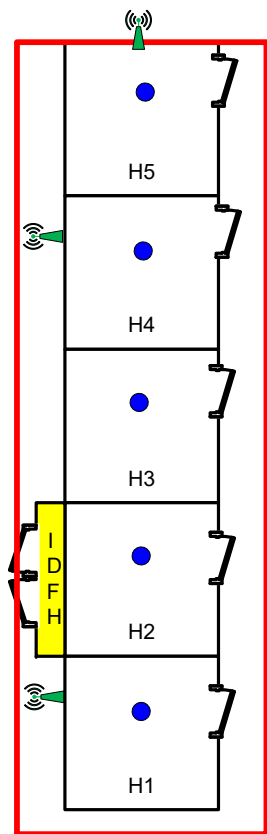


Unsworth Elementary School
9001 Lindsey Avenue
Downey, CA 90240
562-904-3576

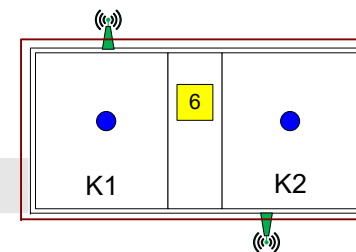


E.W. Ward
 8851 Adoree St
 Downey, CA 90242

Downey Unified School District - Confidential

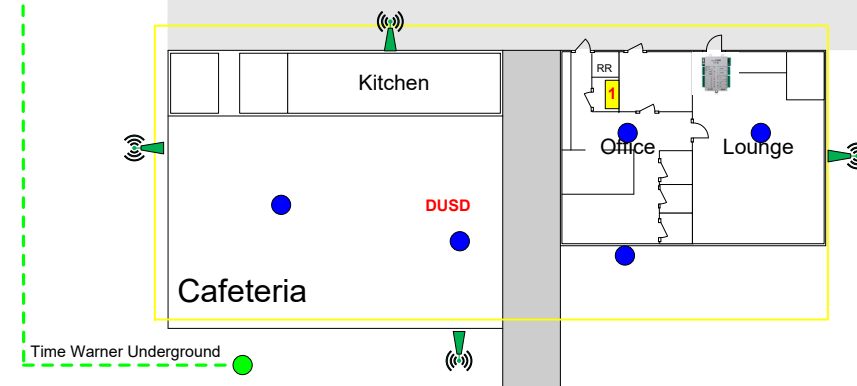

Adoree St

Revised: 5/2018 mh

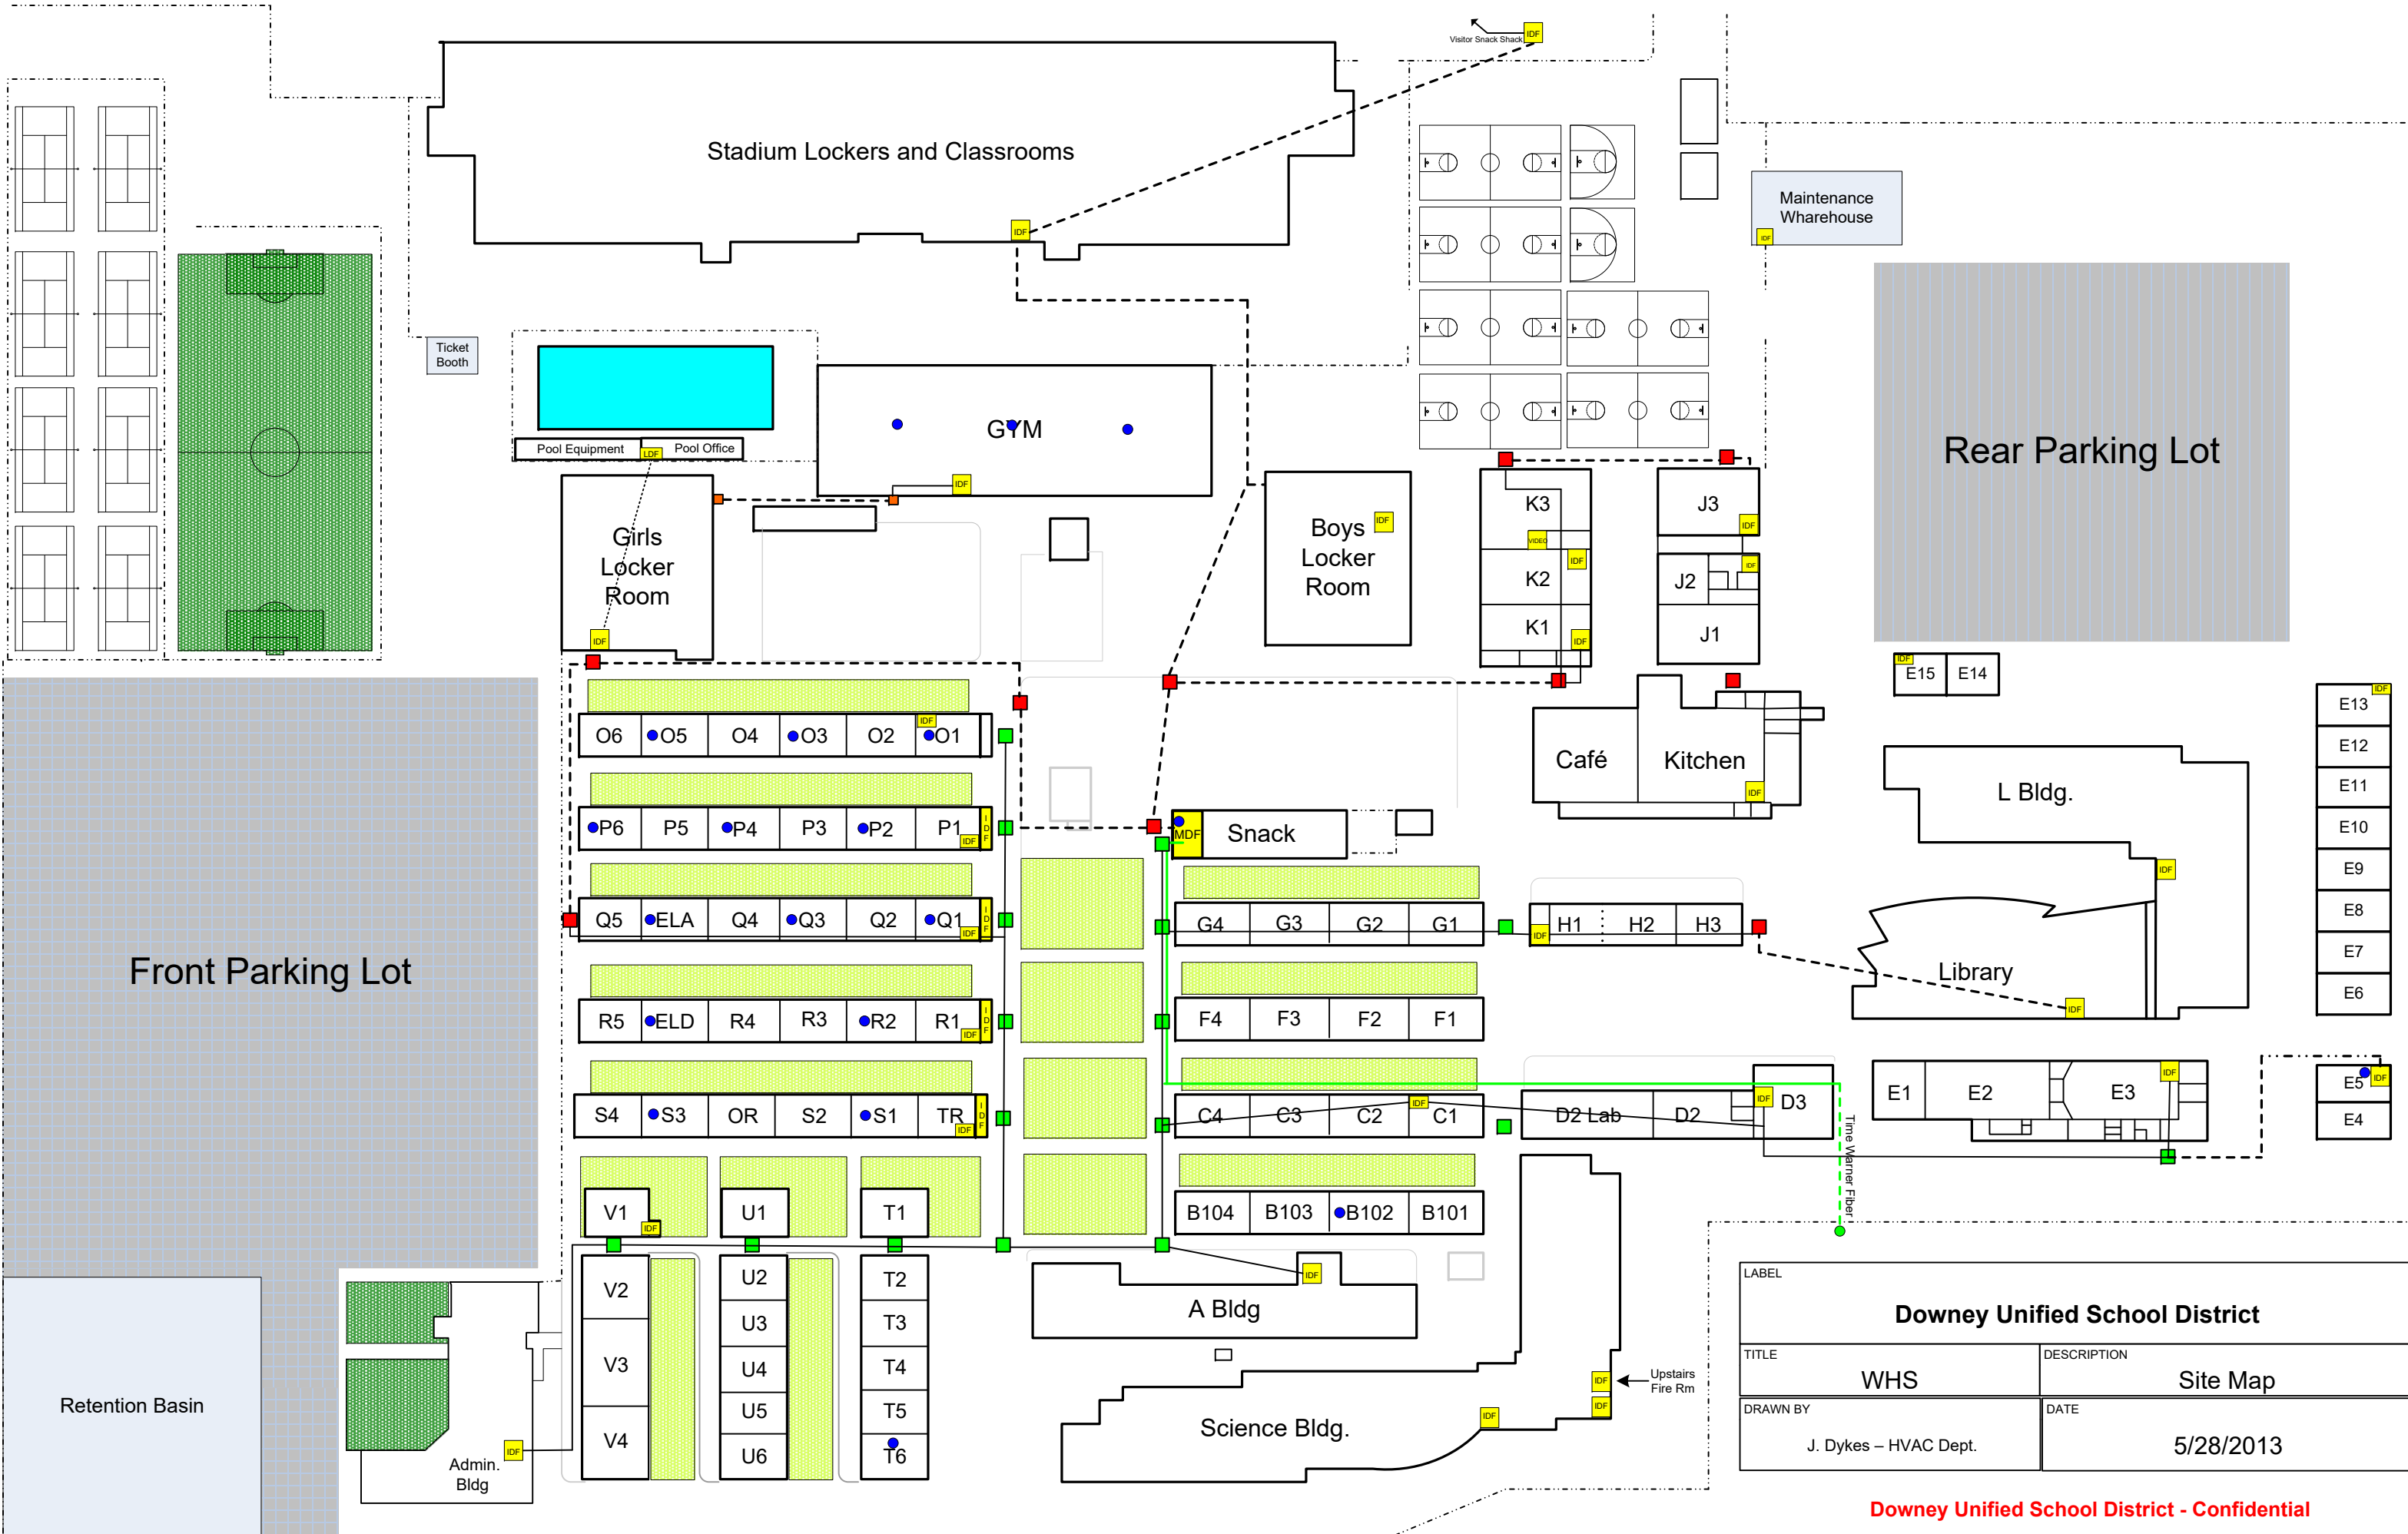

LABEL	
Downey Unified School District	
TITLE	DESCRIPTION
WHS	Site Map
DRAWN BY	DATE
J. Dykes – HVAC Dept.	5/28/2013

Williams
Elementary
7530 Arnett Street
Downey, CA 90241

- EAP
- IAP
- Salto Controller

